




Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors
Milestones												
PID 117955												
233008 FAY-435												
PROJECT WIDE												
☒	A1000	PROJECT START	0d	0d	0d	19-Oct-23	19-Oct-23			233008 7 Day No Restriction - 233008 7 Day No Restriction		BU1-0000
☐	A1160	I-71 RAMP A	30d	30d	18d	22-Mar-24	18-Apr-24	02-May-24	28-May-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-135, BU4-P1-135	BU4-P1-195, BU4-P1-195
☐	A1200	AREA 2	22d	22d	45d	25-Mar-24	29-May-24	23-Apr-24	25-Jun-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-415, BU4-P1-415	BU4-P1-475, BU4-P1-475
☐	A1240	35 to 435 RAMP D	53d	53d	93d	04-Apr-24	01-Aug-24	17-Jun-24	24-Oct-24	Standard 5 Day Workweek - Standard 5 Day Workweek	D-P1-1000, D-P1-1000	D-P2-1190, D-P2-1190
☐	A1190	AREA 1	19d	19d	46d	24-Apr-24	26-Jun-24	20-May-24	23-Jul-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-480, BU4-P1-480	BU4-P1-545, BU4-P1-545
☐	A1180	I-71 RAMP D	27d	27d	17d	07-May-24	29-May-24	12-Jun-24	05-Jul-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-205, BU4-P1-205	BU4-P1-270, BU4-P1-270
☐	A1210	AREA 3	25d	25d	46d	20-May-24	23-Jul-24	21-Jun-24	26-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-550, BU4-P1-550	BU4-P1-610, BU4-P1-610
☐	A1170	I-71 RAMP B	40d	40d	16d	12-Jun-24	05-Jul-24	06-Aug-24	28-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-280, BU4-P1-280	BU4-P2-405, BU4-P2-405
☐	A1040	DETOUR 729	19d	19d	0d	12-Aug-24	04-Sep-24	05-Sep-24	05-Sep-24	Standard 5 Day Workweek - Standard 5 Day Workweek	729-P3-1090, 729-P3-1090	729-P3-1080, 729-P3-1080
☐	A1010	INTERIM COMPLETION 435 WEST	0d	0d	18d			20-Aug-24	13-Sep-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU6-100-001, BU6-100-002, BU6-100-0...	A1050
☐	A1030	INTERIM COMPLETION 435 EAST	0d	0d	0d			31-Oct-24	31-Oct-24	Standard 5 Day Workweek - Standard 5 Day Workweek	435-P5-1060, D-P2-1200	A1050
☒	A1050	PROJECT COMPLETION	0d	0d	0d			01-Jul-25	01-Jul-25	Standard 5 Day Workweek - Standard 5 Day Workweek	BU6-100-003, A1030, 435-P6-1040, A1010	
Preconstruction												
435 PROJECT WIDE												
DESIGN												
PROJECT ADMINISTRATION												
☒	BU1-0000	DESIGN BUILD NTP & PRE-DESIGN MEETING	1d	1d	0d	19-Oct-23	19-Oct-23	19-Oct-23	19-Oct-23	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	A1000	BU1-1000
☐	A1220	PERFORM CEMENT STABILIZATION MIX DESIGN	25d	25d	29d	31-Jan-24	13-Mar-24	06-Mar-24	16-Apr-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-1010	A1230
☐	BU2-1030	SECURE NOI PERMIT	20d	20d	28d	01-Feb-24	13-Mar-24	29-Feb-24	09-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1025	BU2-1035
☐	BU2-1035	INITIATE SWPPP	3d	3d	28d	01-Mar-24	10-Apr-24	05-Mar-24	12-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1030	BU2-P1-100
☐	A1230	ODOT REVIEW CEMENT STABILIZATION MIX DESIGN	10d	10d	29d	06-Mar-24	17-Apr-24	20-Mar-24	30-Apr-24	Standard 5 Day Workweek - Standard 5 Day Workweek	A1220	BU4-P1-160
☐	A1100	REQUEST NEW POWER SERVICE	10d	10d	113d	07-Mar-24	14-Aug-24	21-Mar-24	27-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU3-1025	A1110
☐	A1140	COORDINATE AT&T FACILITIES	30d	30d	81d	07-Mar-24	01-Jul-24	18-Apr-24	09-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU3-1025	A1150
☐	A1120	COORDINATE AES RELOCATION	30d	30d	91d	07-Mar-24	15-Jul-24	18-Apr-24	23-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU3-1025	A1130
☐	A1110	AES SETUP POWER SERVICE	5d	5d	113d	21-Mar-24	28-Aug-24	28-Mar-24	03-Sep-24	Standard 5 Day Workweek - Standard 5 Day Workweek	A1100	D-P1-1080
☐	A1150	AT&T RELOCATE FACILITIES	20d	20d	81d	18-Apr-24	12-Aug-24	16-May-24	06-Sep-24	Standard 5 Day Workweek - Standard 5 Day Workweek	A1140	435-P4-1000
☐	A1130	AES RELOCATE POWER POLES & LINES	10d	10d	91d	18-Apr-24	26-Aug-24	02-May-24	06-Sep-24	Standard 5 Day Workweek - Standard 5 Day Workweek	A1120	435-P4-1000
PROJECT WIDE												
☒	BU1-1000	Design BU1 - Geometrics	10d	10d	0d	20-Oct-23	20-Oct-23	02-Nov-23	02-Nov-23	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU1-0000	BU1-1010
☒	BU1-1010	ODOT REVIEW & ACCEPT BU1	10d	10d	0d	03-Nov-23	03-Nov-23	16-Nov-23	16-Nov-23	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU1-1000	BU5-1000, BU3-1000, BU2-1000, BU4-1000
☒	BU3-1000	DESIGN PRELIM BU3 - TRFFIC SIGNALS & LIGHTING	25d	25d	1d	17-Nov-23	20-Nov-23	22-Dec-23	26-Dec-23	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU1-1010	BU3-1005
☐	BU5-1000	DESIGN PRELIM BU5 - 435 EAST - RAB - RAMP D	40d	40d	0d	17-Nov-23	17-Nov-23	17-Jan-24	17-Jan-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU1-1010	BU5-1005
☐	BU2-1000	DESIGN PRELIM BU2 - WATER/SANITARY	10d	10d	28d	17-Nov-23	29-Dec-23	01-Dec-23	12-Jan-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU1-1010	BU2-1005
☐	BU4-1000	DESIGN PRELIM BU4 - 435 WEST & I-71 RAMPS	30d	30d	19d	17-Nov-23	15-Dec-23	02-Jan-24	30-Jan-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU1-1010	BU7-1000, BU4-1005
☐	BU2-1005	ODOT REVIEW PRELIM BU2	10d	10d	28d	04-Dec-23	16-Jan-24	15-Dec-23	29-Jan-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1000	BU2-1010
☐	BU2-1010	DESIGN STAGE 2 BU2	5d	5d	28d	18-Dec-23	30-Jan-24	22-Dec-23	05-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1005	BU2-1015
☒	BU3-1005	ODOT REVIEW PRELIM BU3	10d	10d	1d	26-Dec-23	27-Dec-23	09-Jan-24	10-Jan-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU3-1000	BU3-1010
☐	BU2-1015	ODOT REVIEW STAGE 2 BU2	10d	10d	28d	26-Dec-23	06-Feb-24	09-Jan-24	20-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1010	BU2-1020

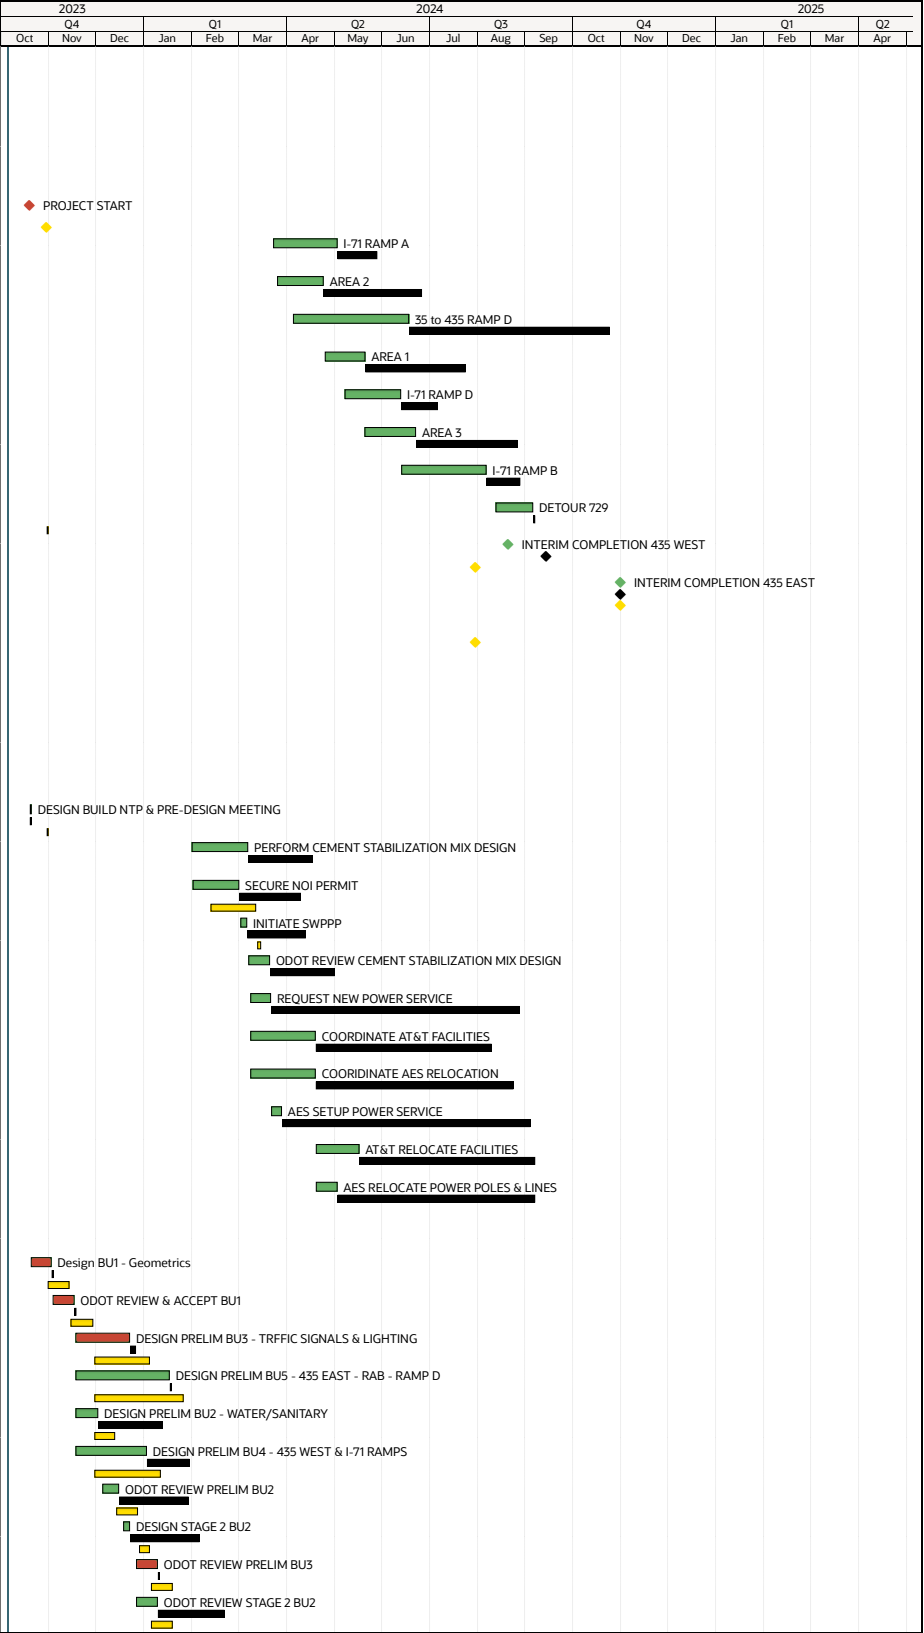

Current

Progress

Critical

Float (Fallback)

Original Baseline

Milestones

Summary

PROJECT NUMBER: 233008

PID#: 117955, CONTRACT ID: FAY117955

COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024

INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024

PROJECT COMPLETION: 7/1/2025



Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors	
	☐	BU7-1000	DESIGN PRELIM BU7 - BOX CULVERT	10d	10d	24d	03-Jan-24	07-Feb-24	17-Jan-24	21-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU4-1000	BU7-1005
	☐	BU4-1005	ODOT REVIEW PRELIM BU4	10d	10d	19d	03-Jan-24	31-Jan-24	17-Jan-24	13-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU4-1000	BU4-1010
	☐	BU2-1020	DESIGN RFC PLANS BU2	5d	5d	28d	10-Jan-24	21-Feb-24	17-Jan-24	27-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1015	BU2-1025
	☒	BU3-1010	DESIGN STAGE 2 BU3	15d	15d	1d	10-Jan-24	11-Jan-24	31-Jan-24	01-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU3-1005	BU3-1015
	☐	BU4-1010	DESIGN STAGE 2 BU4	10d	10d	19d	18-Jan-24	14-Feb-24	31-Jan-24	28-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU4-1005	A1220, A1060, BU4-1015
	☐	BU2-1025	ODOT ACCEPT RFC PLANS BU2	10d	10d	28d	18-Jan-24	28-Feb-24	31-Jan-24	12-Mar-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU2-1020	BU2-1030
	☐	BU5-1005	ODOT REVIEW PRELIM BU5	10d	10d	0d	18-Jan-24	18-Jan-24	31-Jan-24	31-Jan-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU5-1000	BU5-1010
	☐	BU7-1005	ODOT REVIEW PRELIM BU7 - BOX CULVERT	10d	10d	24d	18-Jan-24	22-Feb-24	31-Jan-24	06-Mar-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU7-1000	BU7-1010
	☐	BU5-1010	DESIGN STAGE 2 BU5	10d	10d	0d	01-Feb-24	01-Feb-24	14-Feb-24	14-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU5-1005	BU5-1015
	☐	BU7-1010	DESIGN STAGE 2 BU7	10d	10d	24d	01-Feb-24	07-Mar-24	14-Feb-24	20-Mar-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU7-1005	BU7-1015
	☐	BU4-1015	ODOT REVIEW STAGE 2 BU4	10d	10d	19d	01-Feb-24	29-Feb-24	14-Feb-24	13-Mar-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU4-1010	BU4-1020
	☒	BU3-1015	ODOT REVIEW STAGE 2 BU3	10d	10d	1d	01-Feb-24	02-Feb-24	14-Feb-24	15-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU3-1010	BU3-1020
	☐	BU5-1015	ODOT REVIEW STAGE2 BU5	10d	10d	0d	15-Feb-24	15-Feb-24	29-Feb-24	29-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU5-1010	BU5-1020
	☒	BU3-1020	DESIGN RFC PLANS BU3	5d	5d	1d	15-Feb-24	16-Feb-24	22-Feb-24	23-Feb-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU3-1015	A1080, A1090, BU3-1025
	☐	BU4-1020	DESIGN RFC PLANS BU4	15d	15d	19d	15-Feb-24	14-Mar-24	07-Mar-24	03-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU4-1015	BU4-1025
	☐	BU7-1015	ODOT REVIEW STAGE 2 BU7	10d	10d	24d	15-Feb-24	21-Mar-24	29-Feb-24	03-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU7-1010	BU7-1020, A1070
	☐	BU3-1025	ODOT ACCEPT RFC PLANS BU3	10d	10d	80d	23-Feb-24	17-Jun-24	07-Mar-24	28-Jun-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU3-1020	D-P1-1070, A1140, A1120, A1100
	☐	BU5-1020	DESIGN RFC PLANS BU5	10d	10d	0d	01-Mar-24	01-Mar-24	14-Mar-24	14-Mar-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU5-1015	BU5-1025, 435-P1-1000
	☐	BU7-1020	DESIGN RFC BU7	10d	10d	24d	01-Mar-24	04-Apr-24	14-Mar-24	17-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU7-1015	BU7-1025
	☐	BU4-1025	ODOT ACCEPT BU4	10d	10d	19d	08-Mar-24	04-Apr-24	21-Mar-24	17-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU4-1020	BU4-P1-100, BU4-P1-135
	☐	BU5-1025	ODOT ACCEPT BU5	10d	10d	12d	15-Mar-24	02-Apr-24	28-Mar-24	15-Apr-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU5-1020	BU6-1000, BG-P1-1040
	☐	BU7-1025	ODOT ACCEPT RFC BU7	10d	10d	24d	15-Mar-24	18-Apr-24	28-Mar-24	01-May-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU7-1020	435-P2-1030
	☐	BU6-1000	DESIGN PRELIM BU6 - TRAFFIC CONTROL	5d	5d	62d	29-Mar-24	26-Jun-24	04-Apr-24	02-Jul-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU5-1025	BU6-1005
	☐	BU6-1005	ODOT REVIEW PRELIM BU6	10d	10d	62d	05-Apr-24	03-Jul-24	18-Apr-24	17-Jul-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU6-1000	BU6-1010
	☐	BU6-1010	DESIGIN STAGE 2 BU6	10d	10d	62d	19-Apr-24	18-Jul-24	02-May-24	31-Jul-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU6-1005	BU6-1015
	☐	BU6-1015	ODOT REVIEW STAGE 2 BU6	10d	10d	62d	03-May-24	01-Aug-24	16-May-24	14-Aug-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU6-1010	BU6-1020
	☐	BU6-1020	DESIGN RFC PLANS BU6	10d	10d	62d	17-May-24	15-Aug-24	31-May-24	28-Aug-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU6-1015	BU6-1025
	☐	BU6-1025	ODOT ACCEPT RFC BU6	10d	10d	62d	03-Jun-24	29-Aug-24	14-Jun-24	12-Sep-24	233008 ODOT 5 Day w/Holidays - 233008 ODOT 5 Day w/Holidays	BU6-1020	BU6-100-000
	SUBMITTALS & FABRICATION												
	PROJECT WIDE												
	☐	A1060	DESIGN FABRICATE & DELIVER PRECAST STORM ST...	10d	10d	120d	01-Feb-24	23-Jul-24	14-Feb-24	05-Aug-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU4-1010	BU4-P1-125
	☒	A1090	PROCURE SIGNAL STRAIN POLES	180d	180d	1d	23-Feb-24	26-Feb-24	06-Nov-24	07-Nov-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU3-1020	435-P6-1000
☐	A1080	PROCURE LIGHT POLES	100d	100d	28d	23-Feb-24	03-Apr-24	16-Jul-24	23-Aug-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU3-1020	BG-P3-1025	
☐	A1070	DESIGN FABRICATE & DELIVER BOX CULVERT	10d	10d	33d	01-Mar-24	18-Apr-24	14-Mar-24	01-May-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU7-1015	435-P2-1030	
Construction													
435 PROJECT WIDE													
PHASE 1													
SR435													
☐	BU2-P1-100	INSTALL SWPPP BMPs	2d	2d	19d	06-Mar-24	15-Apr-24	07-Mar-24	16-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-1035	BU2-P1-105	
☐	BU2-P1-105	INSALL FORCE MAIN 6" & 12"	10d	10d	19d	11-Mar-24	18-Apr-24	29-Mar-24	07-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-100	BU2-P1-110	
☐	BU2-P1-110	INSTALL AIR RELEASE VALVES	2d	2d	19d	02-Apr-24	08-May-24	03-Apr-24	09-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-105	BU2-P1-115	
☐	BU2-P1-115	TEST FORCE MAIN 6" & 12"	2d	2d	19d	04-Apr-24	10-May-24	09-Apr-24	13-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-110	BU2-P1-120	

Current

Progress

Critical

Float (Fallback)


Original Baseline

Milestones

Summary

PROJECT NUMBER: 233008
PID#: 117955, CONTRACT ID: FAY117955
COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024
INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024
PROJECT COMPLETION: 7/1/2025

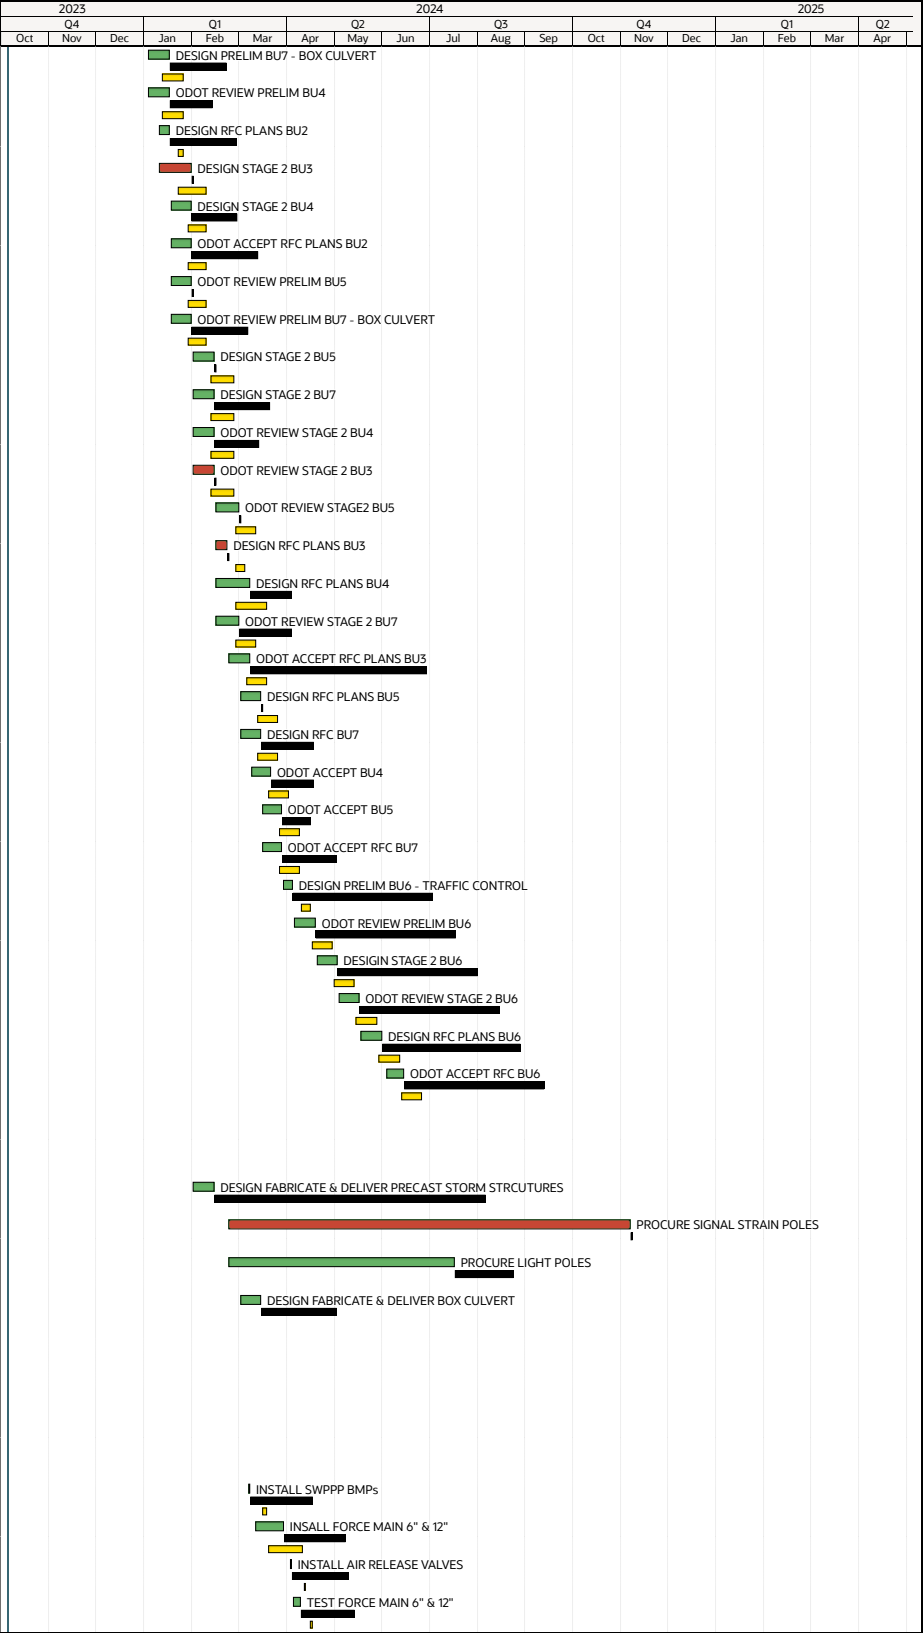



Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors	
		BU2-P1-120	TIE IN FORCE MAIN	1d	1d	19d	10-Apr-24	15-May-24	10-Apr-24	15-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-115	BU2-P1-125
		BU2-P1-125	INSTALL WATERMAIN & FIRE HYDRANTS	12d	12d	19d	11-Apr-24	16-May-24	01-May-24	06-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-120	BU2-P1-130
		BU2-P1-130	TEST WATERMAIN & FIRE HYDRANTS	2d	2d	19d	02-May-24	10-Jun-24	07-May-24	12-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-125	BU2-P1-135
		BU2-P1-135	TIE IN WATER MAIN	1d	1d	19d	08-May-24	13-Jun-24	08-May-24	13-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU2-P1-130	435-P2-1130
435 WEST													
PHASE 1													
SR435													
	BU4-P1-100	INSTALL SWPPP BMPS	1d	1d	95d	21-Mar-24	02-Aug-24	22-Mar-24	02-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-1025	BU4-P1-105	
	BU4-P1-105	DIG SOIL SAMPLES	1d	1d	95d	22-Mar-24	05-Aug-24	25-Mar-24	05-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-100	BU4-P1-125	
	BU4-P1-125	INSTALL STORM EXTENSION RAMP A	2d	2d	95d	25-Mar-24	06-Aug-24	27-Mar-24	07-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-105, A1060	BU4-P1-130	
	BU4-P1-130	INSTALL STORM EXTENSION RAMP D	2d	2d	95d	27-Mar-24	08-Aug-24	29-Mar-24	09-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-125	BU4-P1-115	
	BU4-P1-115	INSTALL STORM 435 AREA 2	3d	3d	95d	29-Mar-24	12-Aug-24	03-Apr-24	14-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-130	BU4-P1-110	
	BU4-P1-110	INSTALL STORM 435 AREA 3	7d	7d	95d	03-Apr-24	15-Aug-24	12-Apr-24	23-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-115	BU4-P1-120	
	BU4-P1-120	INSTALL STORM EXTENSION RAMP B	2d	2d	95d	12-Apr-24	26-Aug-24	16-Apr-24	27-Aug-24	Standard 5 Day Workweek - Standard 5 Day Workweek	BU4-P1-110	BU4-P2-396	
RAMP A (NW)													
	BU4-P1-135	INSTALL MOT TRAFFIC SHIFT RAMP A	1d	1d	13d	22-Mar-24	18-Apr-24	22-Mar-24	18-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-1025	A1160, BU4-P1-140, BU4-P1-415, A1160	
	BU4-P1-140	PLACE PCB RAMP A	1d	1d	13d	26-Mar-24	19-Apr-24	26-Mar-24	19-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-135	BU4-P1-145	
	BU4-P1-145	REMOVE PAVEMENT	2d	2d	13d	27-Mar-24	22-Apr-24	29-Mar-24	23-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-140	BU4-P1-150	
	BU4-P1-150	EXCAVATE & BUILD SUBGRADE RAMP WIDENING	2d	2d	13d	02-Apr-24	24-Apr-24	03-Apr-24	26-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-145	BU4-P1-155	
	BU4-P1-155	PLACE & COMPACT EMBANKMENT RAMP WIDENING	1d	1d	13d	04-Apr-24	30-Apr-24	04-Apr-24	30-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-150	BU4-P1-160	
	BU4-P1-160	STABILIZE SUBGRADE	1d	1d	13d	09-Apr-24	01-May-24	09-Apr-24	01-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-155, A1230	BU4-P1-165	
	BU4-P1-165	CURE SUBGRADE	5d	5d	22d	10-Apr-24	02-May-24	14-Apr-24	06-May-24	233008 7 Day No Restriction - 233008 7 Day No Restriction	BU4-P1-160	BU4-P1-170	
	BU4-P1-175	PLACE AGGREGATE BASE	2d	2d	11d	15-Apr-24	07-May-24	16-Apr-24	08-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-170, BU4-P1-170	BU4-P1-180	
	BU4-P1-170	INSTALL UD	1d	1d	11d	15-Apr-24	07-May-24	15-Apr-24	07-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-165	BU4-P1-175, BU4-P1-175	
	BU4-P1-180	PREP & PLACE JPC PAVEMENT	6d	6d	11d	18-Apr-24	09-May-24	26-Apr-24	17-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-175	BU4-P1-185	
	BU4-P1-185	CURE JPC PAVEMENT	5d	5d	22d	27-Apr-24	19-May-24	01-May-24	23-May-24	233008 7 Day No Restriction - 233008 7 Day No Restriction	BU4-P1-180	BU4-P1-192, BU4-P1-192	
	BU4-P1-192	PERFROM FINAL GRADING	1d	1d	12d	01-May-24	23-May-24	01-May-24	23-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-185, BU4-P1-185	BU4-P1-190	
	BU4-P1-193	INSTALL BMPs & SEEDING	1d	1d	12d	02-May-24	28-May-24	02-May-24	28-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-190, BU4-P1-190	BU4-P1-195, BU4-P1-195	
	BU4-P1-195	SHIFT TRAFFIC OPEN RAMP	1d	1d	12d	02-May-24	28-May-24	02-May-24	28-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	A1160, A1160, BU4-P1-193, BU4-P1-193	BU4-P1-200, BU4-P1-205	
	BU4-P1-190	INSTALL TEMPORARY STRIPING	1d	1d	12d	02-May-24	28-May-24	02-May-24	28-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-192	BU4-P1-193, BU4-P1-193	
	BU4-P1-200	PERFORM WEEKEND RAMP/435 TIE-IN	2d	2d	69d	07-May-24	11-Sep-24	08-May-24	12-Sep-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-195	BU6-100-000	
	BU6-100-000	INSTALL BU6 SIGNS & STRIPING	1d	1d	49d	17-Jun-24	13-Sep-24	17-Jun-24	13-Sep-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU6-1025, BU4-P1-200	A1010	
RAMP D (WS)													
	BU4-P1-205	INSTALL MOT TRAFFIC SHIFT RAMP D	1d	1d	12d	07-May-24	29-May-24	07-May-24	29-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-195	BU4-P1-210, A1180, A1180	
	BU4-P1-210	PLACE PCB RAMP D	1d	1d	12d	08-May-24	30-May-24	08-May-24	30-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-205	BU4-P1-215	
	BU4-P1-215	REMOVE PAVEMENT	1d	1d	12d	09-May-24	31-May-24	09-May-24	31-May-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-210	BU4-P1-220	
	BU4-P1-220	EXCAVATE & BUILD SUBGRADE RAMP WIDENING	2d	2d	12d	10-May-24	04-Jun-24	13-May-24	05-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-215	BU4-P1-225	
	BU4-P1-225	PLACE & COMPACT EMBANKMENT RAMP WIDENING	1d	1d	12d	15-May-24	06-Jun-24	15-May-24	06-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-220	BU4-P1-235	
	BU4-P1-235	STABILIZE SUBGRADE	1d	1d	12d	16-May-24	10-Jun-24	16-May-24	10-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-225	BU4-P1-240	
	BU4-P1-240	CURE SUBGRADE	5d	5d	26d	17-May-24	12-Jun-24	21-May-24	16-Jun-24	233008 7 Day No Restriction - 233008 7 Day No Restriction	BU4-P1-235	BU4-P1-230	
	BU4-P1-230	PLACE & COMPACT EMBANKMENT VEG FILTER STRIP	2d	2d	12d	23-May-24	17-Jun-24	28-May-24	18-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-240	BU4-P1-245	
	BU4-P1-245	INSTALL UD	1d	1d	12d	29-May-24	20-Jun-24	29-May-24	20-Jun-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-230	BU4-P1-250, BU4-P1-250	

Current

Progress

Critical

Float (Fallback)


Original Baseline

Milestones

Summary

PROJECT NUMBER: 233008
PID#: 117955, CONTRACT ID: FAY117955
COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024
INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024
PROJECT COMPLETION: 7/1/2025

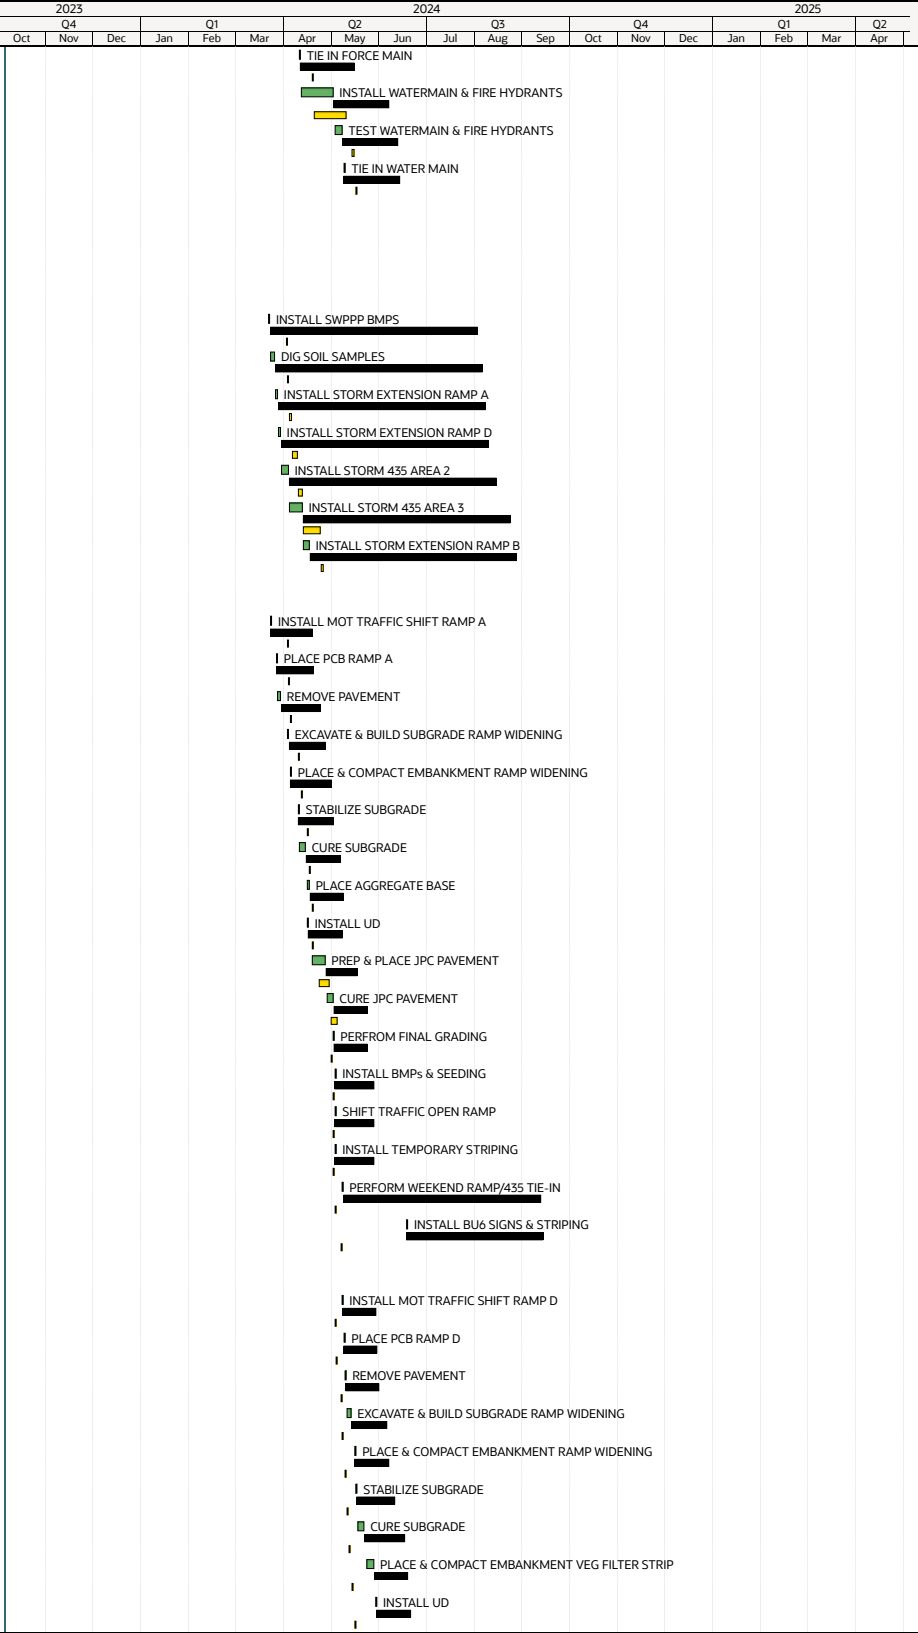

[illegible]

- Current
- Progress
- Critical
- Float (Fallback)

-  Original Baseline
-  Milestones
-  Summary

PROJECT NUMBER: 233008
PID#: 117955, CONTRACT ID: FAY117955
COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024
INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024
PROJECT COMPLETION: 7/1/2025

[illegible]

- Current
- Progress
- Critical
- Float (Fallback)


-  Original Baseline
-  Milestones
-  Summary

PROJECT NUMBER: 233008
PID#: 117955, CONTRACT ID: FAY117955
COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024
INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024
PROJECT COMPLETION: 7/1/2025



Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors	
	☐	BU4-P2-385	PLACE AGGREGATE BASE	1d	1d	12d	23-Jul-24	15-Aug-24	23-Jul-24	15-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-380, BU4-P2-380	BU4-P2-390
	☐	BU4-P2-380	INSTALL UD	1d	1d	12d	23-Jul-24	15-Aug-24	23-Jul-24	15-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-375	BU4-P2-385, BU4-P2-385
	☐	BU4-P2-390	PREP & PLACE JPC PAVEMENT	4d	4d	12d	25-Jul-24	16-Aug-24	31-Jul-24	22-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-385	BU4-P2-395
	☐	BU4-P2-395	CURE JPC PAVEMENT	5d	5d	22d	01-Aug-24	23-Aug-24	05-Aug-24	27-Aug-24	233008 7 Day No Restriction - 233008 7 Day No Restriction	BU4-P2-390	BU4-P2-396
	☐	BU4-P2-396	PERFORM FINAL GRADING	1d	1d	13d	06-Aug-24	28-Aug-24	06-Aug-24	28-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P1-120, BU4-P2-395	BU4-P2-398, BU4-P2-398
	☐	BU4-P2-398	INSTALL BMPs & SEEDING	1d	1d	13d	06-Aug-24	28-Aug-24	06-Aug-24	28-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-396, BU4-P2-396	BU4-P2-400, BU4-P2-400
	☐	BU4-P2-400	INSTALL TEMPORARY STRIPING	1d	1d	13d	06-Aug-24	28-Aug-24	06-Aug-24	28-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-398, BU4-P2-398	BU4-P2-405, BU4-P2-405
	☐	BU4-P2-410	PERFORM WEEKEND RAMP/435 TIE-IN	2d	2d	13d	06-Aug-24	28-Aug-24	07-Aug-24	29-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-405, BU4-P2-405	BU6-P3-1000, BU6-100-003, BU6-100-003
	☐	BU4-P2-405	SHIFT TRAFFIC OPEN RAMP	1d	1d	13d	06-Aug-24	28-Aug-24	06-Aug-24	28-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	A1170, BU4-P2-400, BU4-P2-400, A1170	BU4-P2-410, BU4-P2-410
	☐	BU6-100-003	INSTALL BU6 SIGNS & STRIPING	1d	1d	95d	07-Aug-24	01-Jul-25	07-Aug-24	01-Jul-25	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU4-P2-410, BU4-P2-410	A1050
PHASE 3													
SR435													
☐	BU6-P3-1000	PERFORM FINAL STRIPING	3d	3d	17d	08-Aug-24	03-Sep-24	12-Aug-24	05-Sep-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU4-P2-410, BU6-100-006, BU6-100-005	BU6-P3-1010	
☐	BU6-P3-1010	INSTALL FINAL PAVEMENT MARKERS	2d	2d	17d	13-Aug-24	06-Sep-24	14-Aug-24	09-Sep-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU6-P3-1000	BU6-P3-1020	
☐	BU6-P3-1020	INSTALL FINAL SIGNAGE	2d	2d	17d	15-Aug-24	10-Sep-24	16-Aug-24	11-Sep-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU6-P3-1010	435-P6-1000, BU6-P3-1030	
☐	BU6-P3-1030	PERFORM FINAL DRESS	1d	1d	17d	19-Aug-24	12-Sep-24	19-Aug-24	12-Sep-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU6-P3-1020	BU6-P3-1040	
☐	BU6-P3-1040	PERFORM FINAL BMP & RESEEDING	1d	1d	17d	20-Aug-24	13-Sep-24	20-Aug-24	13-Sep-24	233008 5 Day No Weather - 233008 5 Day No Weather	BU6-P3-1030	A1010	
435 EAST													
PHASE 1													
SR435 EAST													
☐	435-P1-1000	INSTALL BU5 SWPPP BMPs	2d	2d	0d	15-Mar-24	15-Mar-24	18-Mar-24	18-Mar-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU5-1020	435-P1-1010	
☐	435-P1-1010	SHIFT TRAFFIC 435 1 LANE EACH DIRECTION	1d	1d	0d	19-Mar-24	19-Mar-24	19-Mar-24	19-Mar-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	435-P1-1000	435-P1-1020	
☐	435-P1-1020	INSTALL TEMPORARY PAVEMENT 435 & 729	3d	3d	0d	22-Mar-24	22-Mar-24	27-Mar-24	27-Mar-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	435-P1-1010	BG-P1-1000	
☐	BG-P1-1000	INSTALL TEMPORARY PAVEMENT	3d	3d	0d	29-Mar-24	29-Mar-24	03-Apr-24	03-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	435-P1-1020	D-P1-1000, BG-P1-1010	
☐	BG-P1-1010	SHIFT TRAFFIC BG BLVD	1d	1d	0d	04-Apr-24	04-Apr-24	04-Apr-24	04-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1000	BG-P1-1020	
☐	BG-P1-1020	REMOVE PAVEMENT	2d	2d	0d	09-Apr-24	09-Apr-24	10-Apr-24	10-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1010	BG-P1-1030	
☐	BG-P1-1030	EXCAVATE & PLACE FILL	3d	3d	0d	11-Apr-24	11-Apr-24	15-Apr-24	15-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1020	BG-P1-1040	
☐	BG-P1-1040	STABILIZE SUBGRADE	1d	1d	0d	16-Apr-24	16-Apr-24	16-Apr-24	16-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1030, BU5-1025	BG-P1-1050	
☐	BG-P1-1050	CURE STABILIZED SUBGRADE	5d	5d	0d	17-Apr-24	17-Apr-24	21-Apr-24	21-Apr-24	233008 7 Day No Restriction - 233008 7 Day No Restriction	BG-P1-1040	BG-P1-1060	
☐	BG-P1-1080	INSTALL DRIVE ENTRANCE	2d	2d	0d	22-Apr-24	22-Apr-24	23-Apr-24	23-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1070, BG-P1-1070	BG-P1-1090	
☐	BG-P1-1070	PLACE AGGREGATE BASE	2d	2d	0d	22-Apr-24	22-Apr-24	23-Apr-24	23-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1060, BG-P1-1060	BG-P1-1080, BG-P1-1080	
☐	BG-P1-1060	INSTALL UD	1d	1d	0d	22-Apr-24	22-Apr-24	22-Apr-24	22-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1050	BG-P1-1070, BG-P1-1070	
☐	BG-P1-1090	INSTALL BASE ASPHALT	2d	2d	0d	24-Apr-24	24-Apr-24	26-Apr-24	26-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1080	BG-P1-1100	
☐	BG-P1-1110	PREP TO SHIFT TRAFFIC	1d	1d	0d	30-Apr-24	30-Apr-24	30-Apr-24	30-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1100, BG-P1-1100	435-P2-1020	
☐	BG-P1-1100	INSTALL INT ASPHALT	1d	1d	0d	30-Apr-24	30-Apr-24	30-Apr-24	30-Apr-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1090	BG-P1-1110, BG-P1-1110	
US35 RAMP D													
☐	D-P1-1000	INSTALL TEMPORARY PAVMENT	5d	5d	64d	04-Apr-24	01-Aug-24	12-Apr-24	12-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BG-P1-1000	A1240, D-P1-1010, A1240	
☐	D-P1-1010	SHIFT TRAFFIC RAMP D	1d	1d	64d	15-Apr-24	12-Aug-24	15-Apr-24	13-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	D-P1-1000	D-P1-1020	
☐	D-P1-1020	REMOVE PAVEMENT	3d	3d	64d	16-Apr-24	13-Aug-24	19-Apr-24	19-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	D-P1-1010	D-P1-1030	
☐	D-P1-1030	EXCAVATE & PLACE EMBANKMENT	2d	2d	64d	22-Apr-24	19-Aug-24	23-Apr-24	22-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	D-P1-1020	D-P1-1040	
☐	D-P1-1040	STABILIZE SUBGRADE	1d	1d	64d	24-Apr-24	22-Aug-24	24-Apr-24	23-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	D-P1-1030	D-P1-1050	
☐	D-P1-1050	CURE SUBGRADE	5d	5d	120d	25-Apr-24	23-Aug-24	29-Apr-24	27-Aug-24	233008 7 Day No Restriction - 233008 7 Day No Restriction	D-P1-1040	D-P1-1060	

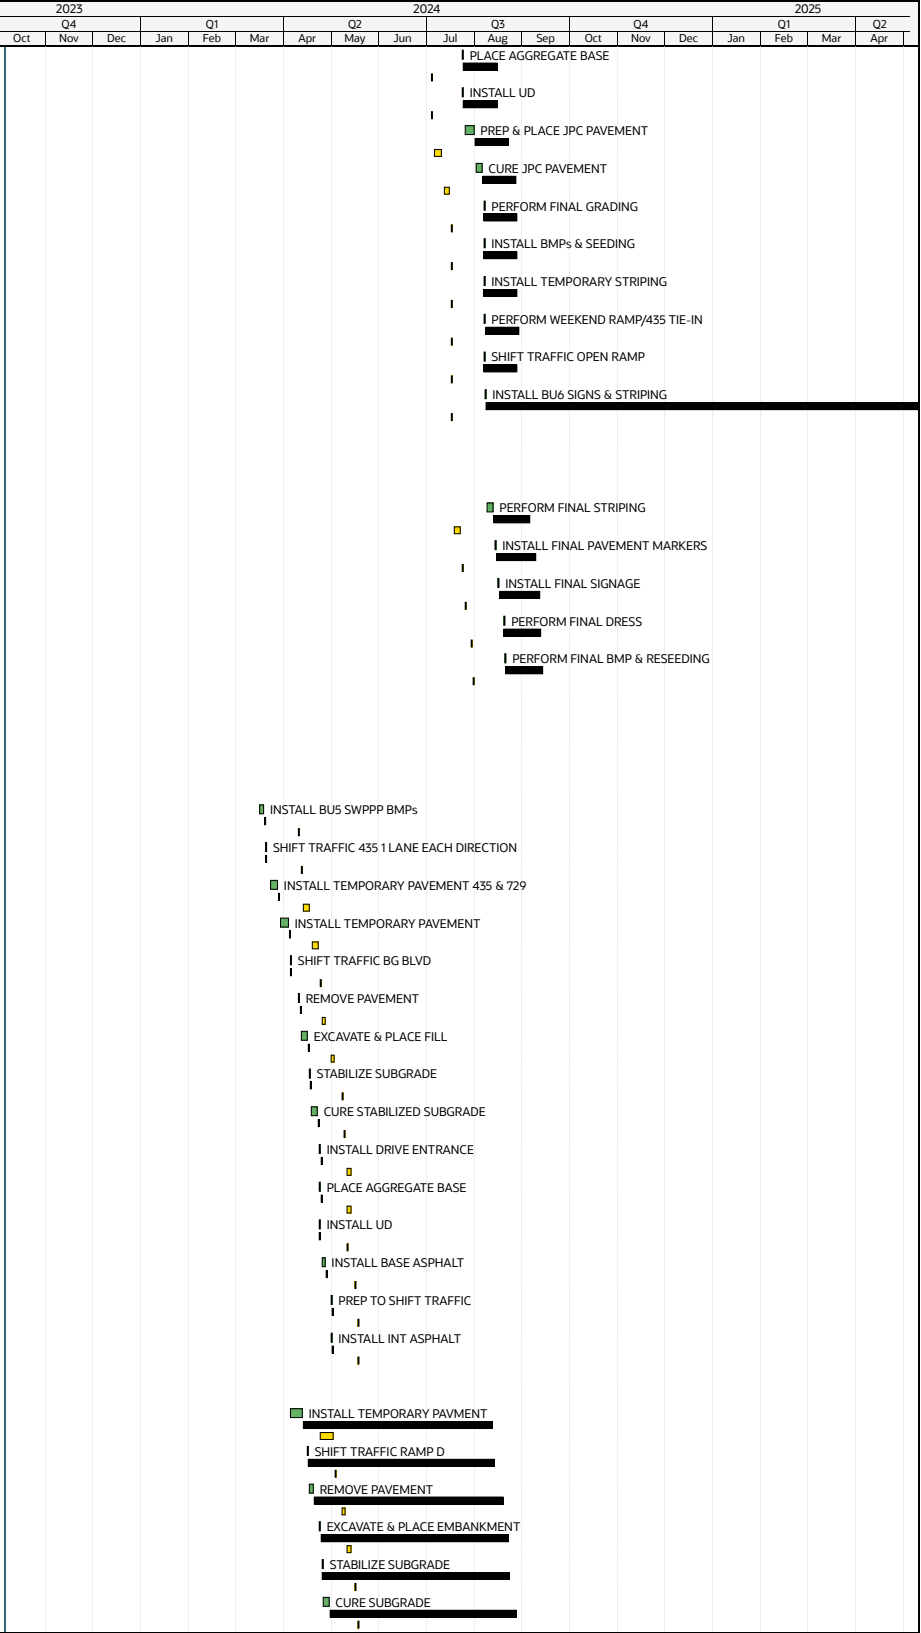

Current

Progress

Critical

Float (Fallback)

Original Baseline

Milestones

Summary

PROJECT NUMBER: 233008

PID#: 117955, CONTRACT ID: FAY117955

COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024

INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024

PROJECT COMPLETION: 7/1/2025



Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors	2023																2024																2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
													Q4			Q1			Q2			Q3			Q4			Q1			Q2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
													Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
	☐	D-P1-1060	INSTALL UD	1d	1d	66d	30-Apr-24	28-Aug-24	30-Apr-24	28-Aug-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	D-P1-1050	D-P1-1070																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																</



Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors	2023				2024						2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
													Q4			Q1			Q2		Q3		Q4			Q1		Q2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
													Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
	435-P2-1210	INSTALL BASE ASPHALT	3d	3d	0d	23-Jul-24	23-Jul-24	26-Jul-24	26-Jul-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P2-1205	435-P2-1220																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												</

Current

Progress

Critical

Float (Fallback)

Original Baseline

Milestones

Summary

PROJECT NUMBER: 233008

PID#: 117955, CONTRACT ID: FAY117955

COUNTY/ROUTE: FAYETTE, SR 435-01.52

INTERIM COMPLETION (RAMPS): 9/15/2024

INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024

PROJECT COMPLETION: 7/1/2025



Longest Path	ID	Name	Plan... Dura...	Rema... Durat...	Total Float	Start	Late Start	Finish	Late Finish	Calendar	Predecessors	Successors	2023			2024													
													Q4			Q1			Q2		Q3		Q4			Q1		Q2	
													Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
PHASE 4																													
SR435 EAST																													
☐	435-P4-1000	SHIFT TRAFFIC INTO PHASE	1d	1d	0d	07-Sep-24	07-Sep-24	07-Sep-24	07-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P3-1070, A1130, 729-P3-1080, 729-...	435-P4-1010																	
☐	435-P4-1010	ADJUST MOT DEVICES	2d	2d	0d	10-Sep-24	10-Sep-24	11-Sep-24	11-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1000	435-P4-1020																	
☐	435-P4-1020	REMOVE PAVEMENT	1d	1d	0d	12-Sep-24	12-Sep-24	12-Sep-24	12-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1010	435-P4-1030																	
☐	435-P4-1030	EXCAVATE & PLACE FILL	2d	2d	0d	13-Sep-24	13-Sep-24	14-Sep-24	14-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1020	435-P4-1040																	
☐	435-P4-1040	STRABILIZE SUBGRADE	1d	1d	0d	16-Sep-24	16-Sep-24	16-Sep-24	16-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1030	435-P4-1050																	
☐	435-P4-1050	GRADE SLOPES & DITCHES	1d	1d	0d	18-Sep-24	18-Sep-24	18-Sep-24	18-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1040	435-P4-1060																	
☐	435-P4-1060	PLACE AGGREGATE BASE	1d	1d	0d	19-Sep-24	19-Sep-24	19-Sep-24	19-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1050	435-P4-1070																	
☐	435-P4-1070	INSTALL RAB CURB & GUTTER	2d	2d	0d	21-Sep-24	21-Sep-24	23-Sep-24	23-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1060	435-P4-1080																	
☐	435-P4-1080	INSTALL RAB ISLANDS	3d	3d	0d	24-Sep-24	24-Sep-24	27-Sep-24	27-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1070	435-P4-1090																	
☐	435-P4-1090	INSTALL BASE ASPHALT	2d	2d	0d	28-Sep-24	28-Sep-24	30-Sep-24	30-Sep-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1080	435-P4-1100																	
☐	435-P4-1100	INSTALL INT ASPHALT	2d	2d	0d	01-Oct-24	01-Oct-24	02-Oct-24	02-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1090	435-P4-1110, 435-P4-1110																	
☐	435-P4-1120	INSTALL PHASE SHIFT MOT STRIPING	1d	1d	0d	02-Oct-24	02-Oct-24	02-Oct-24	02-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1110, 435-P4-1110	435-P4-1130, 435-P4-1130																	
☐	435-P4-1130	SHIFT TRAFFIC NEXT PHASE	1d	1d	0d	02-Oct-24	02-Oct-24	02-Oct-24	02-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1120, 435-P4-1120	435-P5-1000																	
☐	435-P4-1110	INSTALL BMPs & SEEDING	1d	1d	0d	02-Oct-24	02-Oct-24	02-Oct-24	02-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1100, 435-P4-1100	435-P4-1120, 435-P4-1120																	
PHASE 5																													
SR435 EAST																													
☐	435-P5-1000	SHIFT TRAFFIC INTO PERMANENT CONFIGURATION	1d	1d	0d	03-Oct-24	03-Oct-24	03-Oct-24	03-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P4-1130	435-P5-1010																	
☐	435-P5-1010	PEFORM MILL & FILL OPERATION	5d	5d	0d	05-Oct-24	05-Oct-24	12-Oct-24	12-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P5-1000	435-P5-1020																	
☐	435-P5-1020	INSTALL REMAINING SIGNS	4d	4d	0d	14-Oct-24	14-Oct-24	18-Oct-24	18-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P5-1010	435-P5-1030, 435-P5-1030																	
☐	435-P5-1030	INSTALL SURFACE ASPHALT	10d	10d	0d	14-Oct-24	14-Oct-24	26-Oct-24	26-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P5-1020, 435-P5-1020	435-P5-1040																	
☐	435-P5-1040	PERFORM FINAL STRIPING	3d	3d	0d	29-Oct-24	29-Oct-24	31-Oct-24	31-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P5-1030	435-P5-1050, 435-P5-1050																	
☐	435-P5-1050	PERFORM FINAL SEEDING/RESEEDING	3d	3d	0d	29-Oct-24	29-Oct-24	31-Oct-24	31-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P5-1040, 435-P5-1040	435-P5-1060, 435-P5-1060																	
☐	435-P5-1060	INSTALL FINAL BMPs	2d	2d	0d	30-Oct-24	30-Oct-24	31-Oct-24	31-Oct-24	233008 6 Day w/Weather - 233008 6 Day w/Weather	435-P5-1050, 435-P5-1050	A1030																	
PERMANENT SIGNAL																													
SR435 EAST																													
☒	435-P6-1000	INSTALL PERMANENT SIGNALS 71 RAMP B/A	10d	10d	0d	08-Nov-24	08-Nov-24	26-Nov-24	26-Nov-24	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	BU6-P3-1020, A1090	435-P6-1010																	
☒	435-P6-1010	INSTALL PERMANENT SIGNALS 71 RAMP D	10d	10d	0d	27-Nov-24	27-Nov-24	12-May-25	12-May-25	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	435-P6-1000	435-P6-1020																	
☒	435-P6-1020	INSTALL PERMANENT SIGNALS ALLEN RD	10d	10d	0d	14-May-25	14-May-25	30-May-25	30-May-25	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	435-P6-1010	435-P6-1030																	
☒	435-P6-1030	INSTALL PERMANENT SIGNALS 35 RAMP D	10d	10d	0d	03-Jun-25	03-Jun-25	19-Jun-25	19-Jun-25	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	D-P2-1200, D-P1-1150, 435-P6-1020	435-P6-1040																	
☒	435-P6-1040	PERFORM FINAL CLEAN UP & REMEDIATION	7d	7d	0d	20-Jun-25	20-Jun-25	01-Jul-25	01-Jul-25	233008 5 Day w/ Weather - 233008 5 Day w/ Weather	435-P6-1030	A1050																	

Current Progress Critical Float (Fallback)	Original Baseline Milestones Summary	PROJECT NUMBER: 233008 PID#: 117955, CONTRACT ID: FAY117955 COUNTY/ROUTE: FAYETTE, SR 435-01.52	INTERIM COMPLETION (RAMPS): 9/15/2024 INTERIM COMPLETION (EXCEPT SIGNALS): 11/1/2024 PROJECT COMPLETION: 7/1/2025
--	---	--	--
