


THE G.E.I. CO.	REQUESTED 11/15/11	FAC. MAPPING REFERENCE #	GRID # 4722
FILE 52060694	DATE 8/19/11	SHEET 1 OF 6	2 WORKING DAYS
SURVEY FOR INNERBELT BR PROJ - OH RELO TO UG			
ADDRESS FAIRFIELD AVE & SCRANTON AVE			
MUNICIPALITY CITY OF CLEVELAND SCALE NONE			
ORDER FOR OHIO DEPARTMENT OF TRANSPORTATION			
PREPARED BY	SURVEY OFFICE	DRAWN BY GILL	PHONE 440.546.8846
W. 15TH ST. CIRCUIT RELOCATION WORK - OH TO UG (KNOWN AS ODOT PHASE 4)			
CONSTR. PLANS APPROVED		JOINT PROPOSAL	
MARKETING		SAPDR	12769676
CONSUMER'S CHARGE			
DATE	REC.	FOR EST.	DIH
8/19/11	2	1	2
CABLE		SERV	R00
DWC3		BET2	DEB1
RJS1		TOTAL	10



WBS: CE-000224-DU
 CIRCUITS: ~ H-8-CG-L
 ~ H-2-CG-L
 ~ H-8-CG-P

GENERAL NOTES

NO WORK ON V-23 & V-710 RELATED OVERHEAD WORK
 FAIRFIELD WR#54858482
 SCRANTON WR#54880514
 W.15TH REMOVALS WR#54858442

RETURN TO RIGHT-OF-WAY BEFORE SCHEDULING	JOINT POLE RELEASE	GANG MEET	TREE WORK	MUNICIPAL PERMIT INFO
<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
DATE CLEARED				

DATE	DESCRIPTION	APPROVED BY
8/19/11	CABLE INSTALL RELEASE	

A CHECK MARK NEXT TO EACH ITEM ON THE SKETCH, INCLUDING CHANGES, INDICATES THAT THE WORK HAS BEEN COMPLETED	
ITEMS	UNITS OF WORK COMPLETED
POLES	INSTALLED
WIRES	REMOVED
ANCHORS	SHIFTED
KIND OF POLE(S) INSTALLED BY SYMBOL	
POLES LEFT FOR TEL. TO REMOVE	
DATE WORK COMPLETED	SUPERVISOR'S SIGNATURE

UNDERGROUND FACILITIES WARNING	
HIGH PRESSURE PIPELINE	AT SYMBOL
CEI	CHECKED BY
TELEPHONE	BY
D.H. TRANSMISSION CLEARANCE WARNING	
AT SYMBOLS	
ENGINEERING CHECKED BY:	DATE
CONSTRUCTION CHECKED BY:	DATE

CONFIDENTIAL
FIRSTENERGY CORP.

INFORMATION IN THIS DOCUMENT IS PROPRIETARY AND SHALL NOT BE USED, COPIED, REPRODUCED OR DISCLOSED IN WHOLE OR IN PART WITHOUT THE WRITTEN CONSENT OF FIRSTENERGY CORP.

CABLE INSTALL SUMMARY

IN MH 9312-02
 INSTALL 3 TRANSITION SPLICES (500KCMIL EPR TO 600 CUPILC)

FROM MH 9312-02 TO MH 9306-01
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 628 TCF TOTAL ~ H-8-CG-L
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 628 TCF TOTAL ~ H-2-CG-L

FROM MH 9312-02 TO SUBBED P#206208
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 300 TCF TOTAL ~ H-8-CG-P

AT SUBBED P#206208
 INSTALL 3 CABLE TERM CLDHRNK 15KV 3/0-500

IN MH 9306-01
 INSTALL 6-500KCMIL-1C-15KV STRAIGHT SPLICES

FROM MH 9306-01 TO MH 9309-02
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 631 TCF TOTAL ~ H-8-CG-L
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 631 TCF TOTAL ~ H-2-CG-L

IN MH 9309-02
 INSTALL 6-500KCMIL-1C-15KV STRAIGHT DISCONNECTABLE SPLICES

FROM MH 9309-02 TO NEW CABLE POLE P#A
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 145 TCF TOTAL ~ H-2-CG-L

IN MH 9308-06
 PULL CABLE THRU & RACK CABLE


FROM MH 9309-02 TO P#527113
 INSTALL CABLE-15KV 500KCMIL-1C-CU-EPR-FSN TRIPLEXED (3-1C), 210 TCF TOTAL ~ H-8-CG-L

AT P#527113
 INSTALL 3 CABLE TERM CLDHRNK 15KV 3/0-500

AT NEW CABLE POLE P#A
 INSTALL 3 CABLE TERM CLDHRNK 15KV 3/0-500

CABLE REMOVAL SUMMARY

IN MH 9312-02
 SCRAP PILC SPLICE
 REMOVE CABLE FROM MH 9312-02 TO POLE CXC-622462 (REMOVE H-8-CG-L (125") 600 CUPILC)
 SCRAP PILC SPLICE
 REMOVE CABLE FROM MH 9312-02 TO POLE CXC-622463 (REMOVE H-2-CG-L (106") 600 CUPILC)
 SCRAP PILC SPLICE
 REMOVE CABLE FROM MH 9312-02 TO POLE CXC-622463 (REMOVE H-8-CG-P (106") 600 CUPILC)

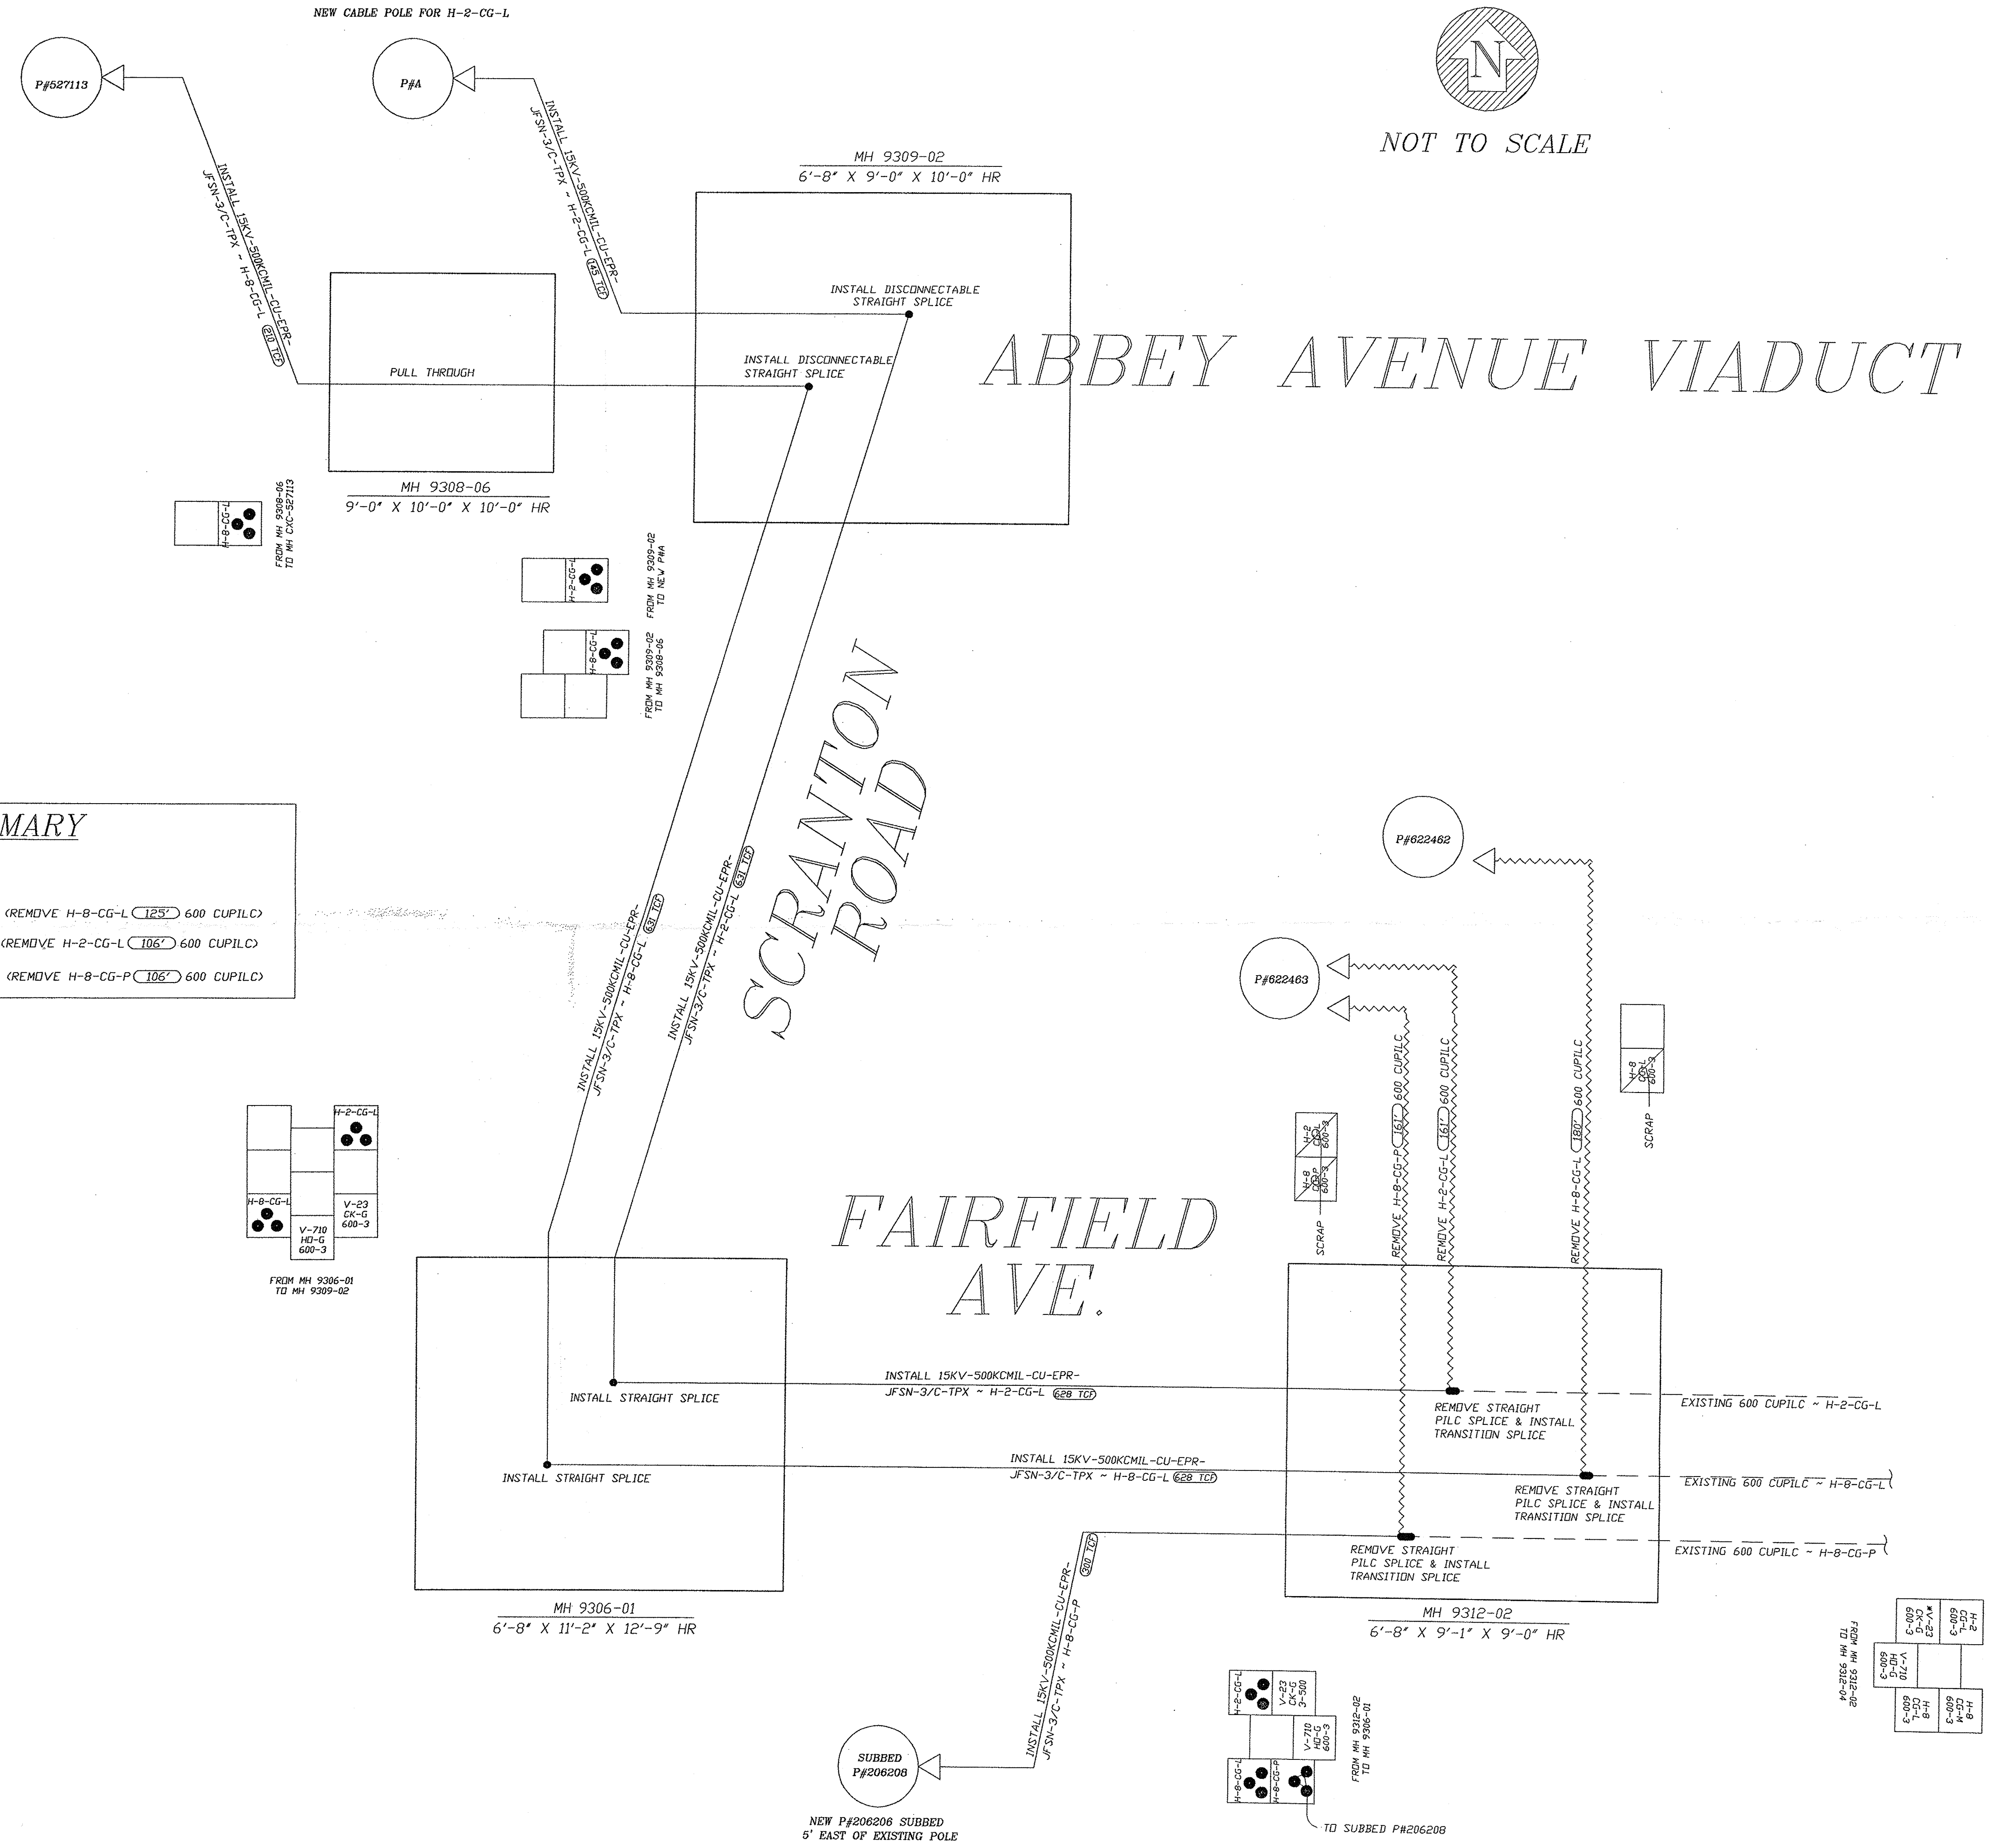

H-8-CG-L	600-3	600-3
H-2-CG-L	600-3	600-3
H-8-CG-P	600-3	600-3
V-23	600-3	600-3
V-710	600-3	600-3

H-8-CG-L	600-3	600-3
H-2-CG-L	600-3	600-3
H-8-CG-P	600-3	600-3
V-23	600-3	600-3
V-710	600-3	600-3
