


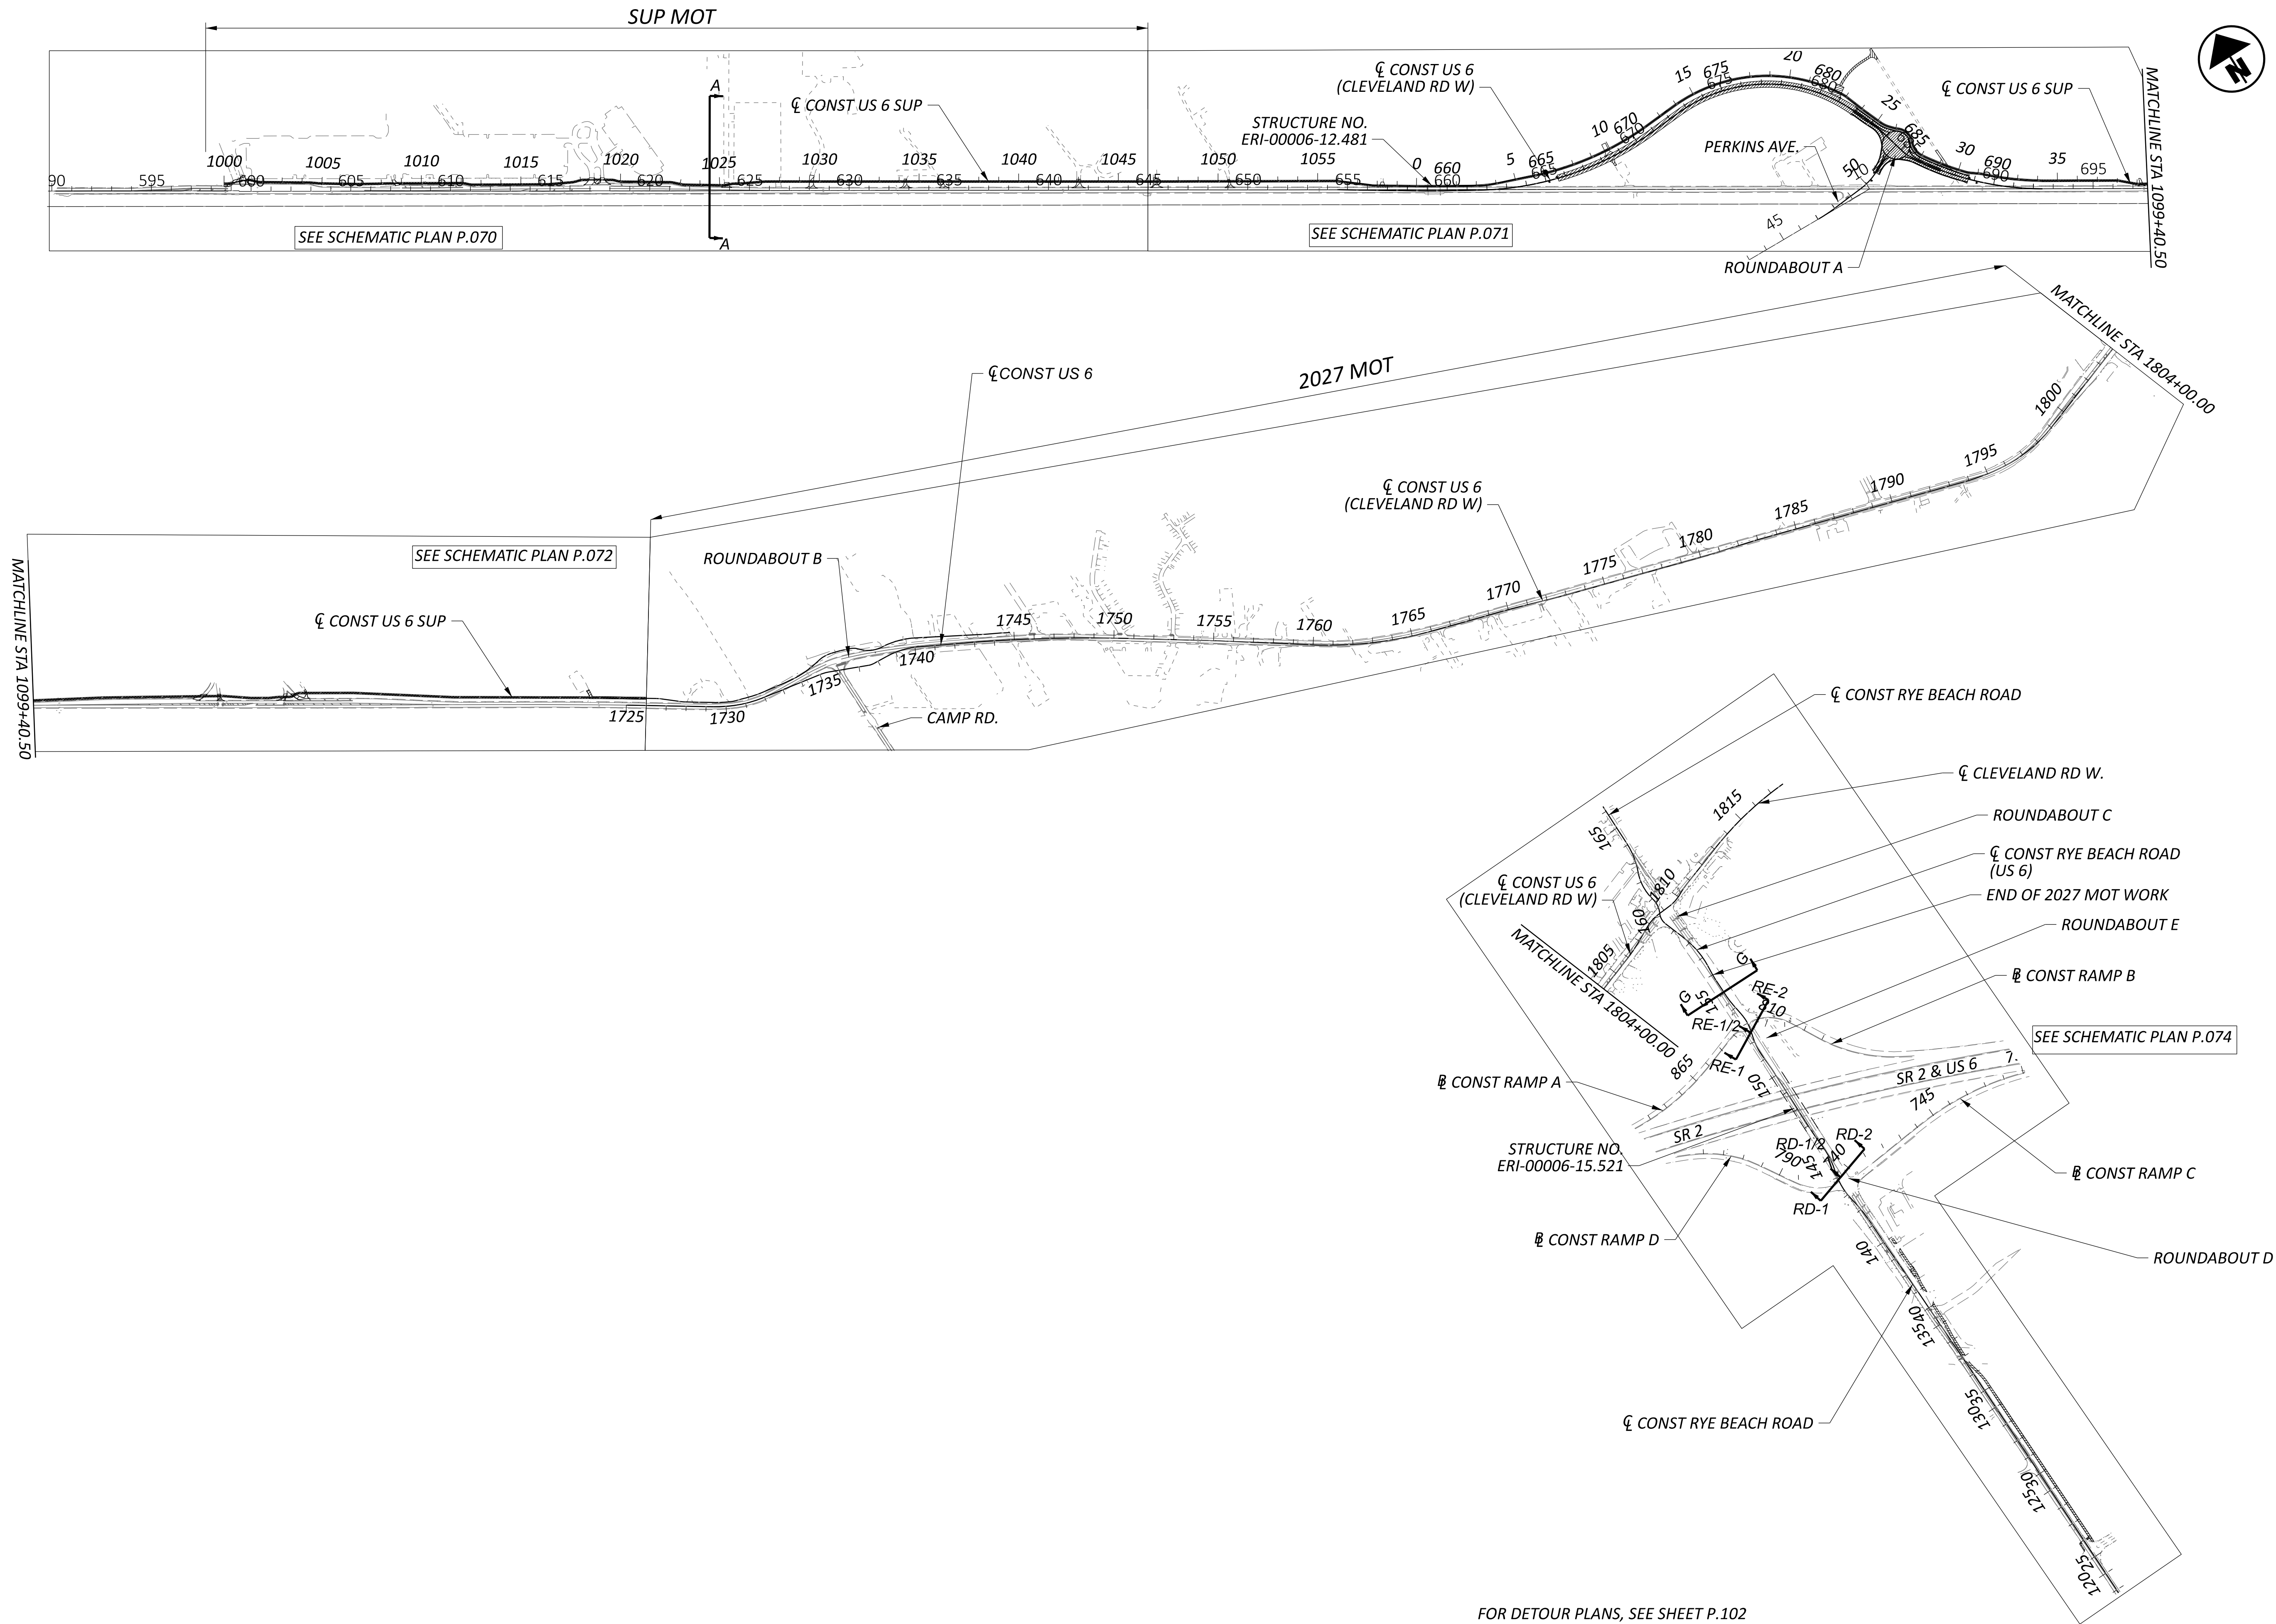

FOR DETOUR PLANS, SEE SHEET P.102

MOT OVERALL SCHEMATIC PLAN - PRE PHASE (2026 CONSTRUCTION)

HORIZONTAL
SCALE IN FEET
0 200 400 800

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
SSA


REVIEWER
SS

02/28/24

PROJECT ID
116570


SHEET
P.071

TOTAL
782

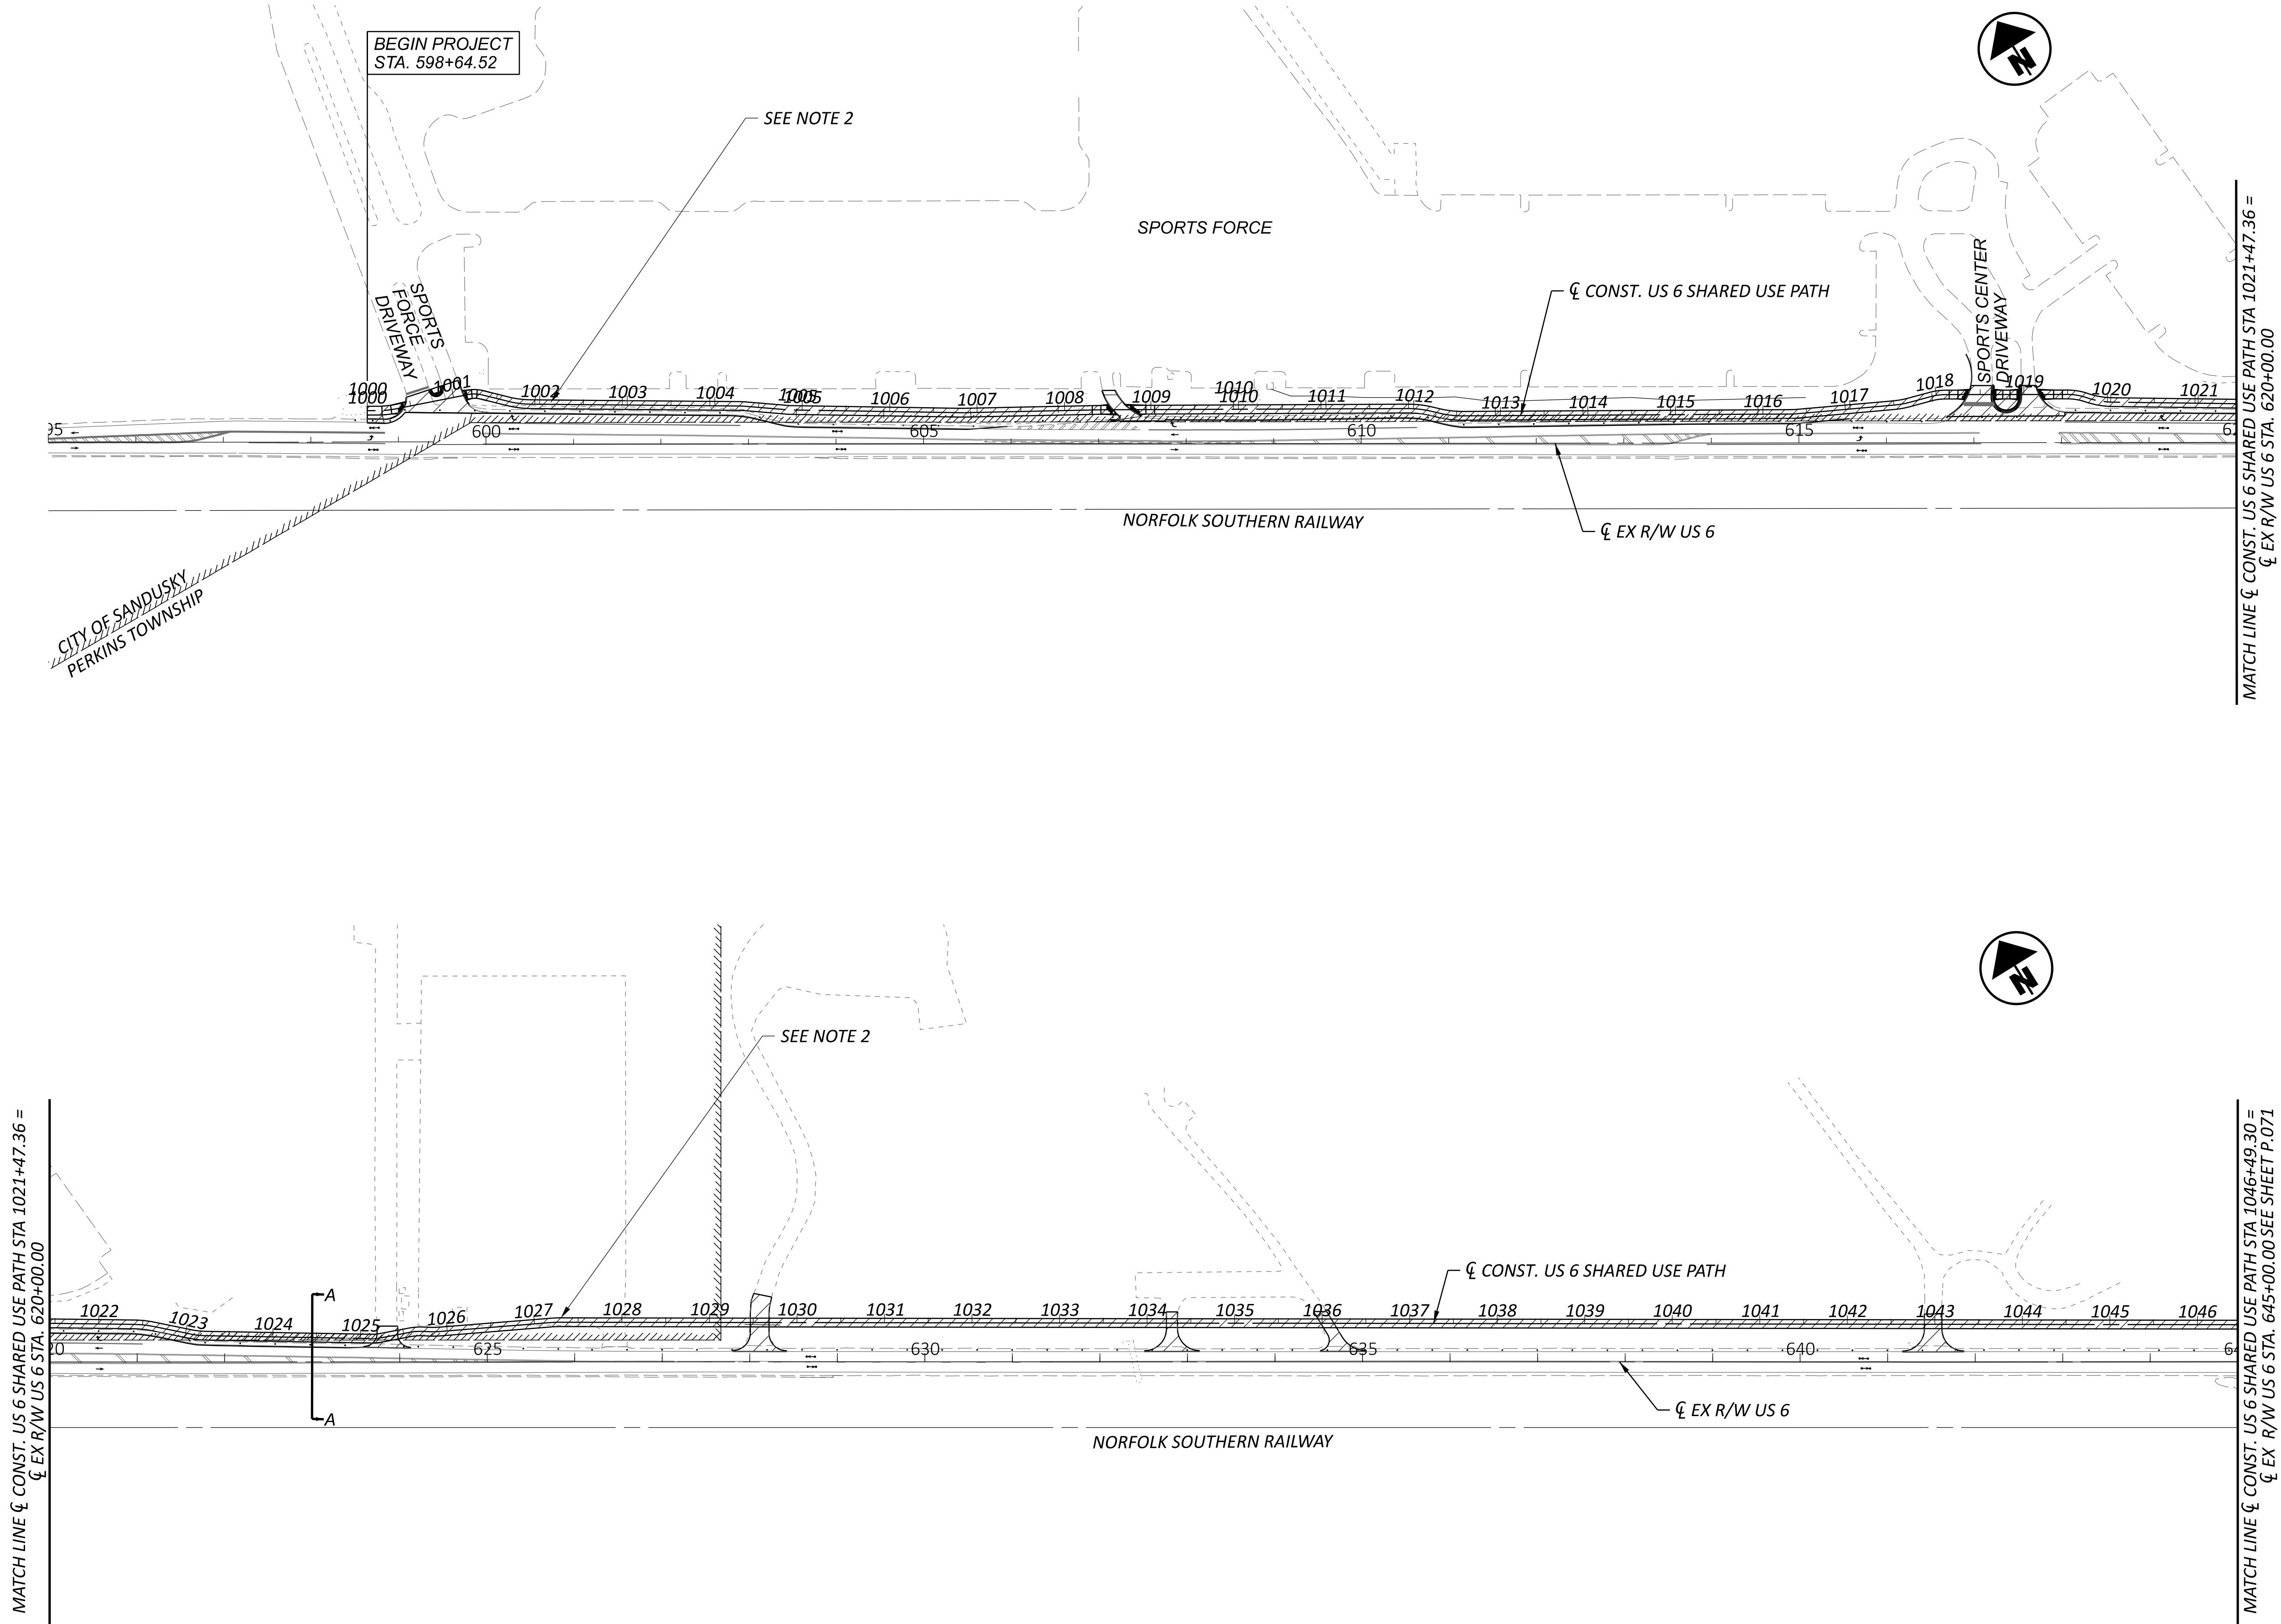


- NOTES:
- FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
 - SUP: USE FLAGGERS TO RESTRICT TRAFFIC TO ONE LANE WHERE NECESSARY TO CONSTRUCT THE RESURFACING AND MULTI-USE PATH OUTSIDE WIDENING AREAS AND PROPOSED ROUNDABOUTS. USE LEOS TO CONTROL TRAFFIC AT SIGNALIZED INTERSECTIONS WHEN NECESSARY. ASSUME SUP CONSTRUCTION DURATION OF 60 DAYS.

HORIZONTAL SCALE IN FEET 0 50 100 200	
MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION) US 6 BEGIN PROJECT TO STA 645+00	
DESIGN AGENCY TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.072	782

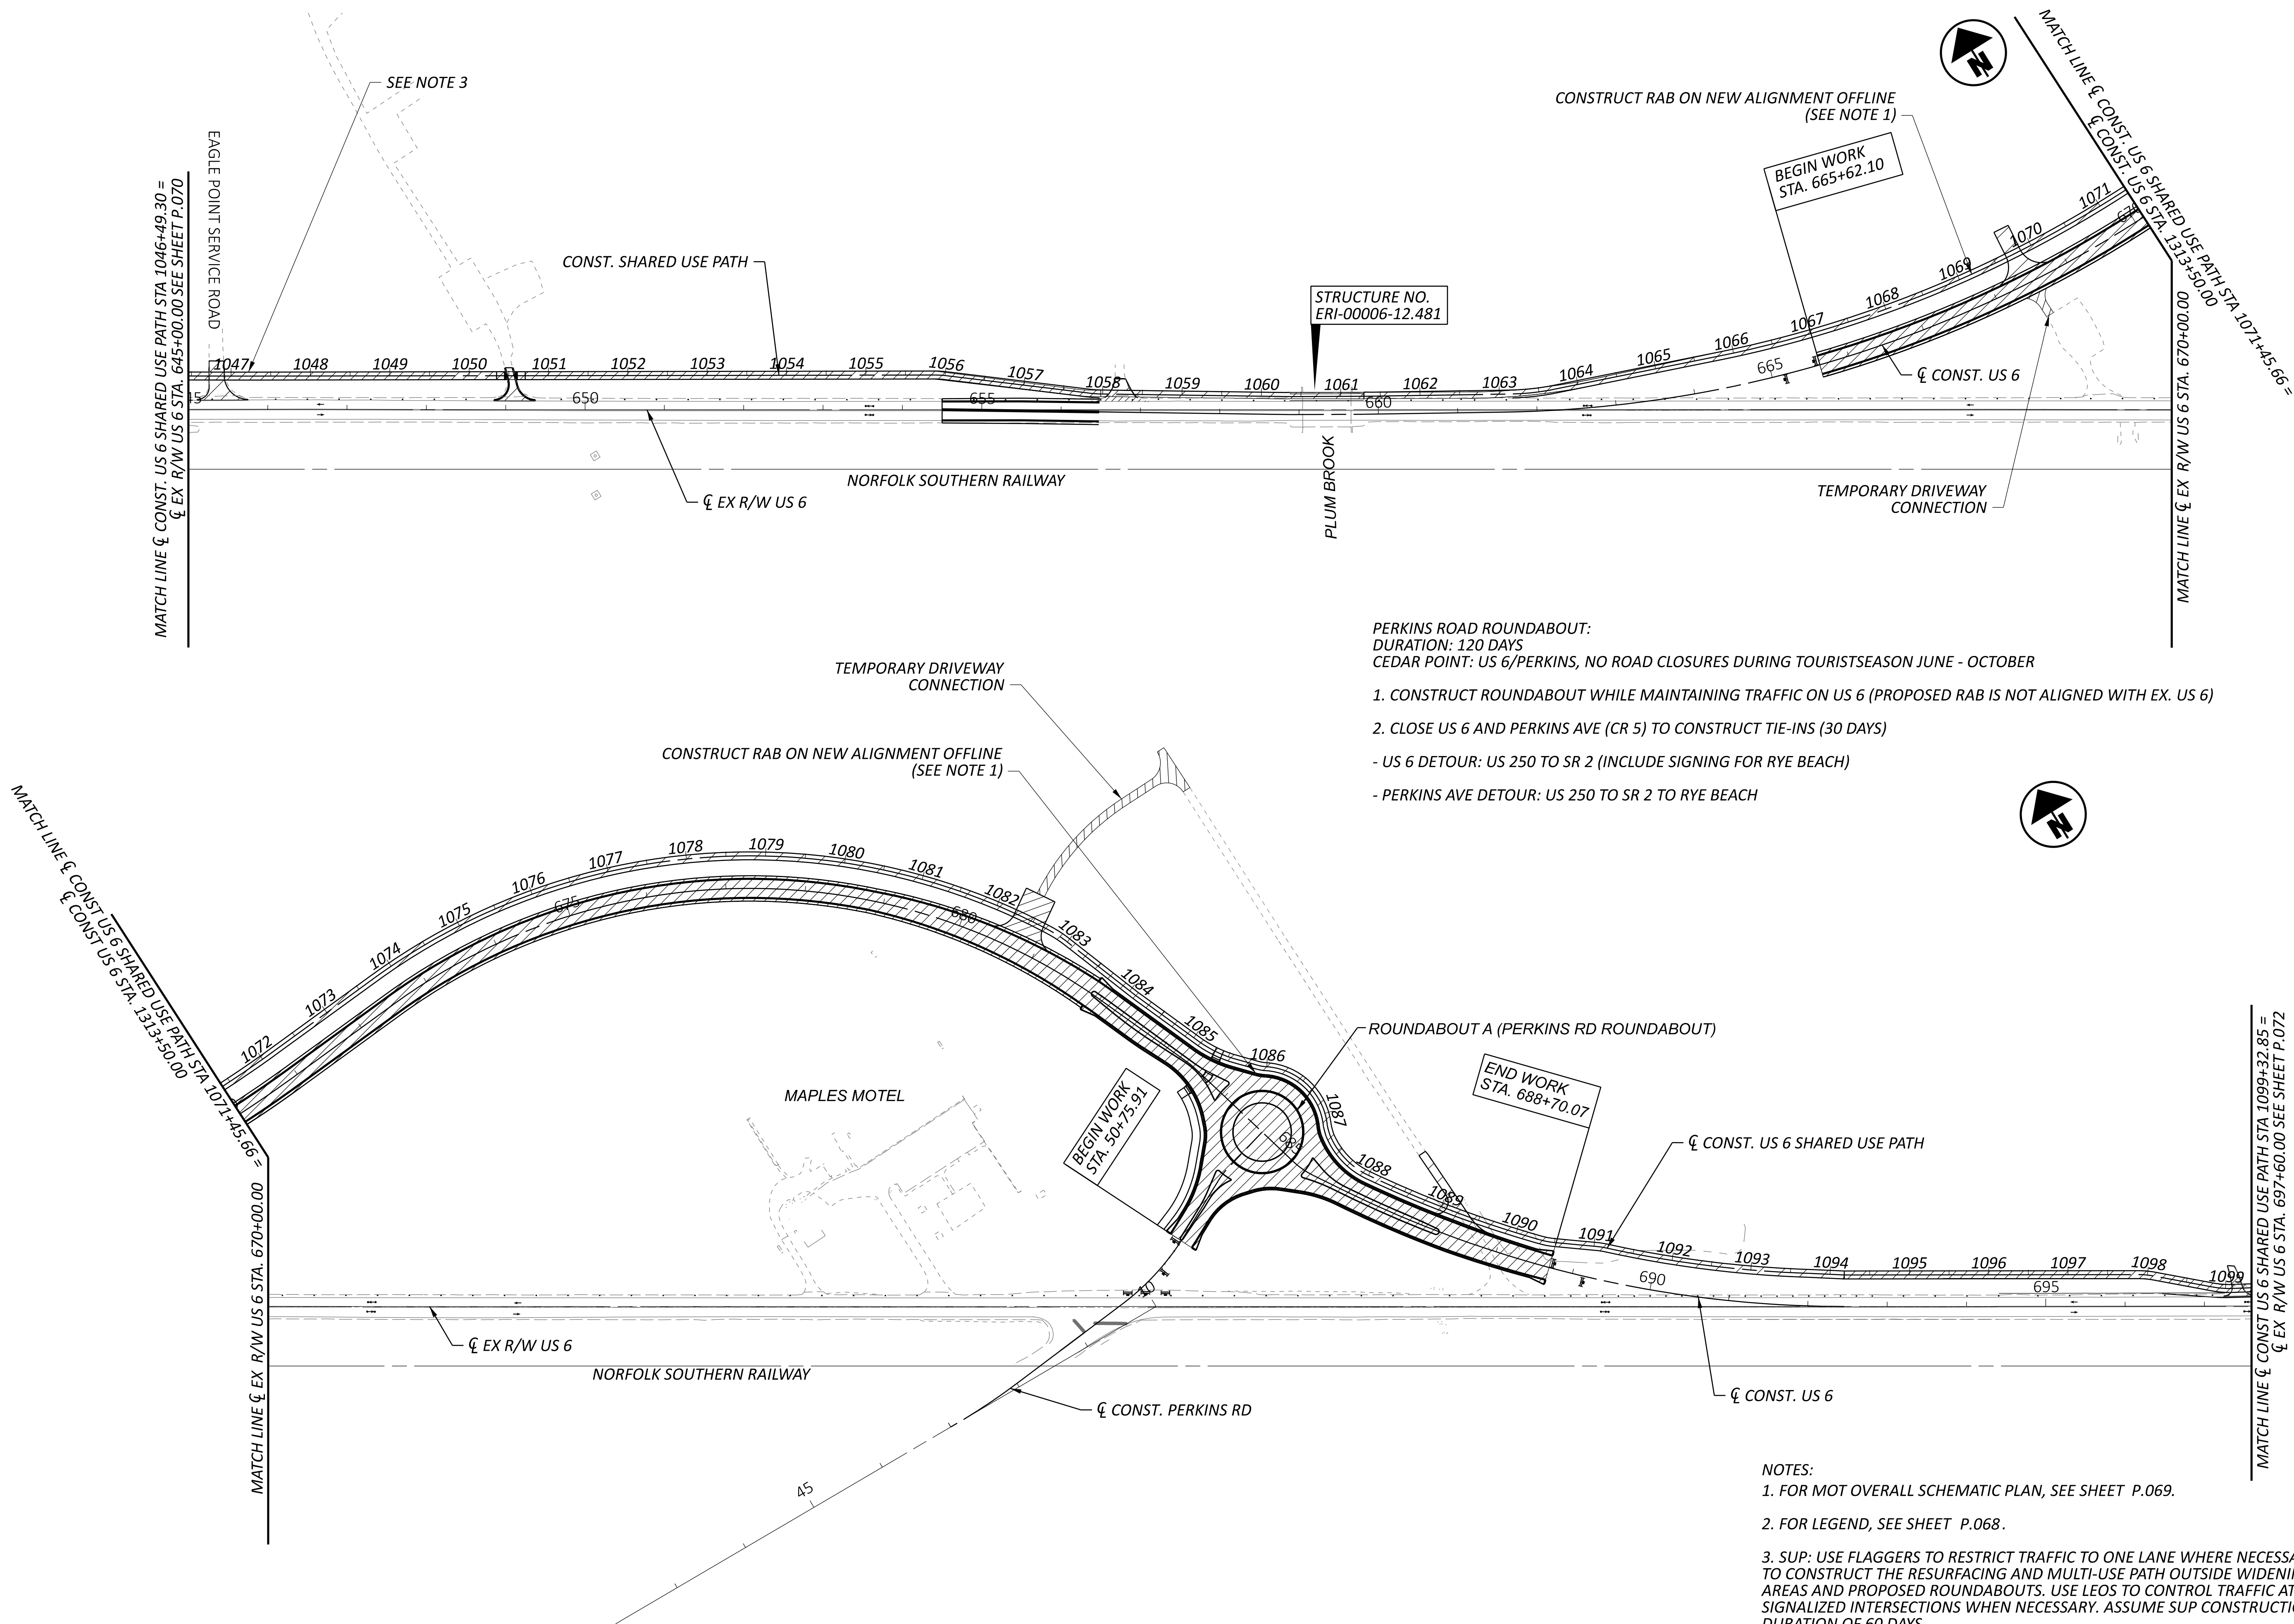

MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION)
US 6 STA 645+00 TO STA 695+00




DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.073 782

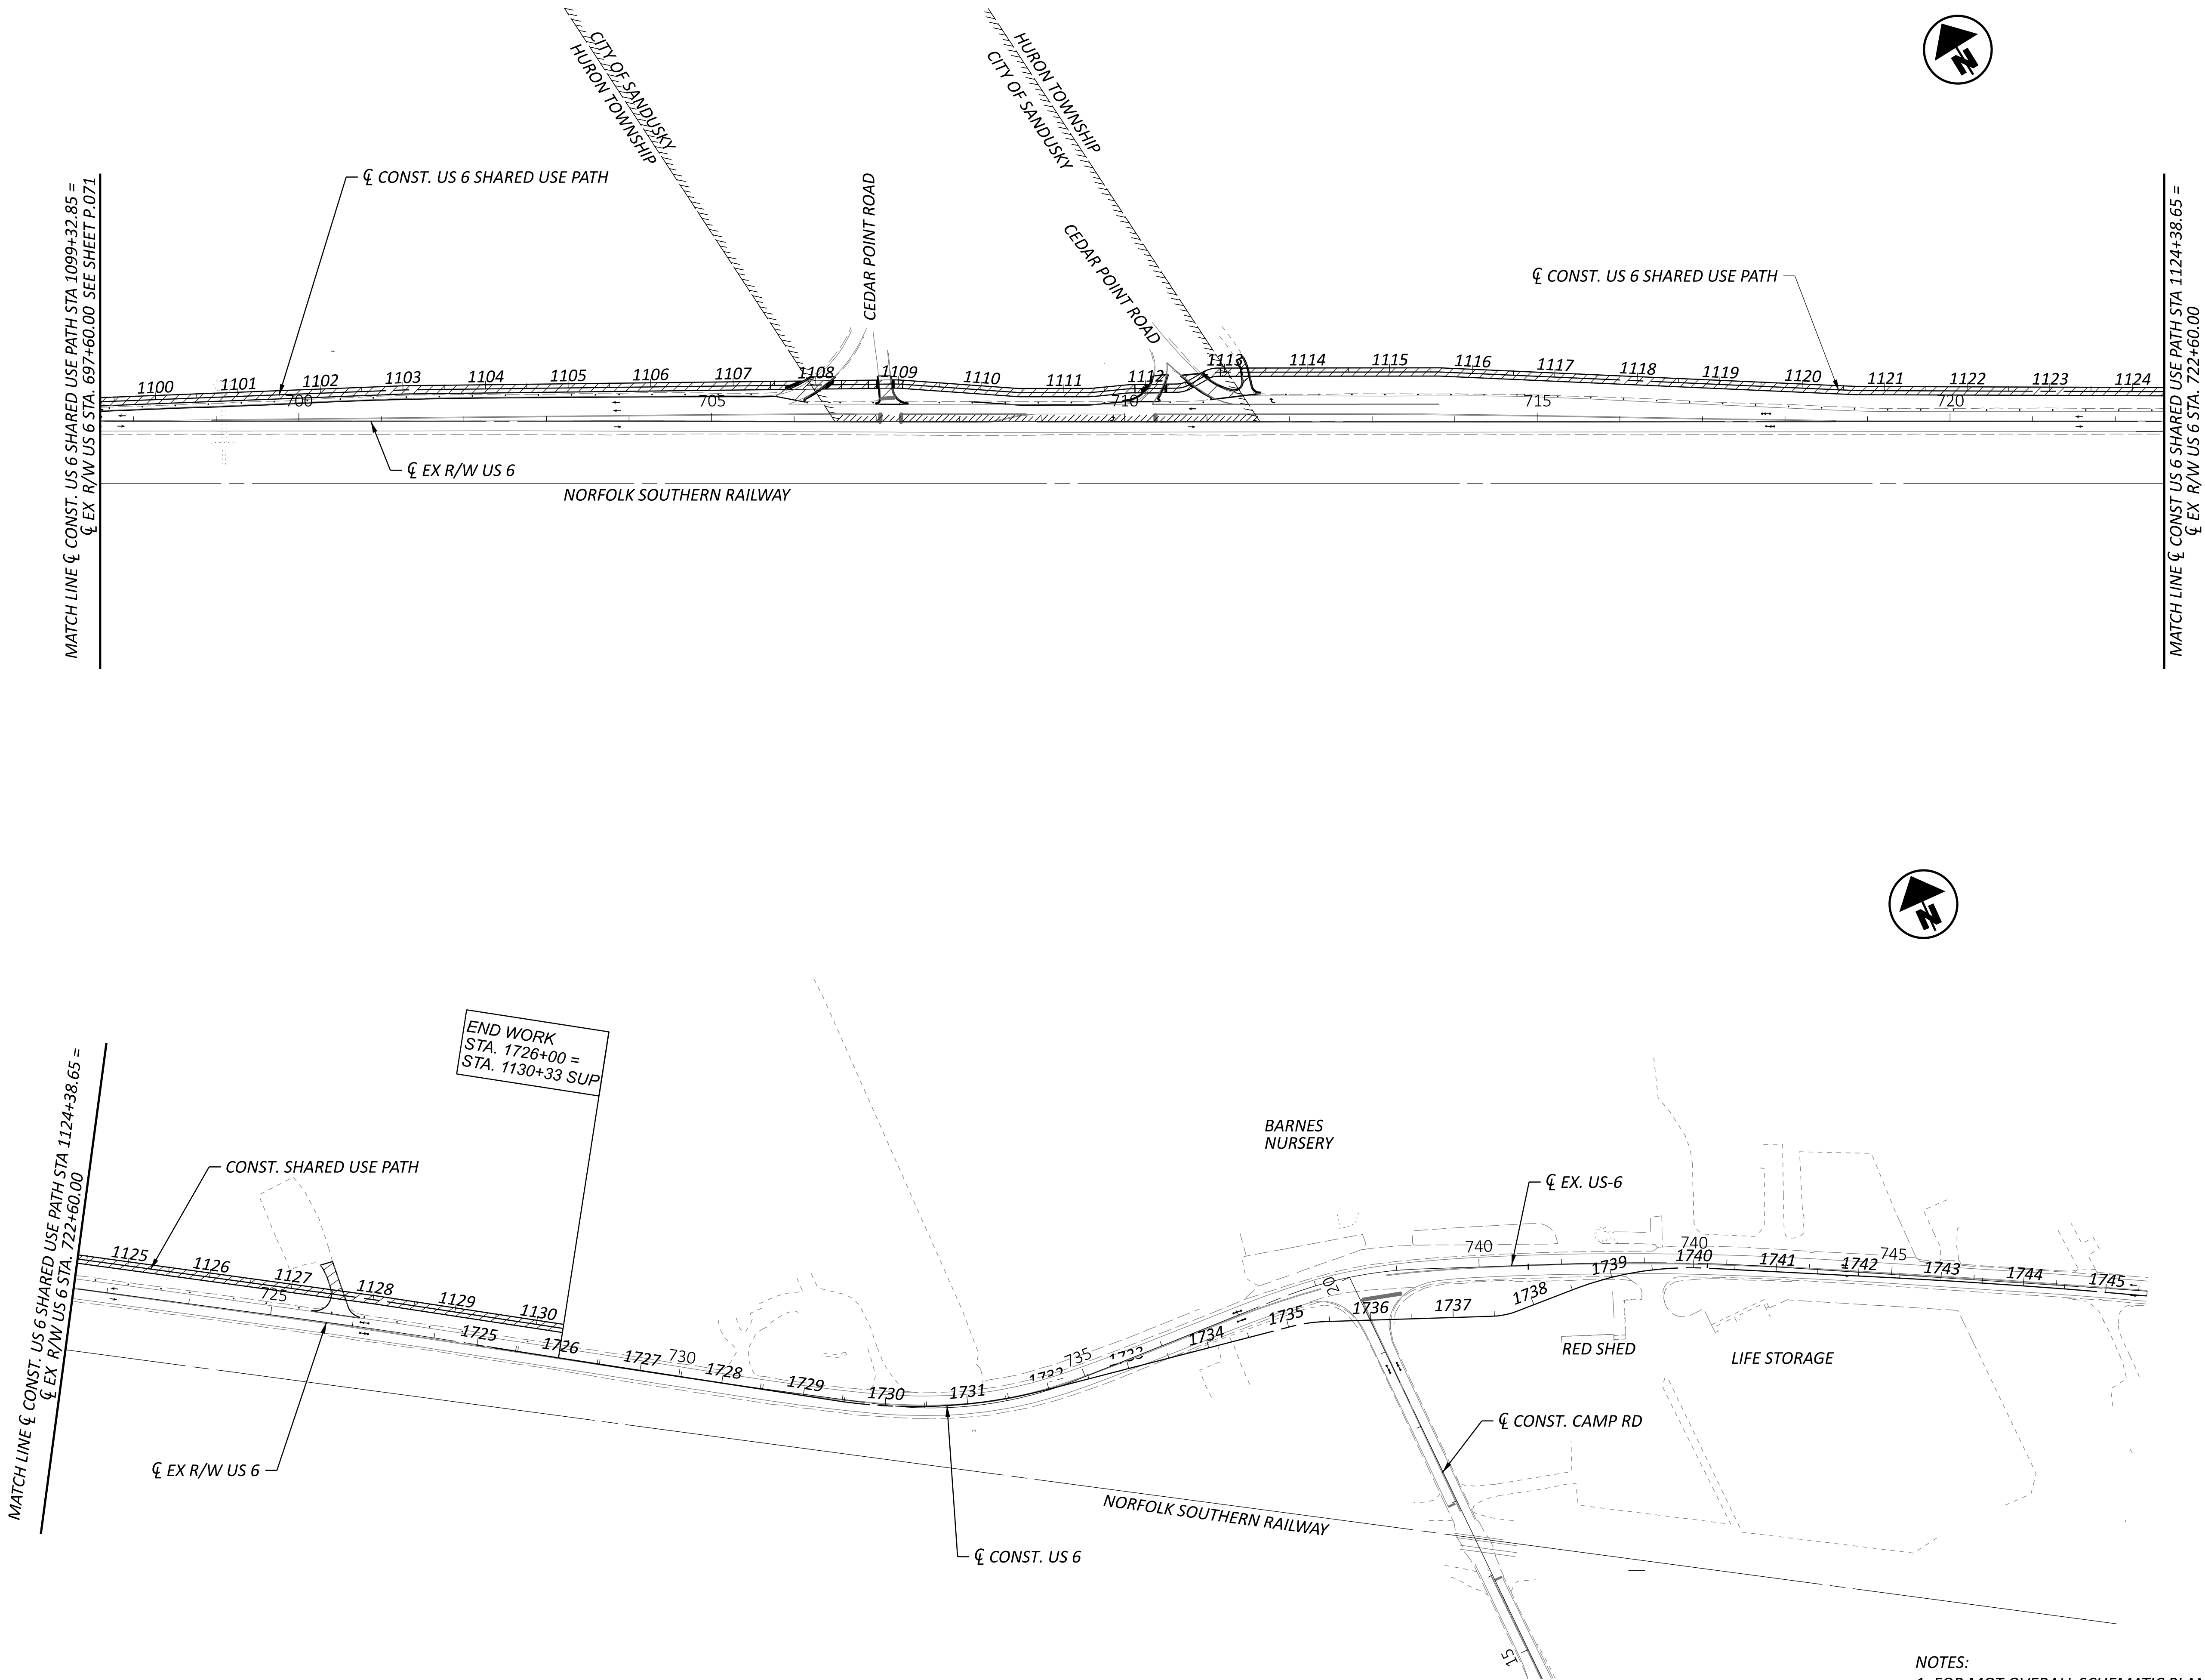

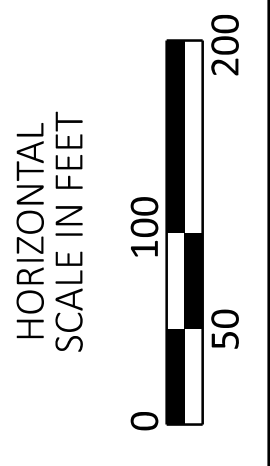

MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION)
WIDENING SECTION STA 745+50.00 TO STA 804+00.00

TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID

116570


SHEET

P.075

TOTAL

782

- NOTES:**
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
 2. FOR LEGEND, SEE SHEET P.068

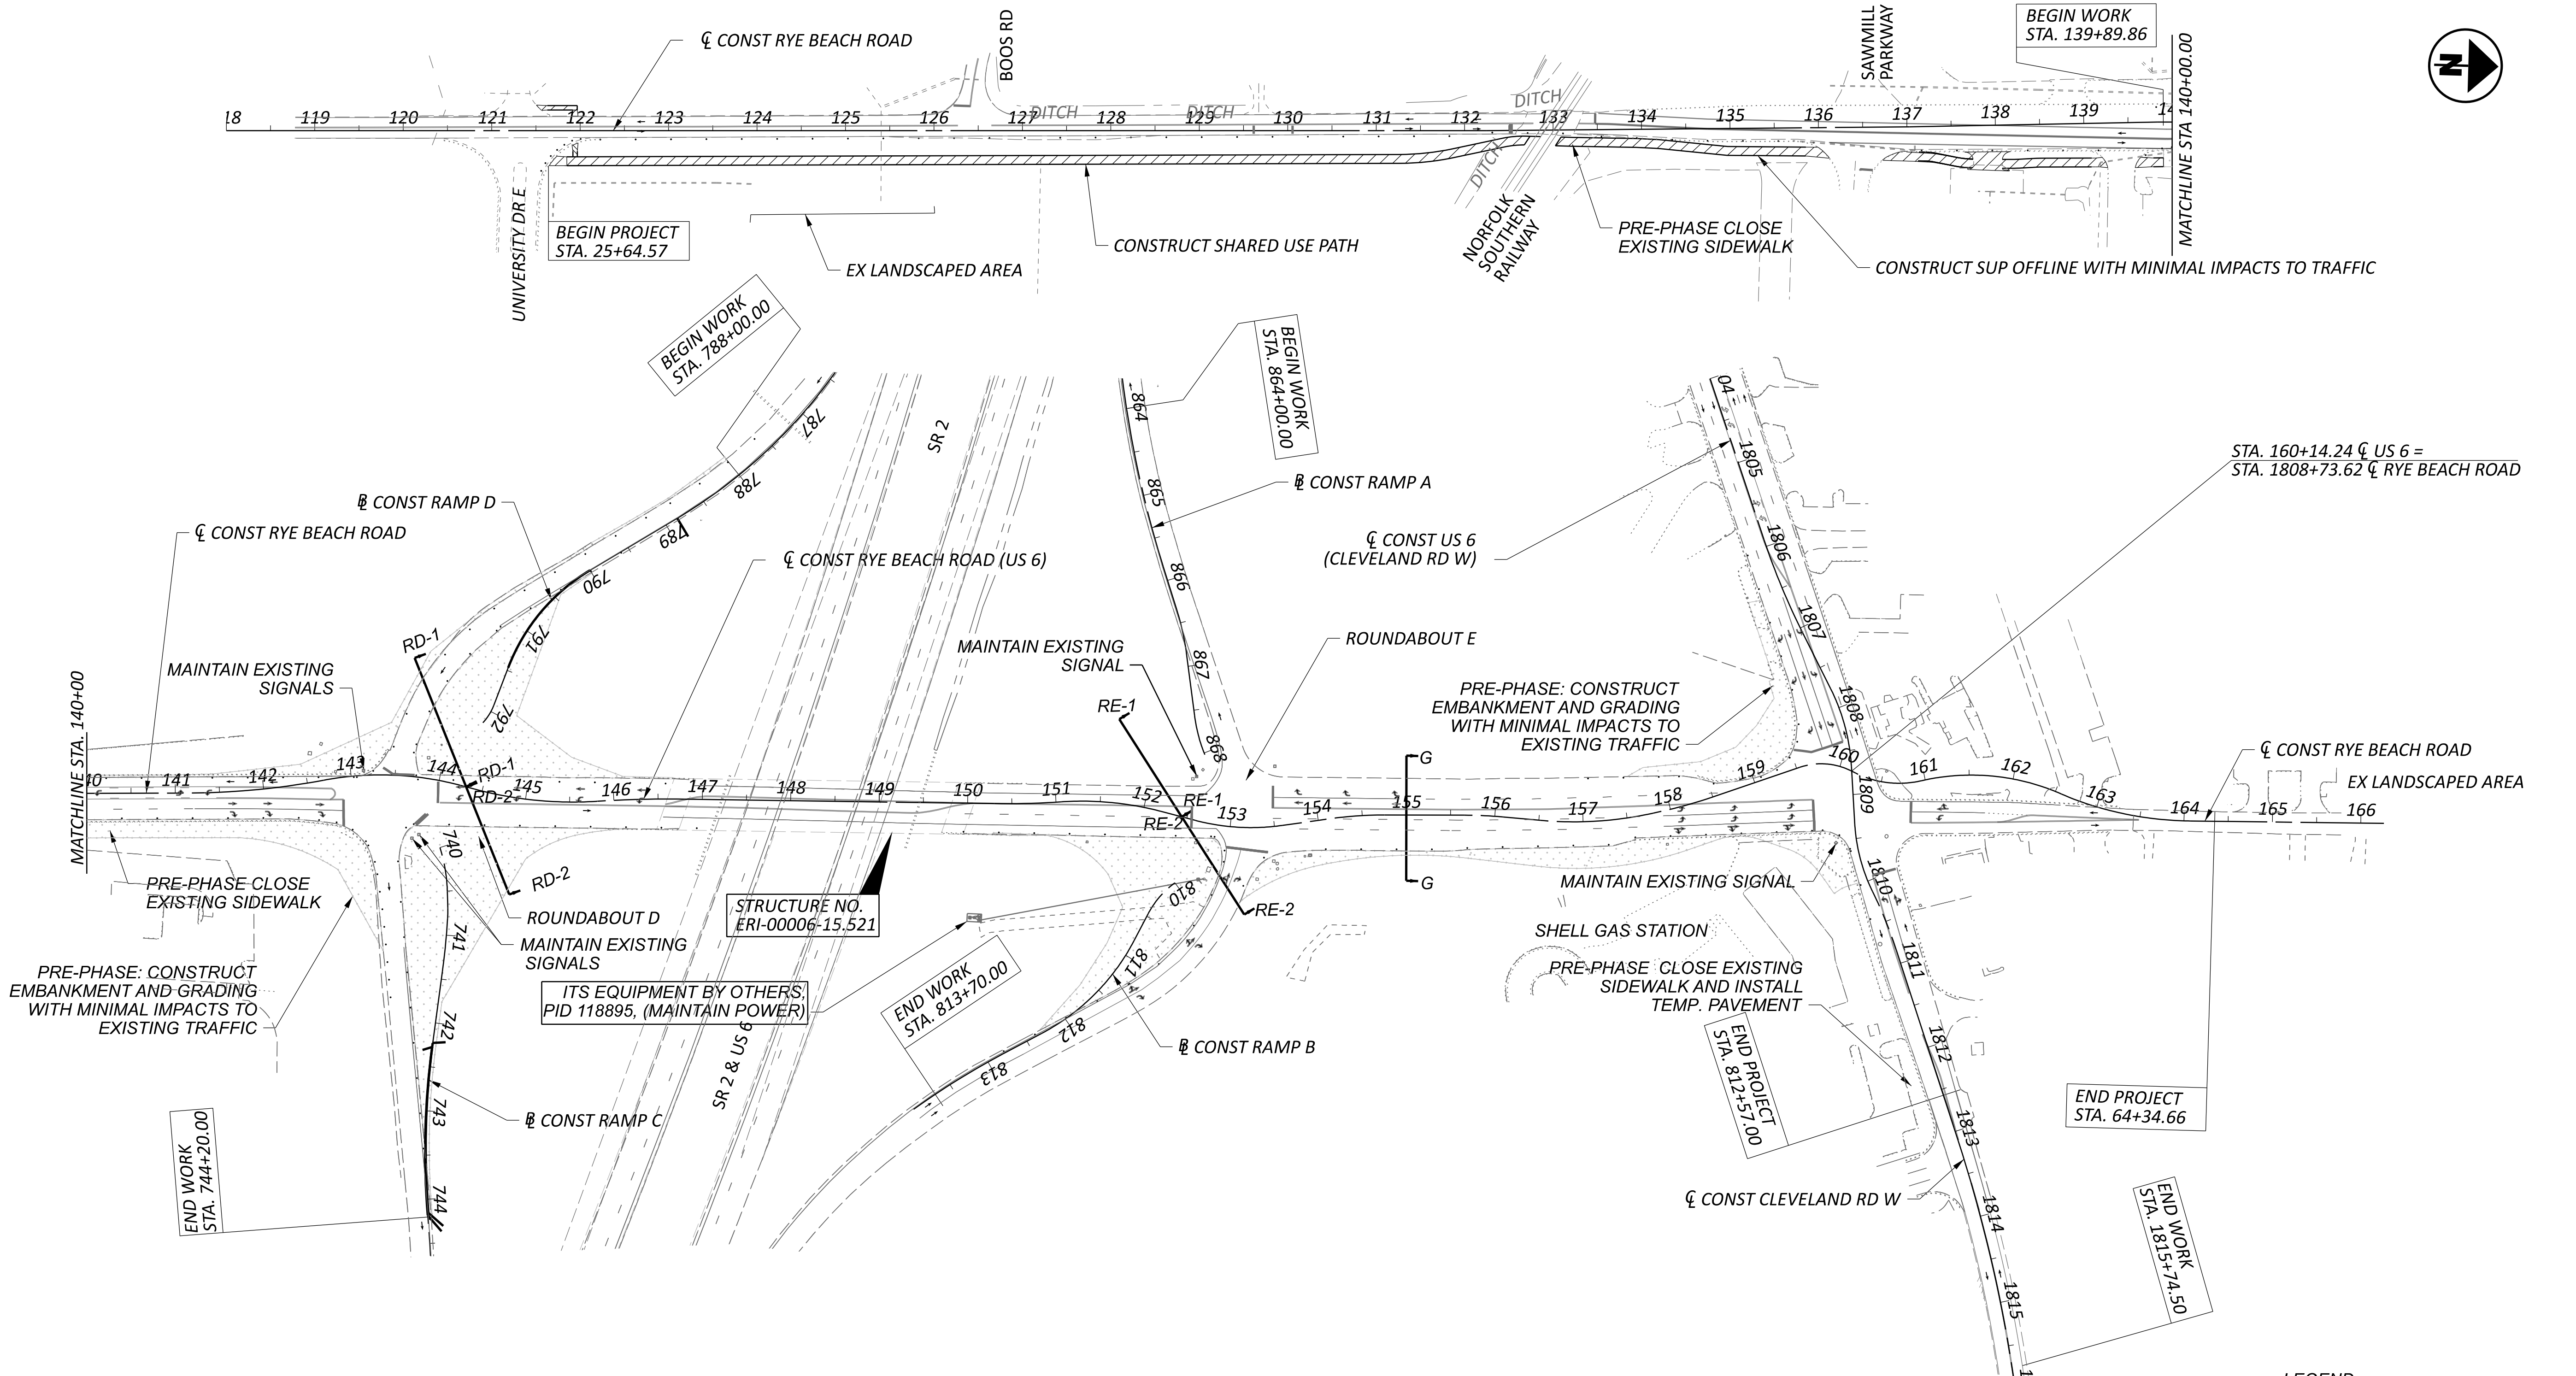

RYE BEACH ROUNDABOUTS:
DURATION: 180 DAYS
CEDAR POINT: NO ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER


PRE-PHASE:
CONSTRUCT EMBANKMENT AND GRADING WITH MINIMAL IMPACTS TO EXISTING TRAFFIC.

LEGEND:

	EMBANKMENT AND GRADING CONSTRUCTED IN PRE-PHASE
	PAVEMENT CONSTRUCTED IN PREVIOUS PHASE
	WORK ZONE
	TEMPORARY PAVEMENT
	DIRECTION OF TRAFFIC
	DRUMS

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

MOT SCHEMATIC PLAN - PRE PHASE (2026 CONSTRUCTION)
RYE BEACH ROAD STA 118+00.00 TO STA 166+00.00



DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID


116570

SHEET

P.076

TOTAL

782

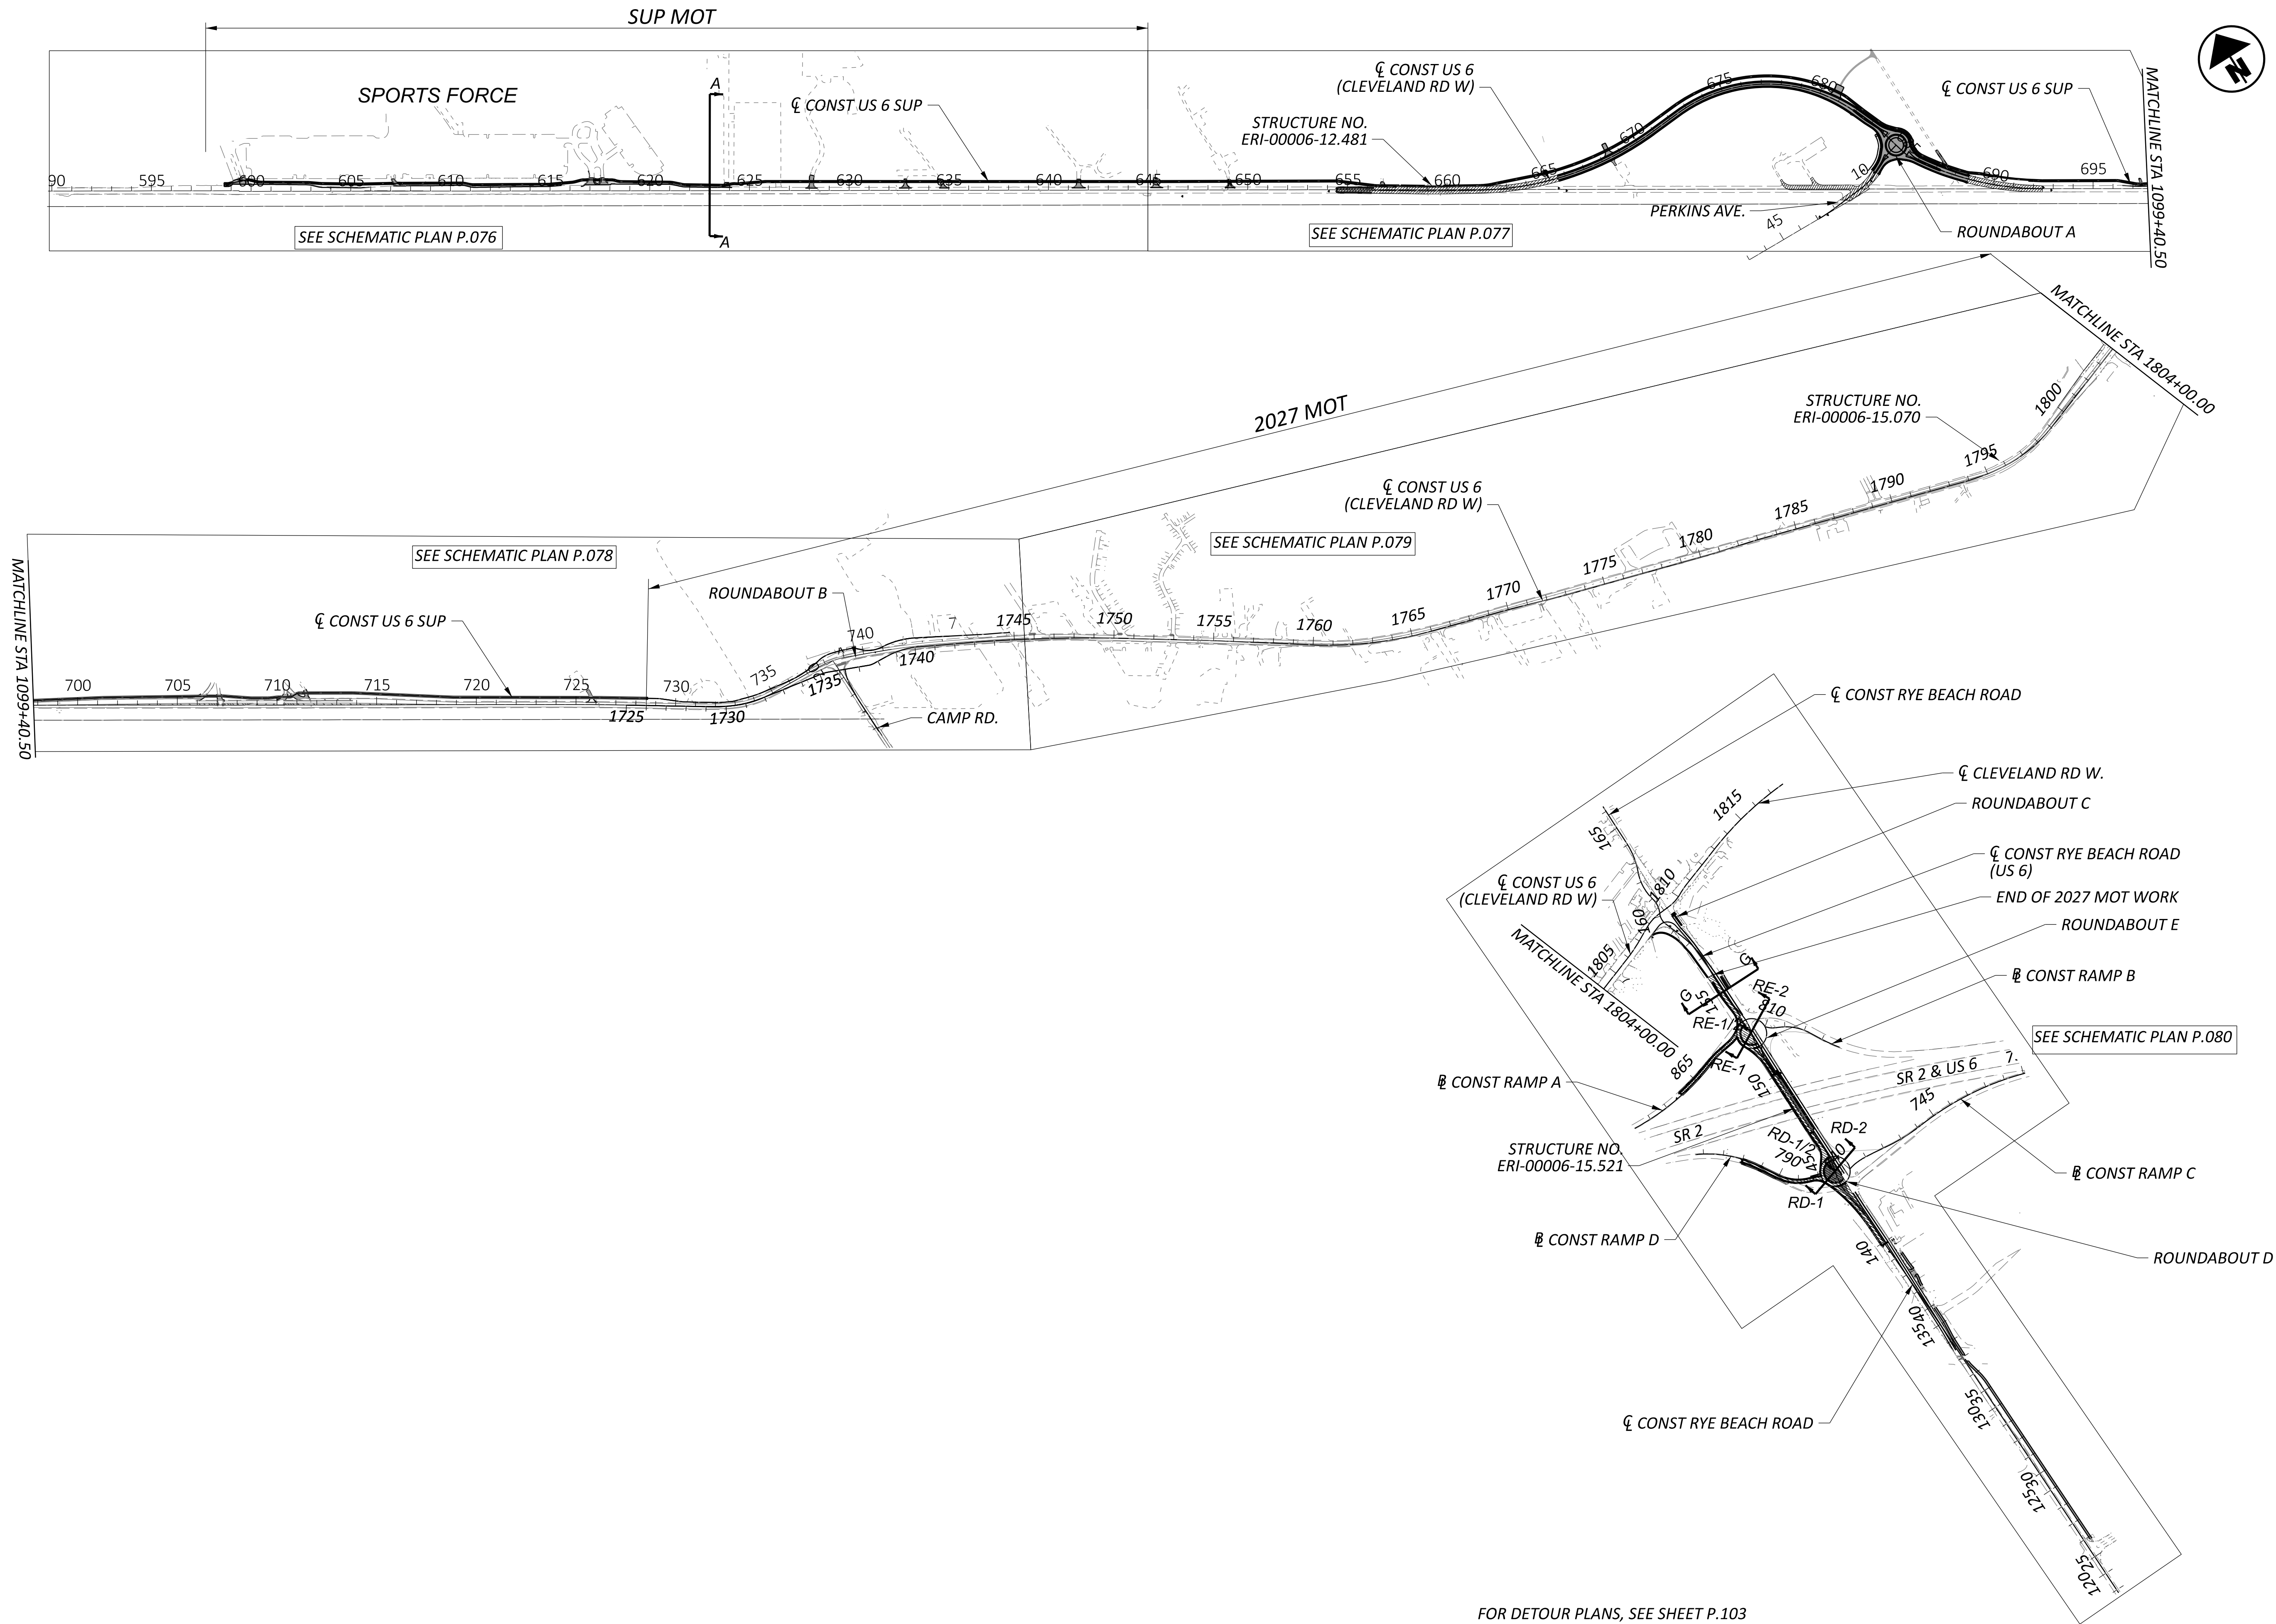

FOR DETOUR PLANS, SEE SHEET P.103

MOT OVERALL SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS

PROJECT ID
02/28/24


SHEET
116570

TOTAL
P.077 | 782

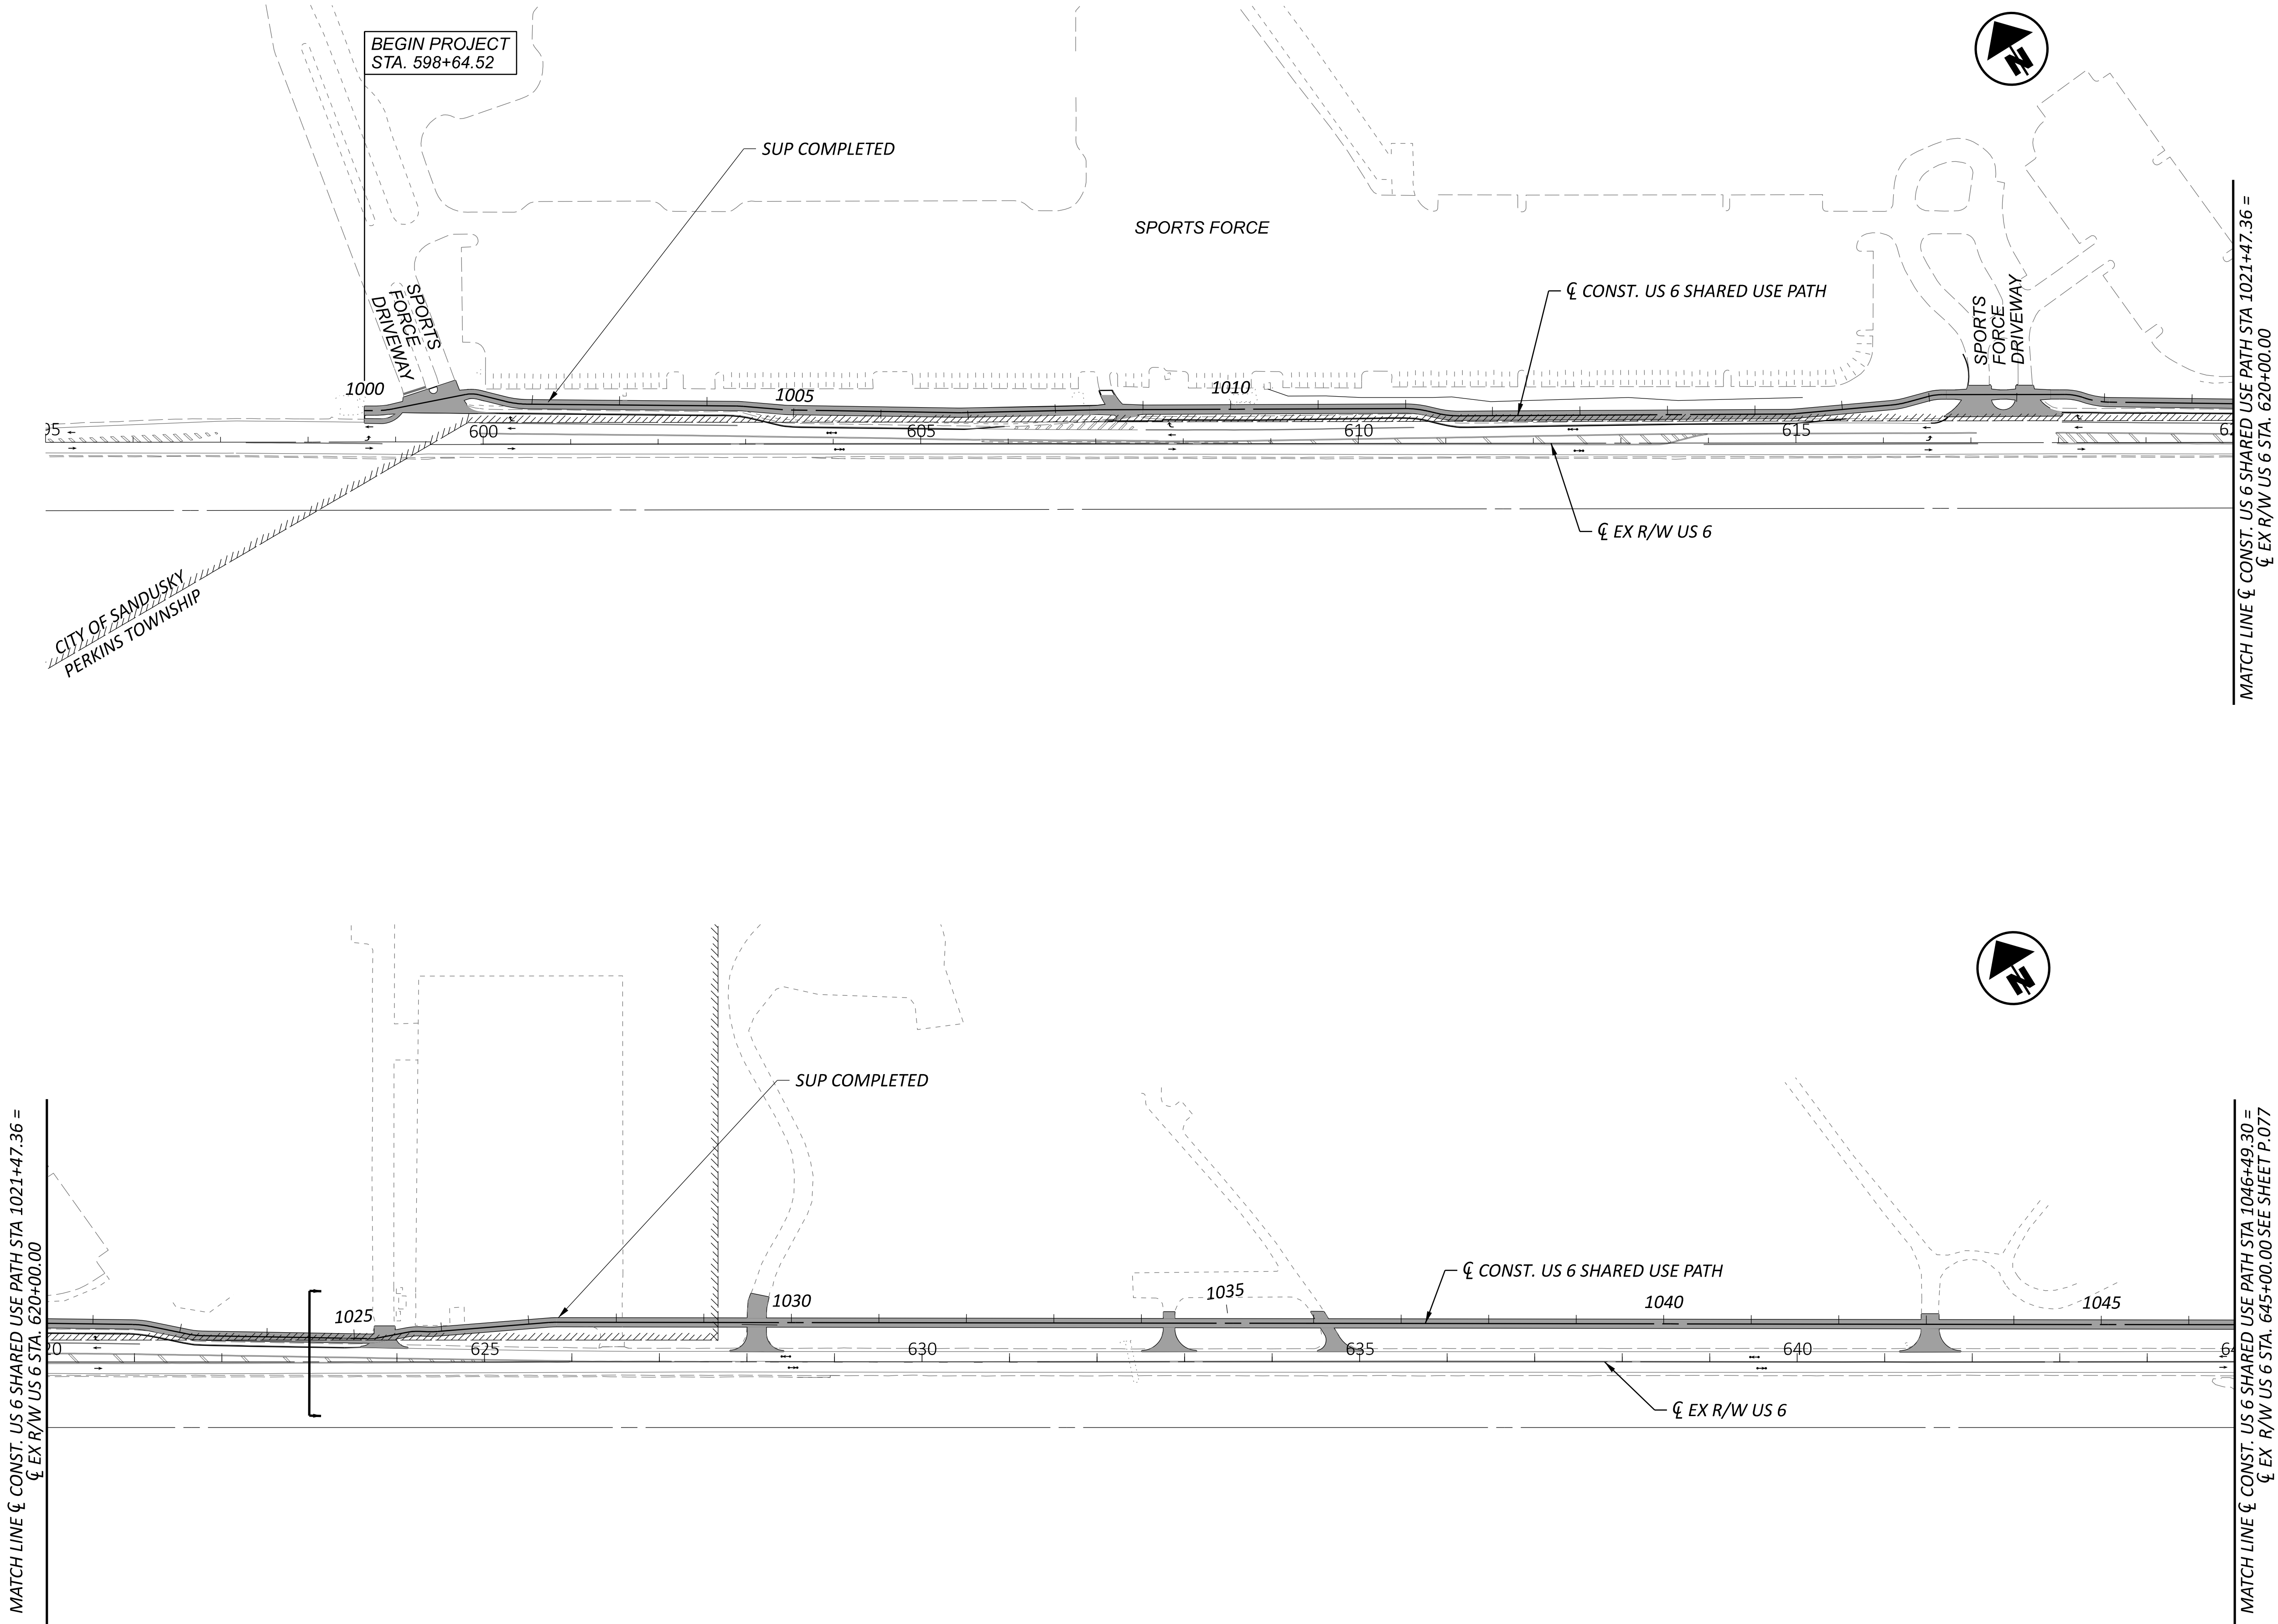


NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
2. FOR LEGEND, SEE SHEET P.076

HORIZONTAL SCALE IN FEET 0 50 100 200	
MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION) US 6 BEGIN PROJECT TO STA 645+00	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.078	782

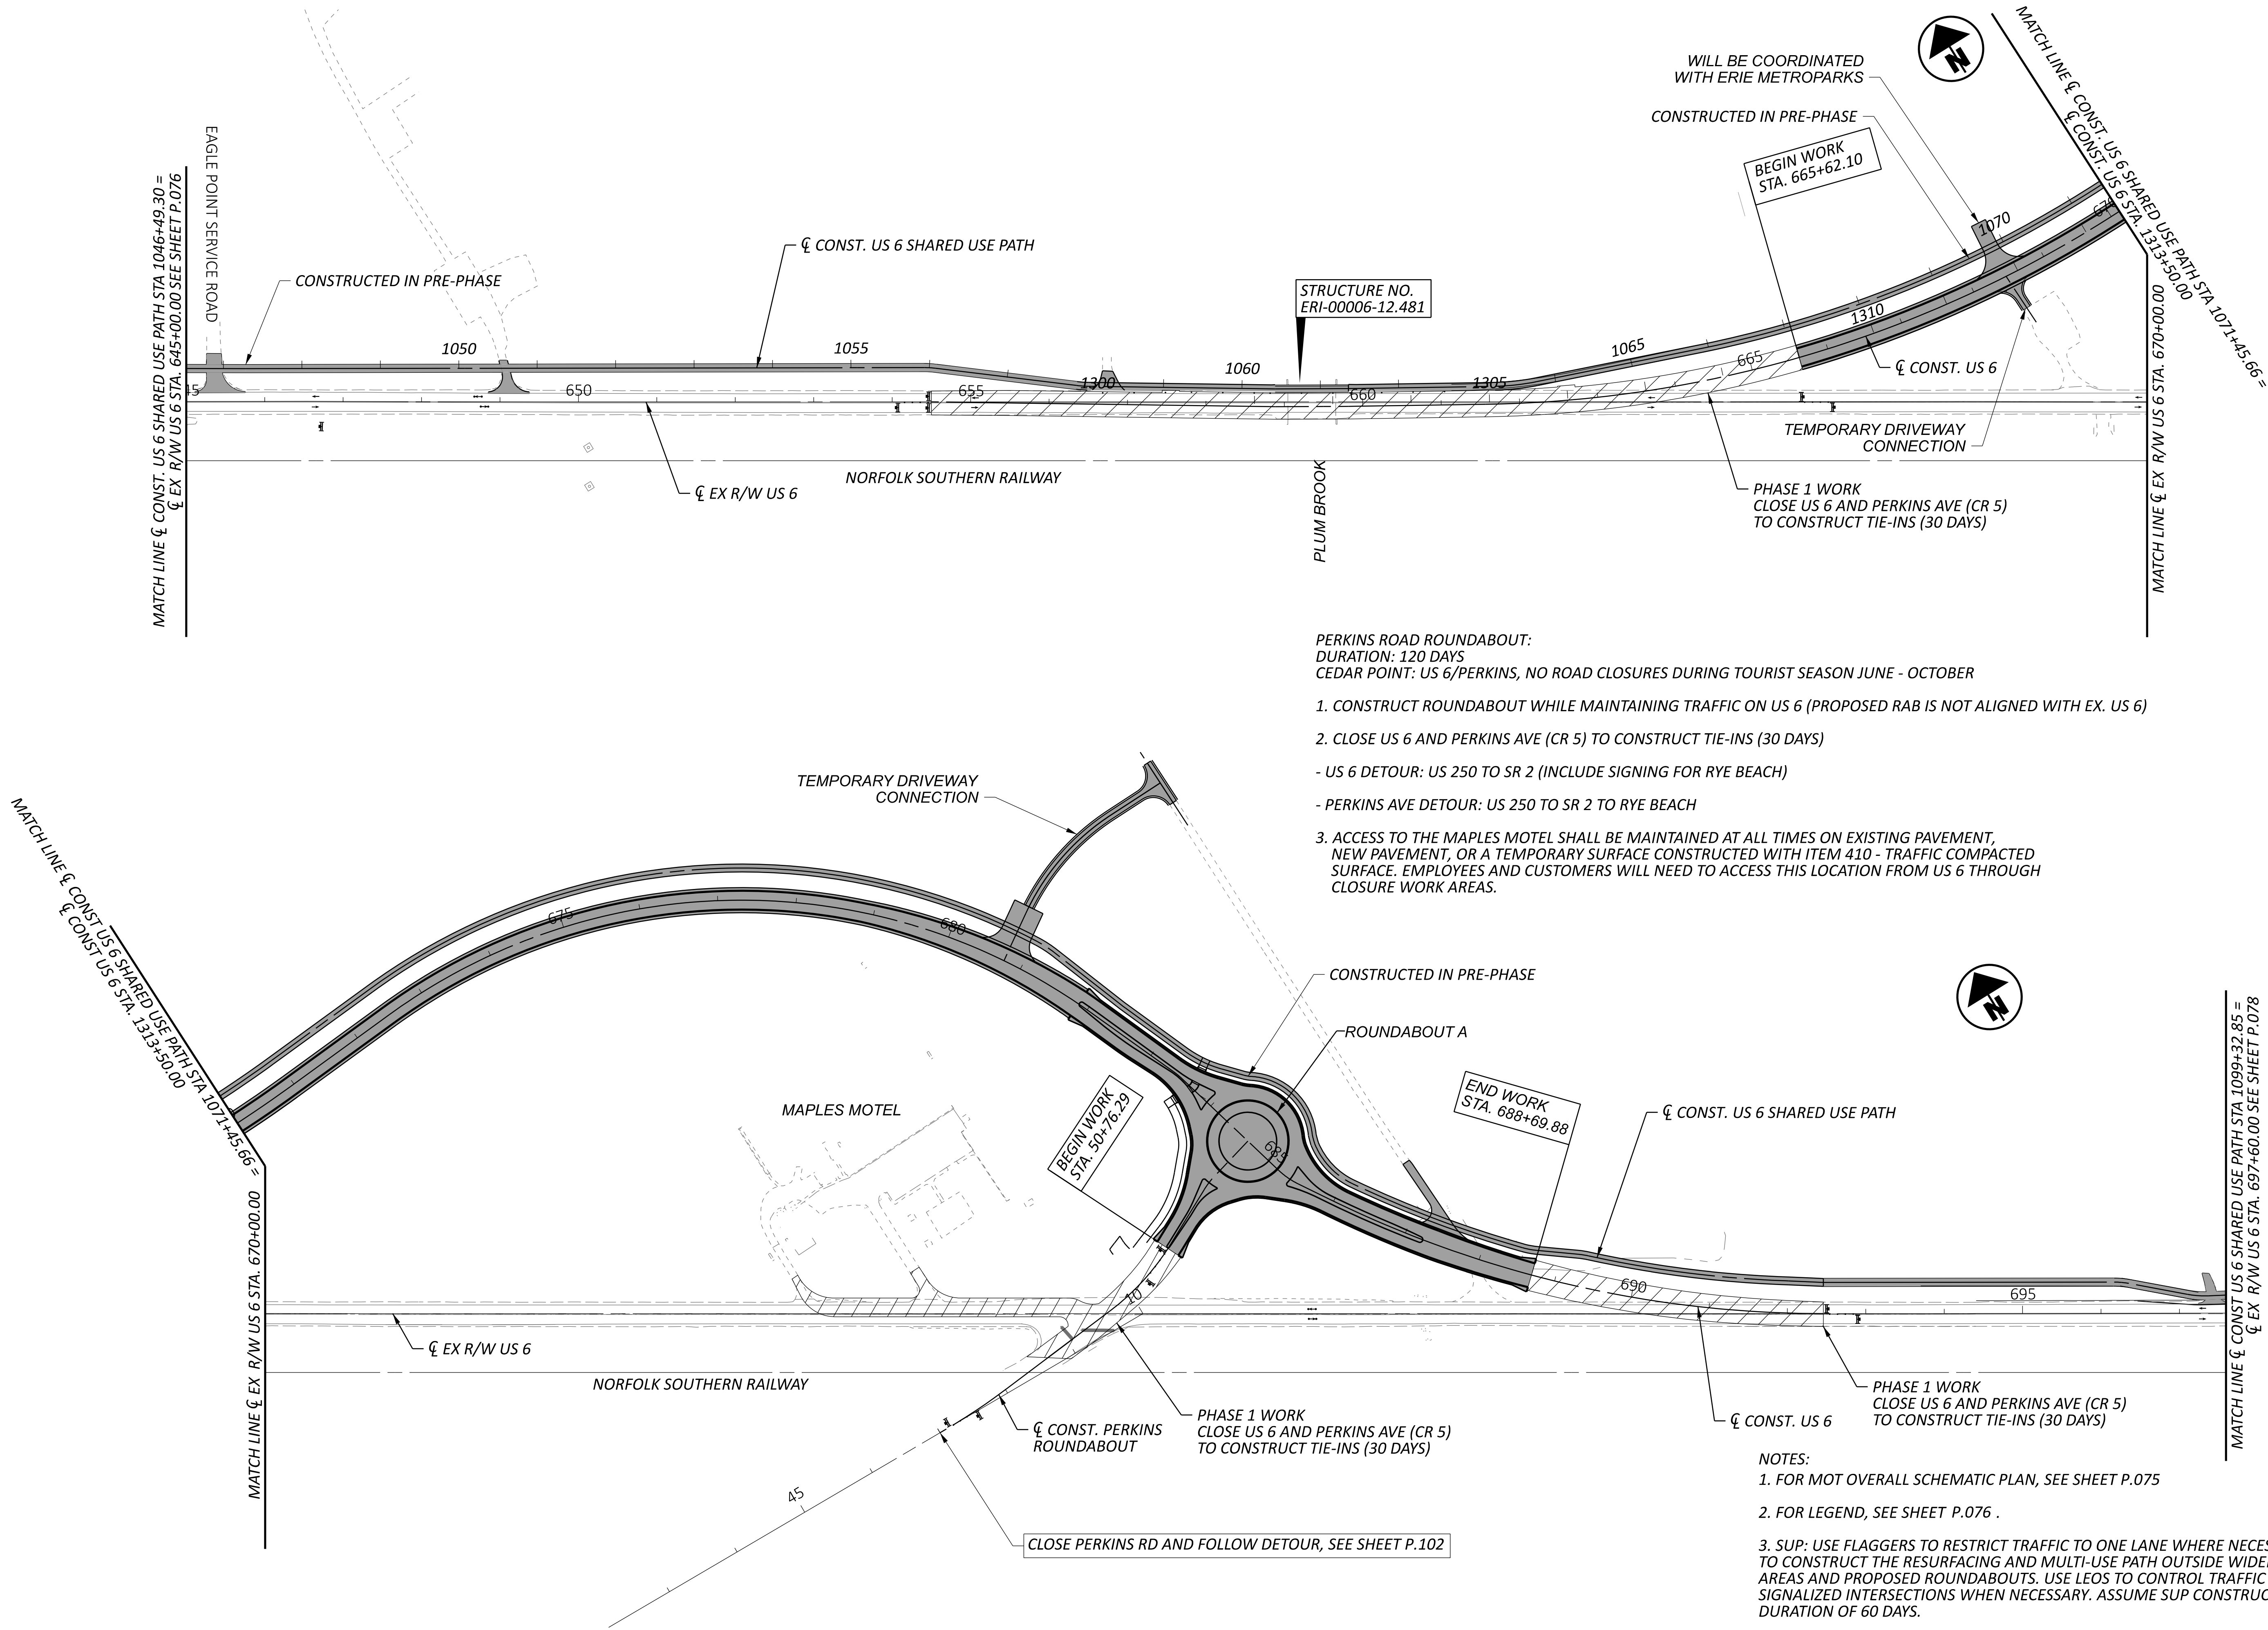

ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: GB103 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:19:37 PM USER: ssadusei
 \\pw\vhohiodot-pw.bentley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\Erle\116570.402-Engineering_TransSystems\MOT\Sheets\116570_M8004_CV2026.dgn

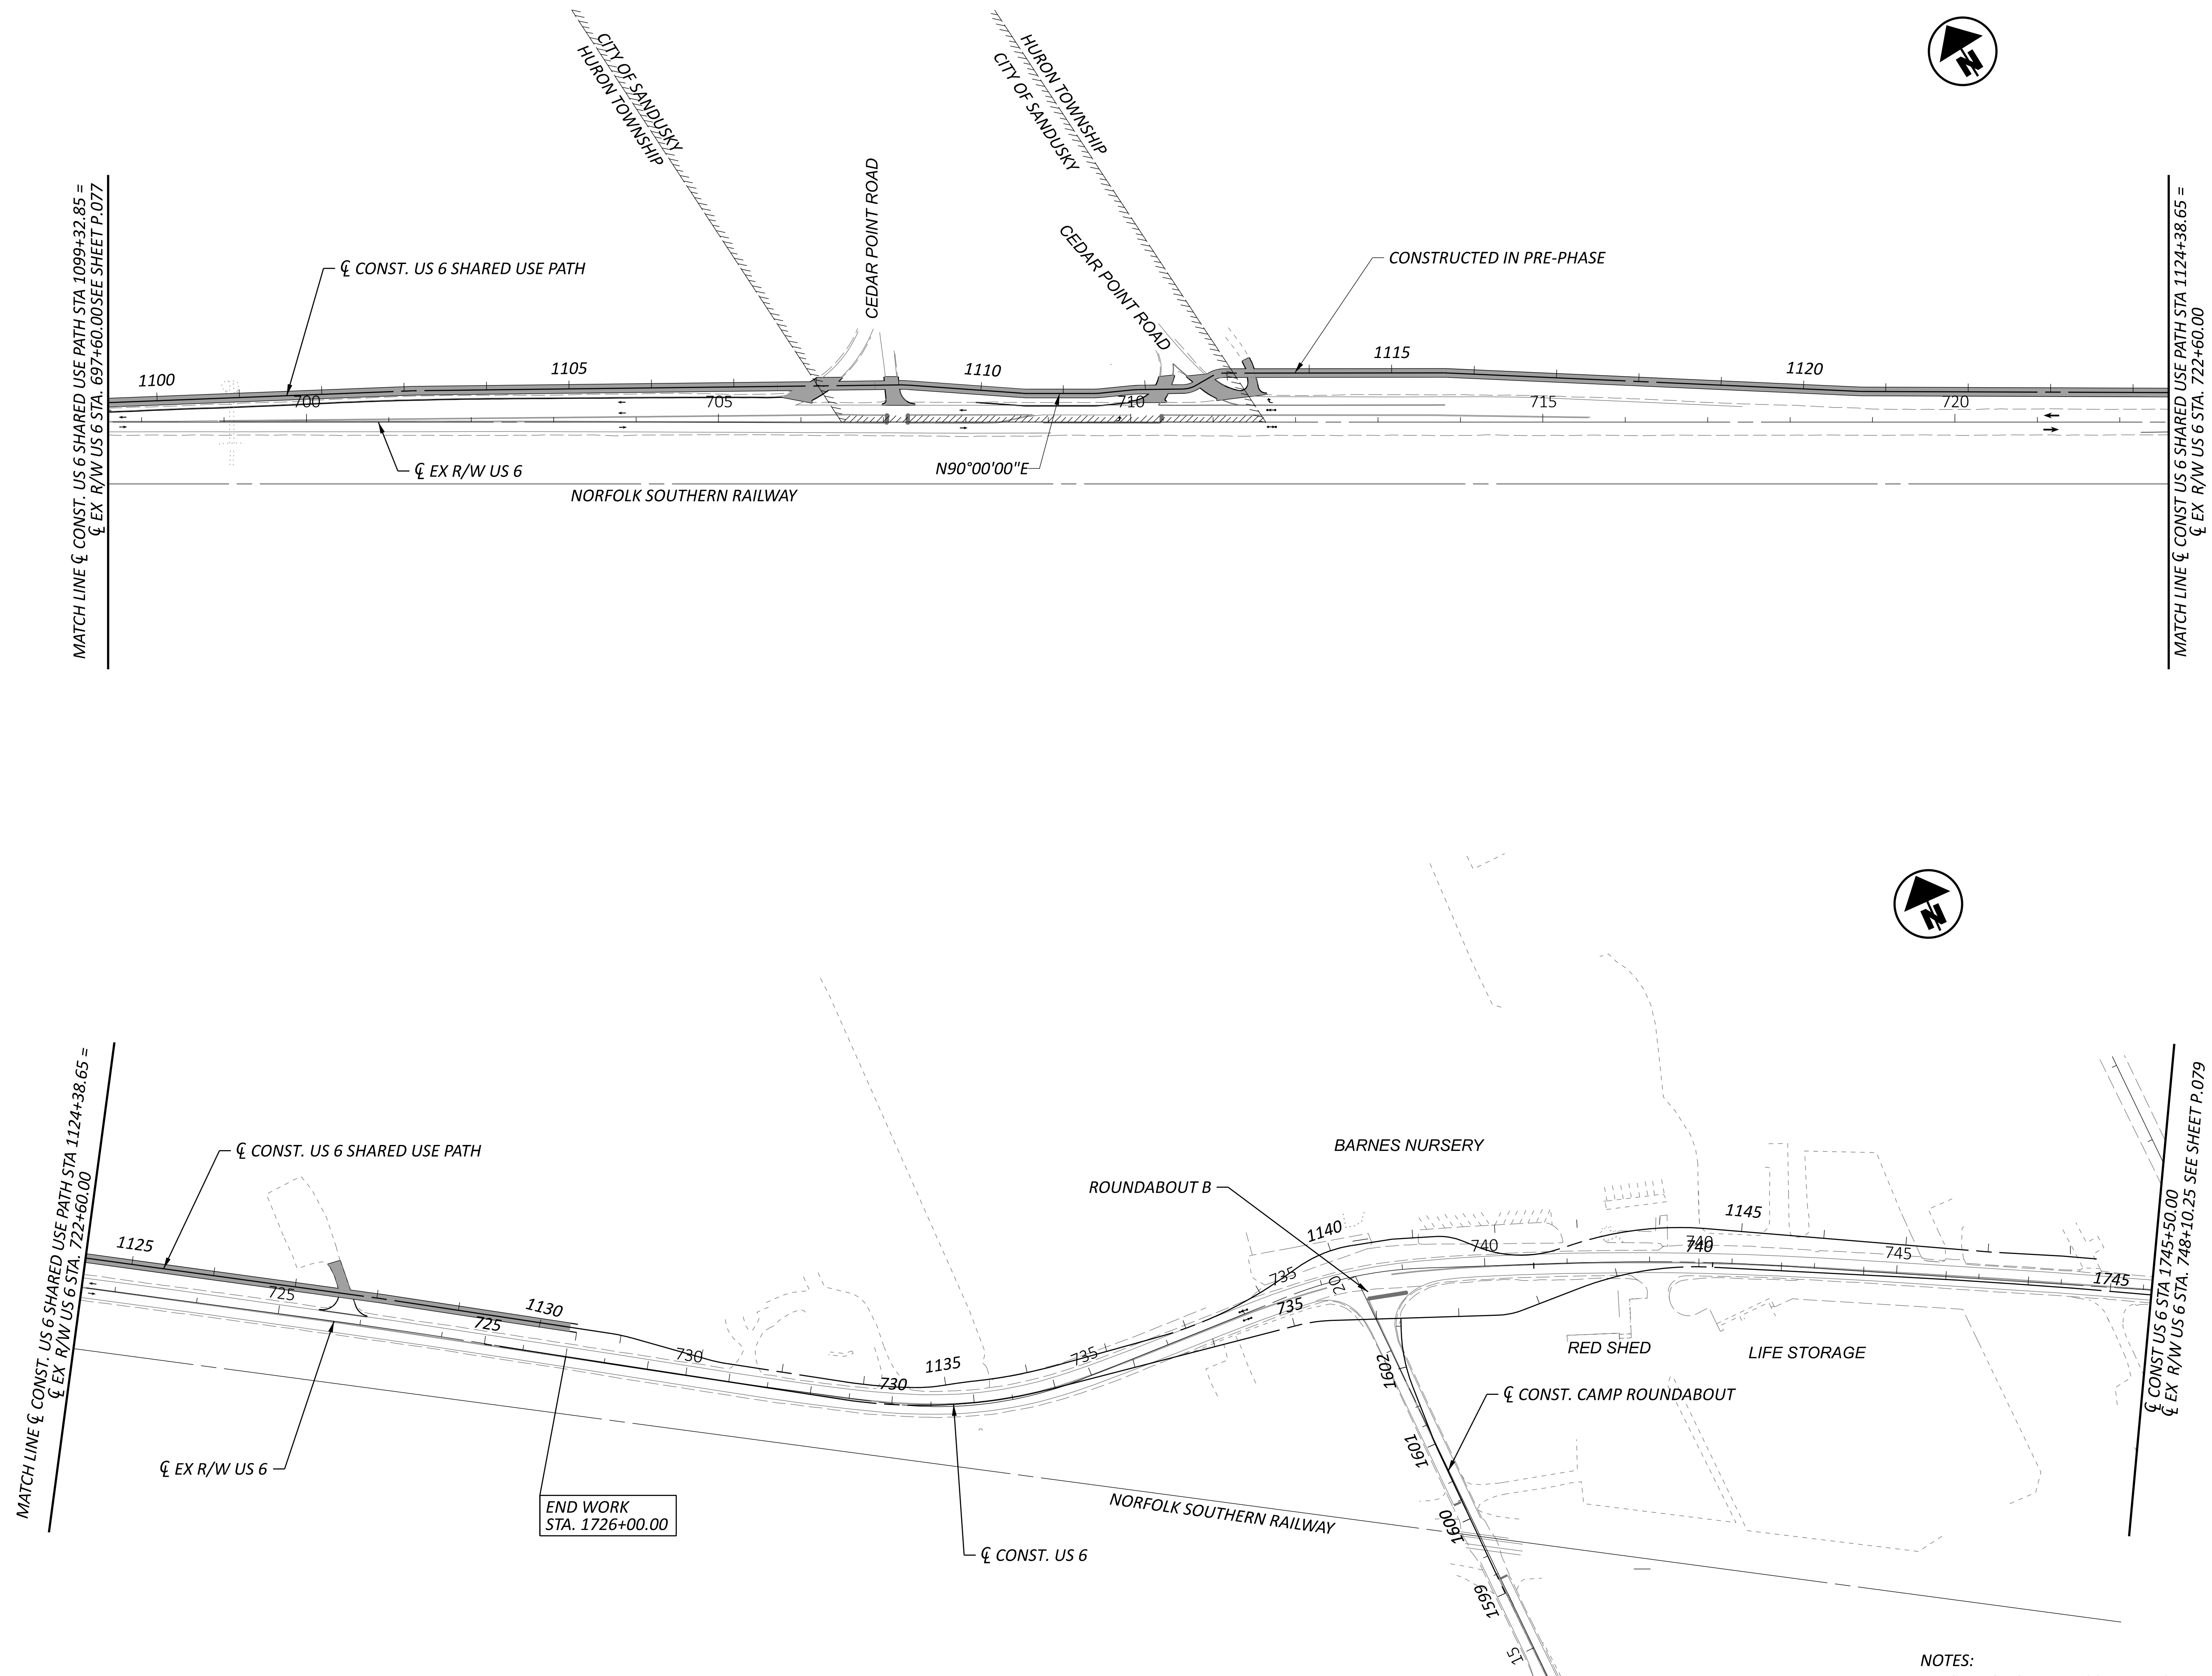

NOTES:

1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
2. FOR LEGEND, SEE SHEET P.076

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.080	782

MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)
US 6 STA 695+00 TO STA 745+50


HORIZONTAL
SCALE IN FEET



0 50 100 200

ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: 100 Scale: 1 PAPER: 34x22 (in.) DATE: 6/16/2025 TIME: 5:19:47 PM USER: ssadusei
pw:\ohiodot-pw\entley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\ERI\116570\402-Engineering_TransSystems\MOT\Sheets\116570_M18003_CY2026.dgn

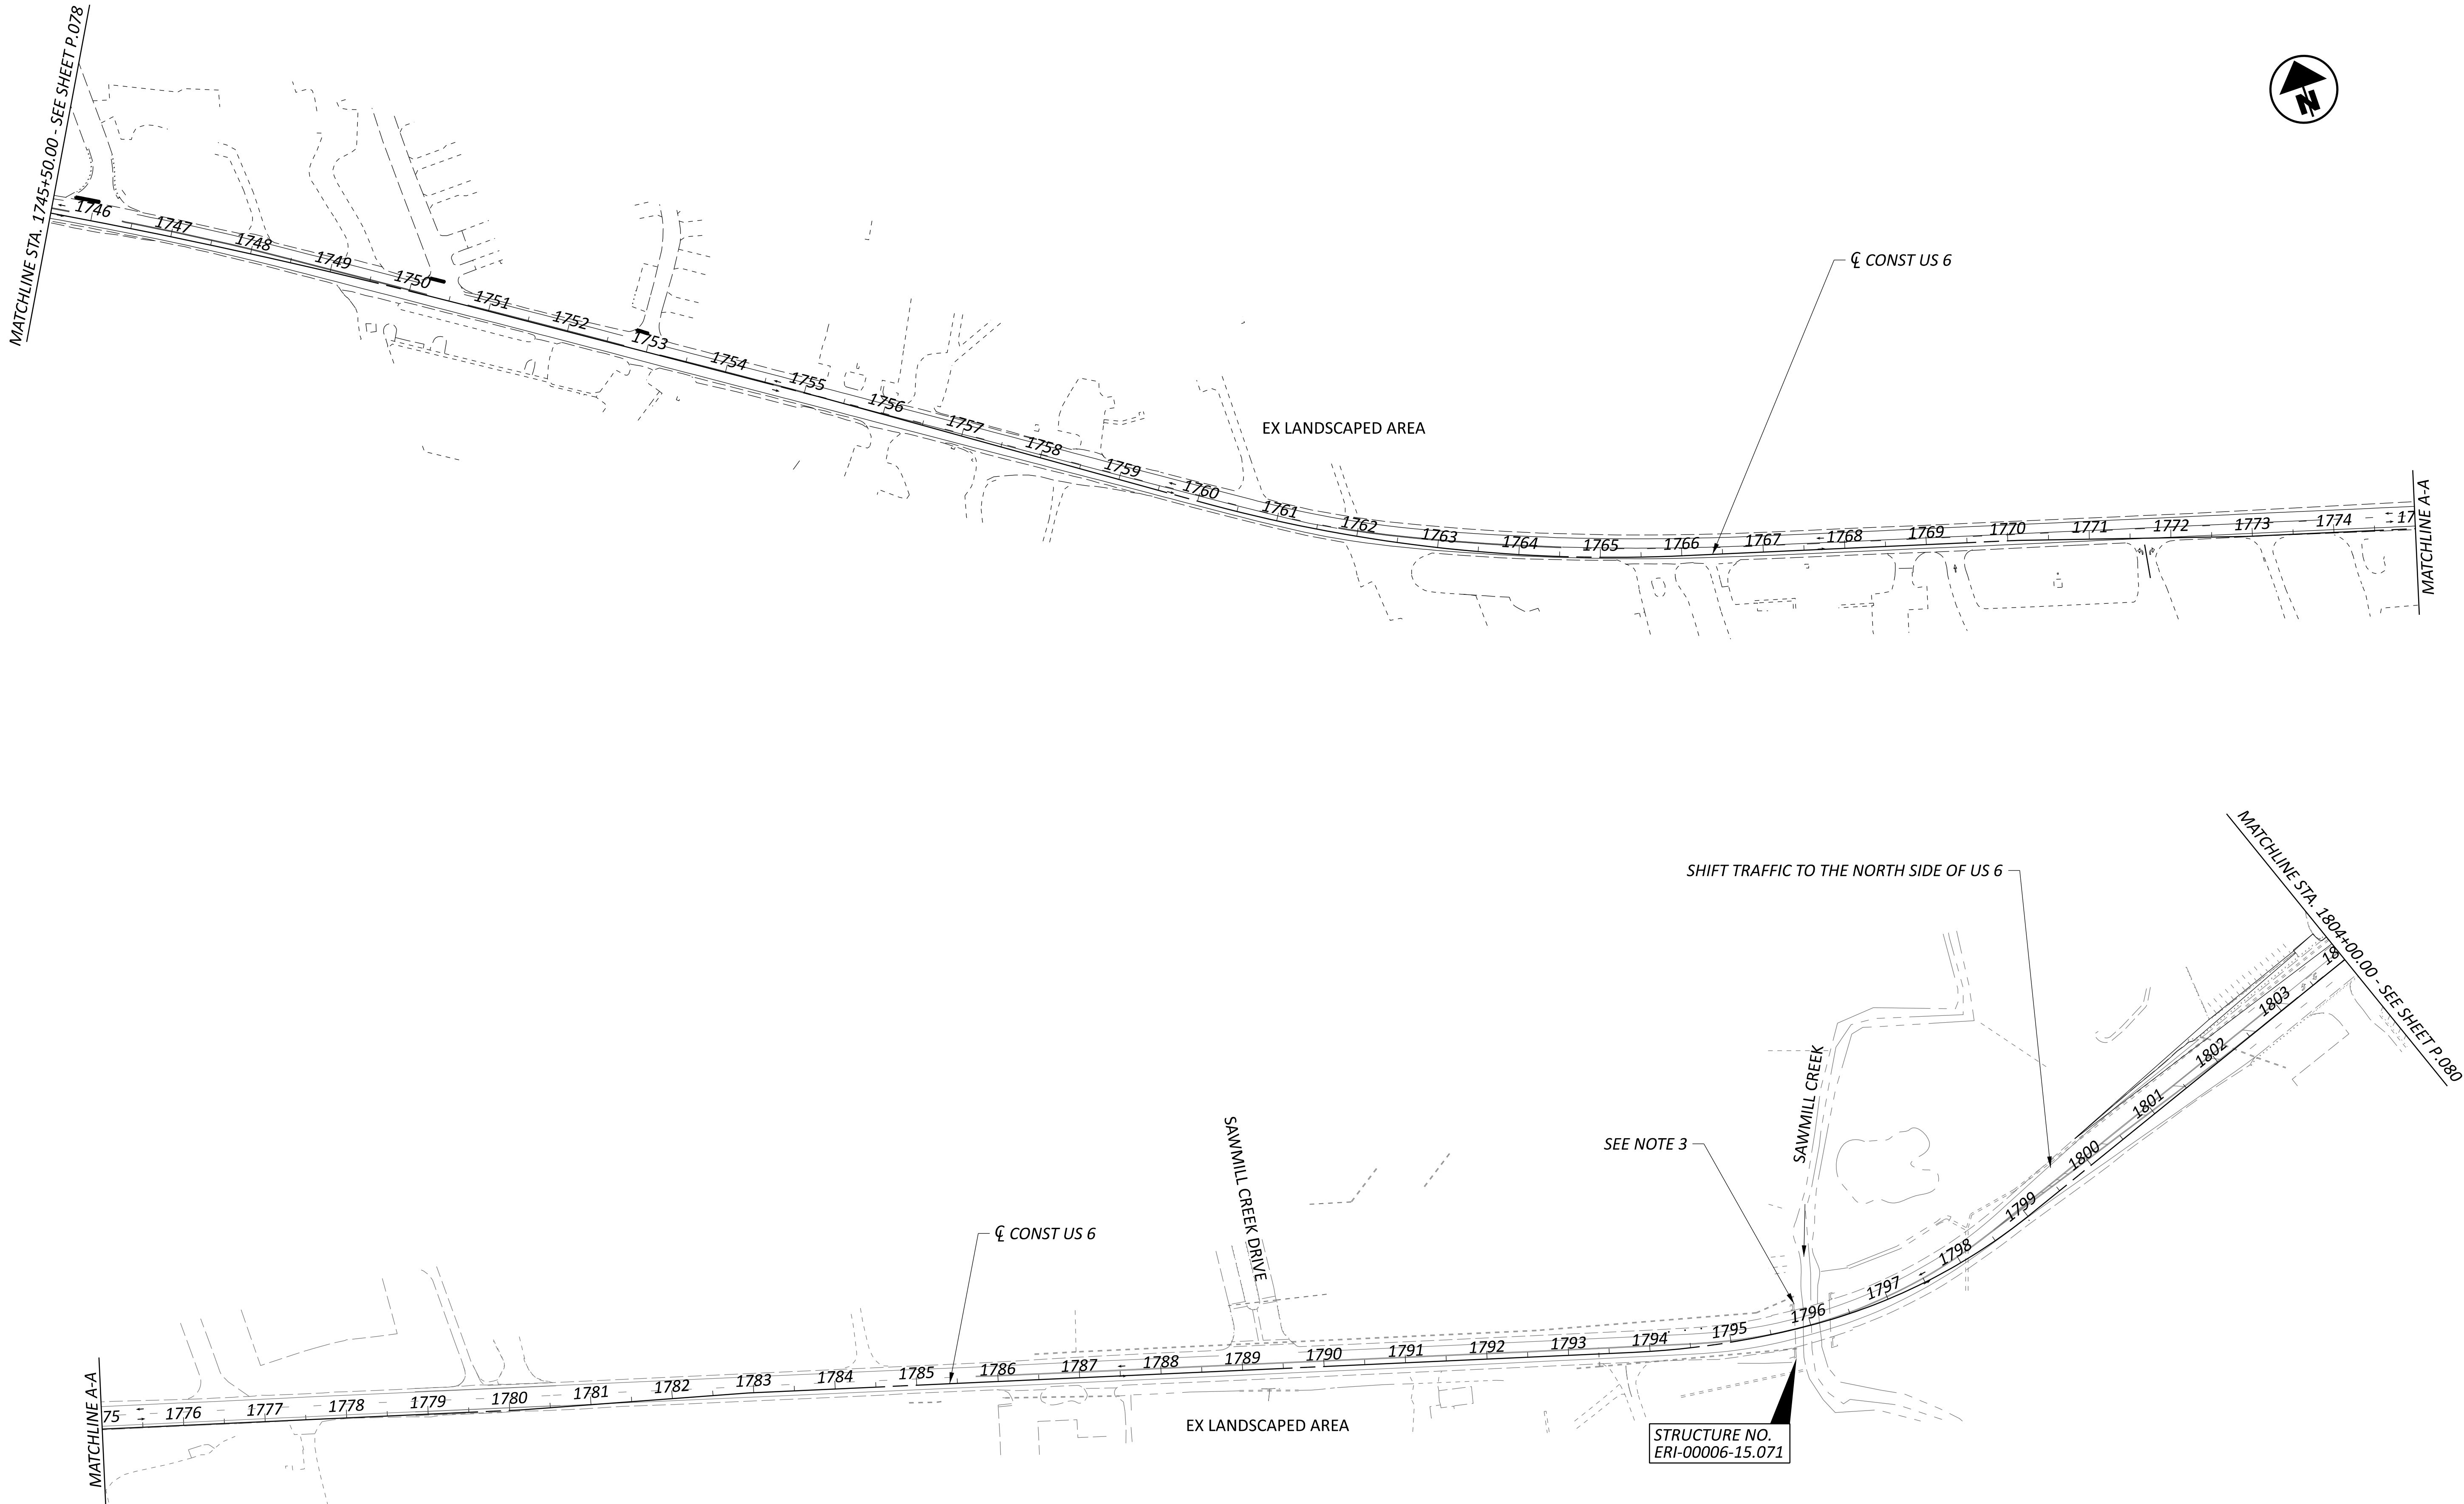

MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)
WIDENING SECTION STA 745+50.00 TO STA 804+00.00

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.081 782

- NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068
3. RELOCATION OF EXISTING UTILITIES IN BETWEEN THE DISTRICT ROW.

RYE BEACH INTERCHANGE:
DURATION: 180 DAYS
CEDAR POINT: NO EAST SIDE ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER

PERFORM THESE PHASES WITH CORRESPONDING PHASES AT THE RYE BEACH/US 6 INTERSECTION:

PHASE 1. SHIFT ONE LANE OF TRAFFIC EACH DIRECTION TO THE EAST SIDE OF RYE BEACH RD AND CONSTRUCT THE WEST SIDE. CLOSE AND DETOUR THE RAMPS ON THE WEST SIDE OF THE INTERCHANGE (THESE CLOSURES CAN BE DONE ANYTIME)

- WB ENTRANCE: SR 2 EB TO SR 13 NB TO SR 2 WB

- EB EXIT: SR 2 EB TO SR 13 NB TO SR 2 WB TO RYE BEACH RD

RYE BEACH ROUNDABOUTS:
DURATION: 180 DAYS
CEDAR POINT: NO ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER

PRE-PHASE:

CONSTRUCT EMBANKMENT AND GRADING WITH MINIMAL IMPACTS TO EXISTING TRAFFIC

PHASE 1. CLOSE THE CLEVELAND RD AND RYE BEACH NORTH LEG OF THE INTERSECTION EXCEPT TO LOCAL BUSINESSES/RESIDENCES

- CONSTRUCT TWO RETAINING WALL SECTIONS WITH THE FOLLOWING ALIGNMENT AND ELEVATION CHARACTERISTICS:

WALL SEGMENT A: BEGIN AT STATION 140+50 WITH A WALL HEIGHT OF 0 FEET, INCREASE TO A MAXIMUM HEIGHT OF 4.5 FEET, THEN TAPER BACK DOWN TO 0 FEET AT STATION 145+50.


WALL SEGMENT B: BEGIN AT STATION 150+60 WITH A WALL HEIGHT OF 0 FEET, INCREASE TO A MAXIMUM HEIGHT OF 5.5 FEET, THEN TAPER BACK DOWN TO 0 FEET AT STATION 160+00.

UPON COMPLETION OF EACH WALL SECTION, INSTALL PCB ON TOP, AS SHOWN IN THE PHASE 1 PLANS.
REFER TO THE PLAN AND PROFILE SHEETS FOR ELEVATION VARIATIONS AND ADDITIONAL GEOMETRIC DETAILS.

- CLEVELAND RD: CENTER STREET TO US 6 WB TO RYE BEACH RD NB. FOR DETOUR PLAN, SEE SHEET P.104

- RYE BEACH RD: SAND DR TO ATWOOD PL THEN FOLLOW CLEVELAND RD DETOUR. FOR DETOUR PLAN, SEE SHEET P.104

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

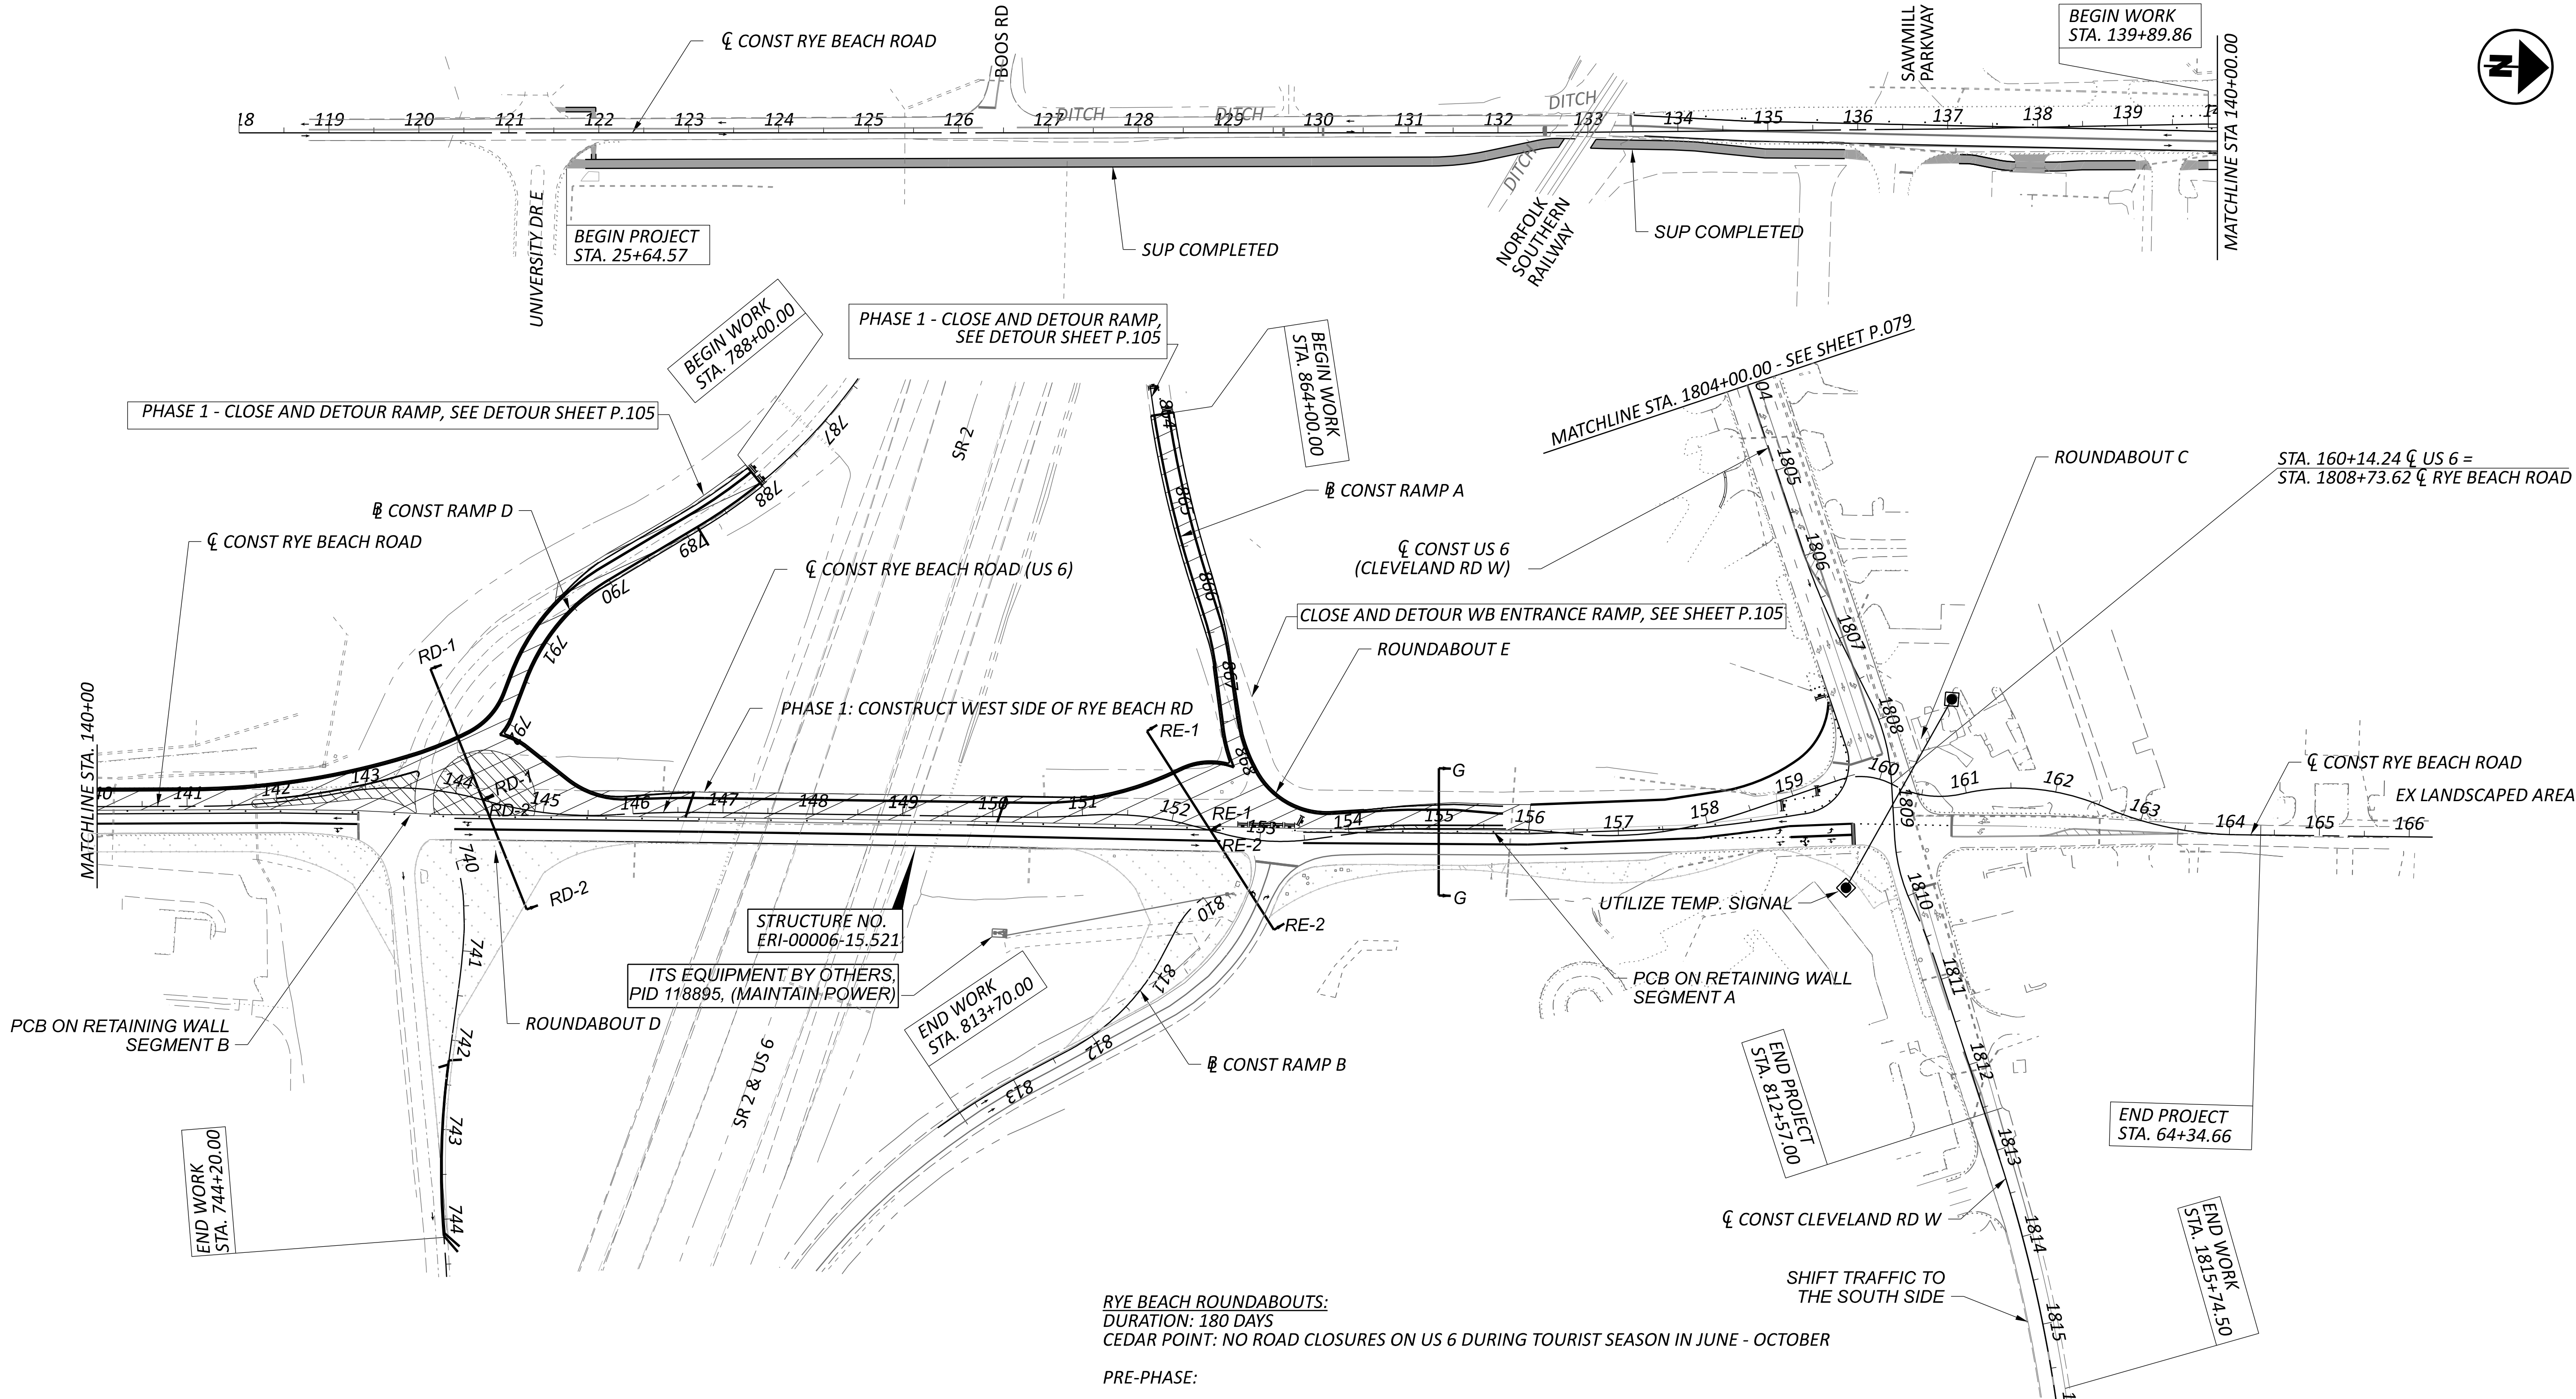

MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)
RYE BEACH ROAD STA 118+00.00 TO STA 166+00.00

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA



REVIEWER
SS 02/28/24

PROJECT ID
116570



SHEET TOTAL
P.082 782

HORIZONTAL
SCALE IN FEET
0 50 100 200

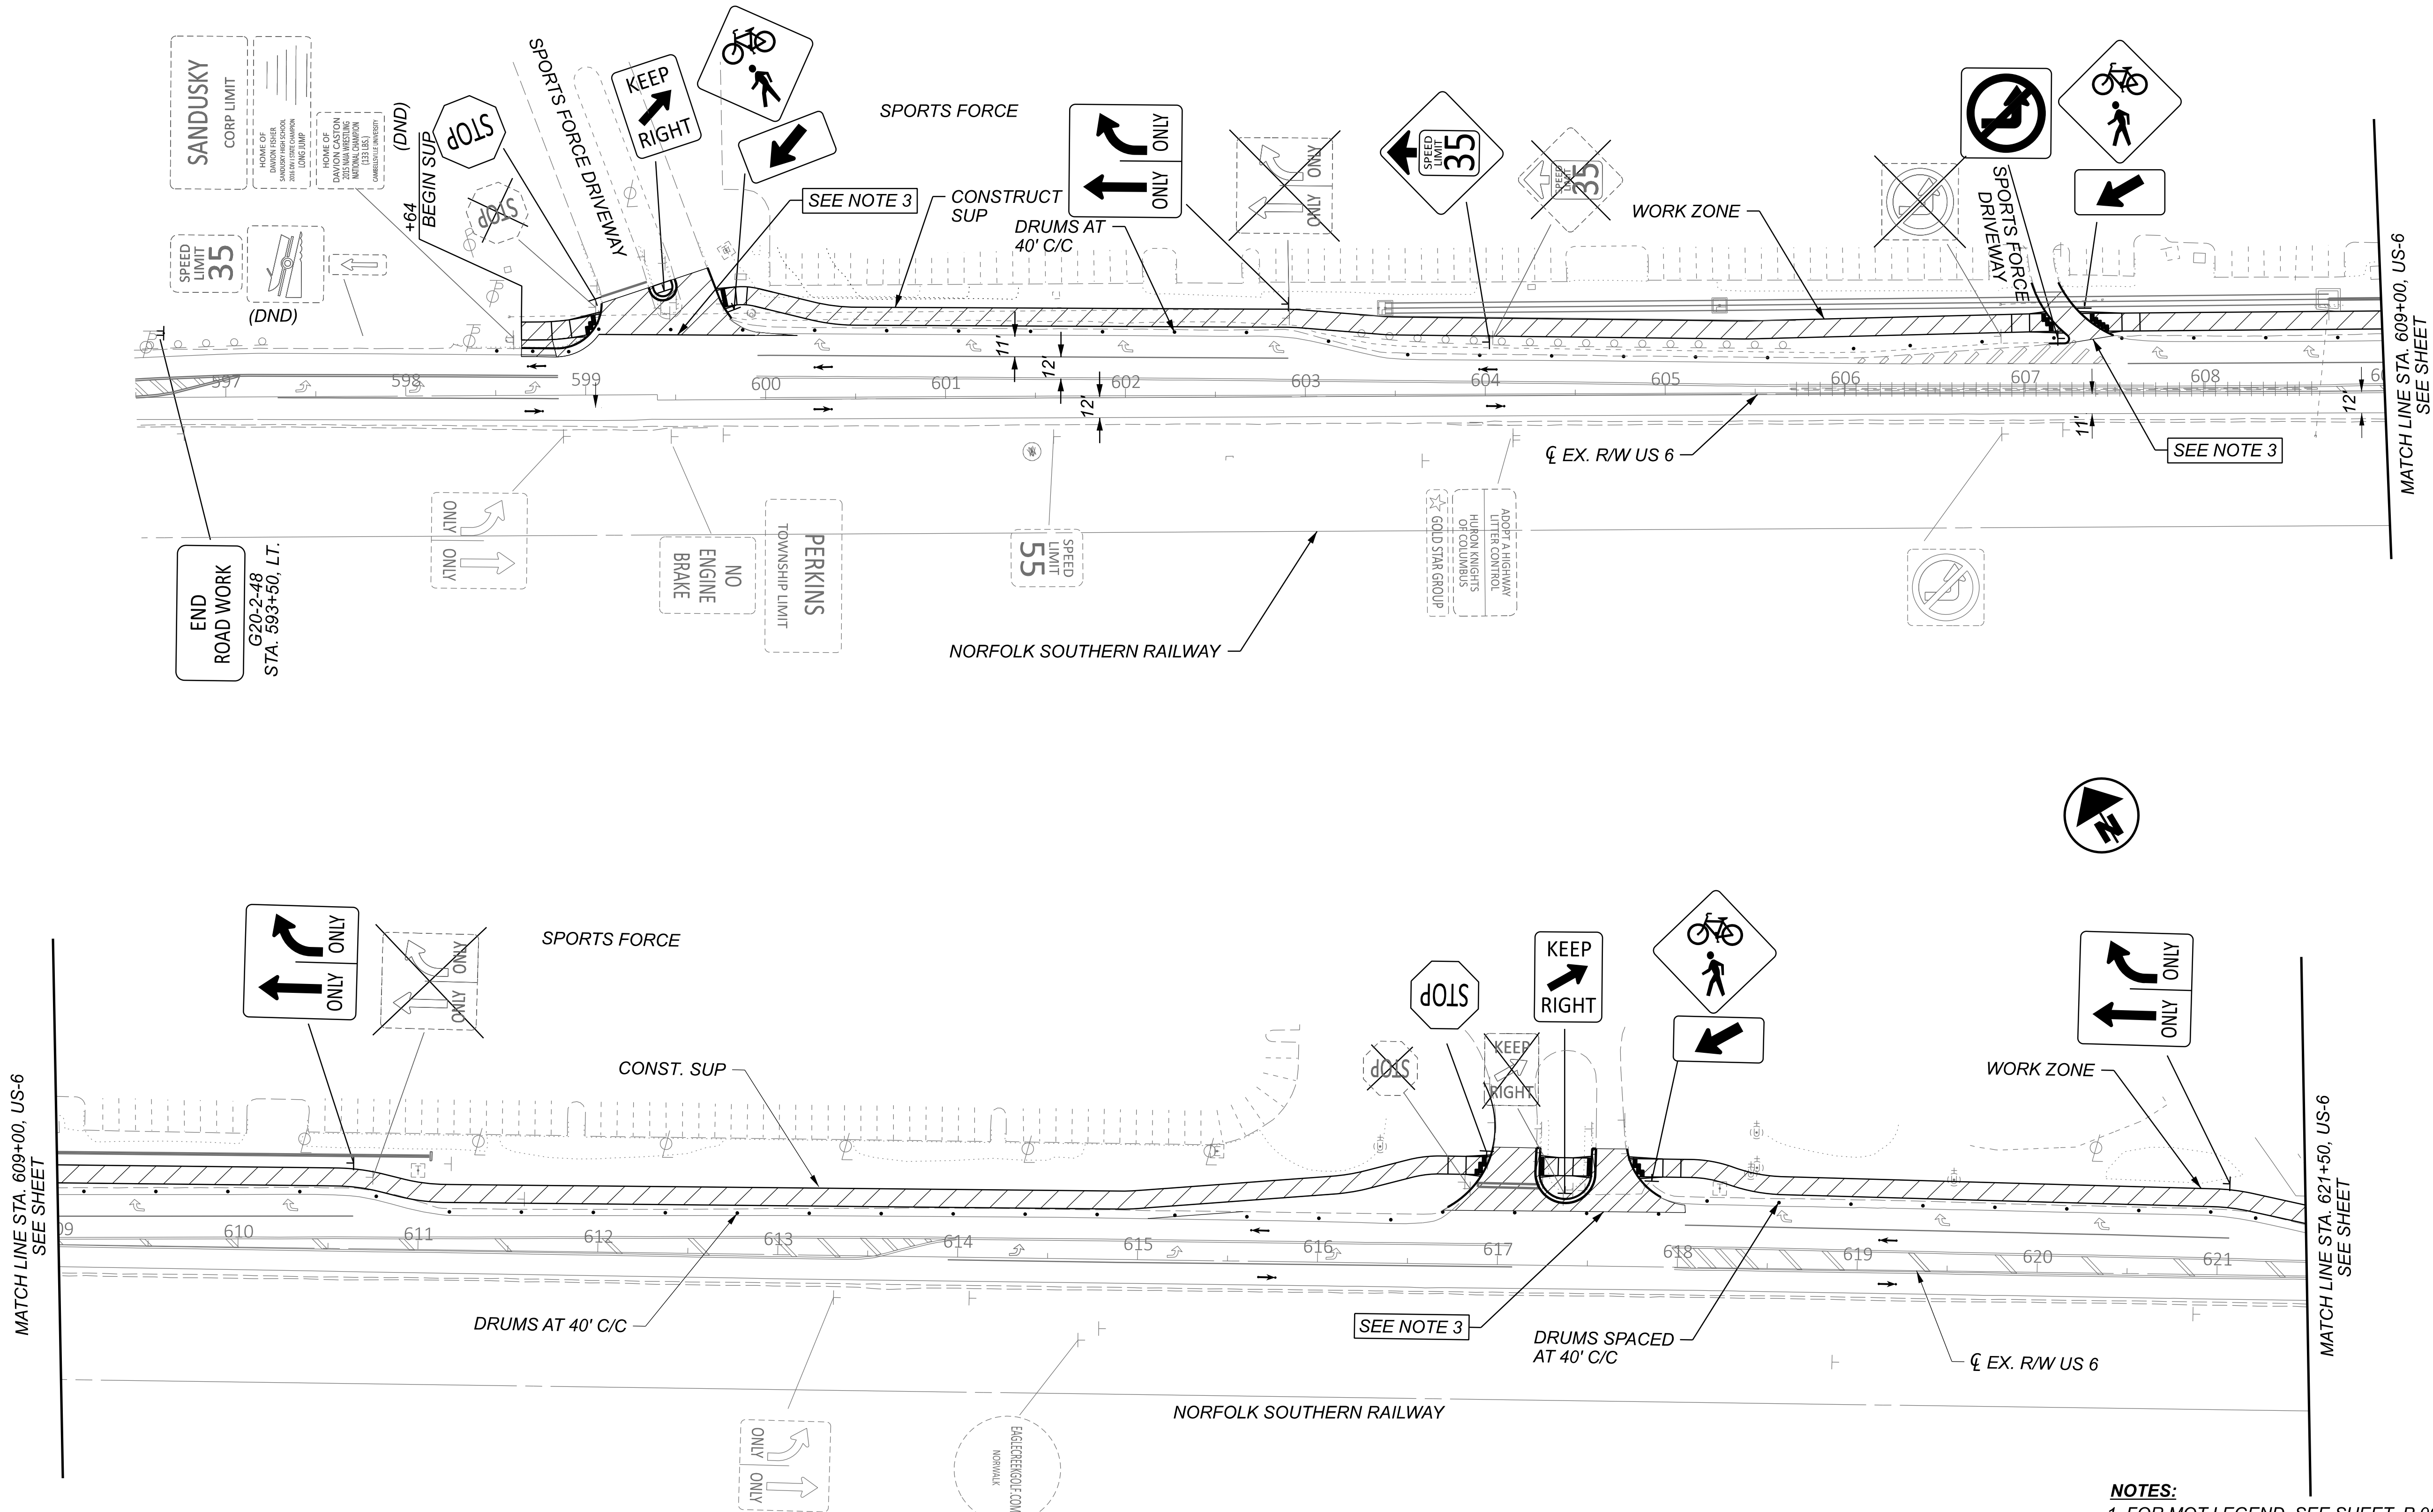

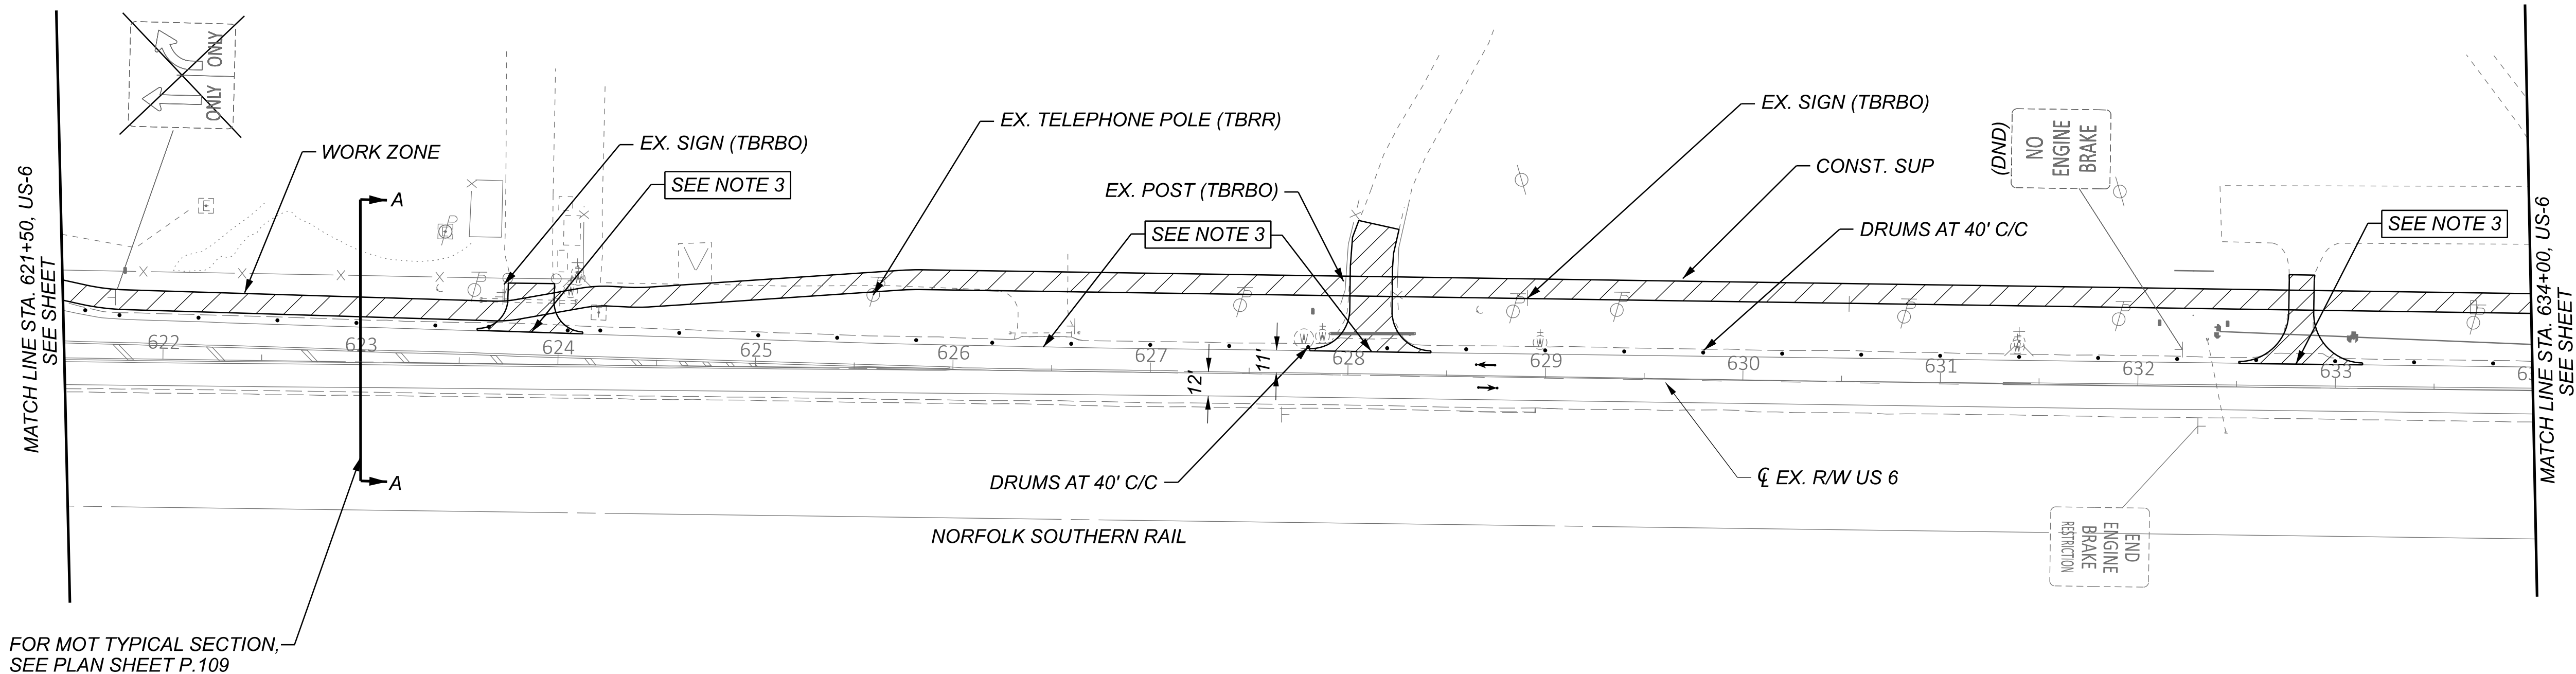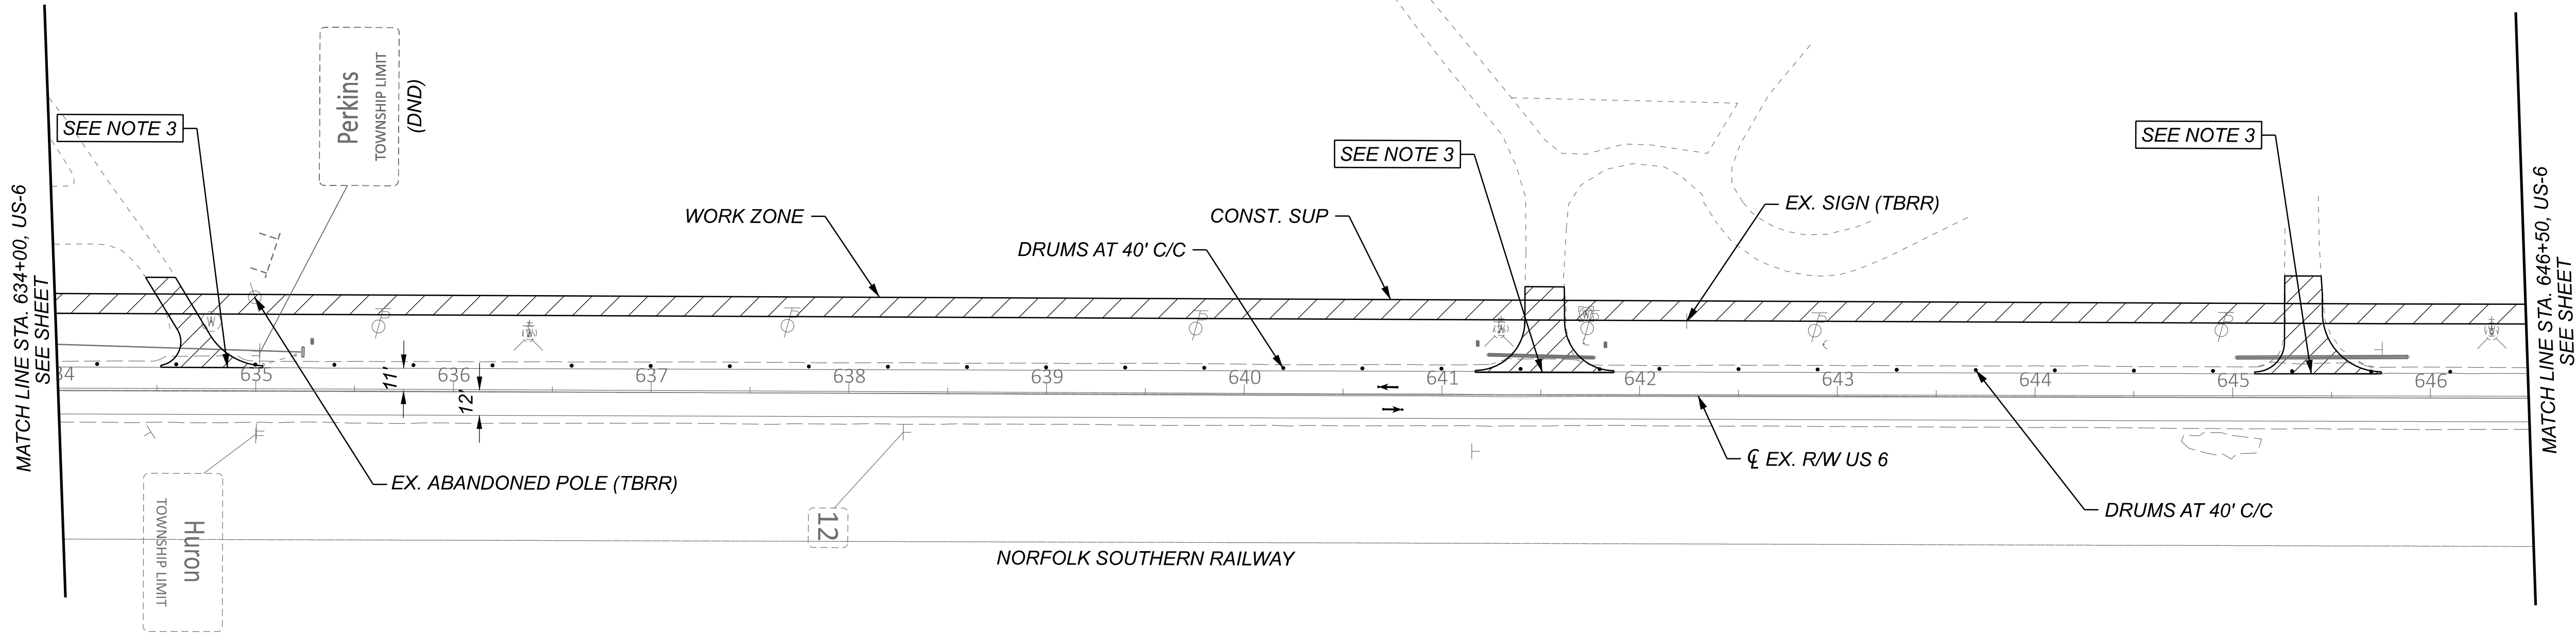


FOR MOT TYPICAL SECTION,
SEE PLAN SHEET P.109



- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSON WIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS
PROJECT ID	02/28/24
SHEET	116570
TOTAL	782

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 621+50.00 TO STA. 646+50.00



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP_1 - Plan 5-6 [Sheet] PAPER:SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:20:10 PM USER: ssadusei
 pw://ohiodot-pw.bentley.com/ohiodot-pw-02/Documents/01 Active Projects/District 03/Erle/116570/402-Engineering_TransSystems/MOT/Sheets/116570_MP000_CV2026.dgn

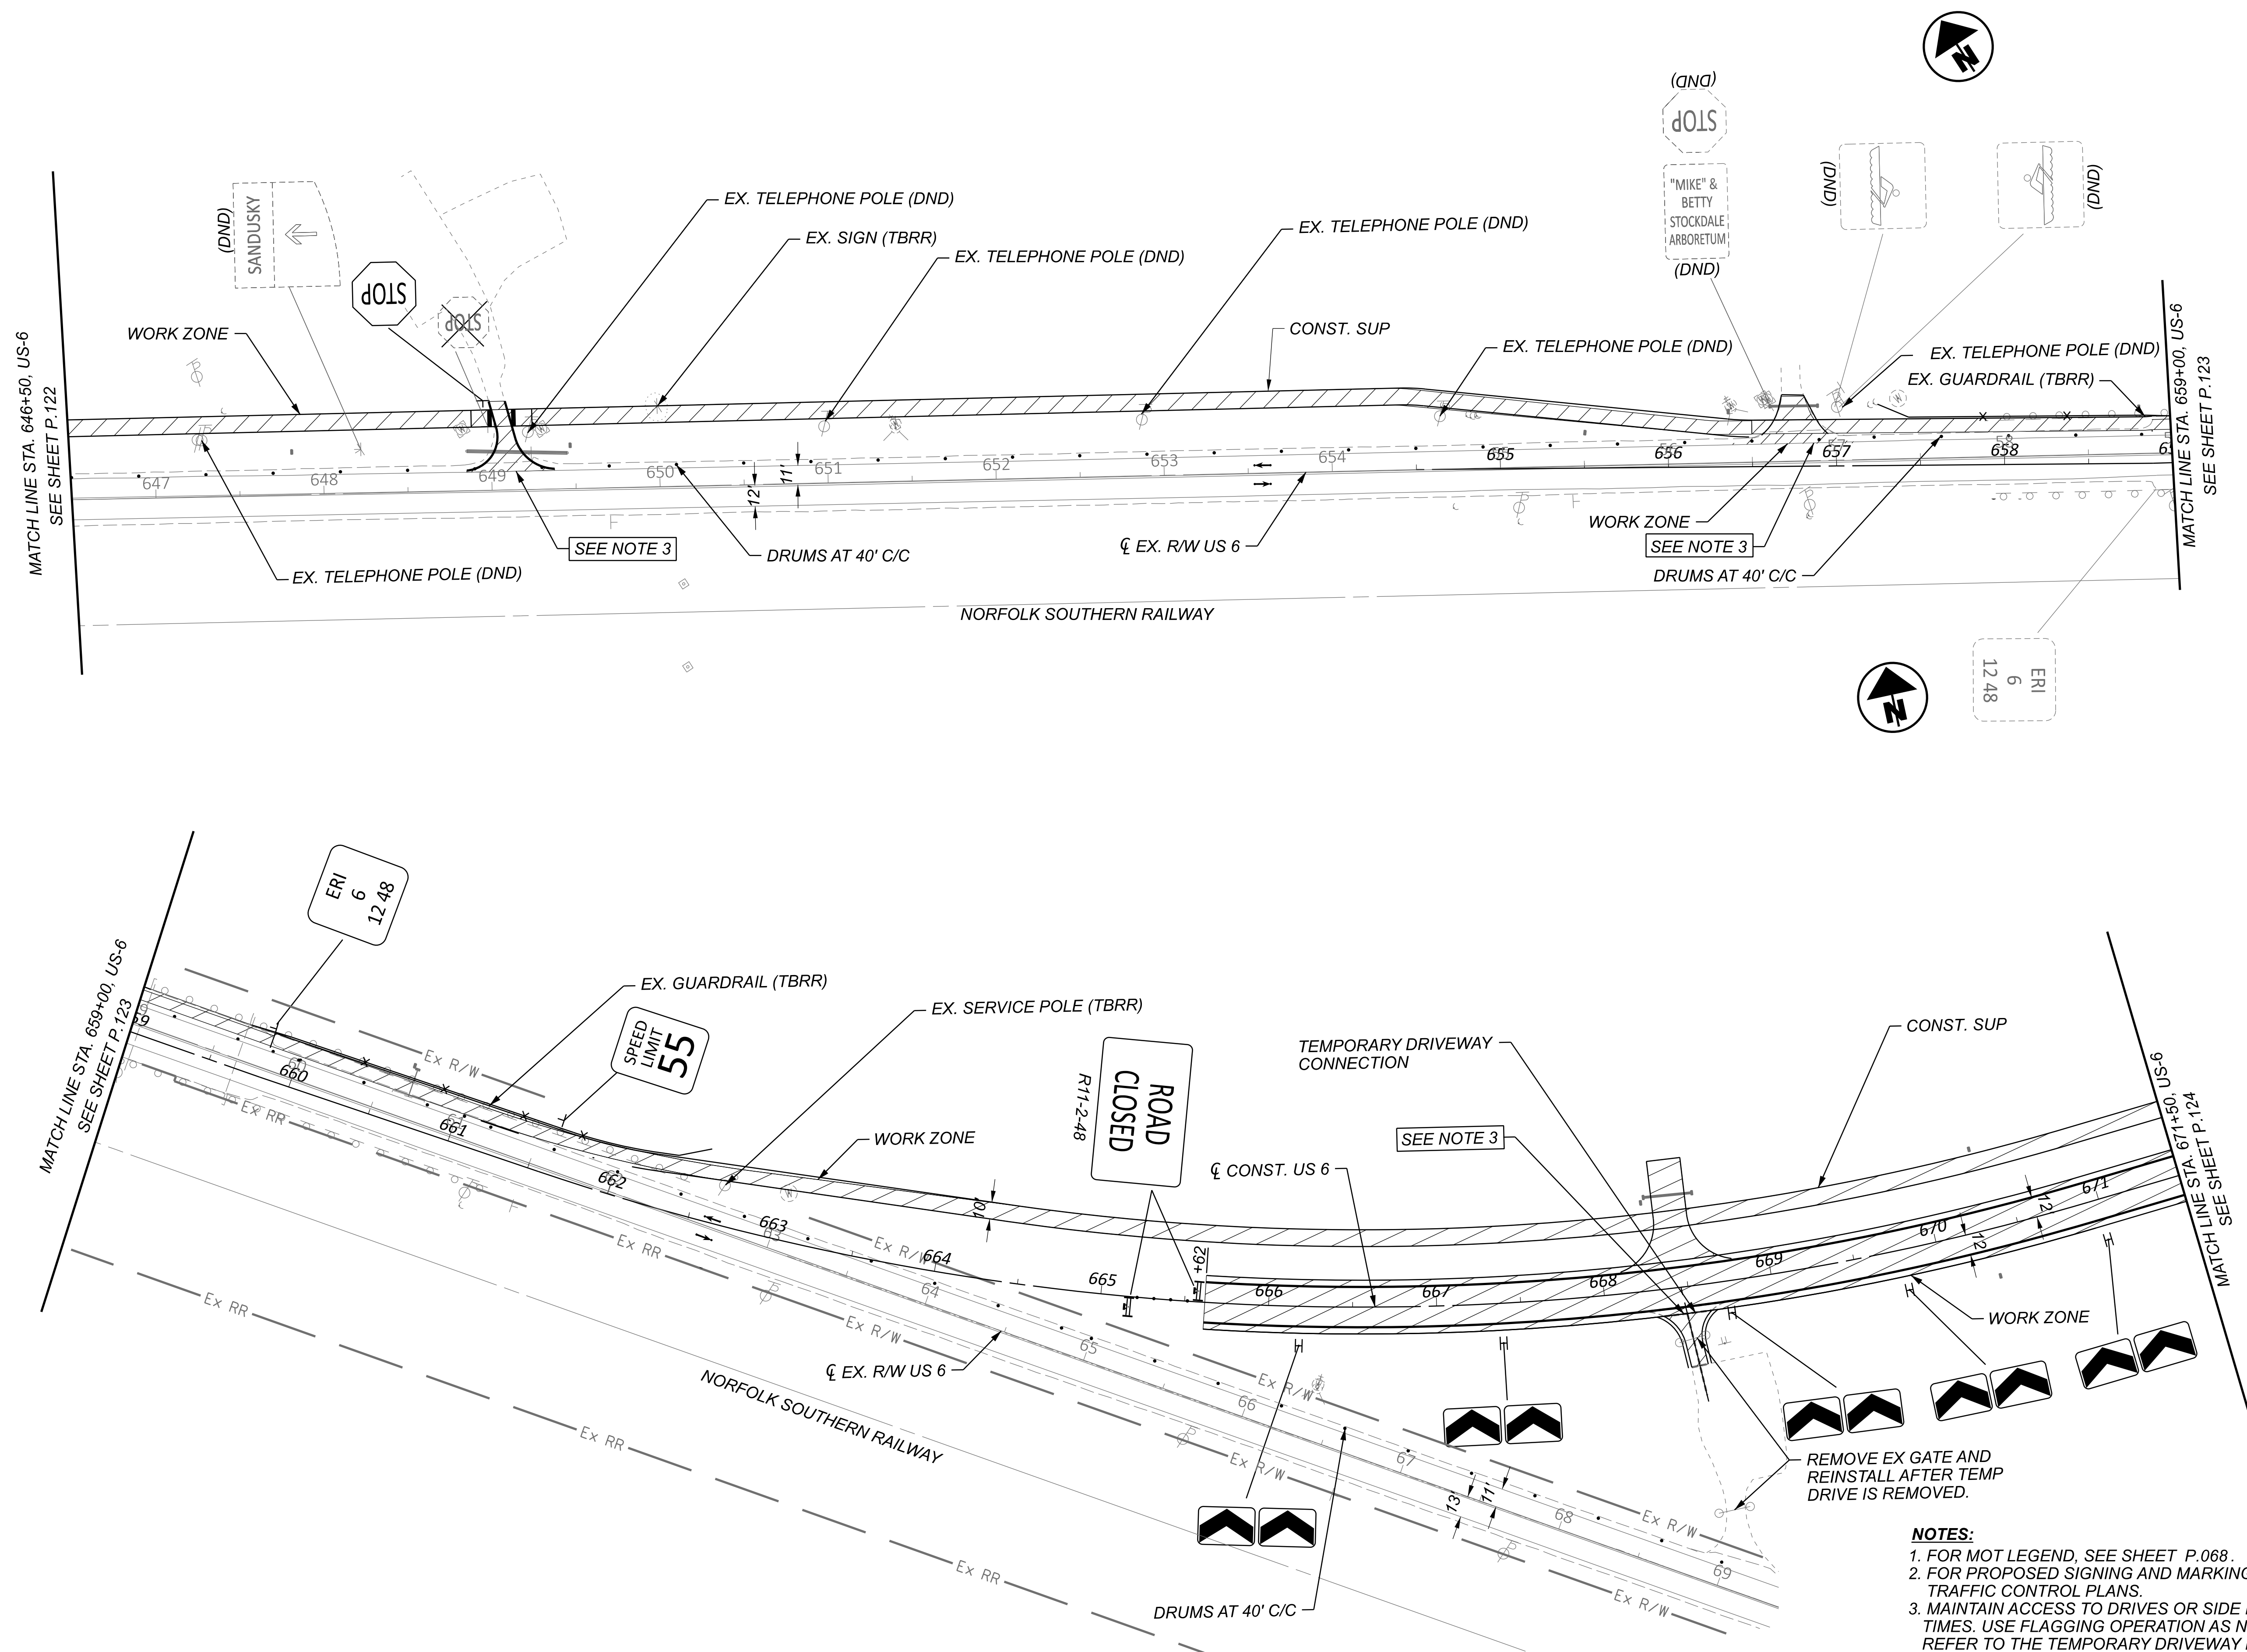

NOTES:


1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.


MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 646+50.00 TO STA. 671+50.00

DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.126	782




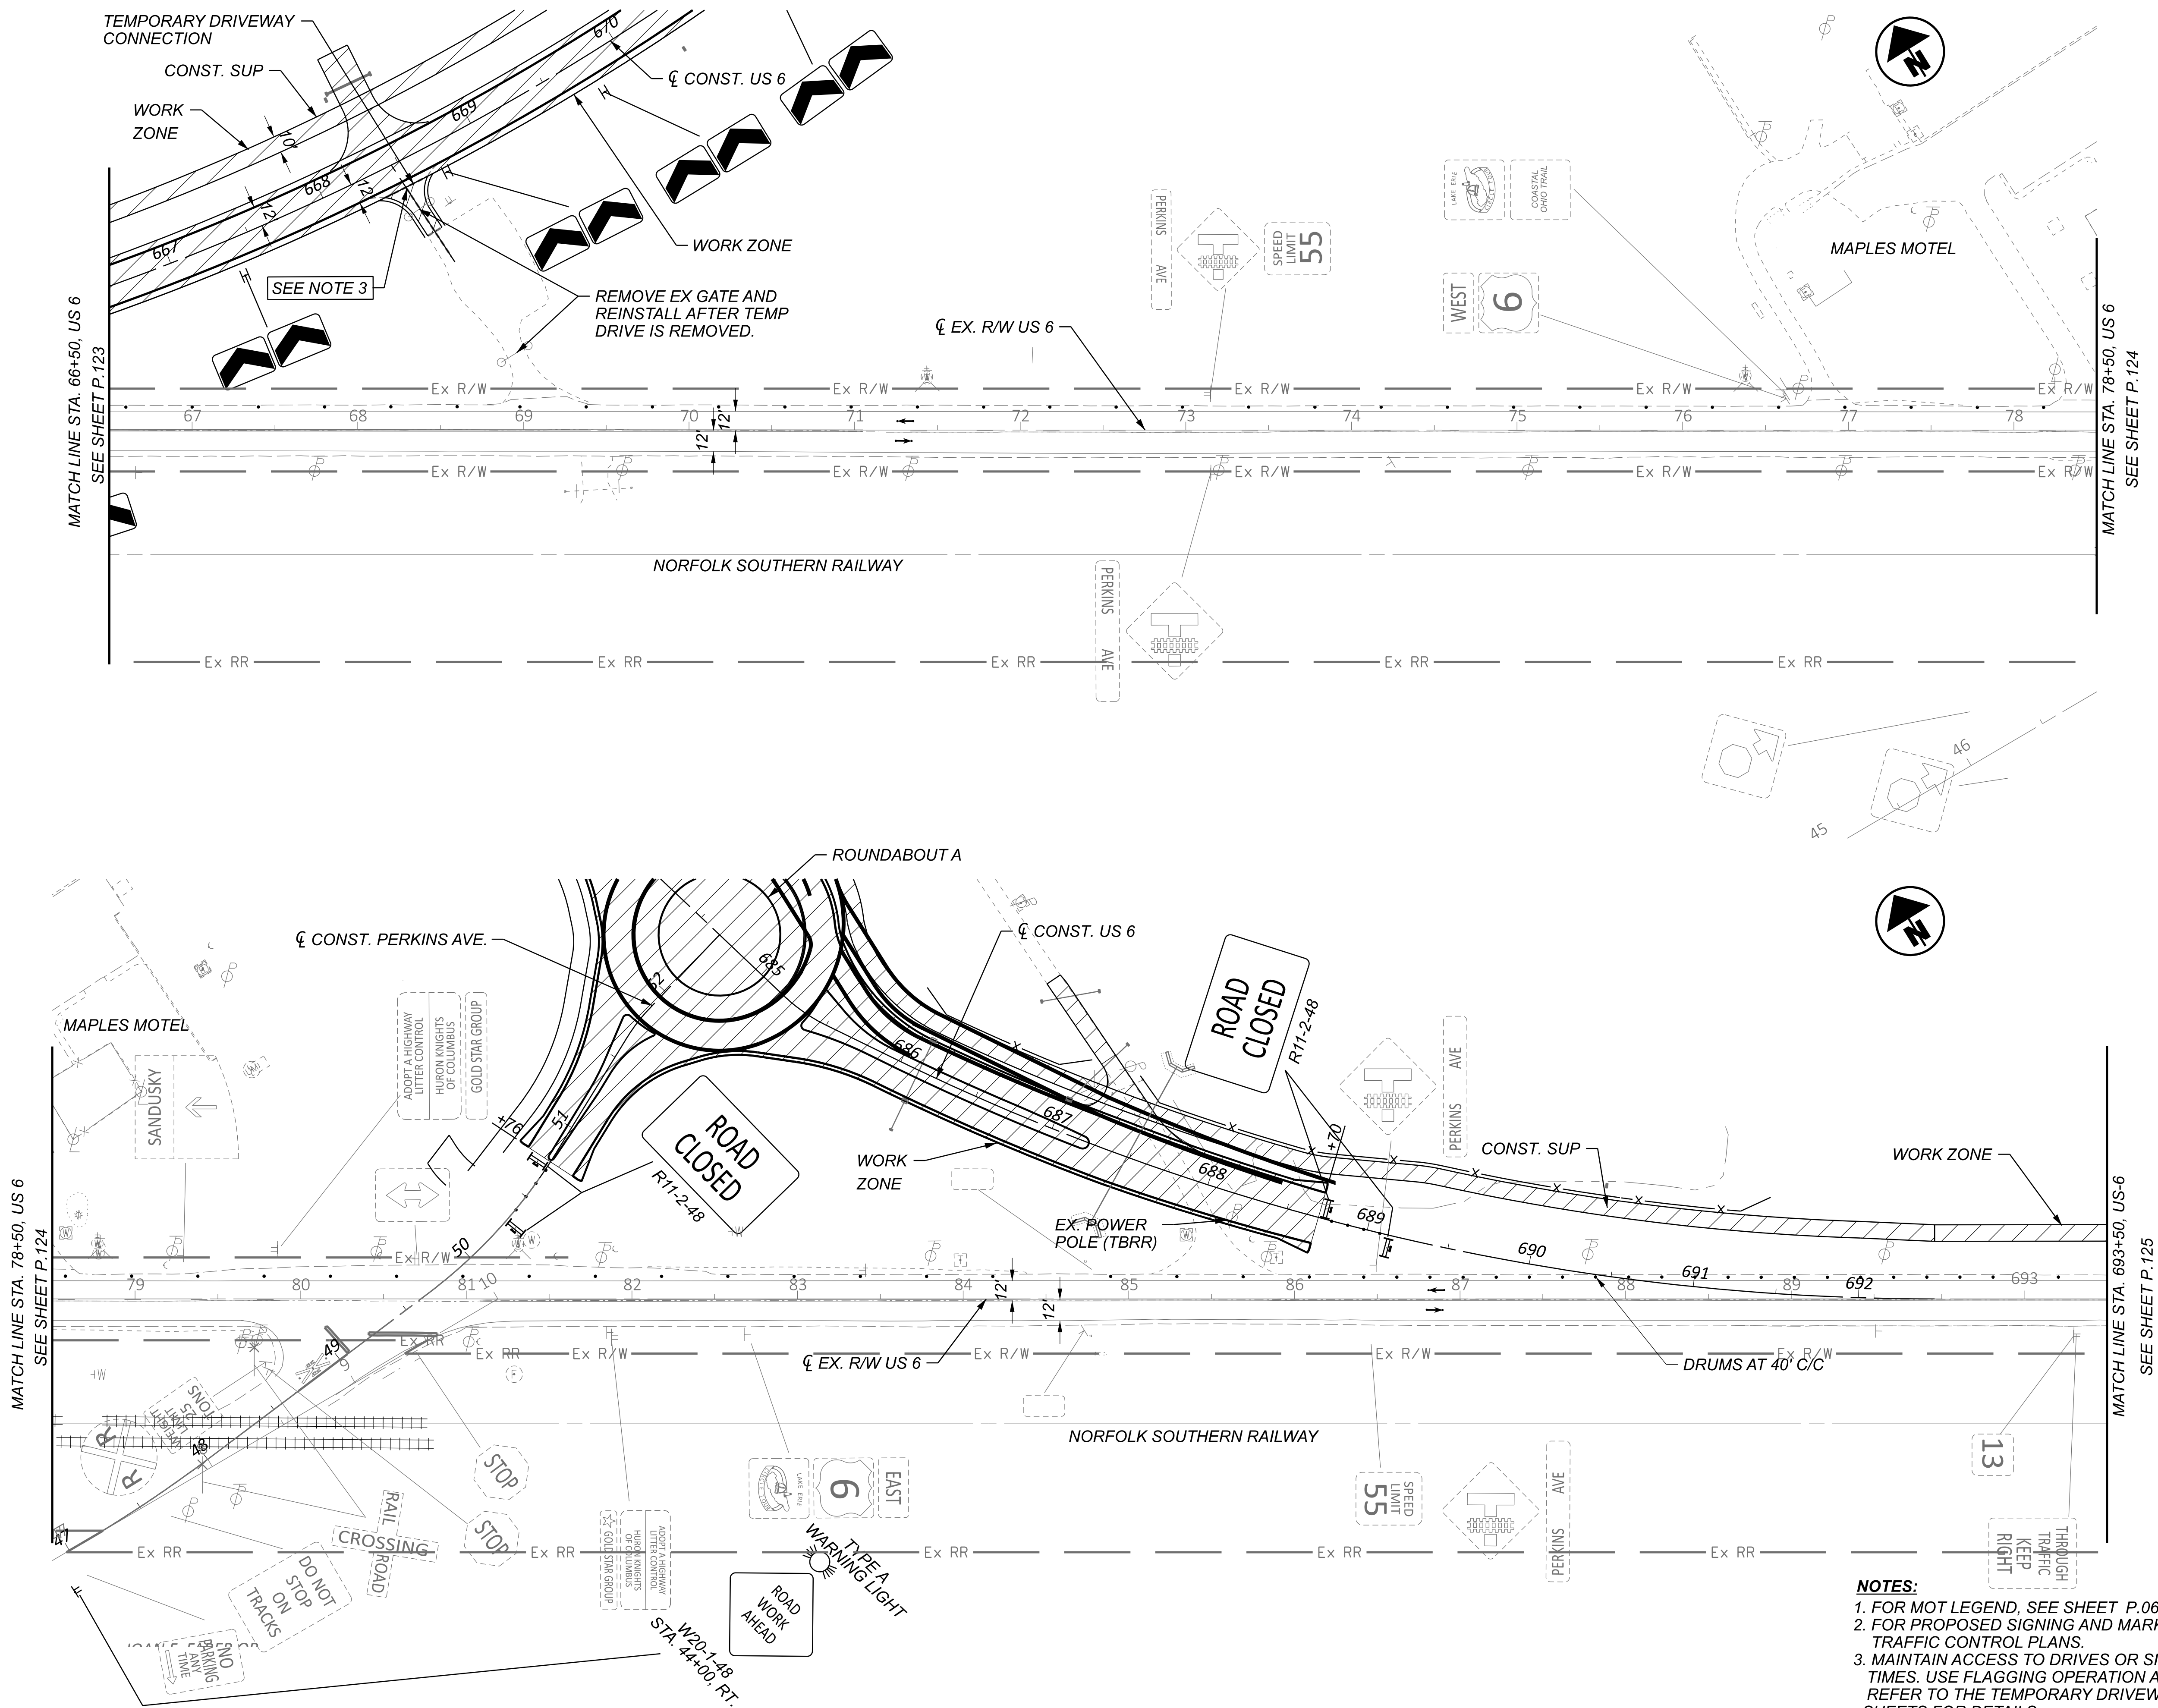


NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 67+00.00 EX. US 6 TO 693+50.00 CONST. US 6 SUP

DESIGN AGENCY	
TRANSYSTEMS	
400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.127	TOTAL 782



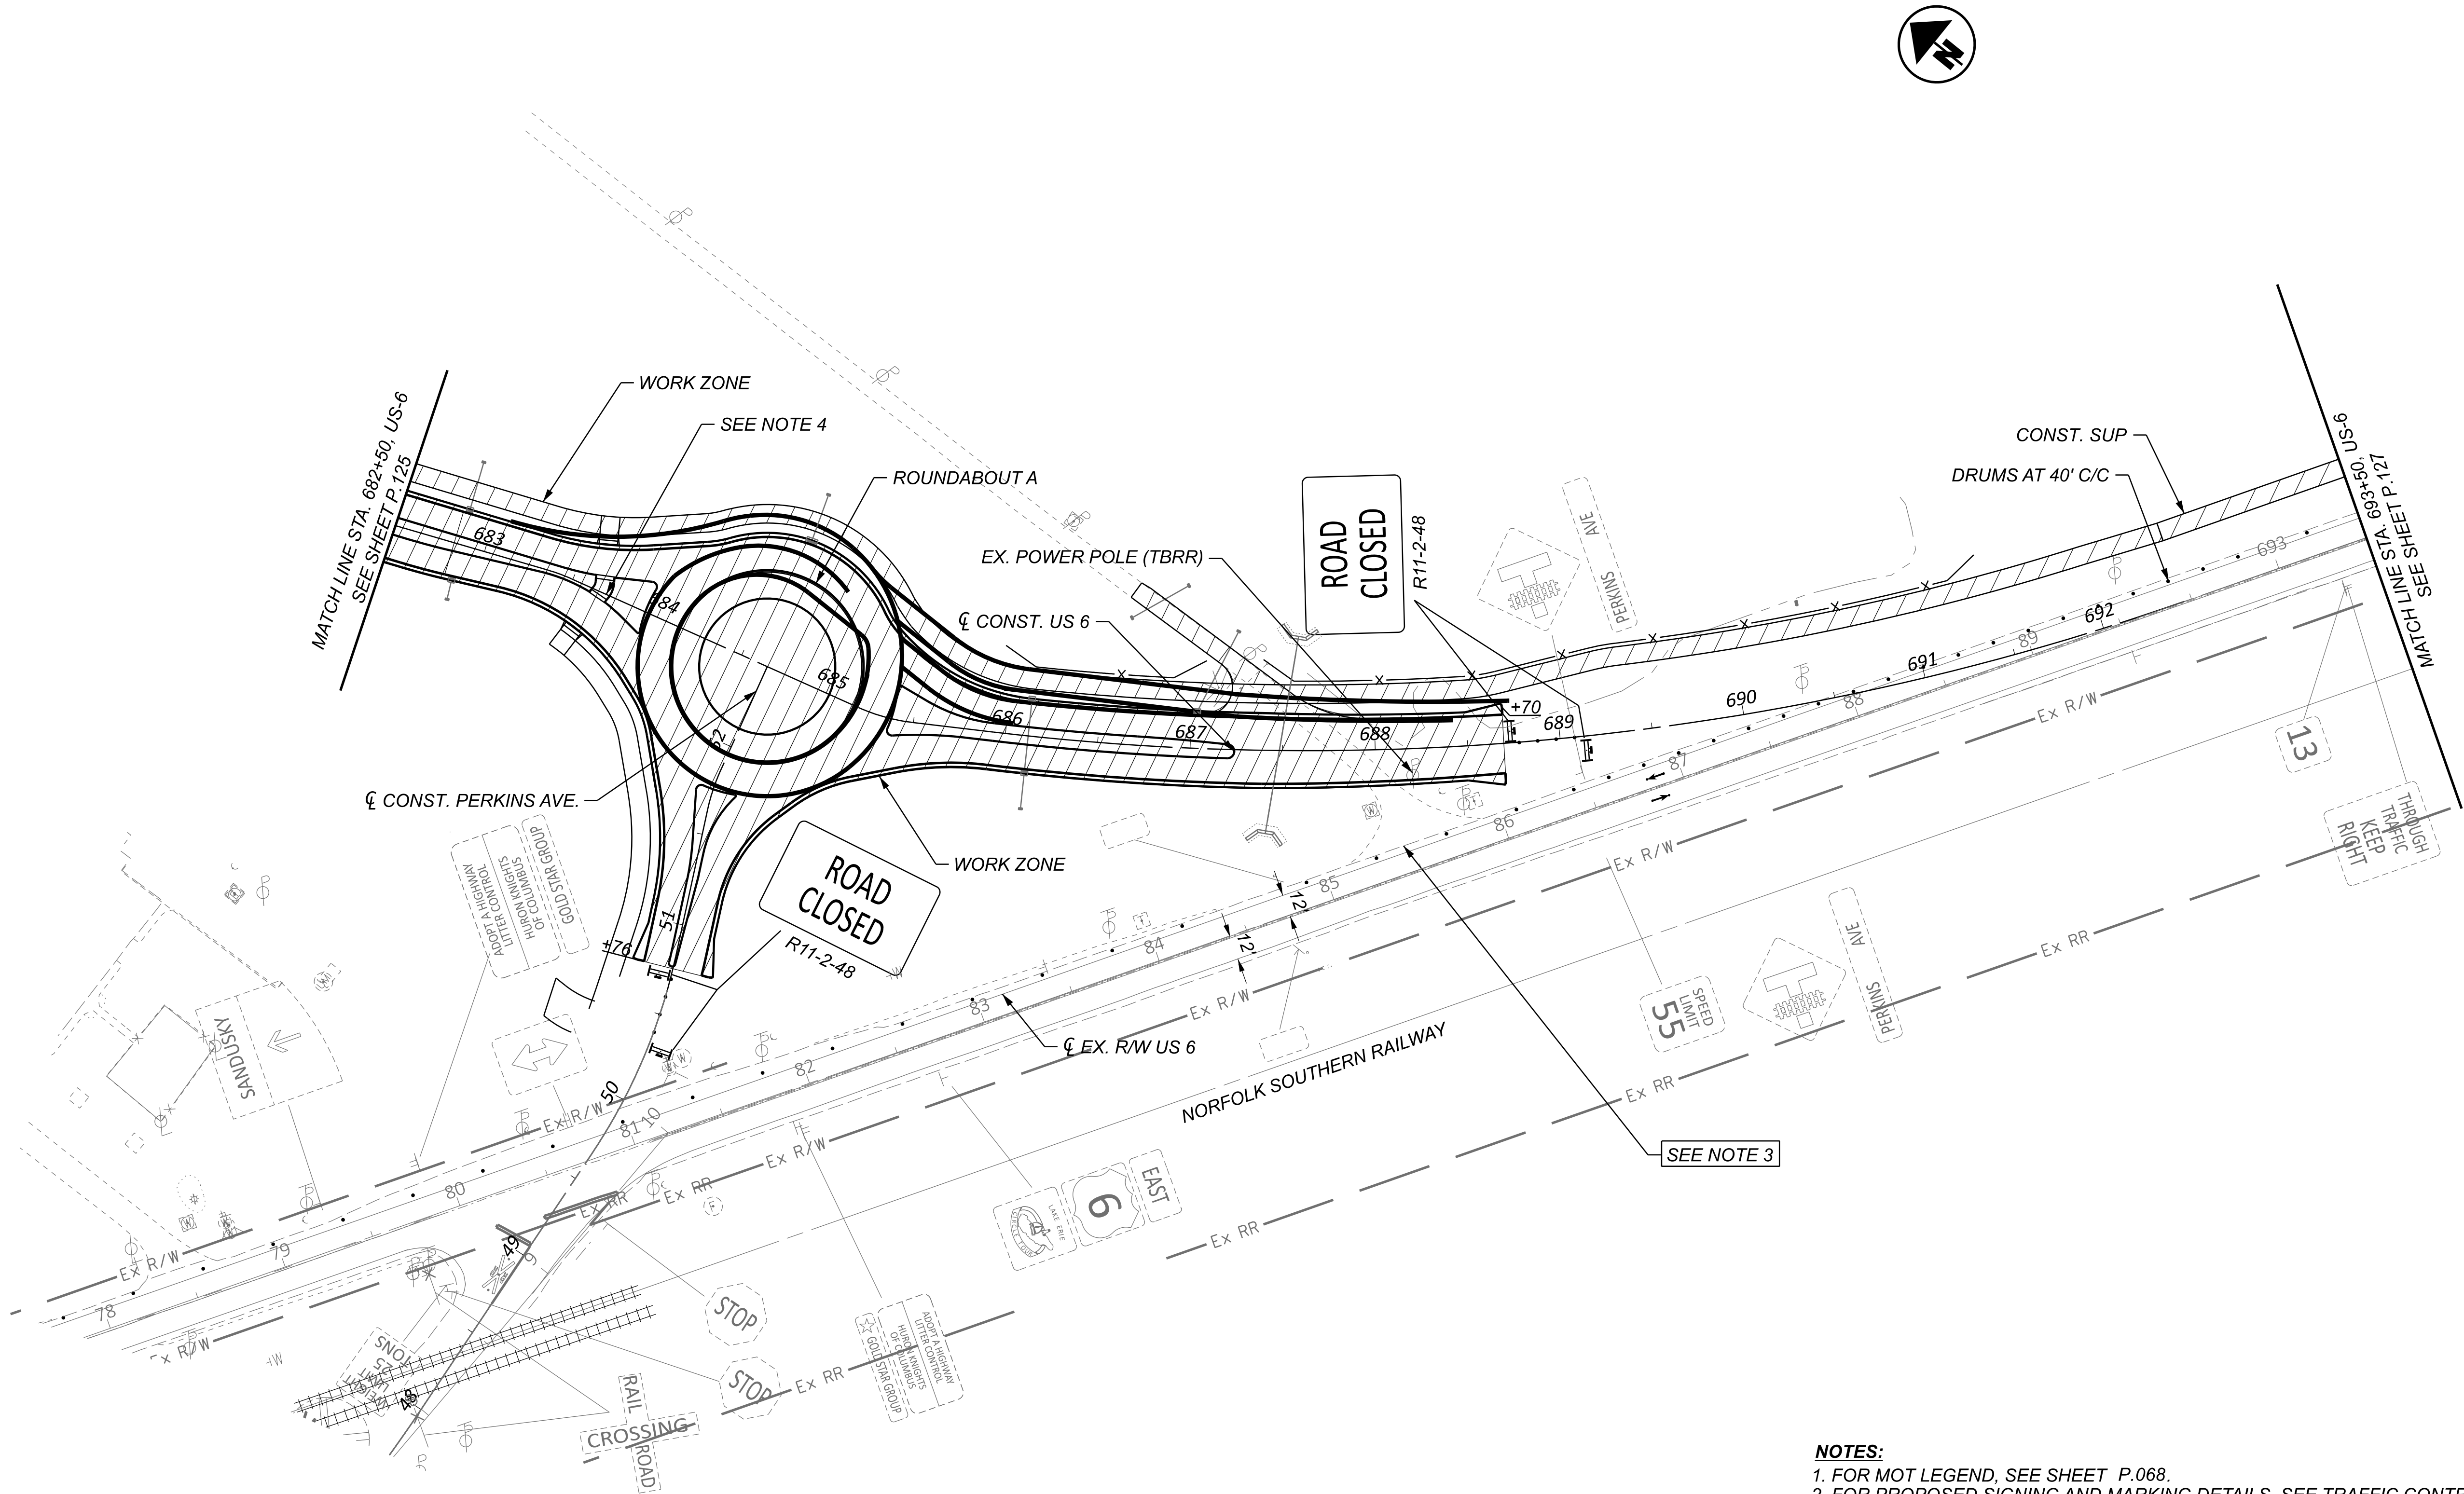


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.
REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.
 4. SOIL STABILIZATION WILL BE REQUIRED ALONG CENTERLINE OF CONSTRUCTION US 6 STA. 681+50 TO 692+50 DUE TO SOFT SOILS ENCOUNTERED IN THE FIELD. THE FILL UNDER THE PROPOSED ROADWAY AND ESPECIALLY THE PROPOSED BOX CULVERT AT STA. 687+50 WILL LIKELY NEED TO BE PRE-LOADED TO ACHIEVE AN ACCEPTABLE BEARING CAPACITY TO PREVENT SETTLEMENT. PRE-LOADING THE FILL REQUIRES MORE TIME DURING CONSTRUCTION, AND IT IS RECOMMENDED THAT THIS AREA BE PRIORITIZED AT THE BEGINNING OF THE CONSTRUCTION SEQUENCING.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 683+00.00 TO STA. 693+50.00


TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.129	782



NOTES:


1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.
4. SOIL STABILIZATION WILL BE REQUIRED ALONG CENTERLINE OF CONSTRUCTION US 6 STA. 681+50 TO 692+50 DUE TO SOFT SOILS ENCOUNTERED IN THE FIELD. THE FILL UNDER THE PROPOSED ROADWAY AND ESPECIALLY THE PROPOSED BOX CULVERT AT STA. 687+50 WILL LIKELY NEED TO BE PRE-LOADED TO ACHIEVE AN ACCEPTABLE BEARING CAPACITY TO PREVENT SETTLEMENT. PRE-LOADING THE FILL REQUIRES MORE TIME DURING CONSTRUCTION, AND IT IS RECOMMENDED THAT THIS AREA BE PRIORITIZED AT THE BEGINNING OF THE CONSTRUCTION SEQUENCING.

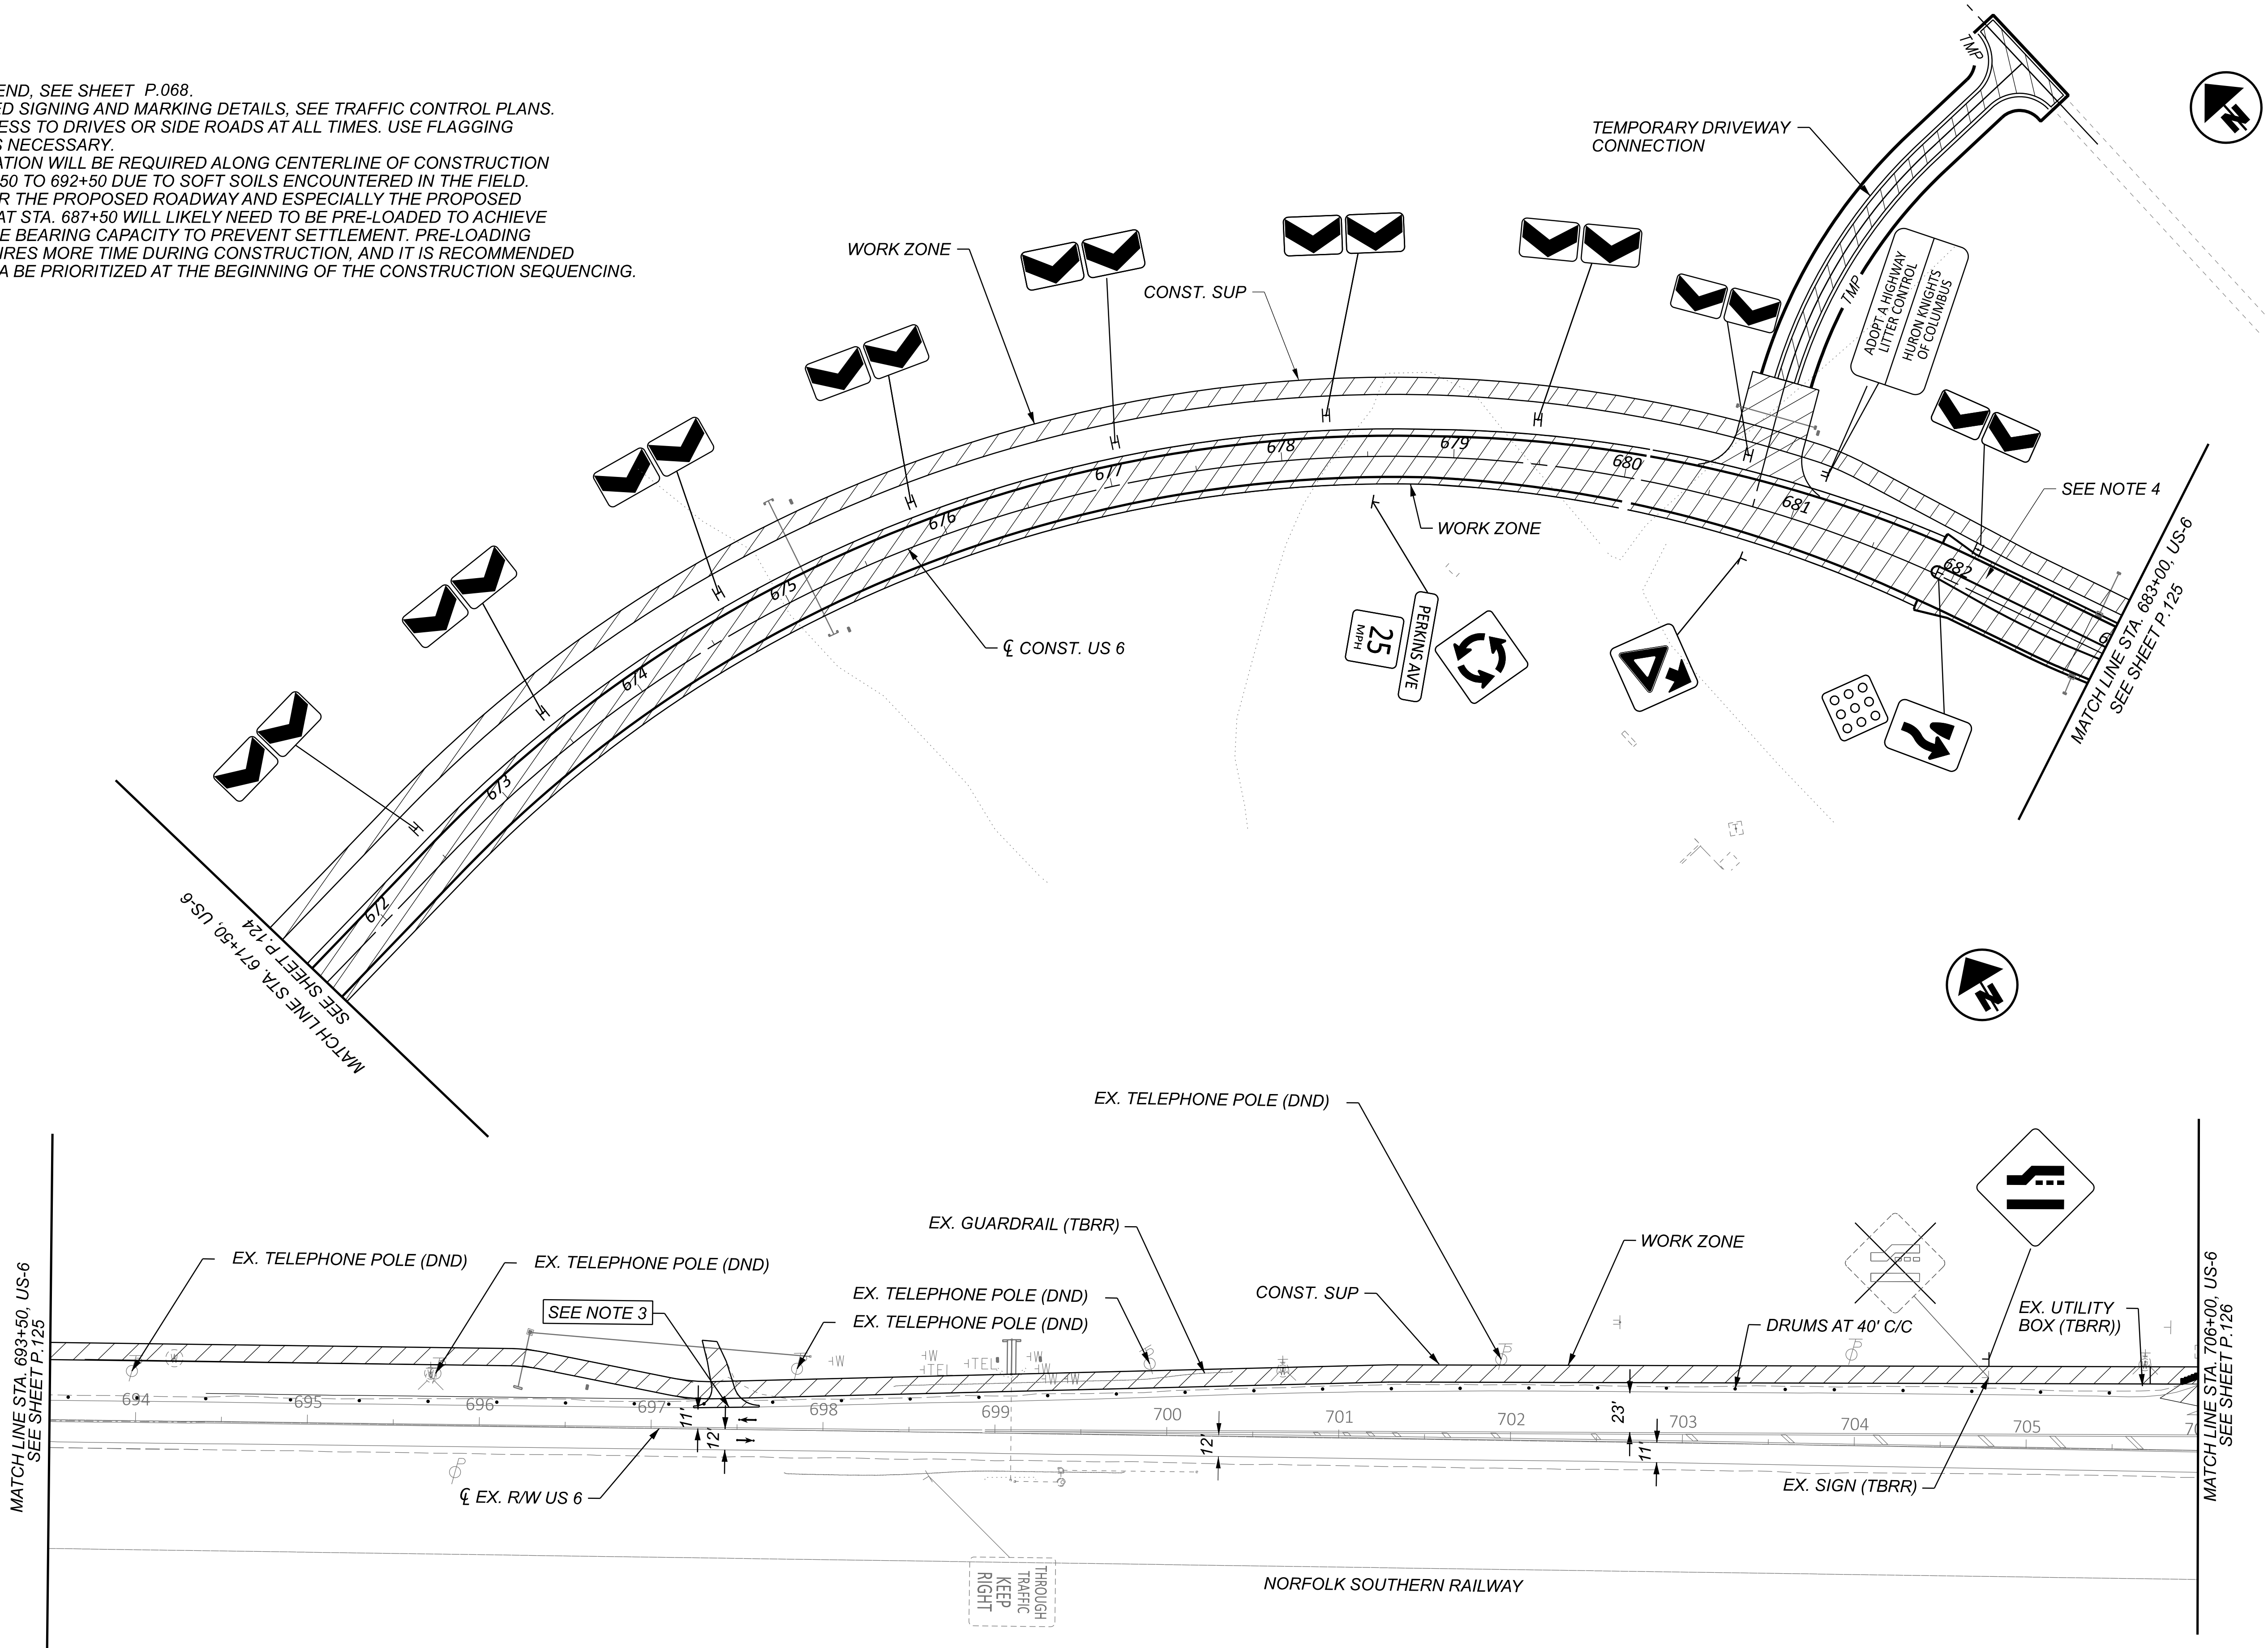


MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 671+50.00 TO STA. 706+00.00

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA
REVIEWER
SS 02/28/24
PROJECT ID
116570
SHEET
P.128
TOTAL
782

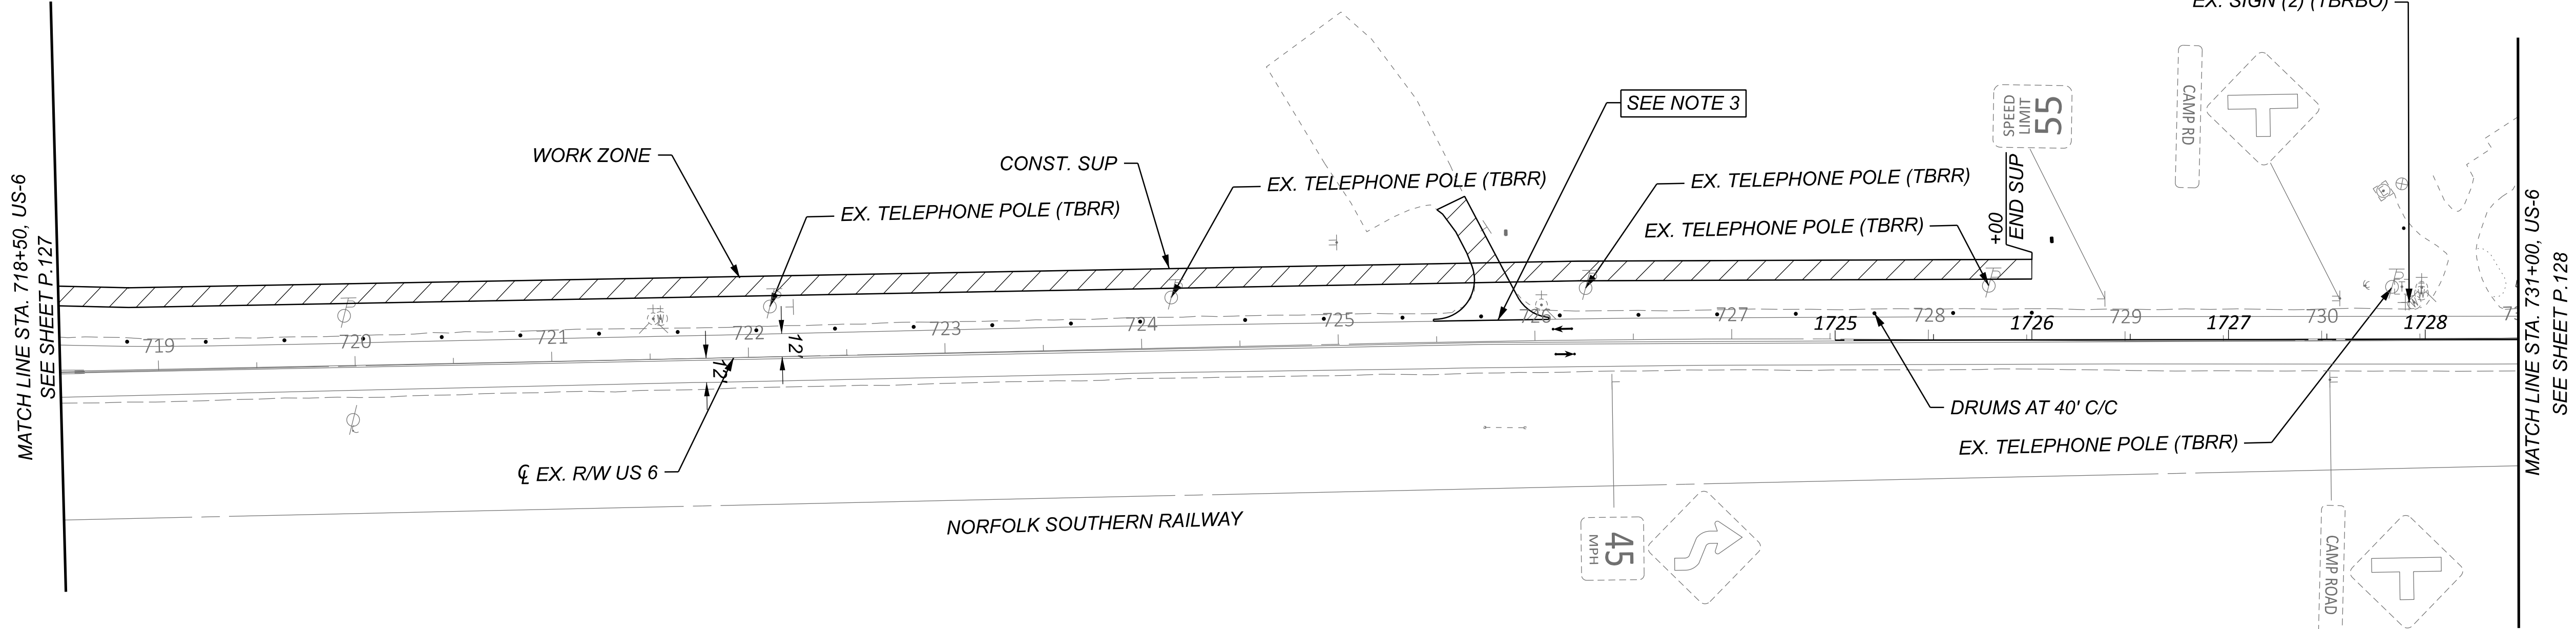


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

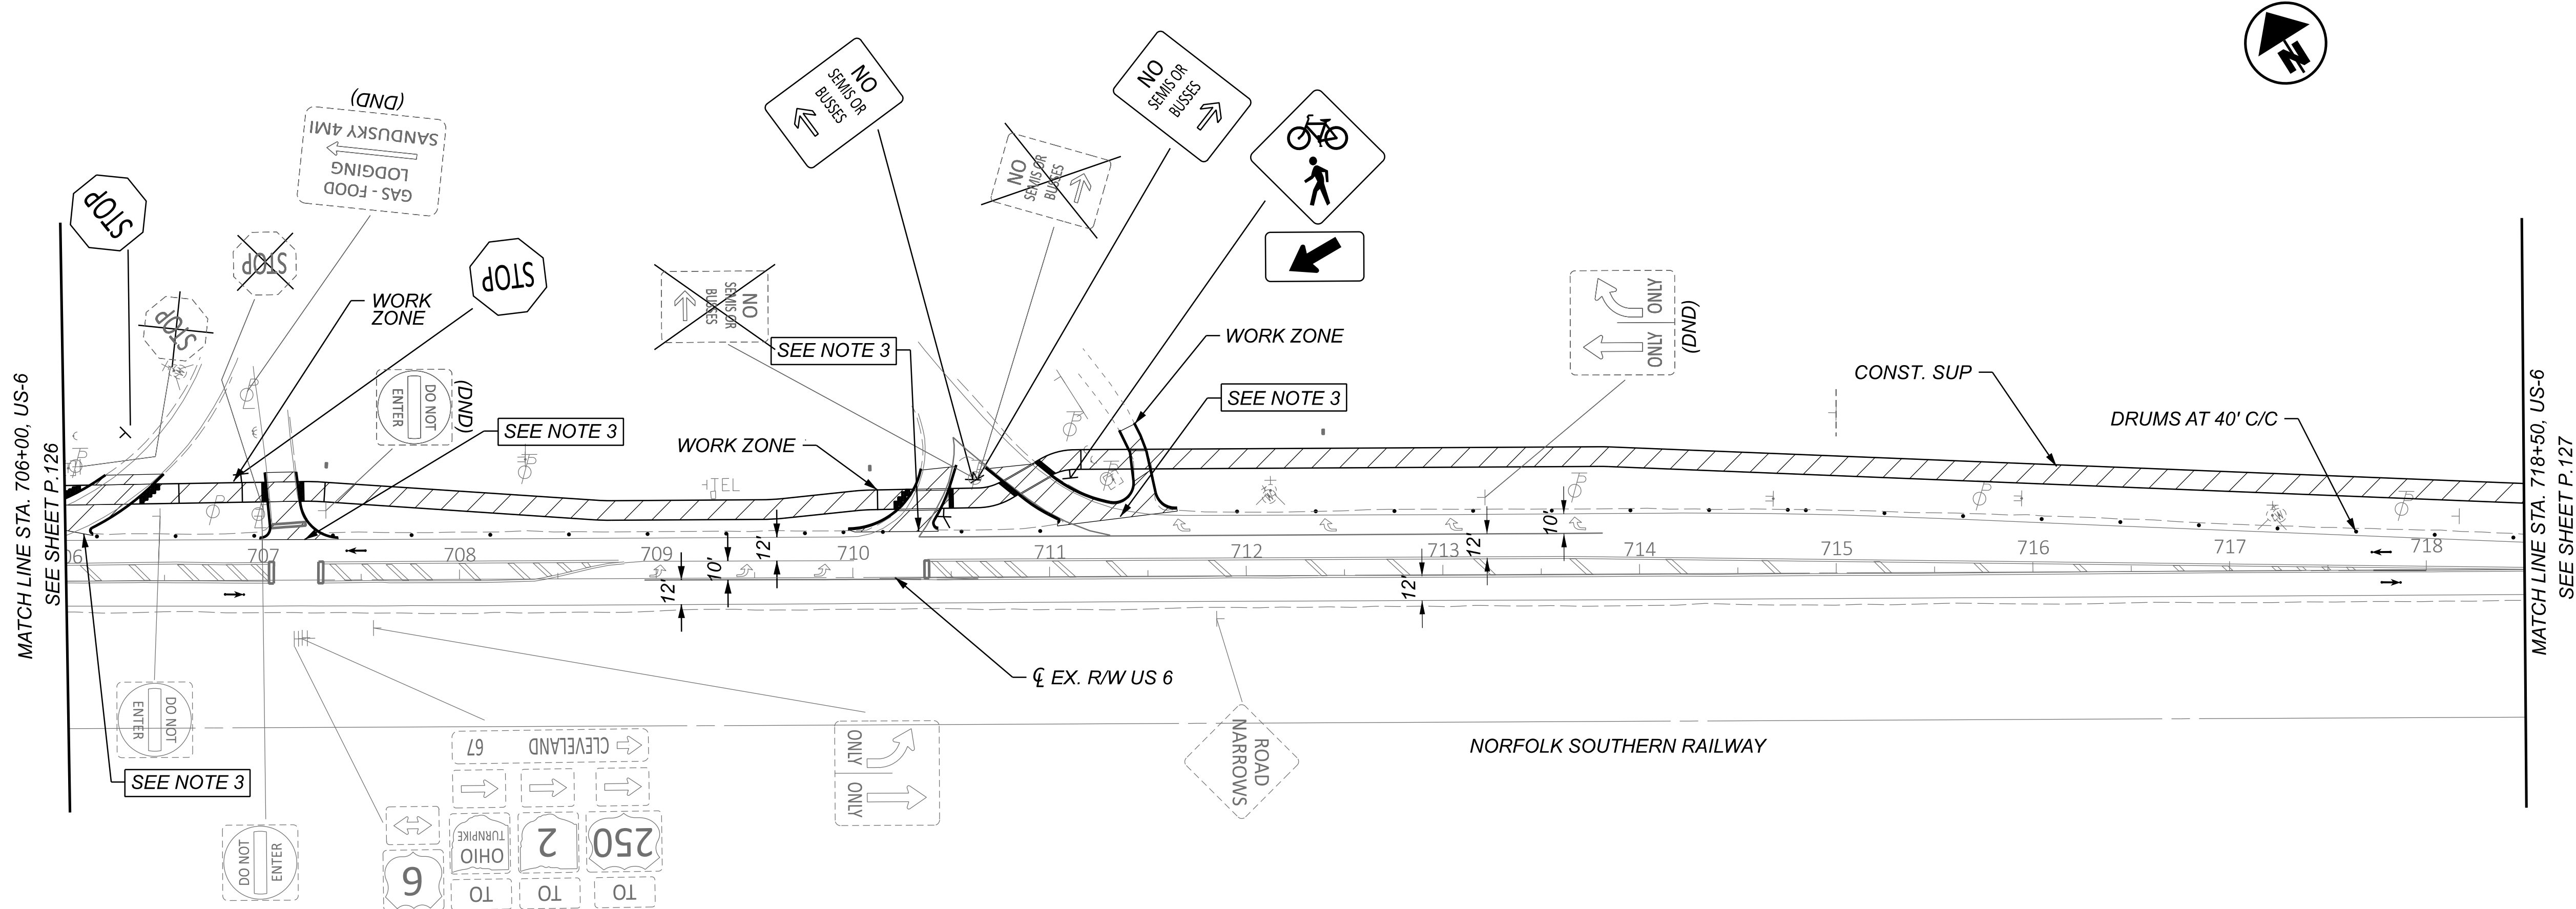


TRANSYSTEMS 400 W. WATKINSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.130	782

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 706+00.00 TO STA. 730+00.00



2026 UTILITY RELOCATION WORK

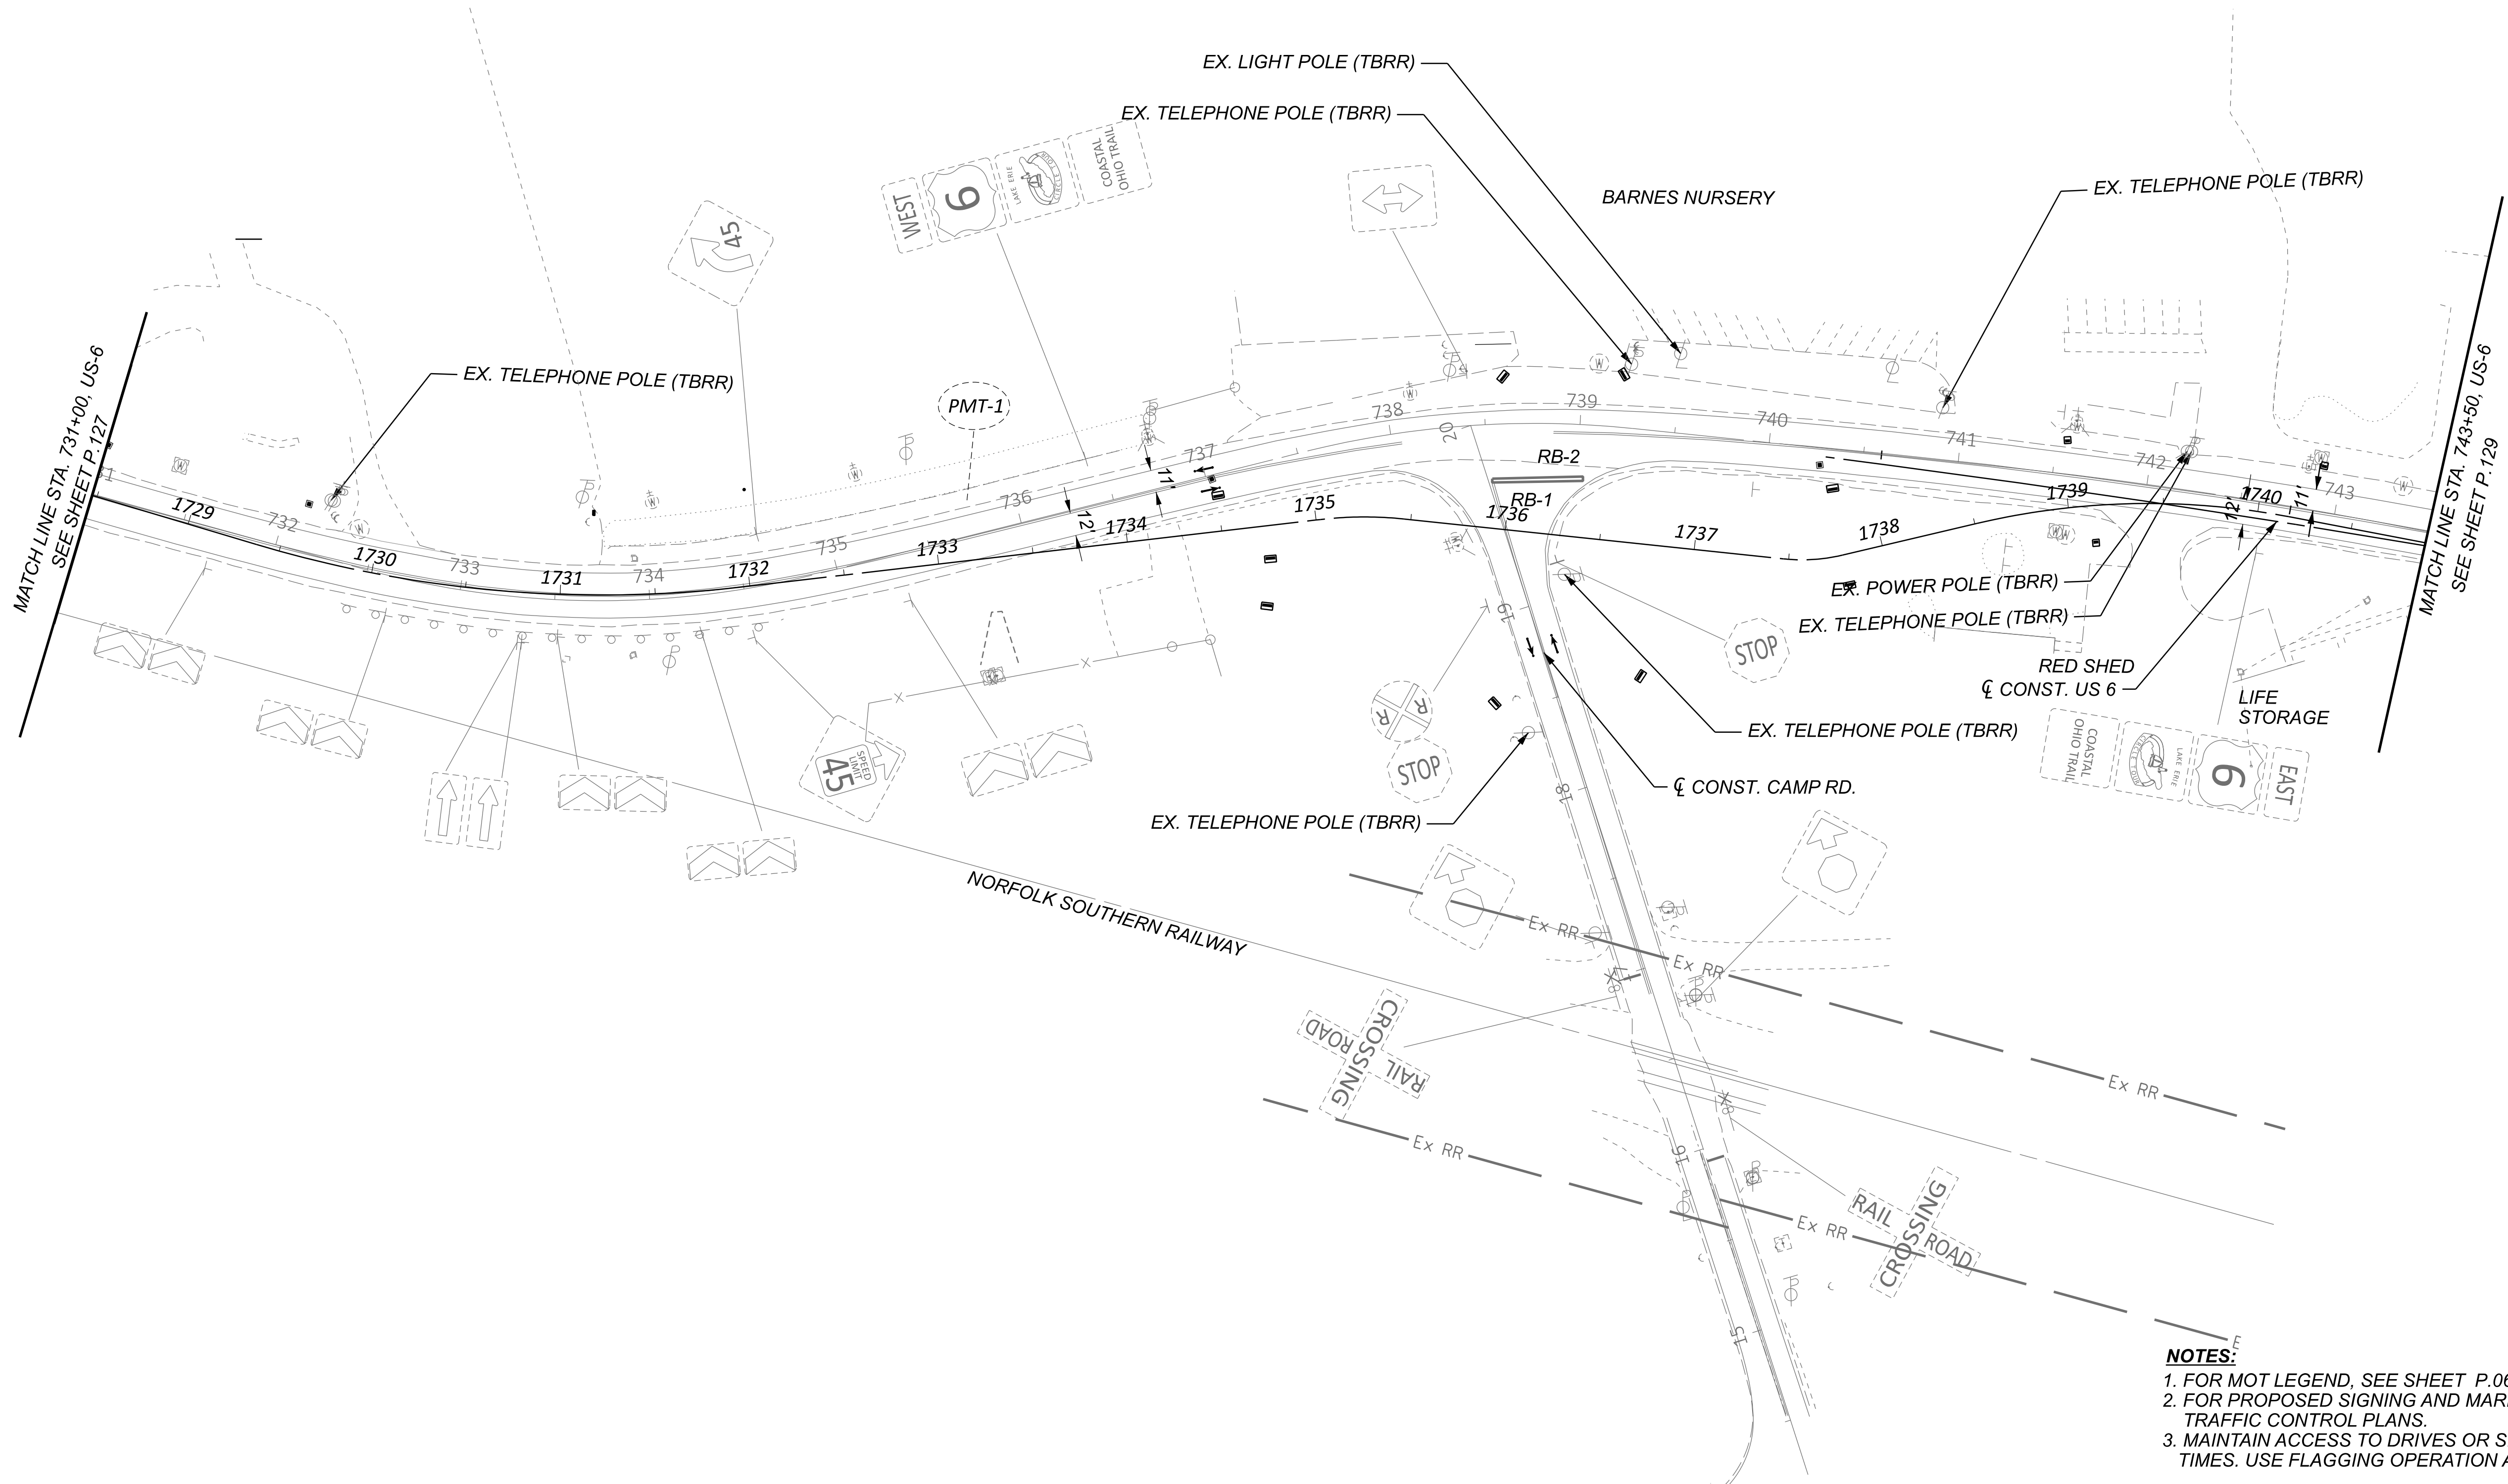


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 731+00.00 TO STA. 743+50.00

TRANSYSTEMS
400 W. WATSON BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.131	782



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 1 - Plan 15-16 (Sheet) PAPERSIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:20:25 PM USER: ssadusei
 path: \\ohiodot-pw.bentley.com:ohiodot-pw-02\Documents\01 Active Projects\District 03\Erie\116570\402-Engineering_TransSystems\TransSystems\116570_MPO00_CV2026.dgn

2026 UTILITY RELOCATION WORK

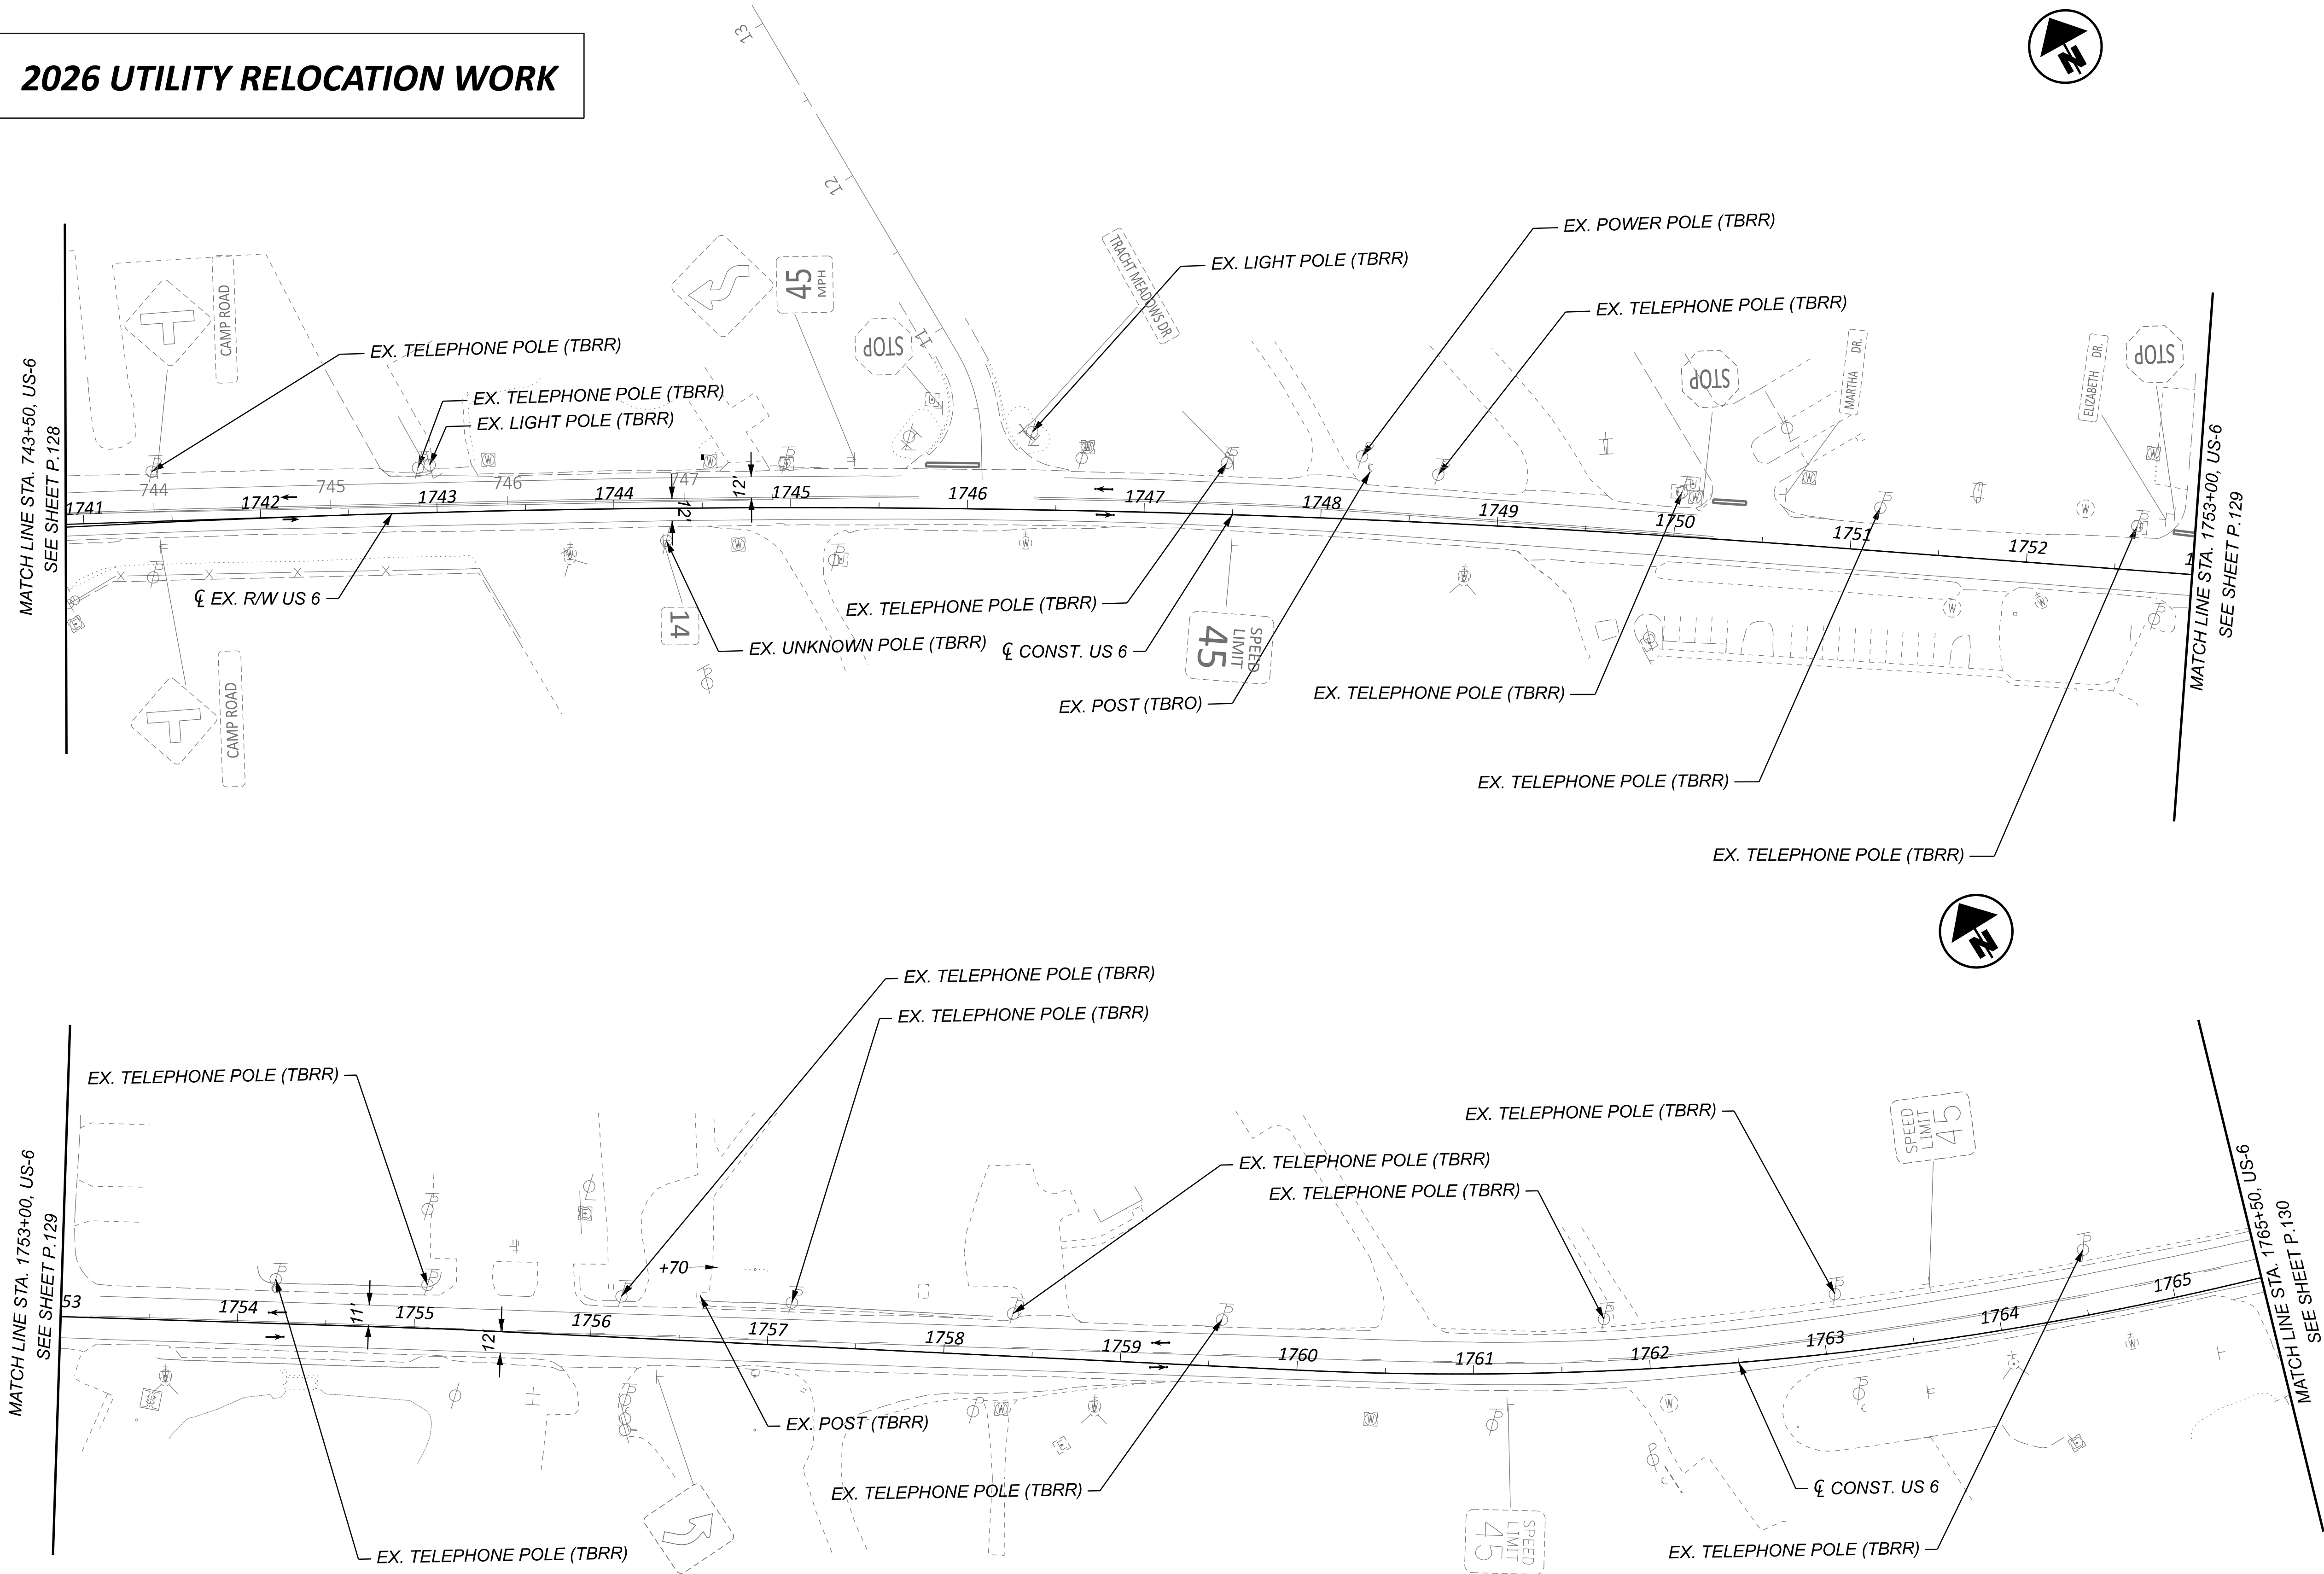

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - EX. US 6 STA. 743+50.00 TO CONST. US 6 STA. 1765+50.00

DESIGN AGENCY

TRANSYSTEMS

400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28

PROJECT ID
116570

SHEET	TOTAL
P.132	78

HORIZONTAL
SCALE IN FEET





25 50 100

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

ERI-US 0006-CONNECTIVITY CORRIDOR

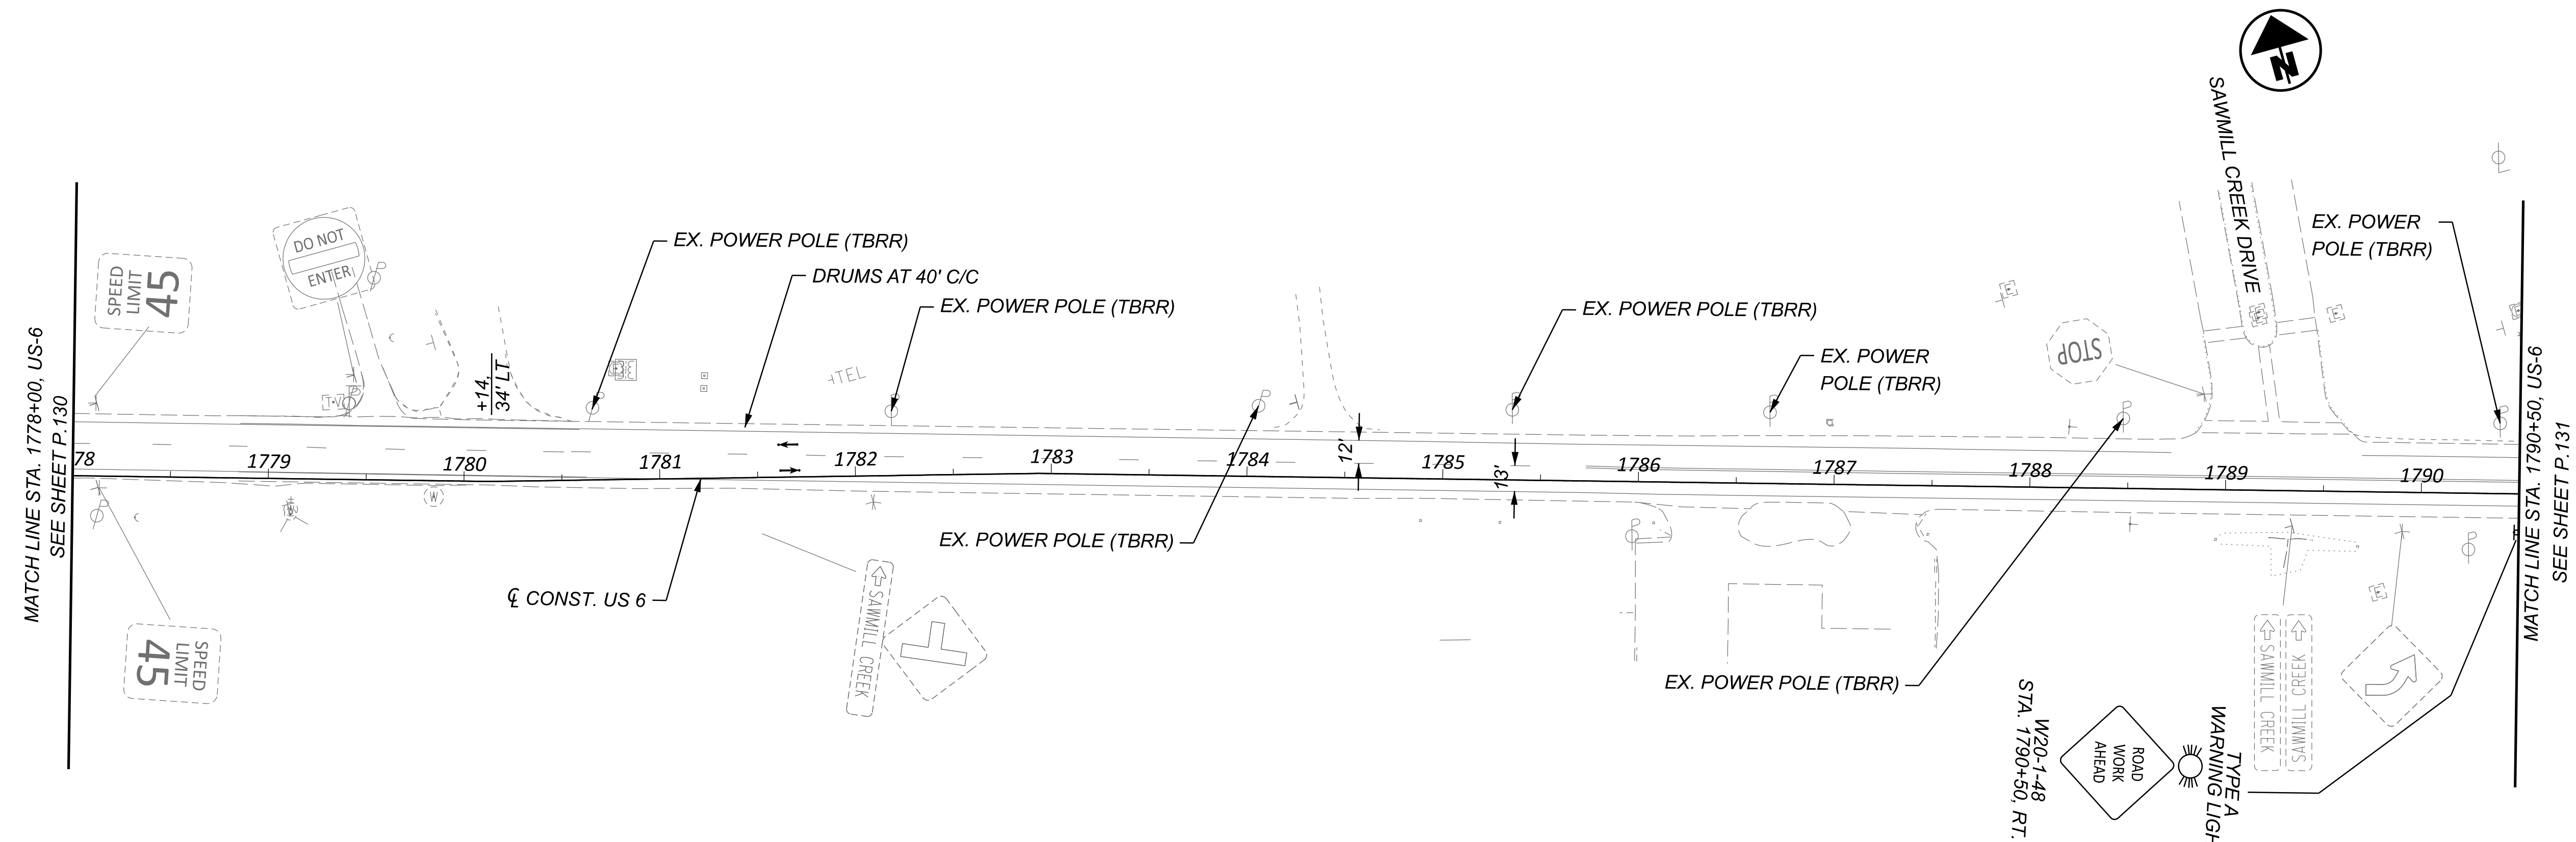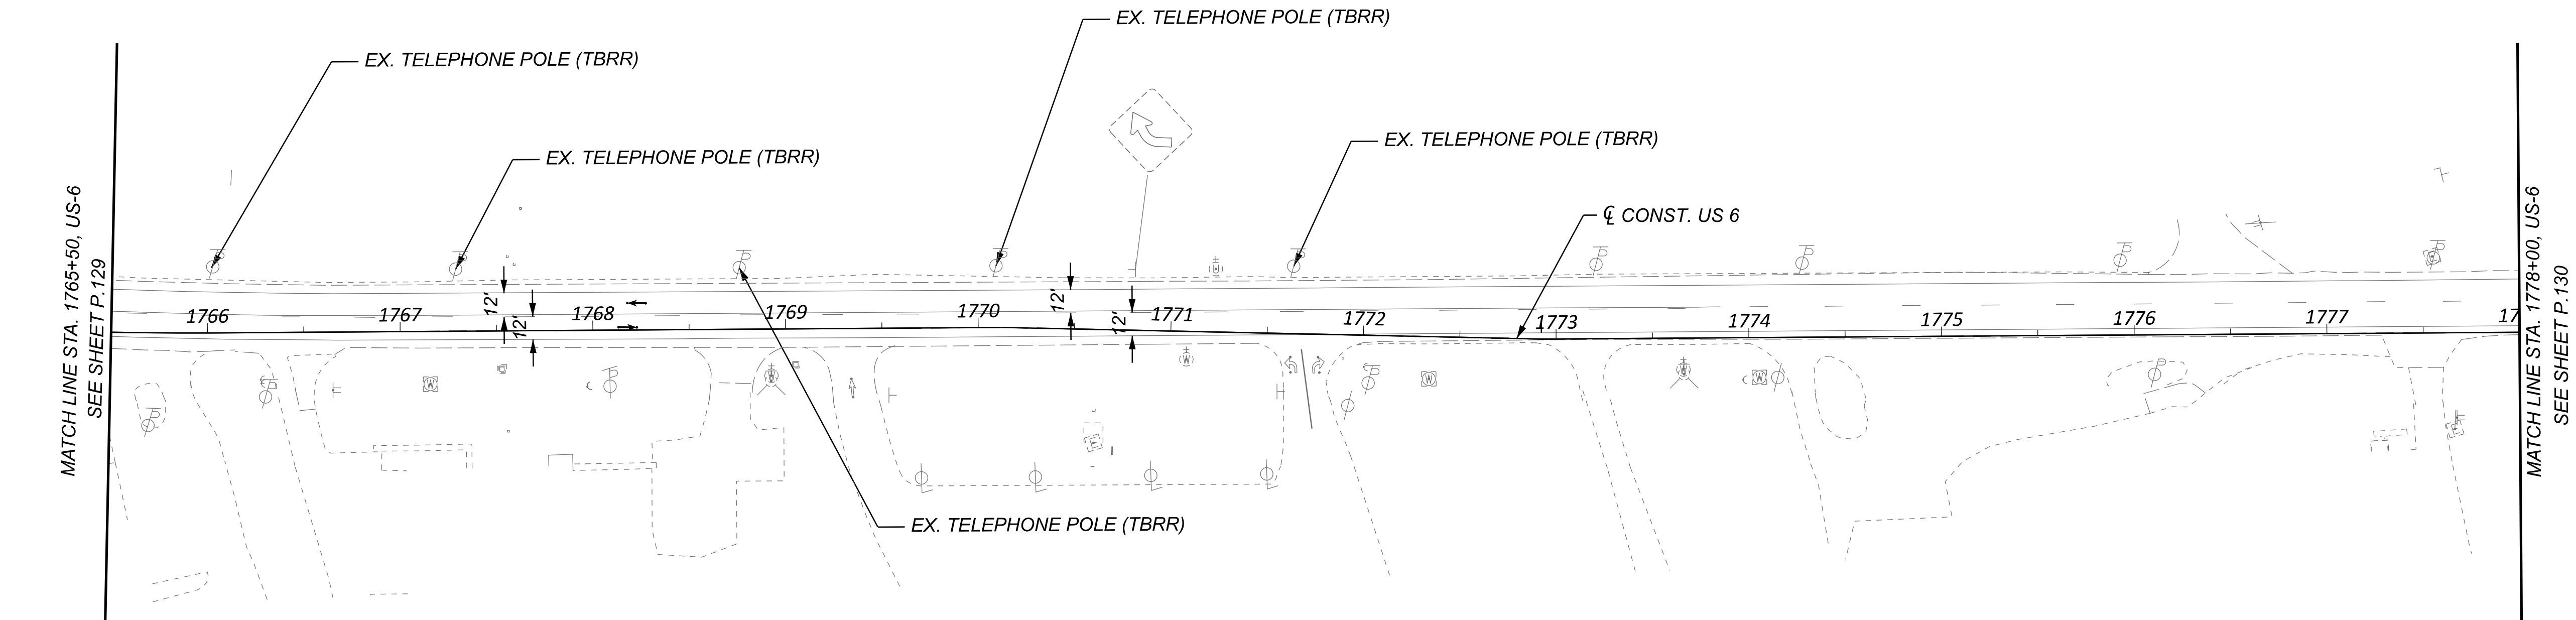

NOTES:


1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 1765+50.00 TO STA. 1790+50.00


DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.133	782

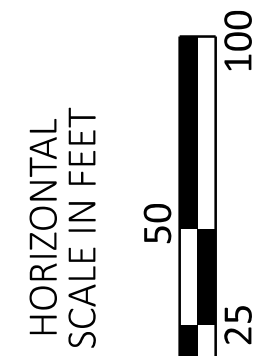

2026 UTILITY RELOCATION WORK

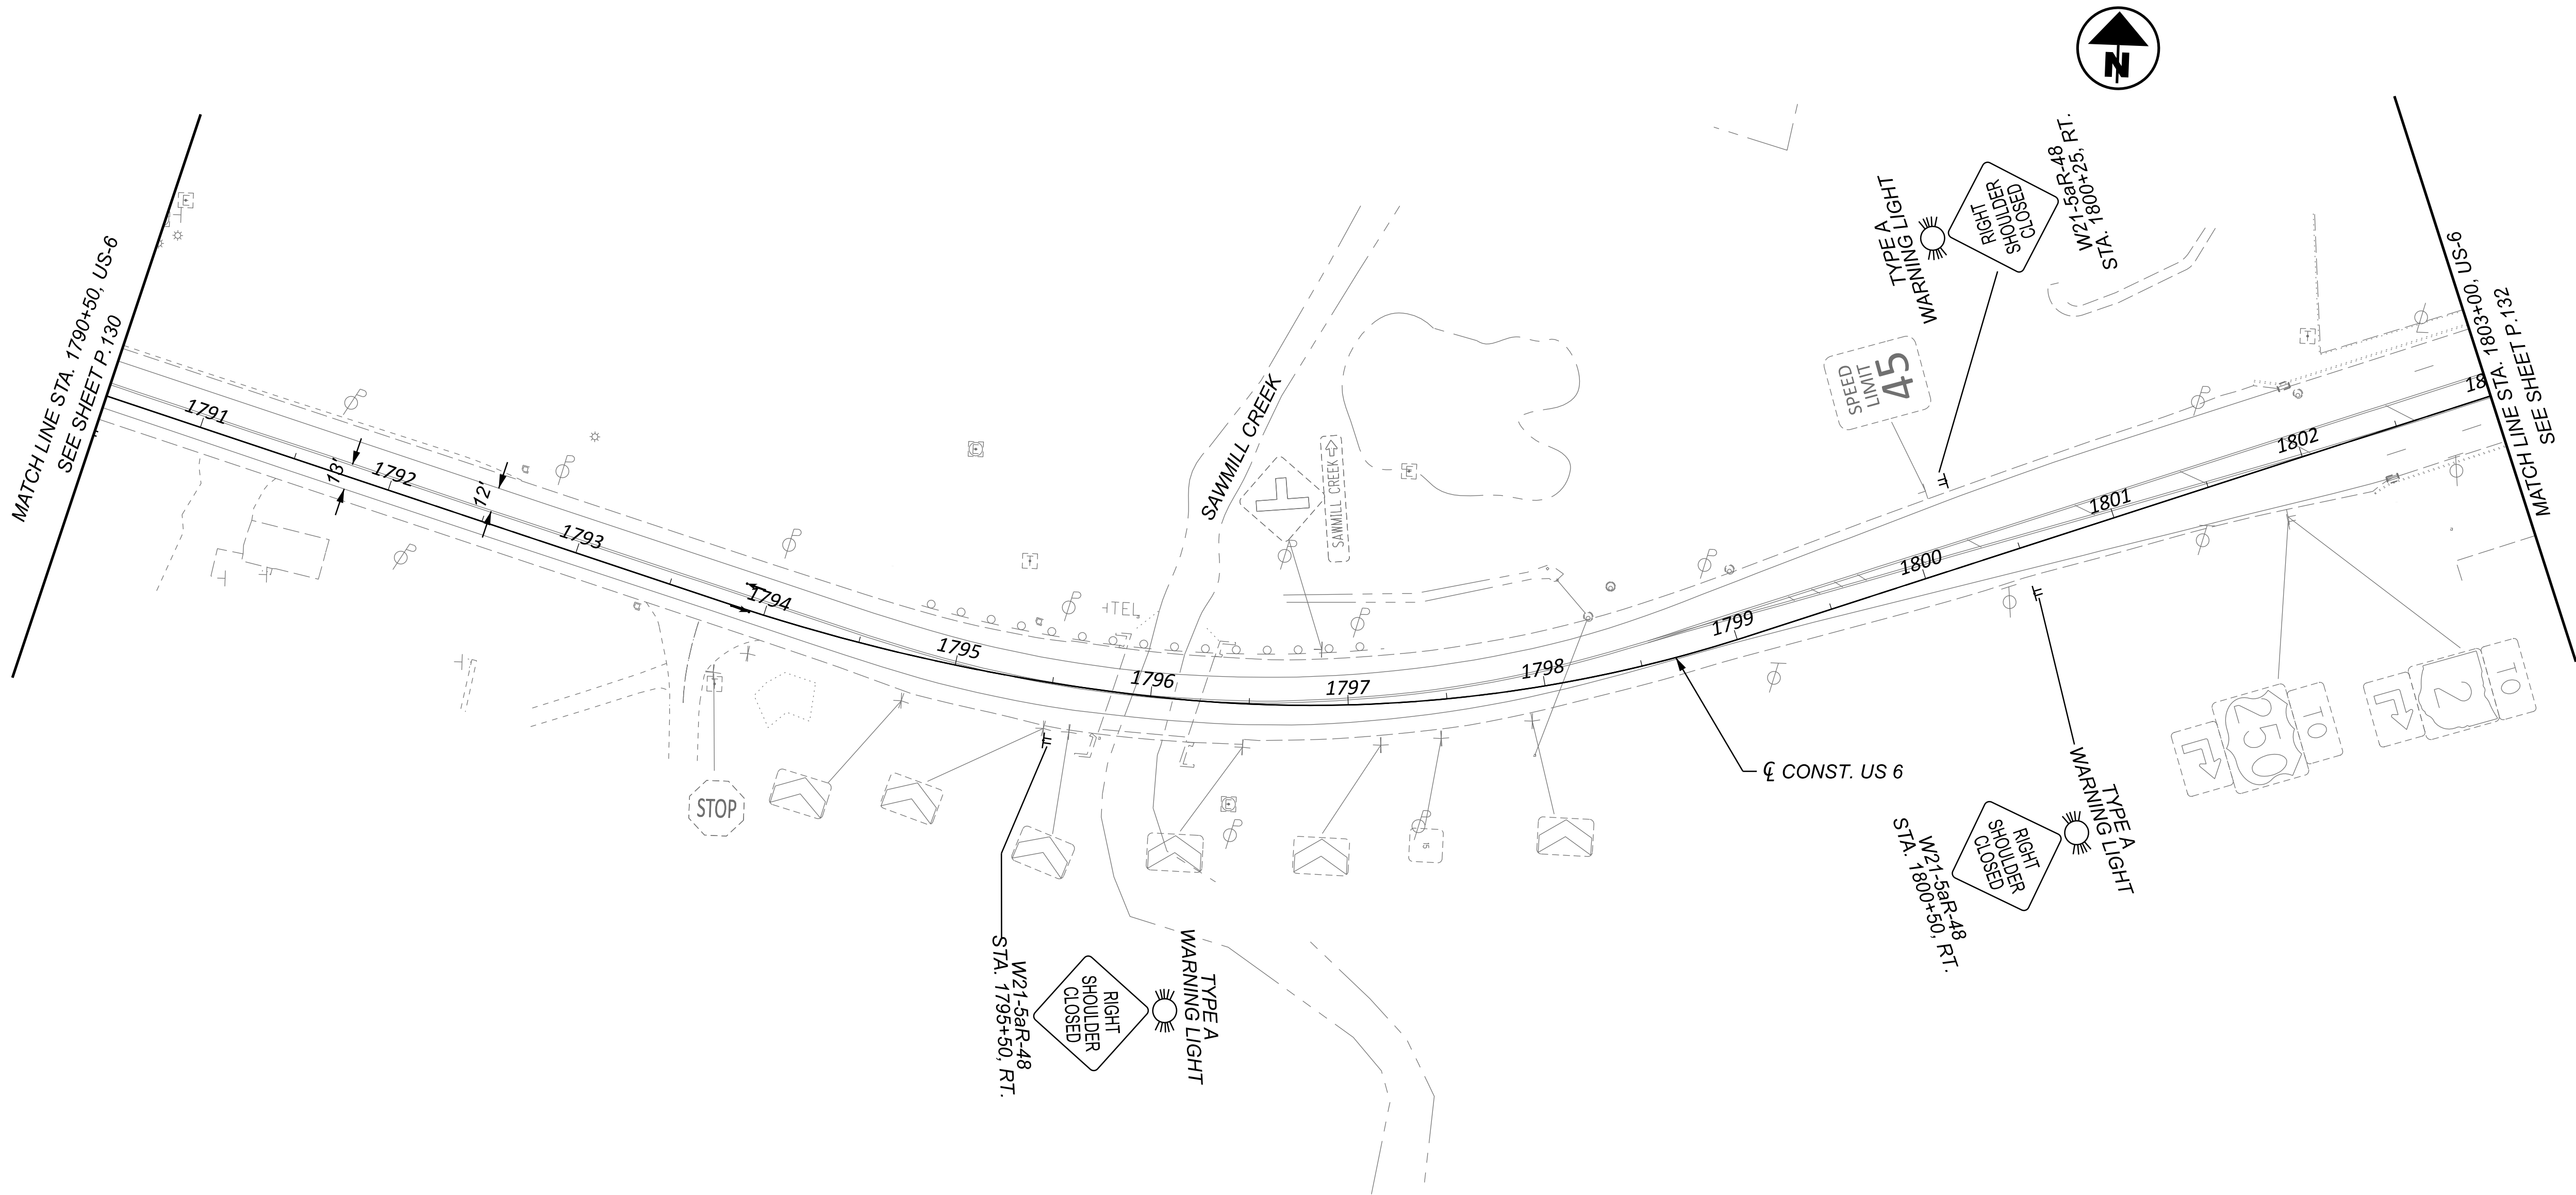

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 1790+50.00 TO STA. 1803+00.00


DESIGN AGENCY
TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET	TOTAL
P.134	782



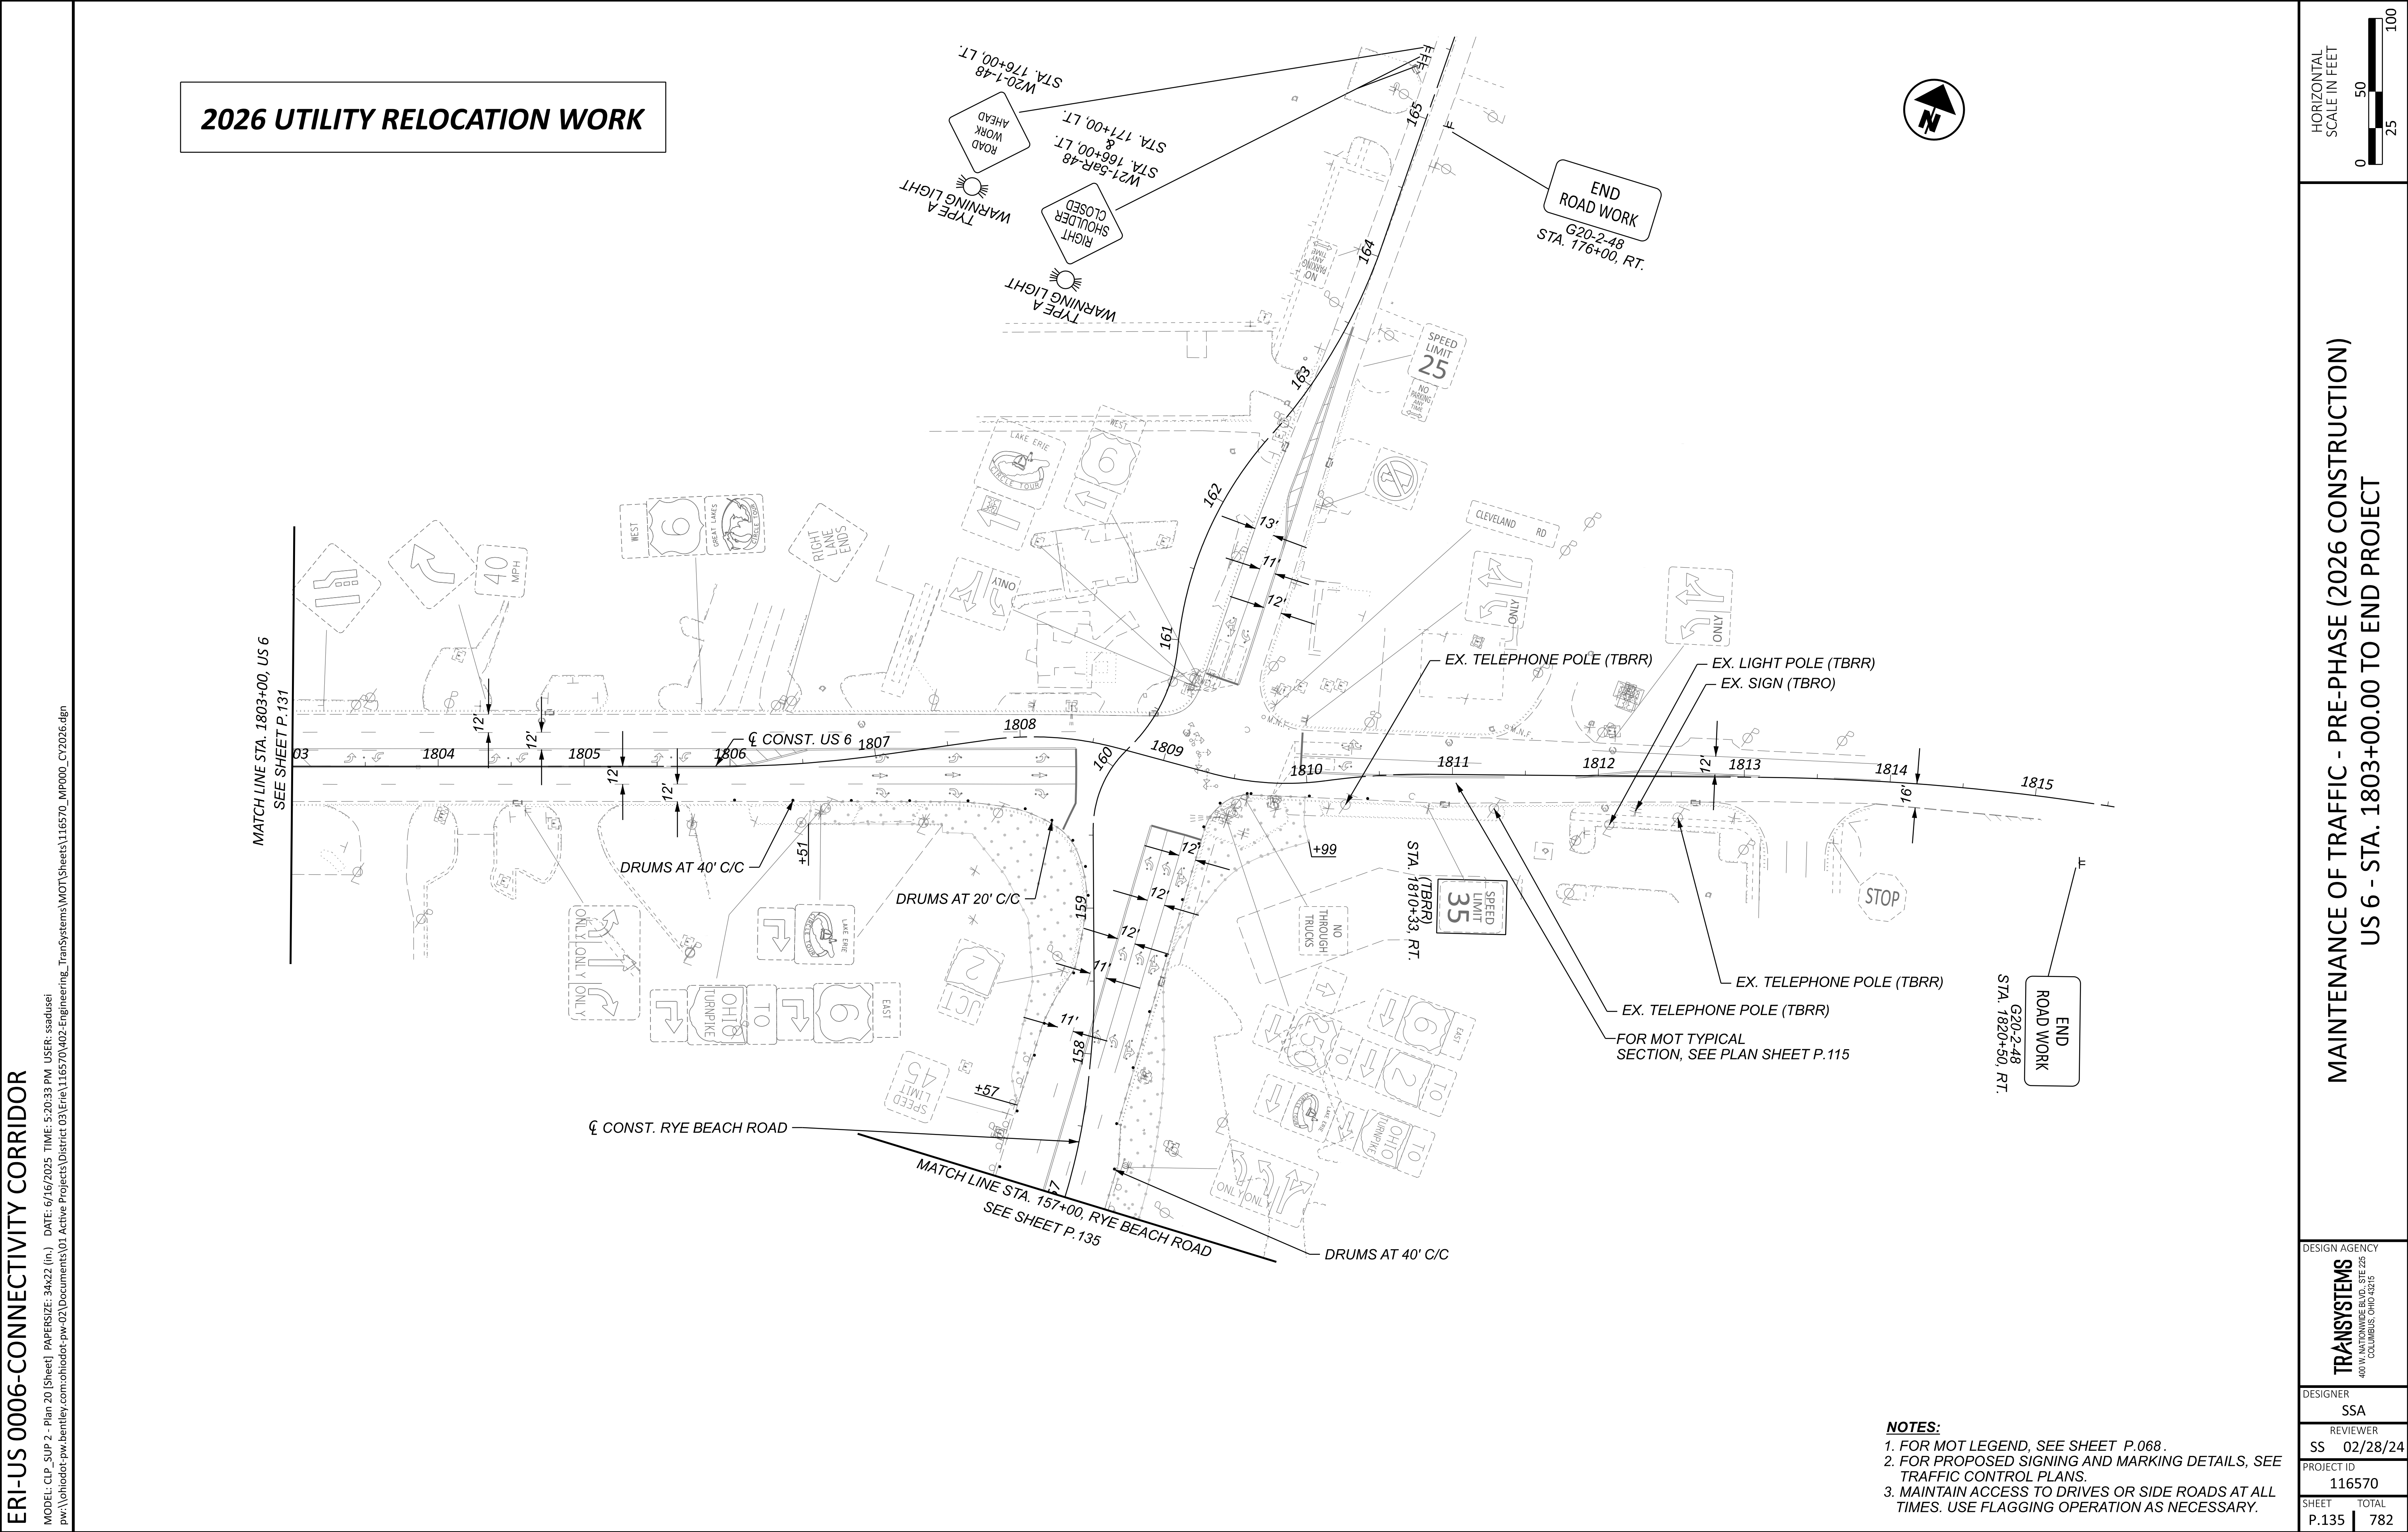

2026 UTILITY RELOCATION WORK


- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 1803+00.00 TO END PROJECT

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.135	782

ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP_2 - Plan 21[Sheet] PAPER:SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:20:34 PM USER: ssadusei
 www\yohiador-pw.bentley.com:ohiodor-pw-02\Documents\01 Active Projects\District 03\Errie\116570\402-Engineering_TransSystems\MOT\Sheets\116570_MP000_C\2026.dgn

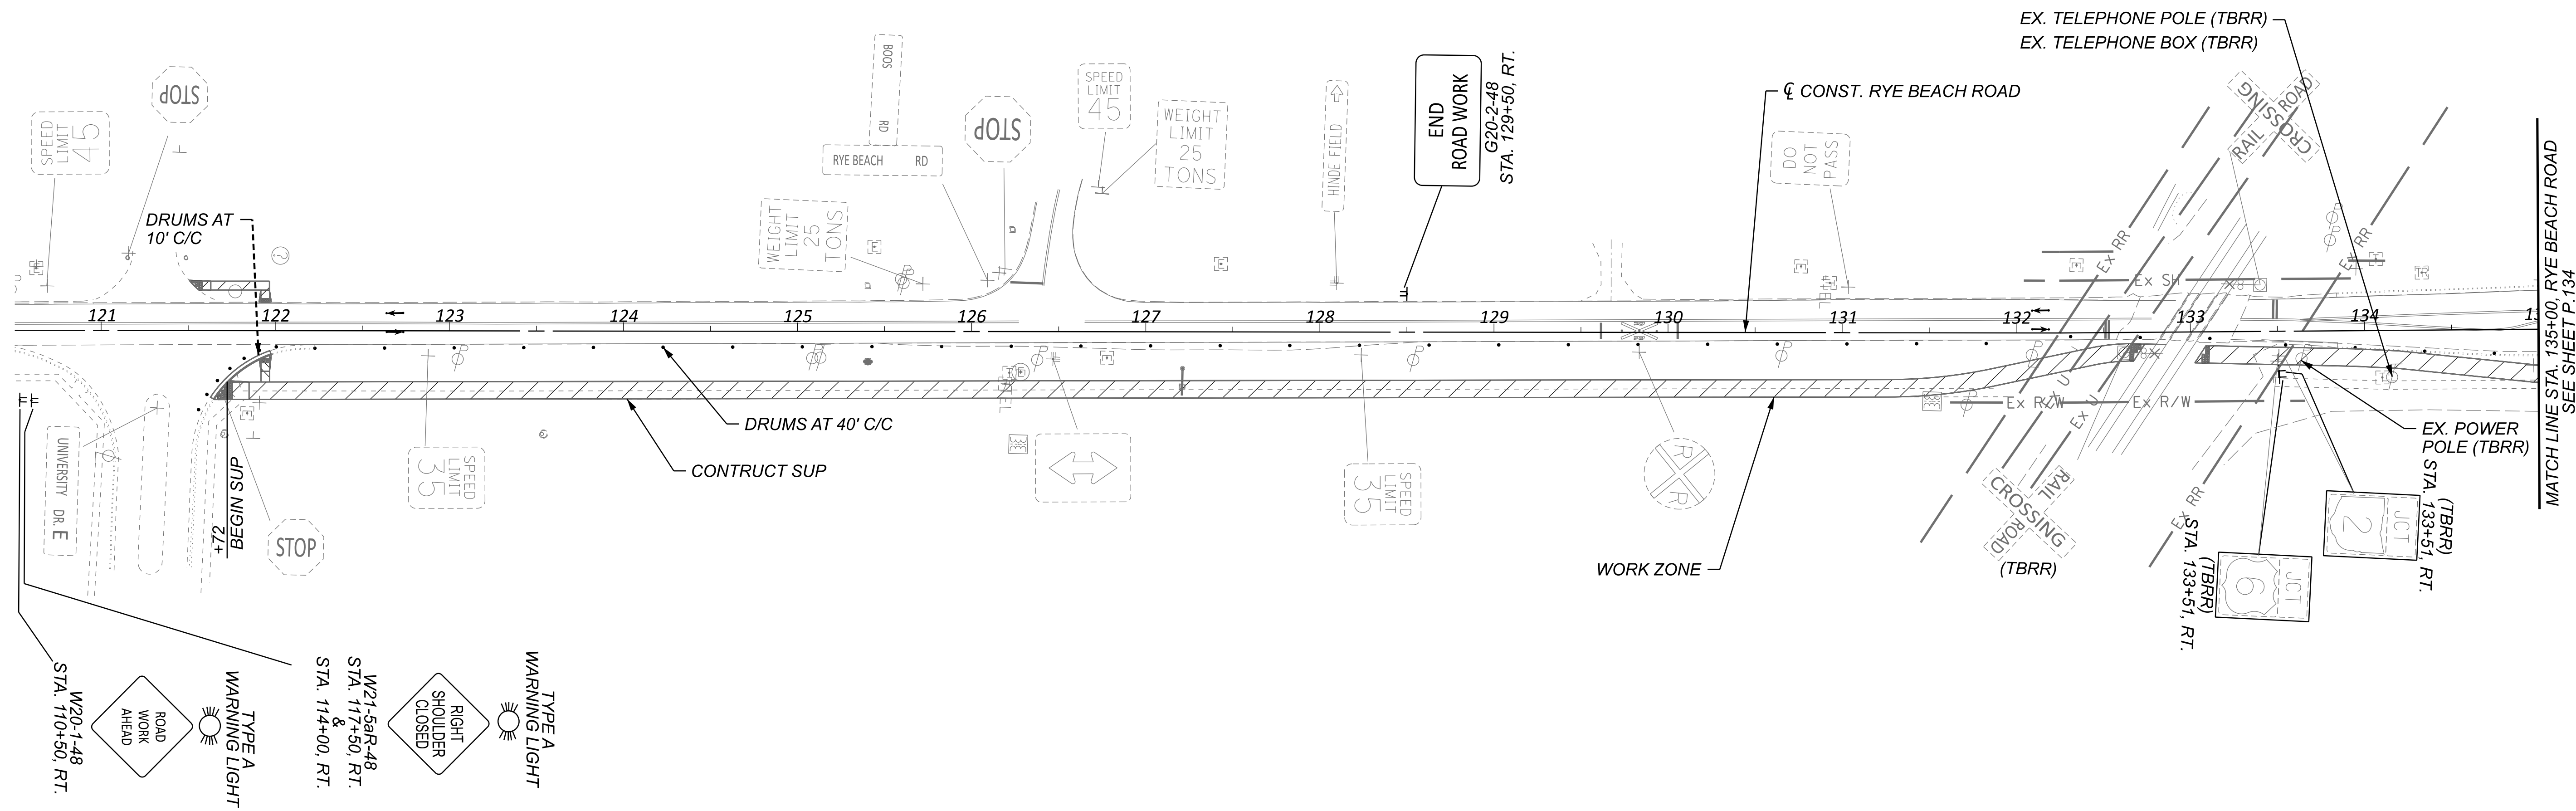

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

DESIGN AGENCY

TRANSYSTEMS

400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER

SS

REVIEWER
SS 02/28/24


PROJECT ID
116570

SHEET	TOTAL
P.136	78

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
 RYE BEACH ROAD - BEGIN PROJECT TO STA. 135+00.00

HORIZONTAL
SCALE IN FEET

A horizontal scale bar is shown, labeled "HORIZONTAL SCALE IN FEET". The bar is marked with 0, 25, 50, and 100. The segment between 25 and 50 is highlighted with a thick black line.

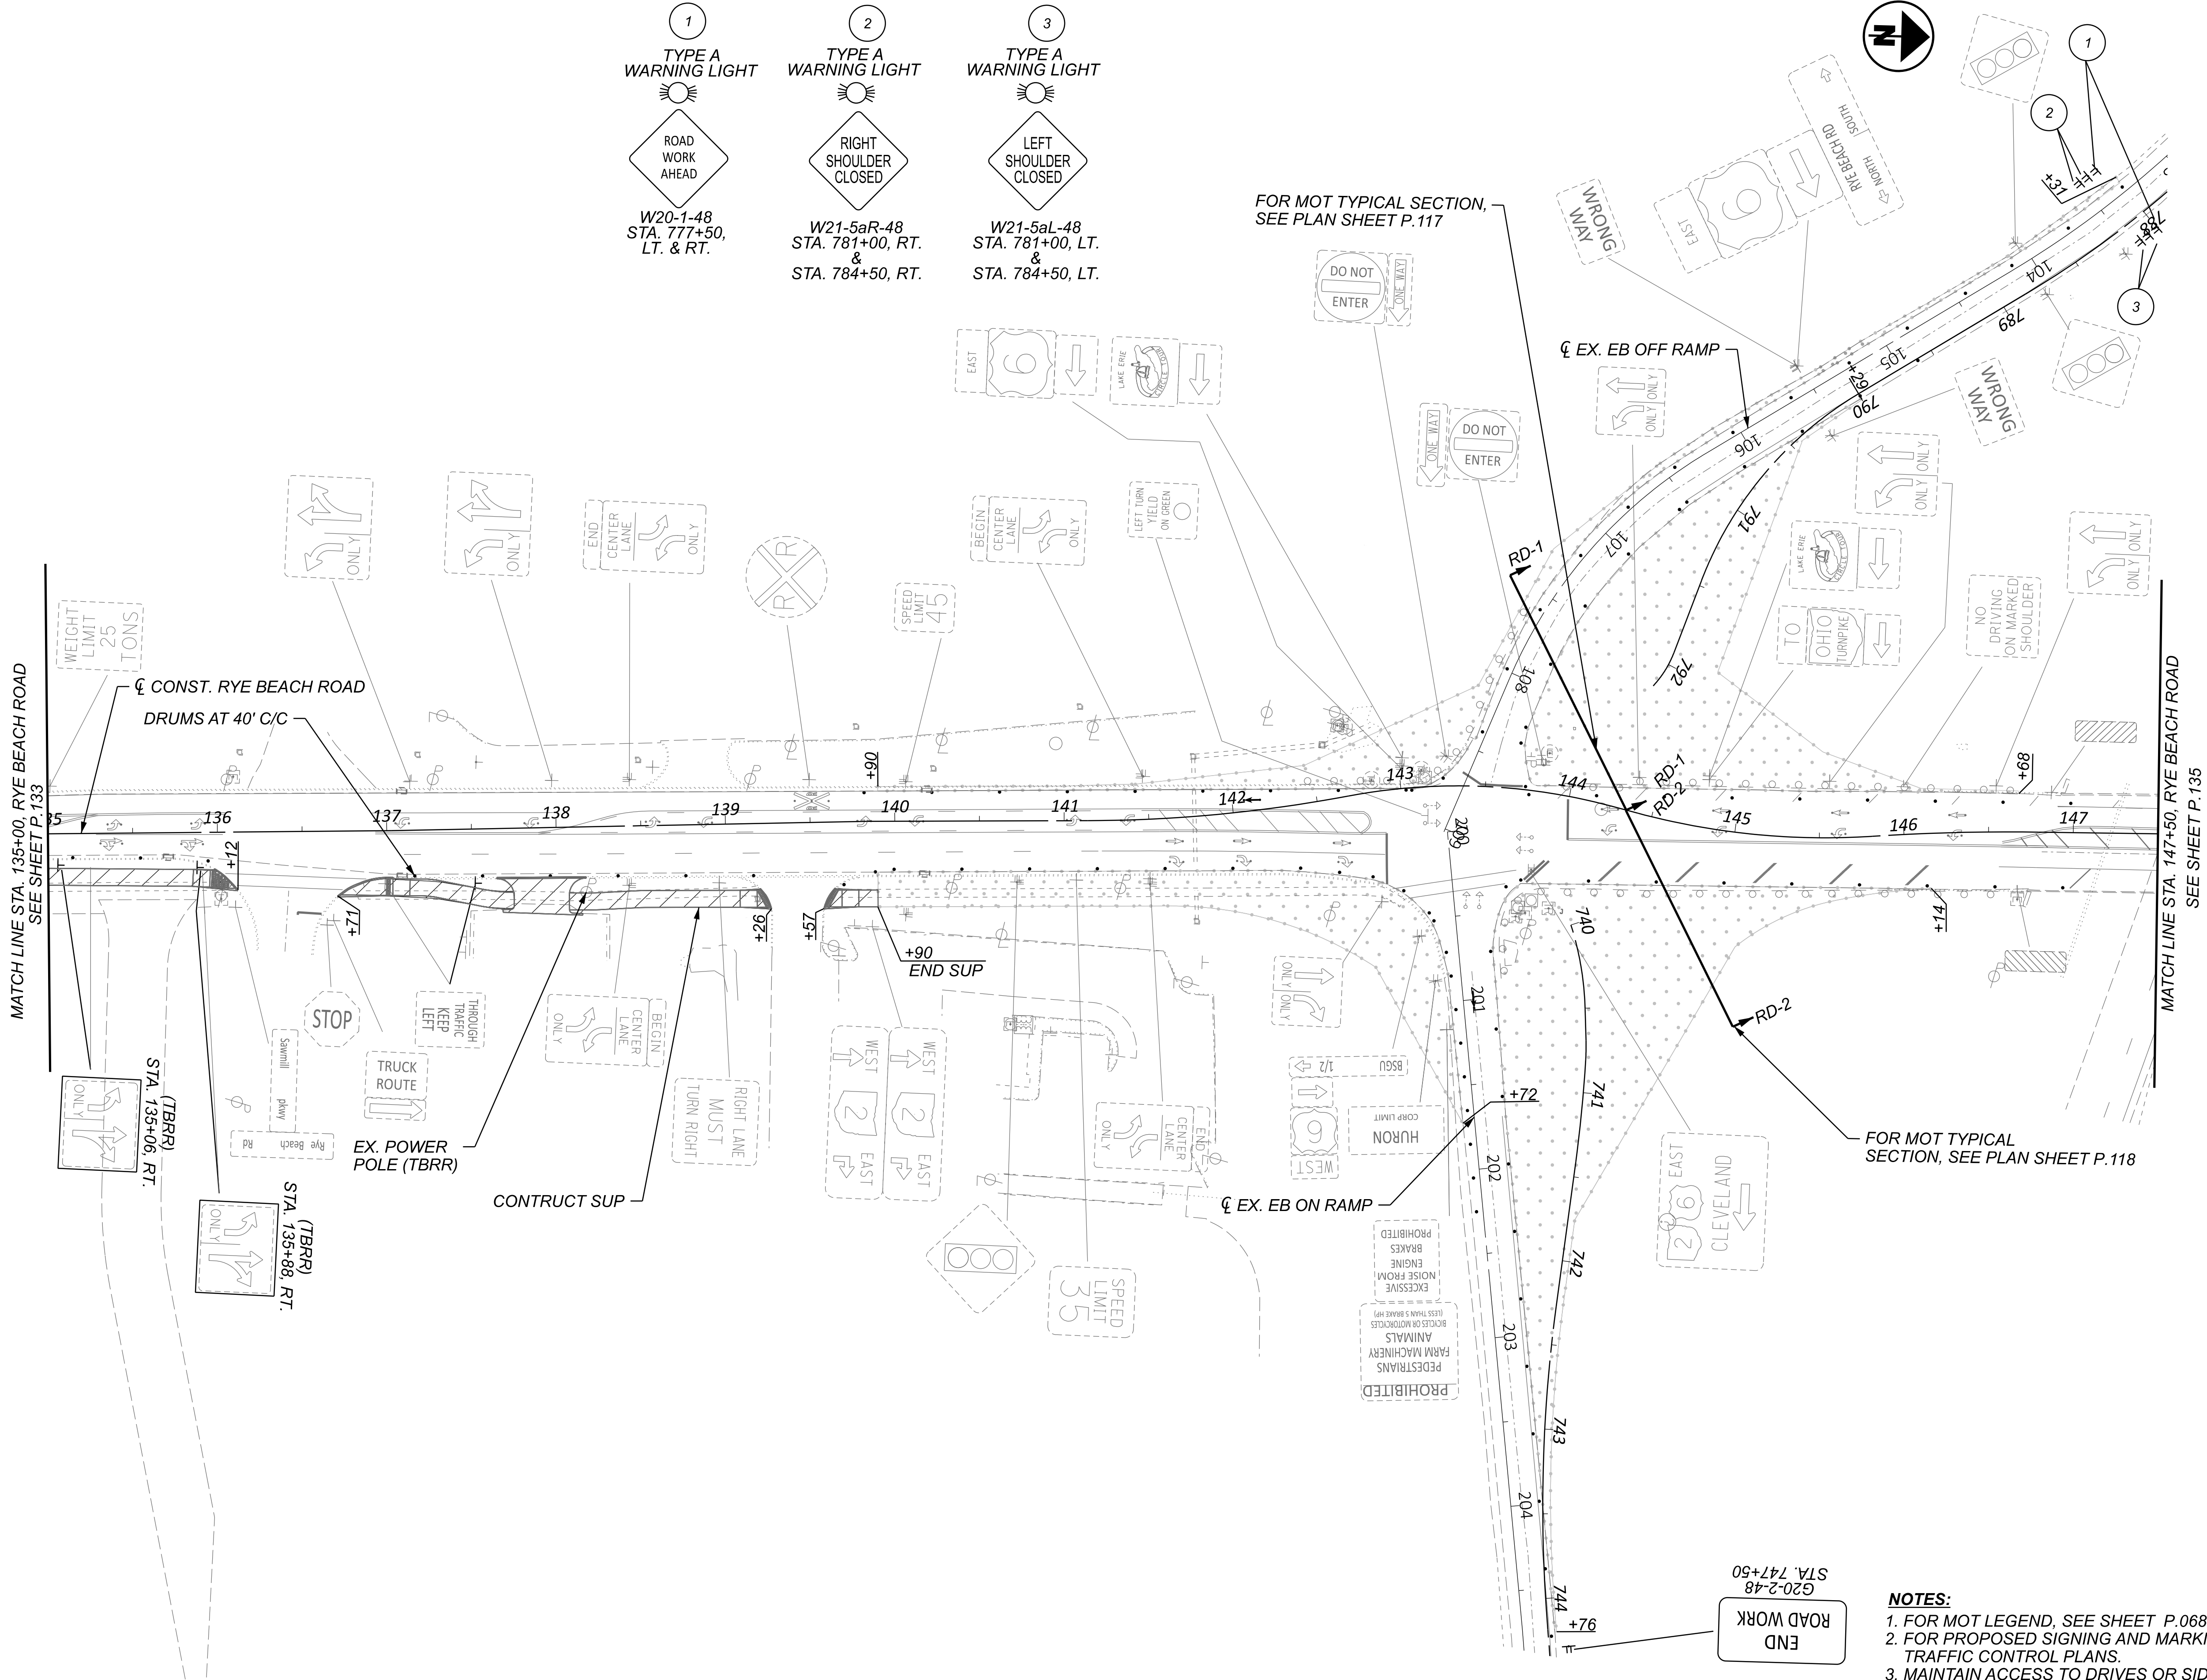

- 1

TYPE A
WARNING LIGHT

ROAD
WORK
AHEAD

W20-1-48
STA. 777+50,
LT. & RT.
- 2

TYPE A
WARNING LIGHT

RIGHT
SHOULDER
CLOSED

W21-5aR-48
STA. 781+00, RT.
&
STA. 784+50, RT.
- 3


TYPE A
WARNING LIGHT

LEFT
SHOULDER
CLOSED


W21-5aL-48
STA. 781+00, LT.
&
STA. 784+50, LT.

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
RYE BEACH ROAD - STA. 135+00.00 TO STA. 147+50.00

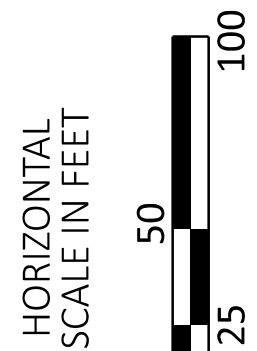

DESIGN AGENCY	
TRANSYSTEMS	
400 W. WATKINSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.137	TOTAL 782

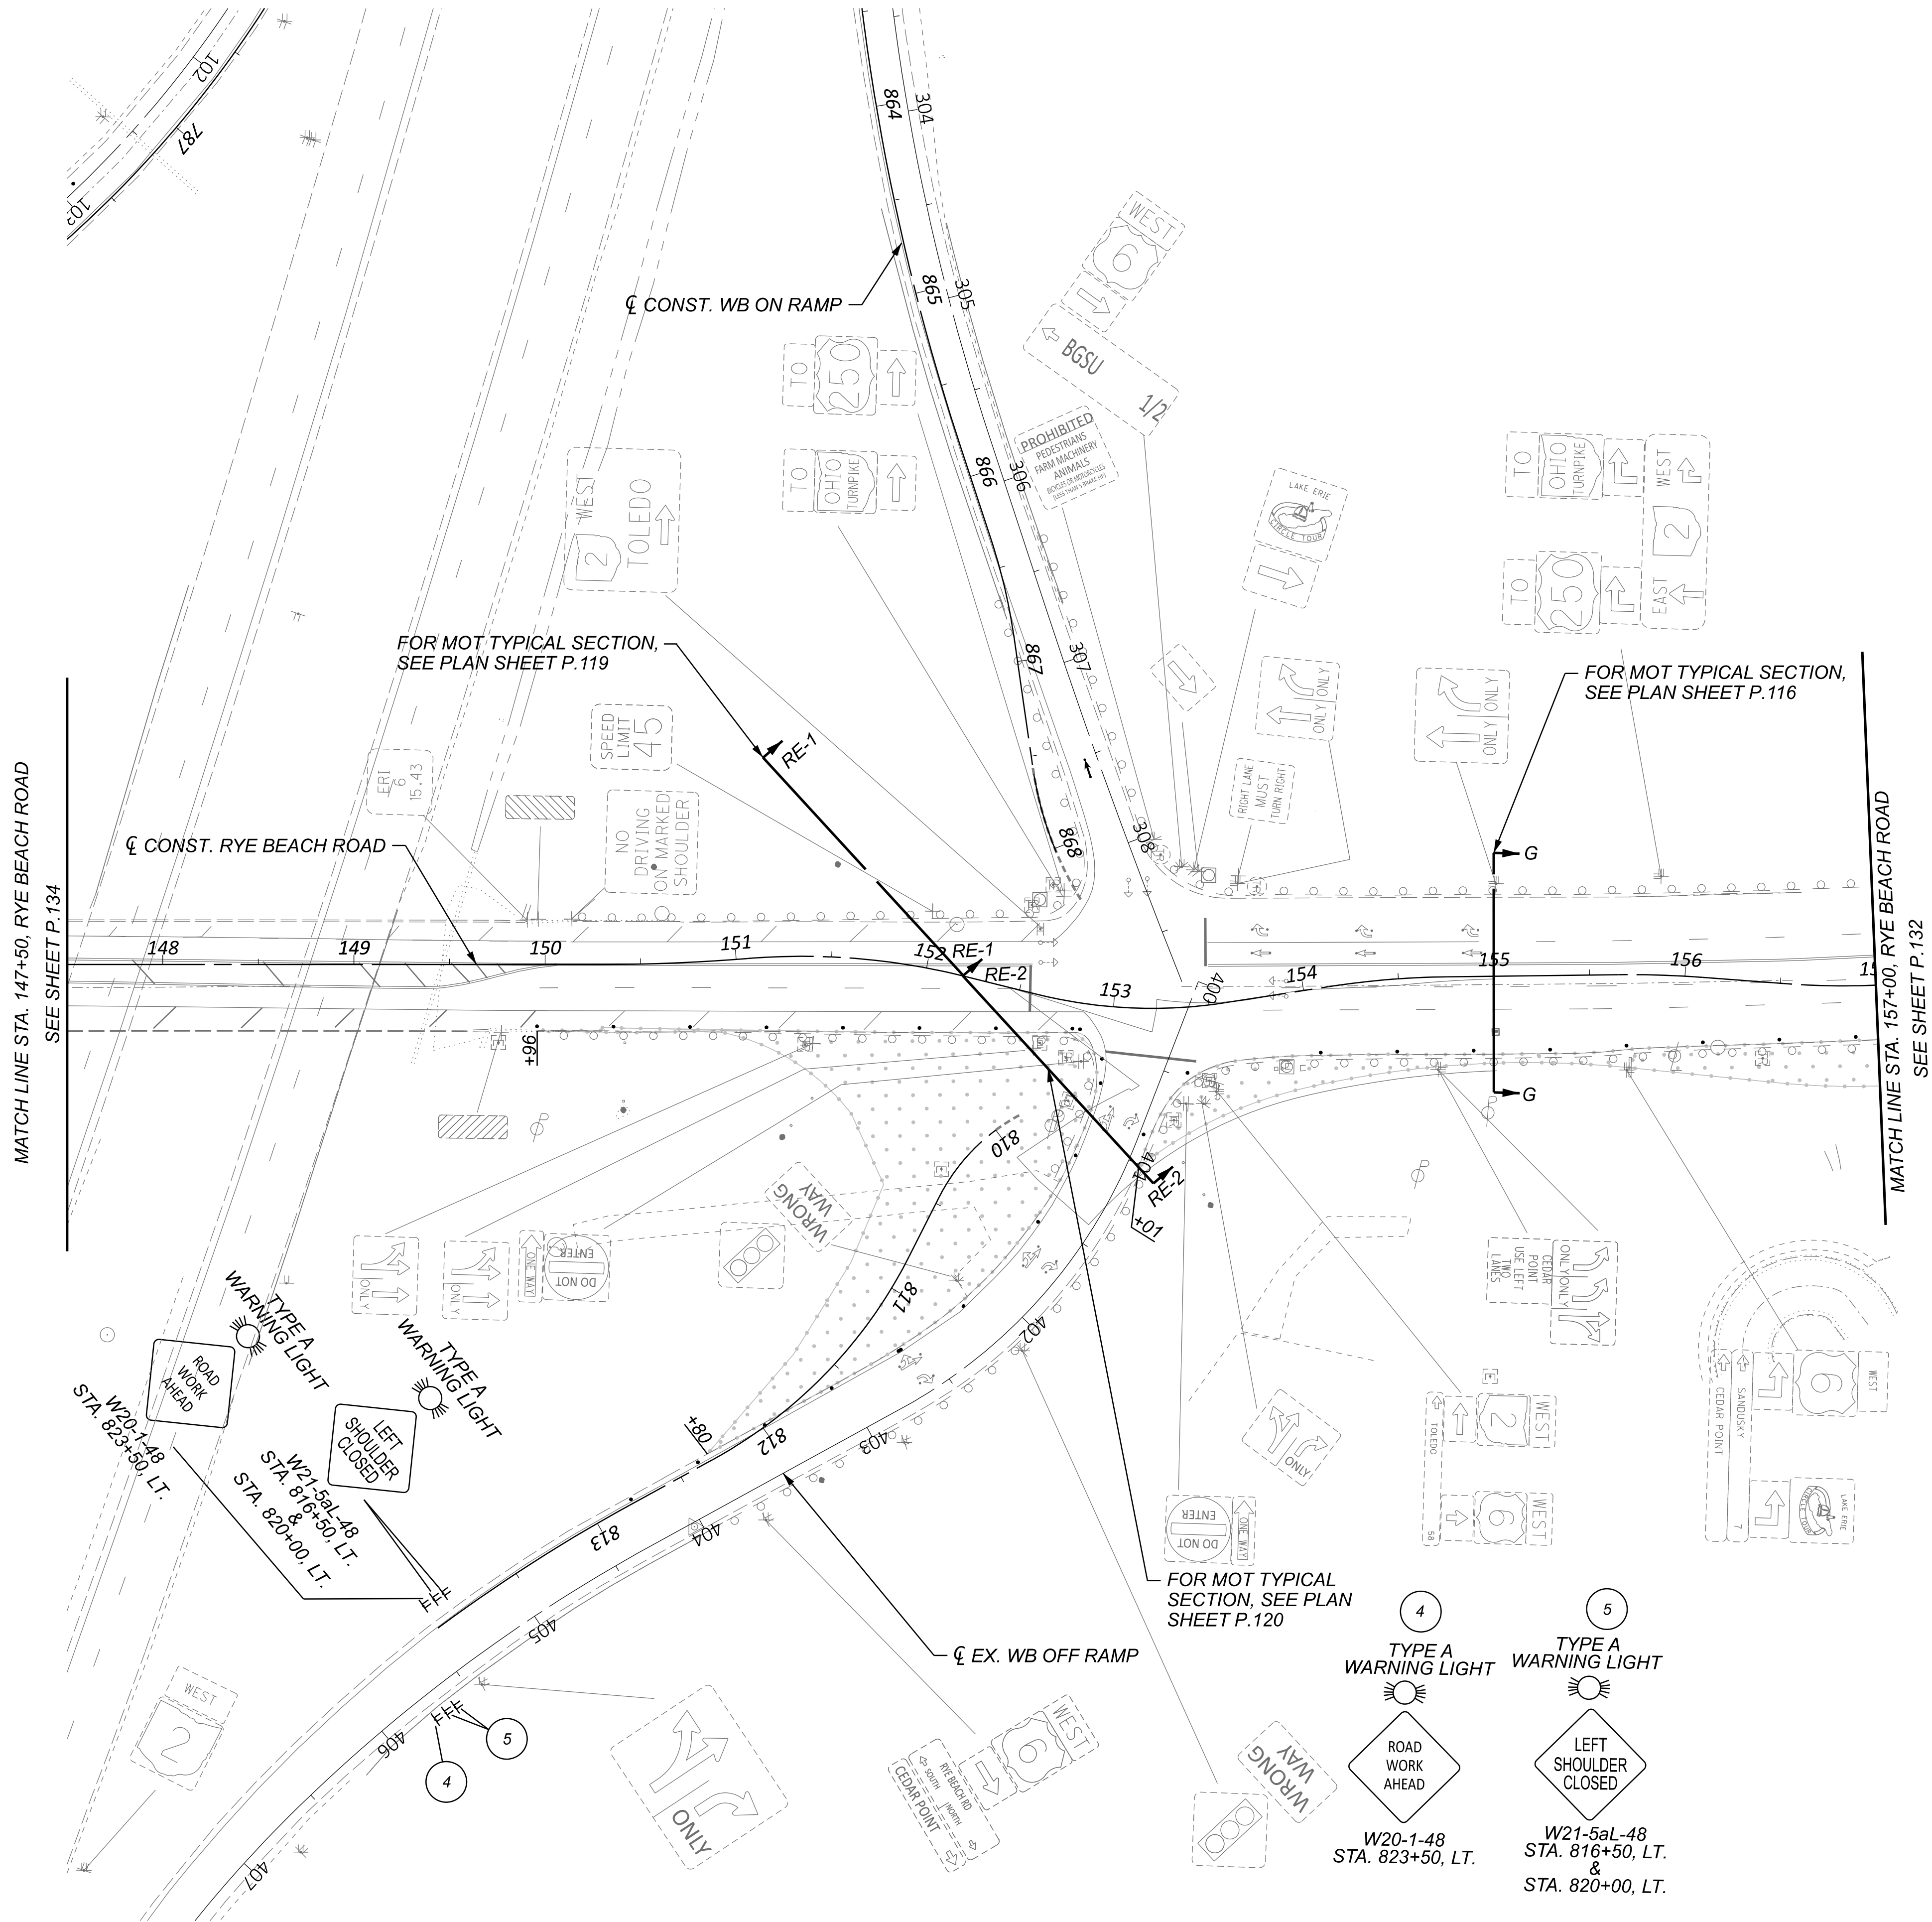




- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.



MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
RYE BEACH ROAD - STA. 147+50.00 TO STA. 157+00.00

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.138	TOTAL 782

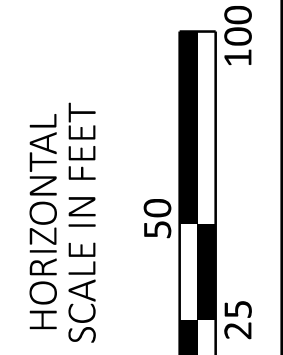

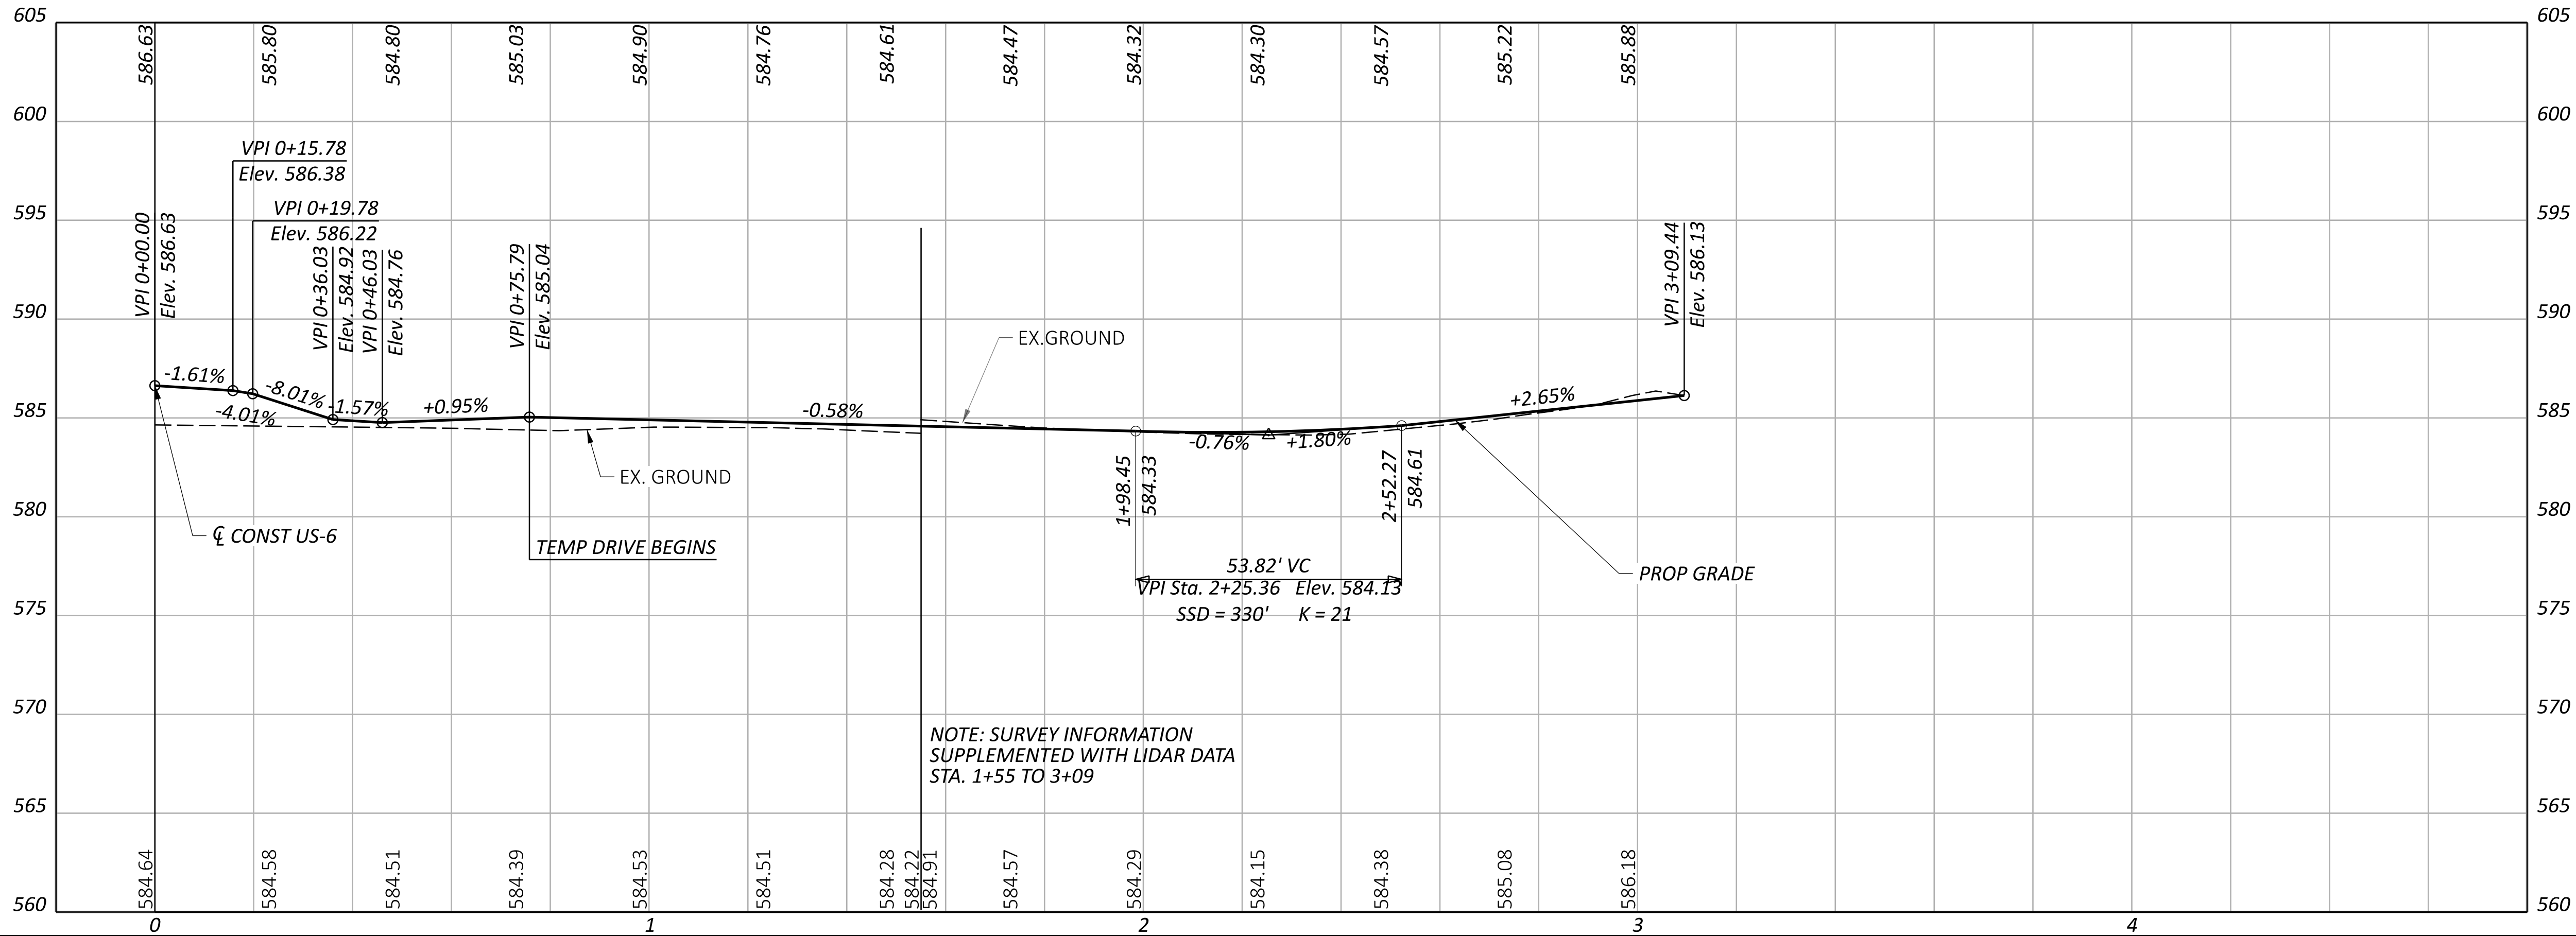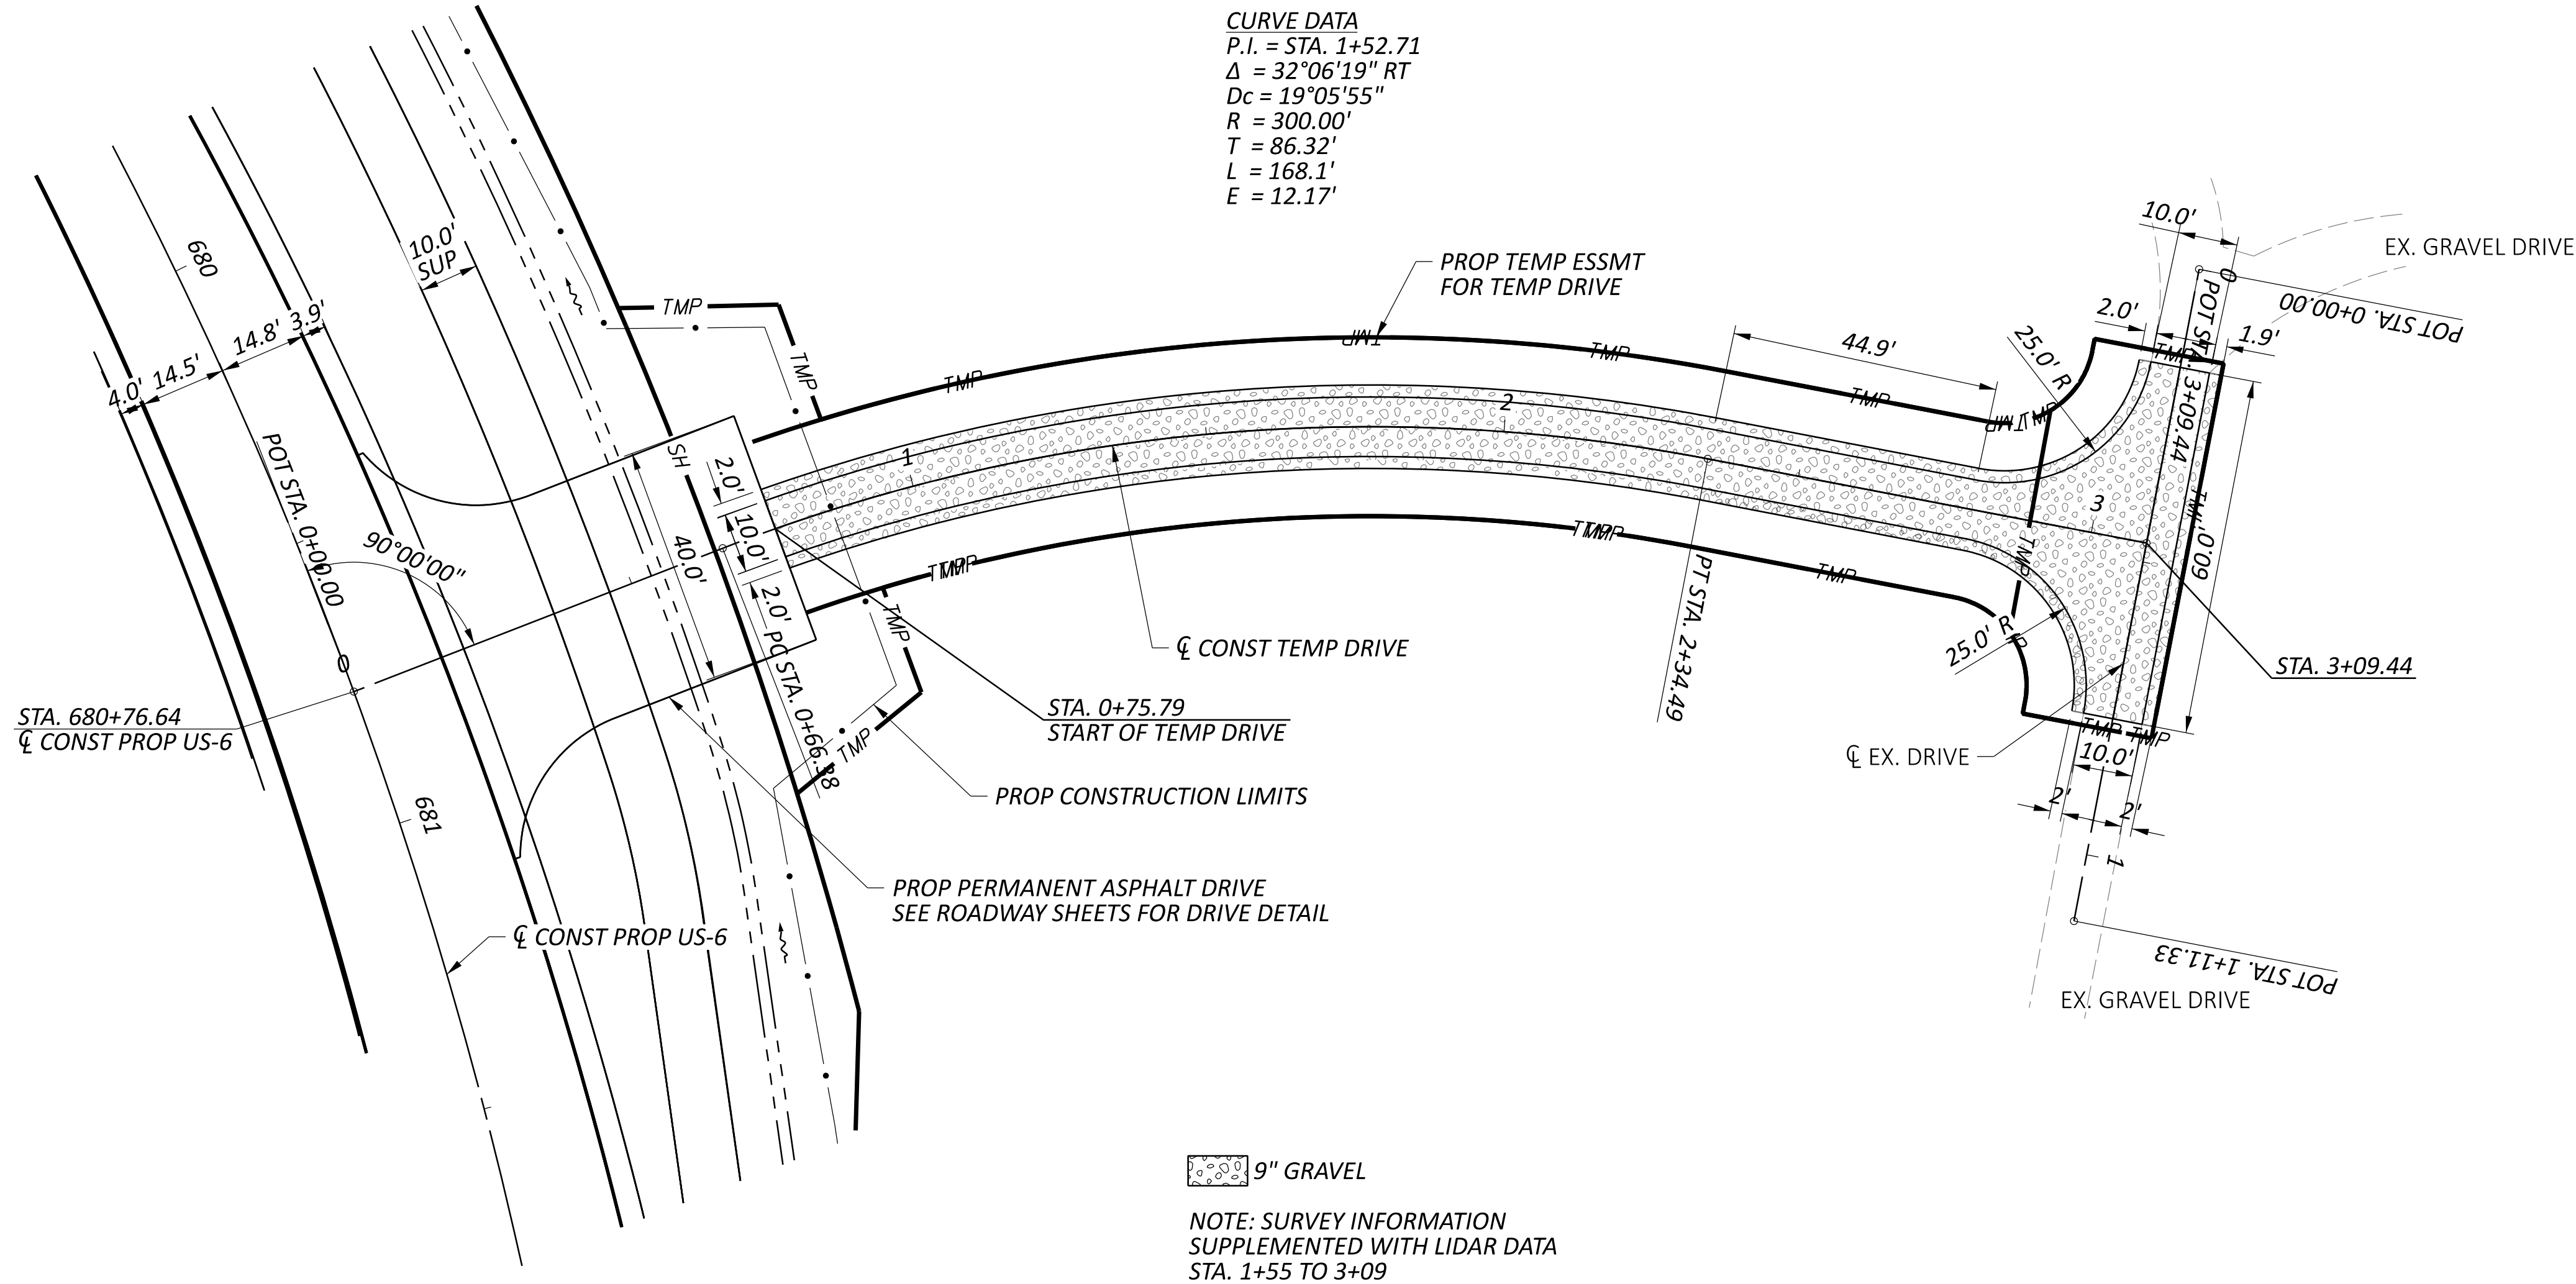

ERI-US 0006-CONNECTIVITY CORRIDOR



HORIZONTAL
SCALE IN FEET



0 20 40


MOT PRE-PHASE - TEMPORARY DRIVEWAY PLAN AND PROFILE
US 6 - STA. 668+45.85

DESIGN AGENCY

TRANSYSTEMS

400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
FACC	
REVIEWER	
XXX MM-DD-YY	
PROJECT ID	
116570	
SHEET	TOTAL
P.0	0

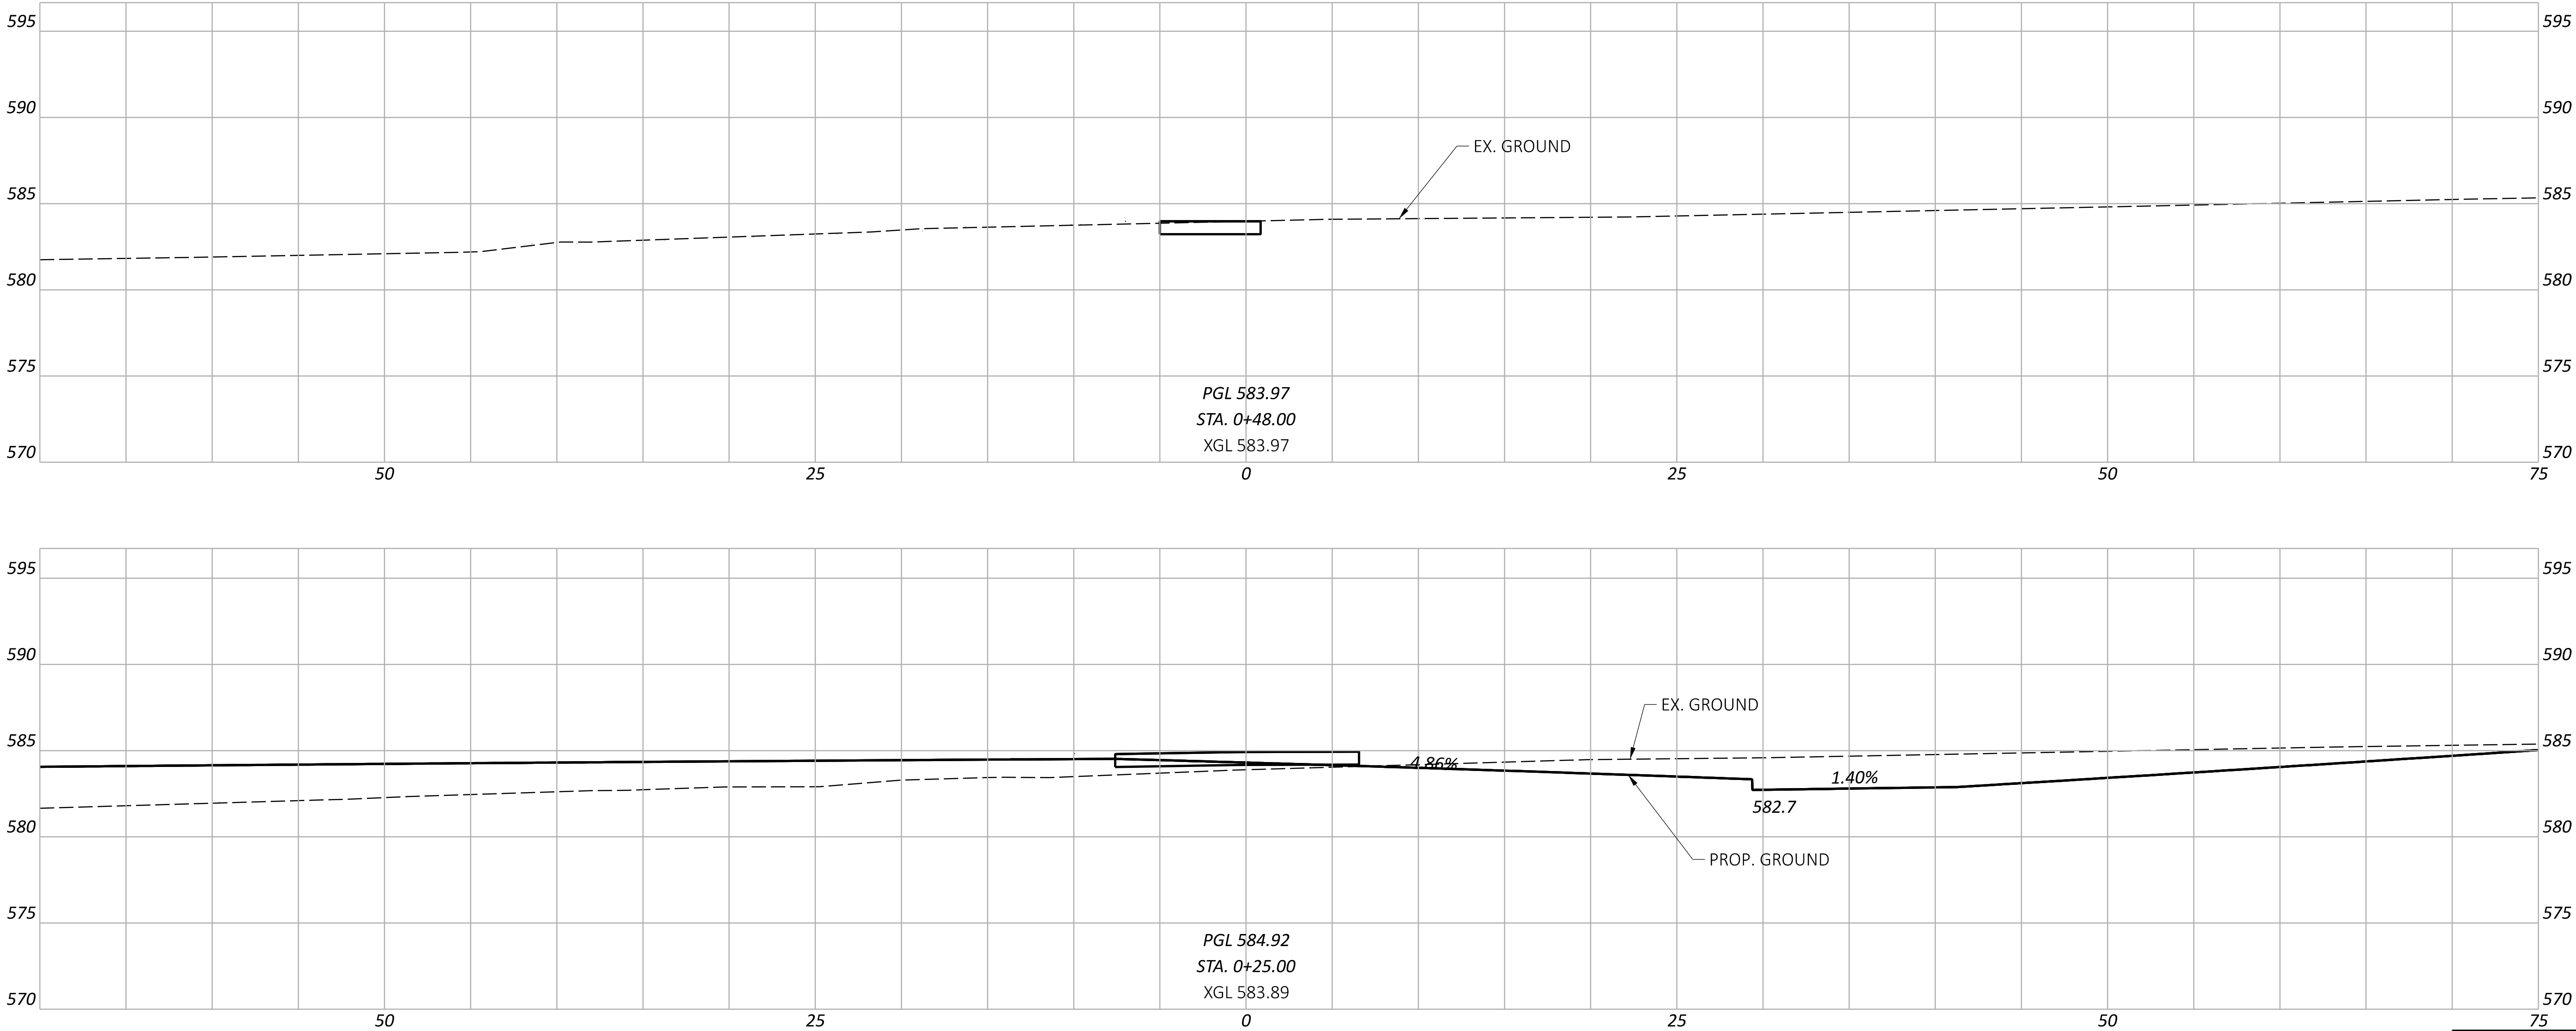




Sheet Totals		
Seeding	Cut	Fill



PROJECT ID	
SHEET	TOTAL
P.0	0

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
FACC


REVIEWER
XXX MM/DD/YY

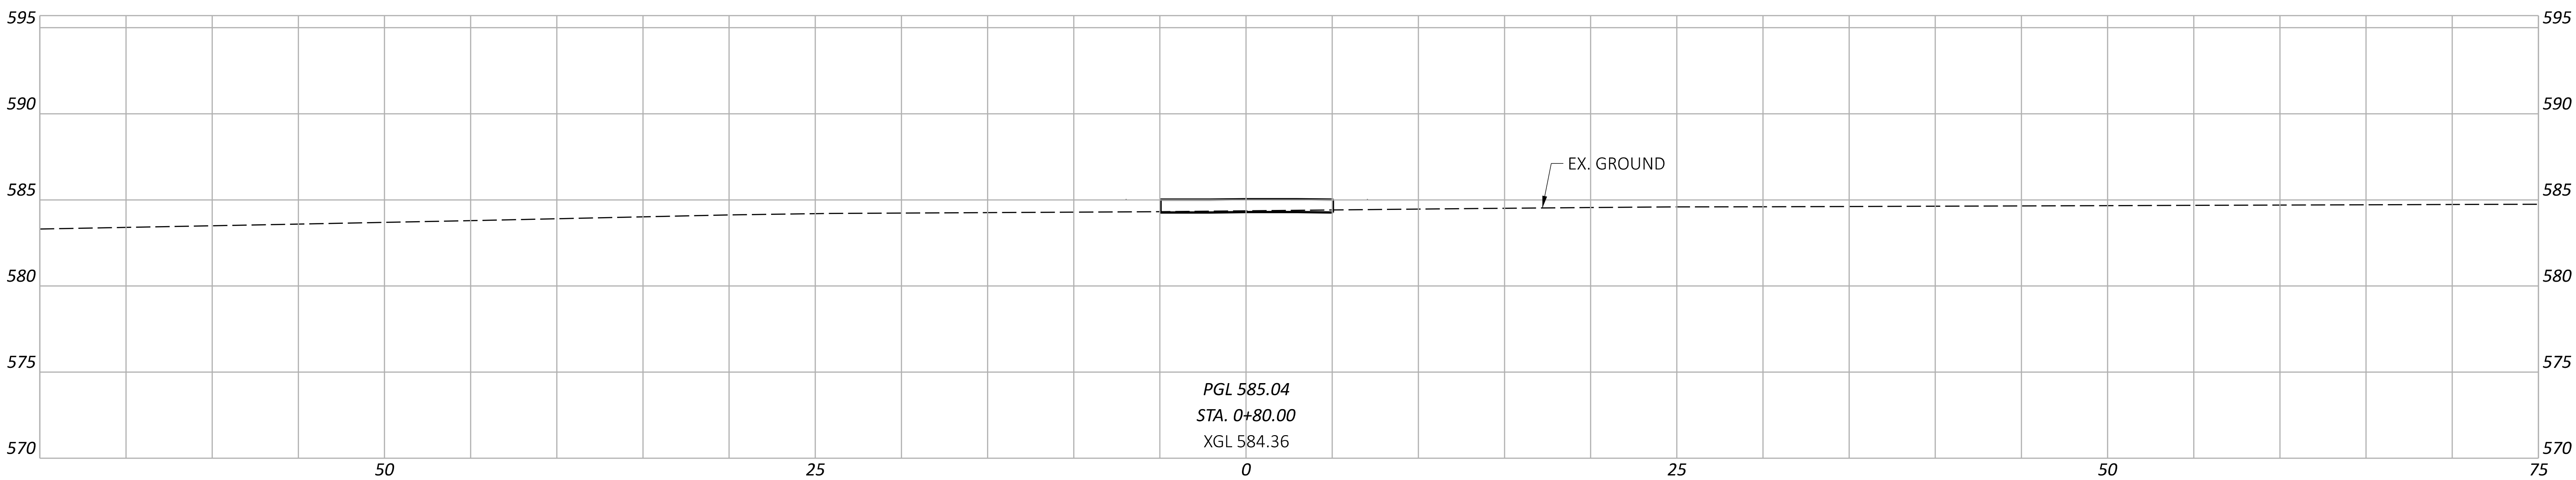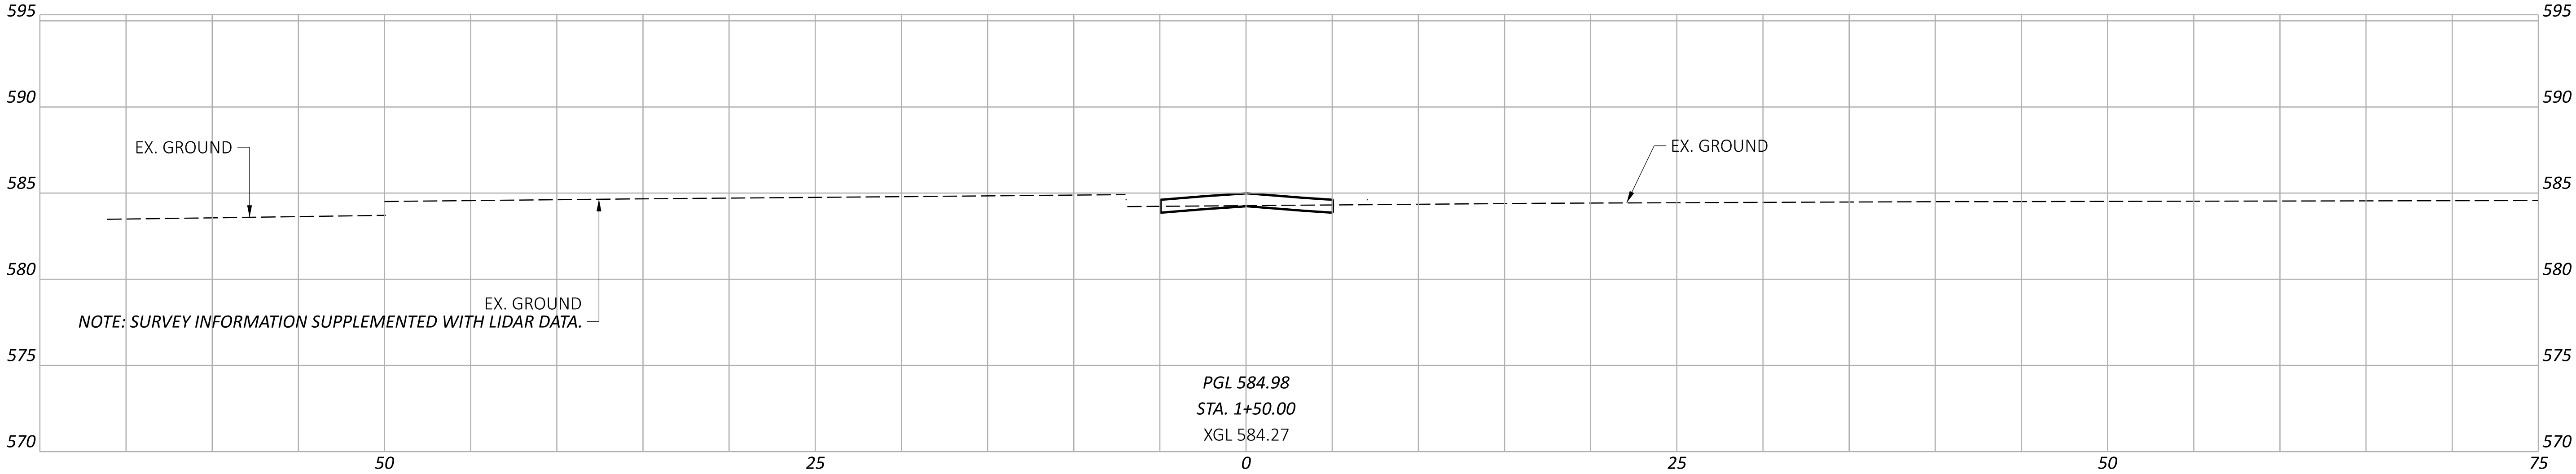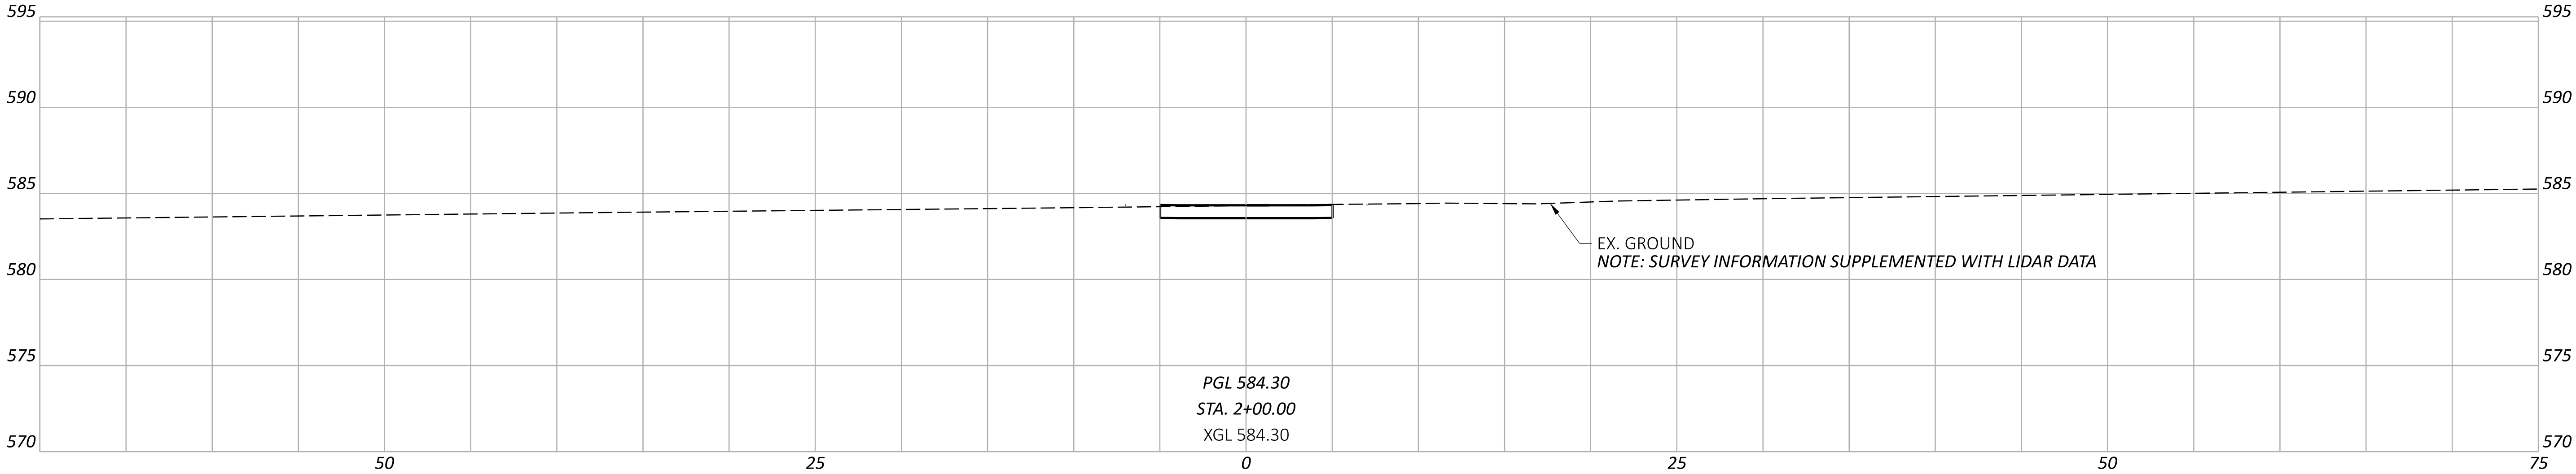

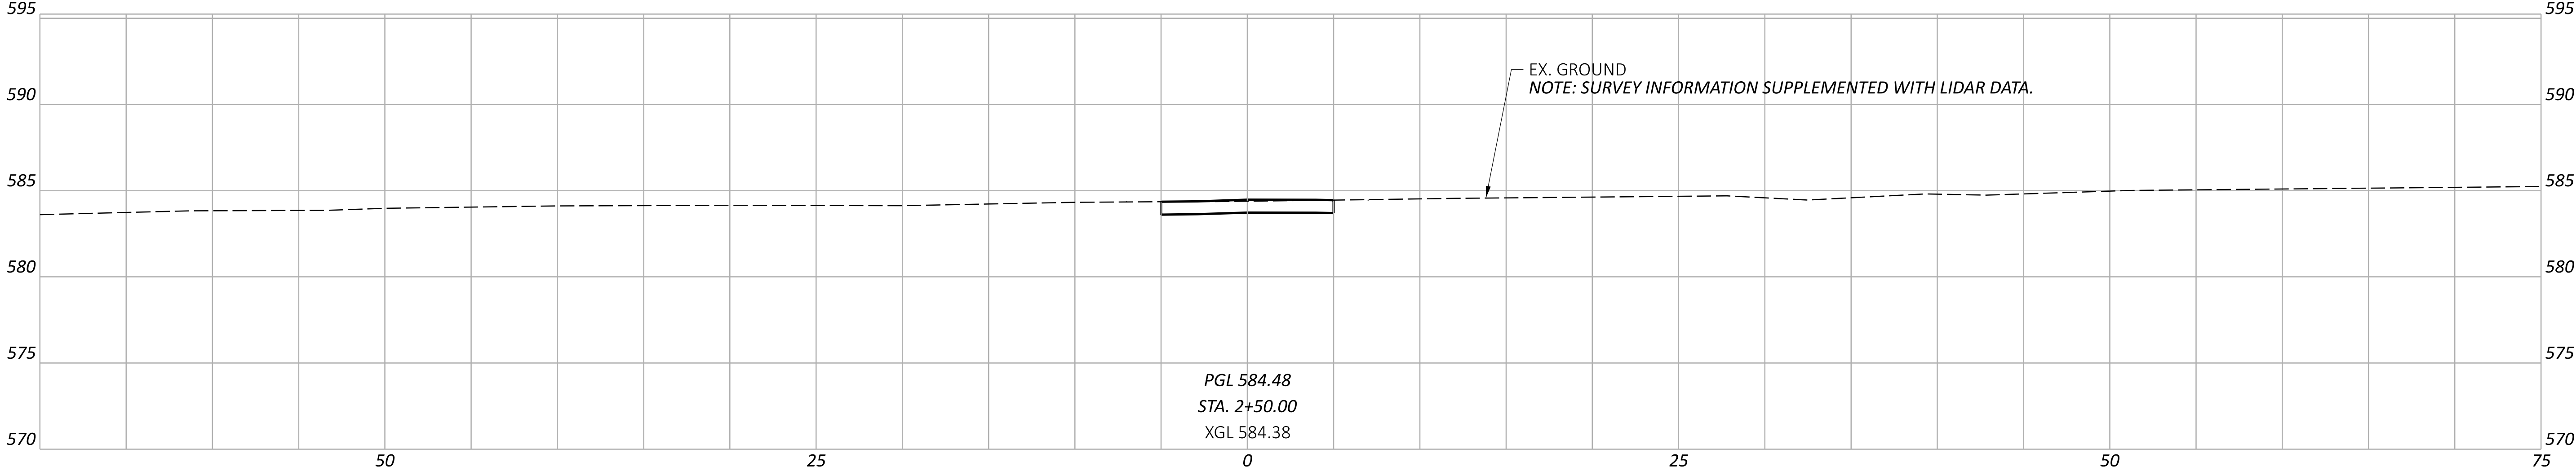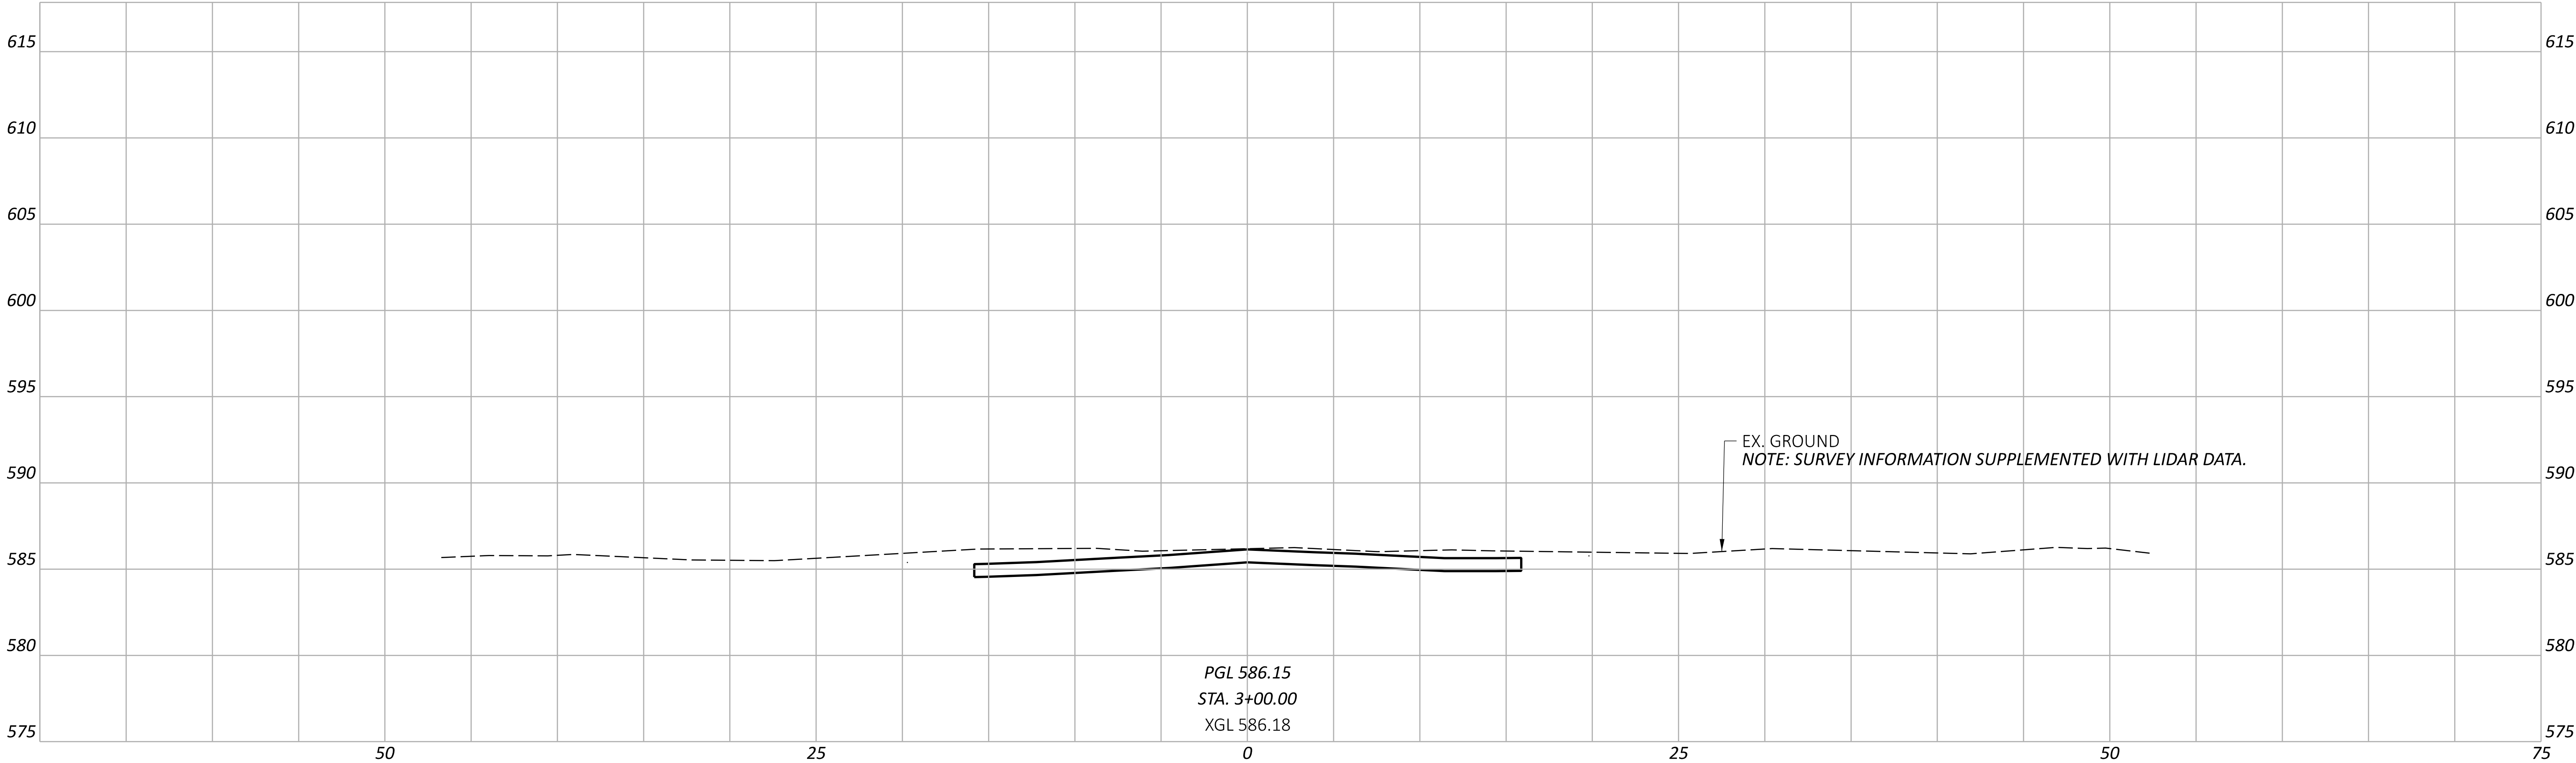


ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 1 - Plan 1-2 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:21:35 PM USER: ssadusei
pw:\ohiodot-pw\entley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\Erie\116570\402-Engineering_TransSystems\MOT\Sheets\116570_MP001_CY2026.dgn

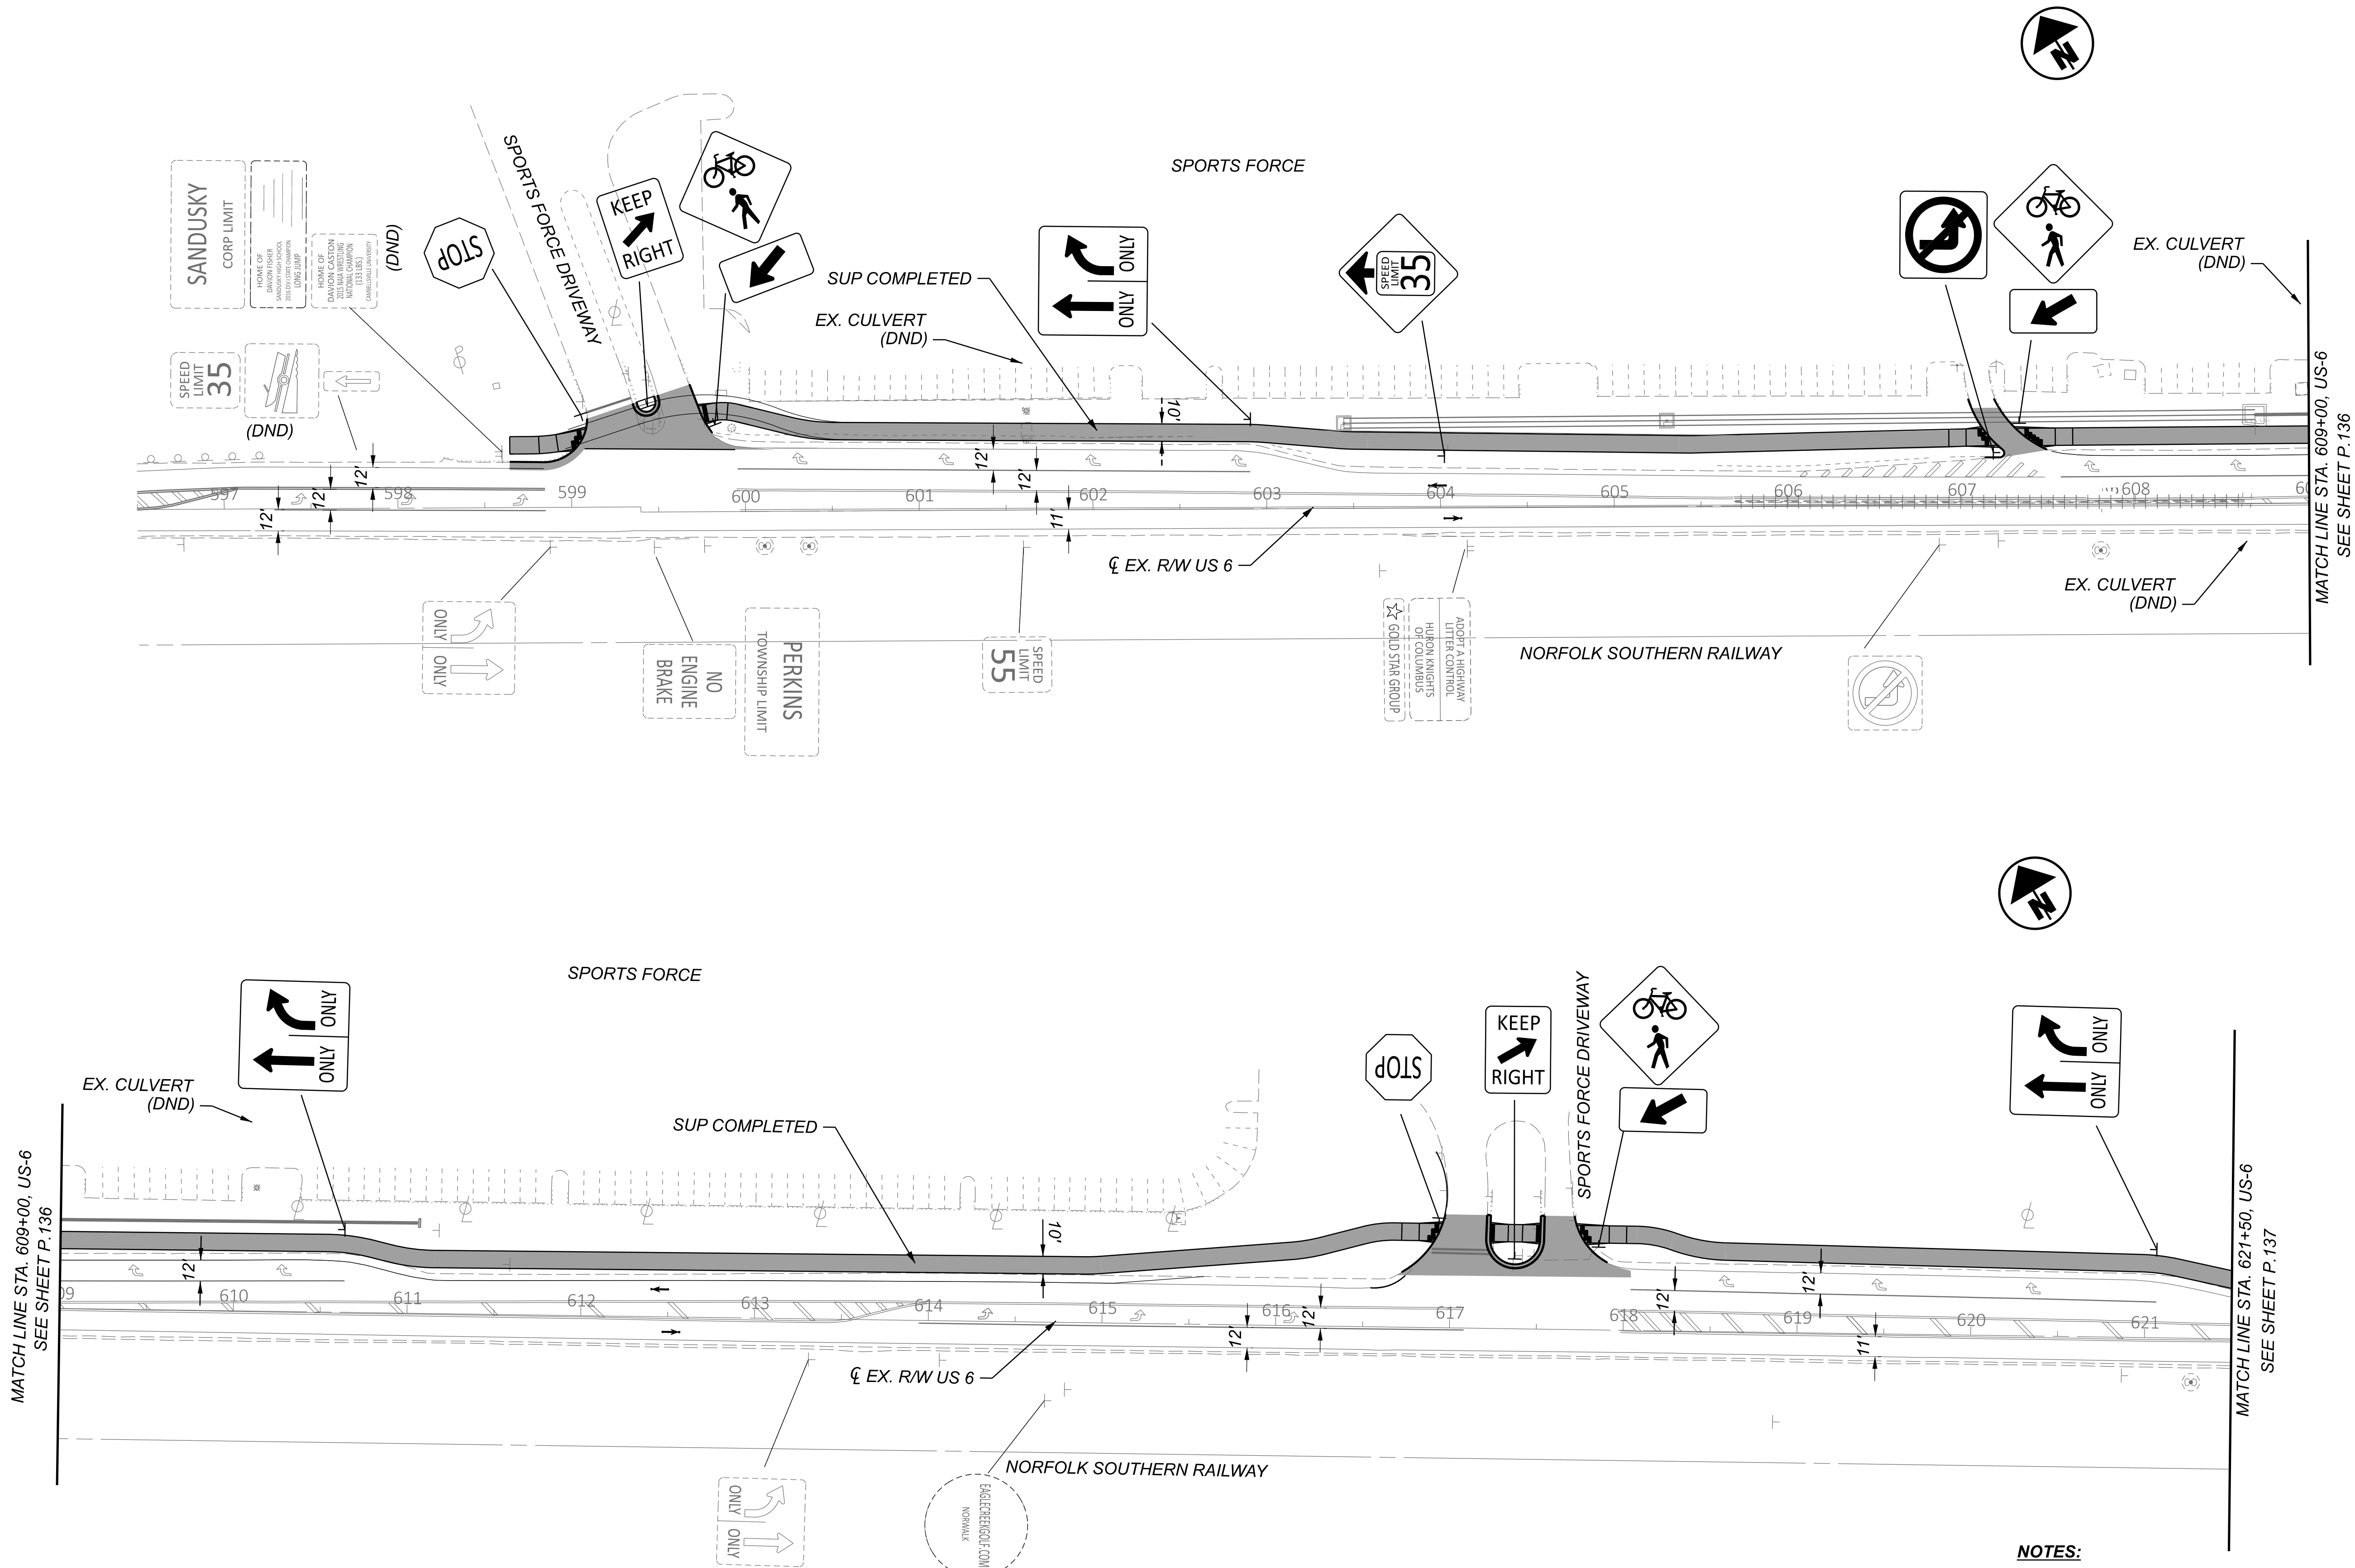

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - BEGIN PROJECT TO STA. 621+50



DESIGN AGENCY	
TRANSYSTEMS	
400 W. WATSONWIDE BLVD., STE. 225	
COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.139	TOTAL 782

ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP_1 - Plan 3-4 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:21:39 PM USER: ssadusei
 pw://vhiodot-pw.bentley.com:vhiodot-pw-02/Documents/01 Active Projects/District 03/Erle/116570/402-Engineering_TransSystems/MOT/Sheets/116570_MP001_CV2026.dgn

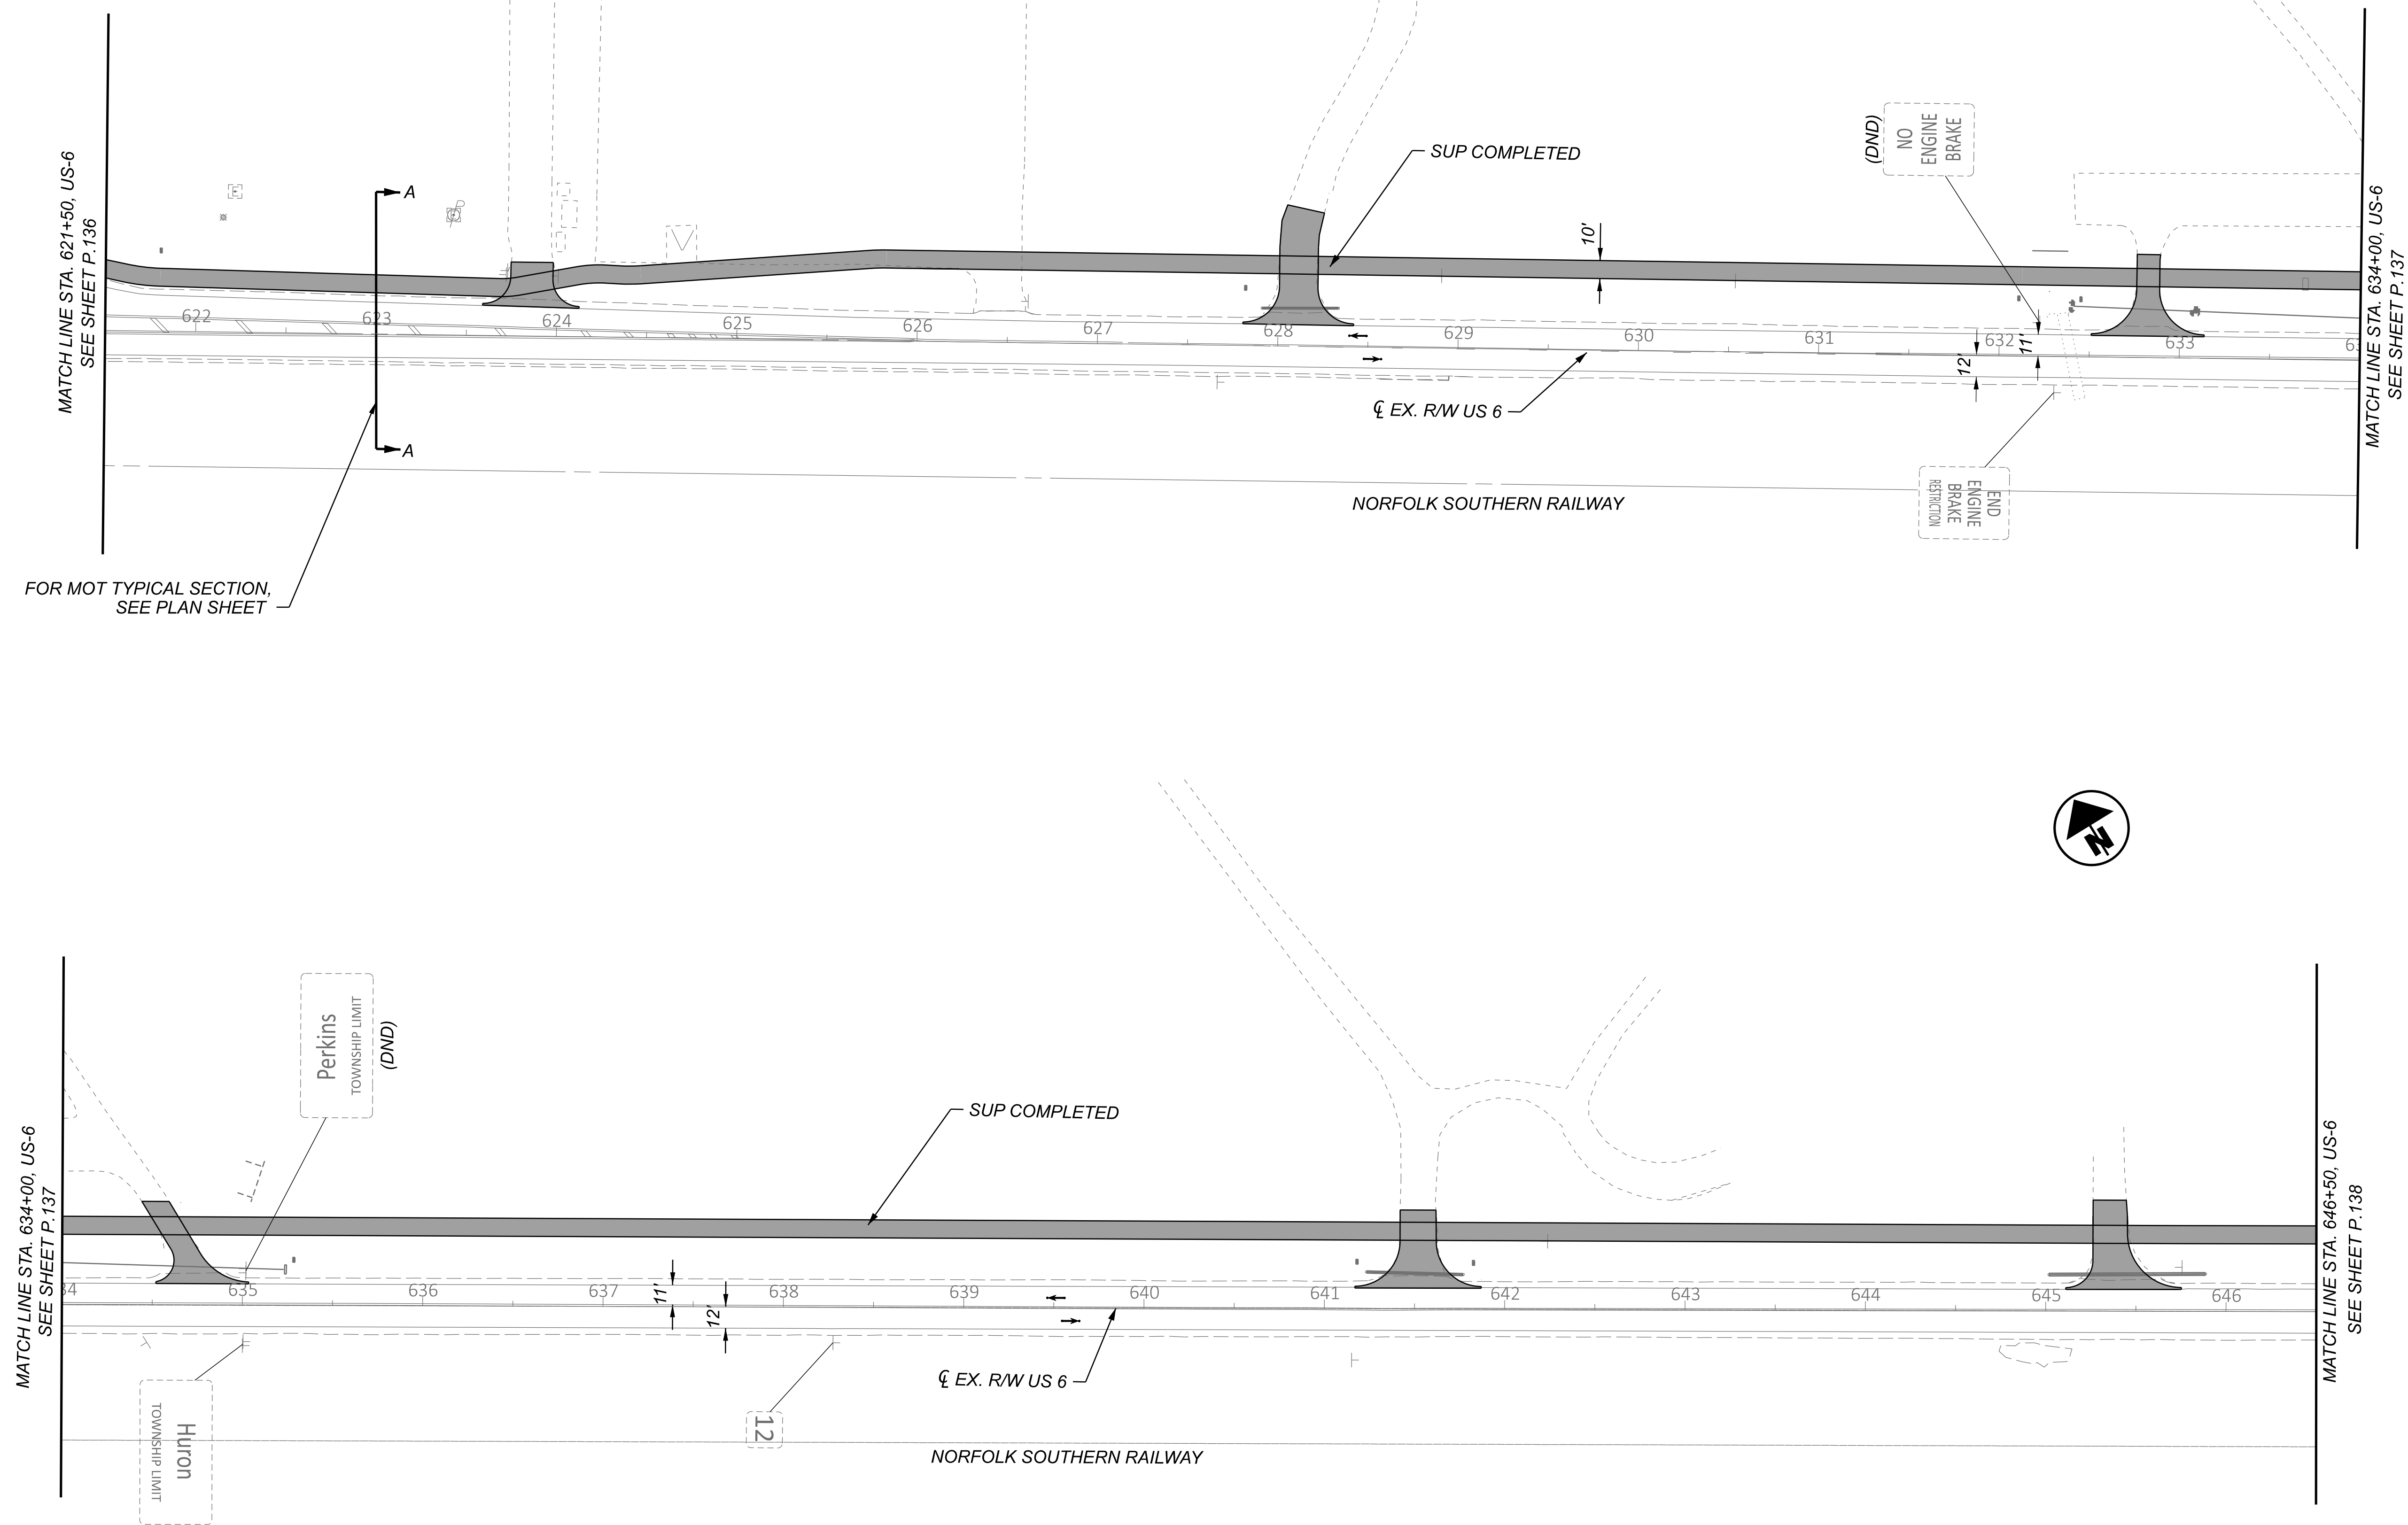

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068 .
2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. FOR SECTION A-A, SEE SHEET P.109 .
4. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALLTIMES. USE FLAGGING OPERATION AS NECESSARY.

DESIGN AGENCY

TRANSYSTEMS

400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID
116570

SHEET	TOTAL
-------	-------

P.140 | 7


--	--	--

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 621+50.00 TO STA. 646+50.00

HORIZONTAL
SCALE IN FEET




0 50

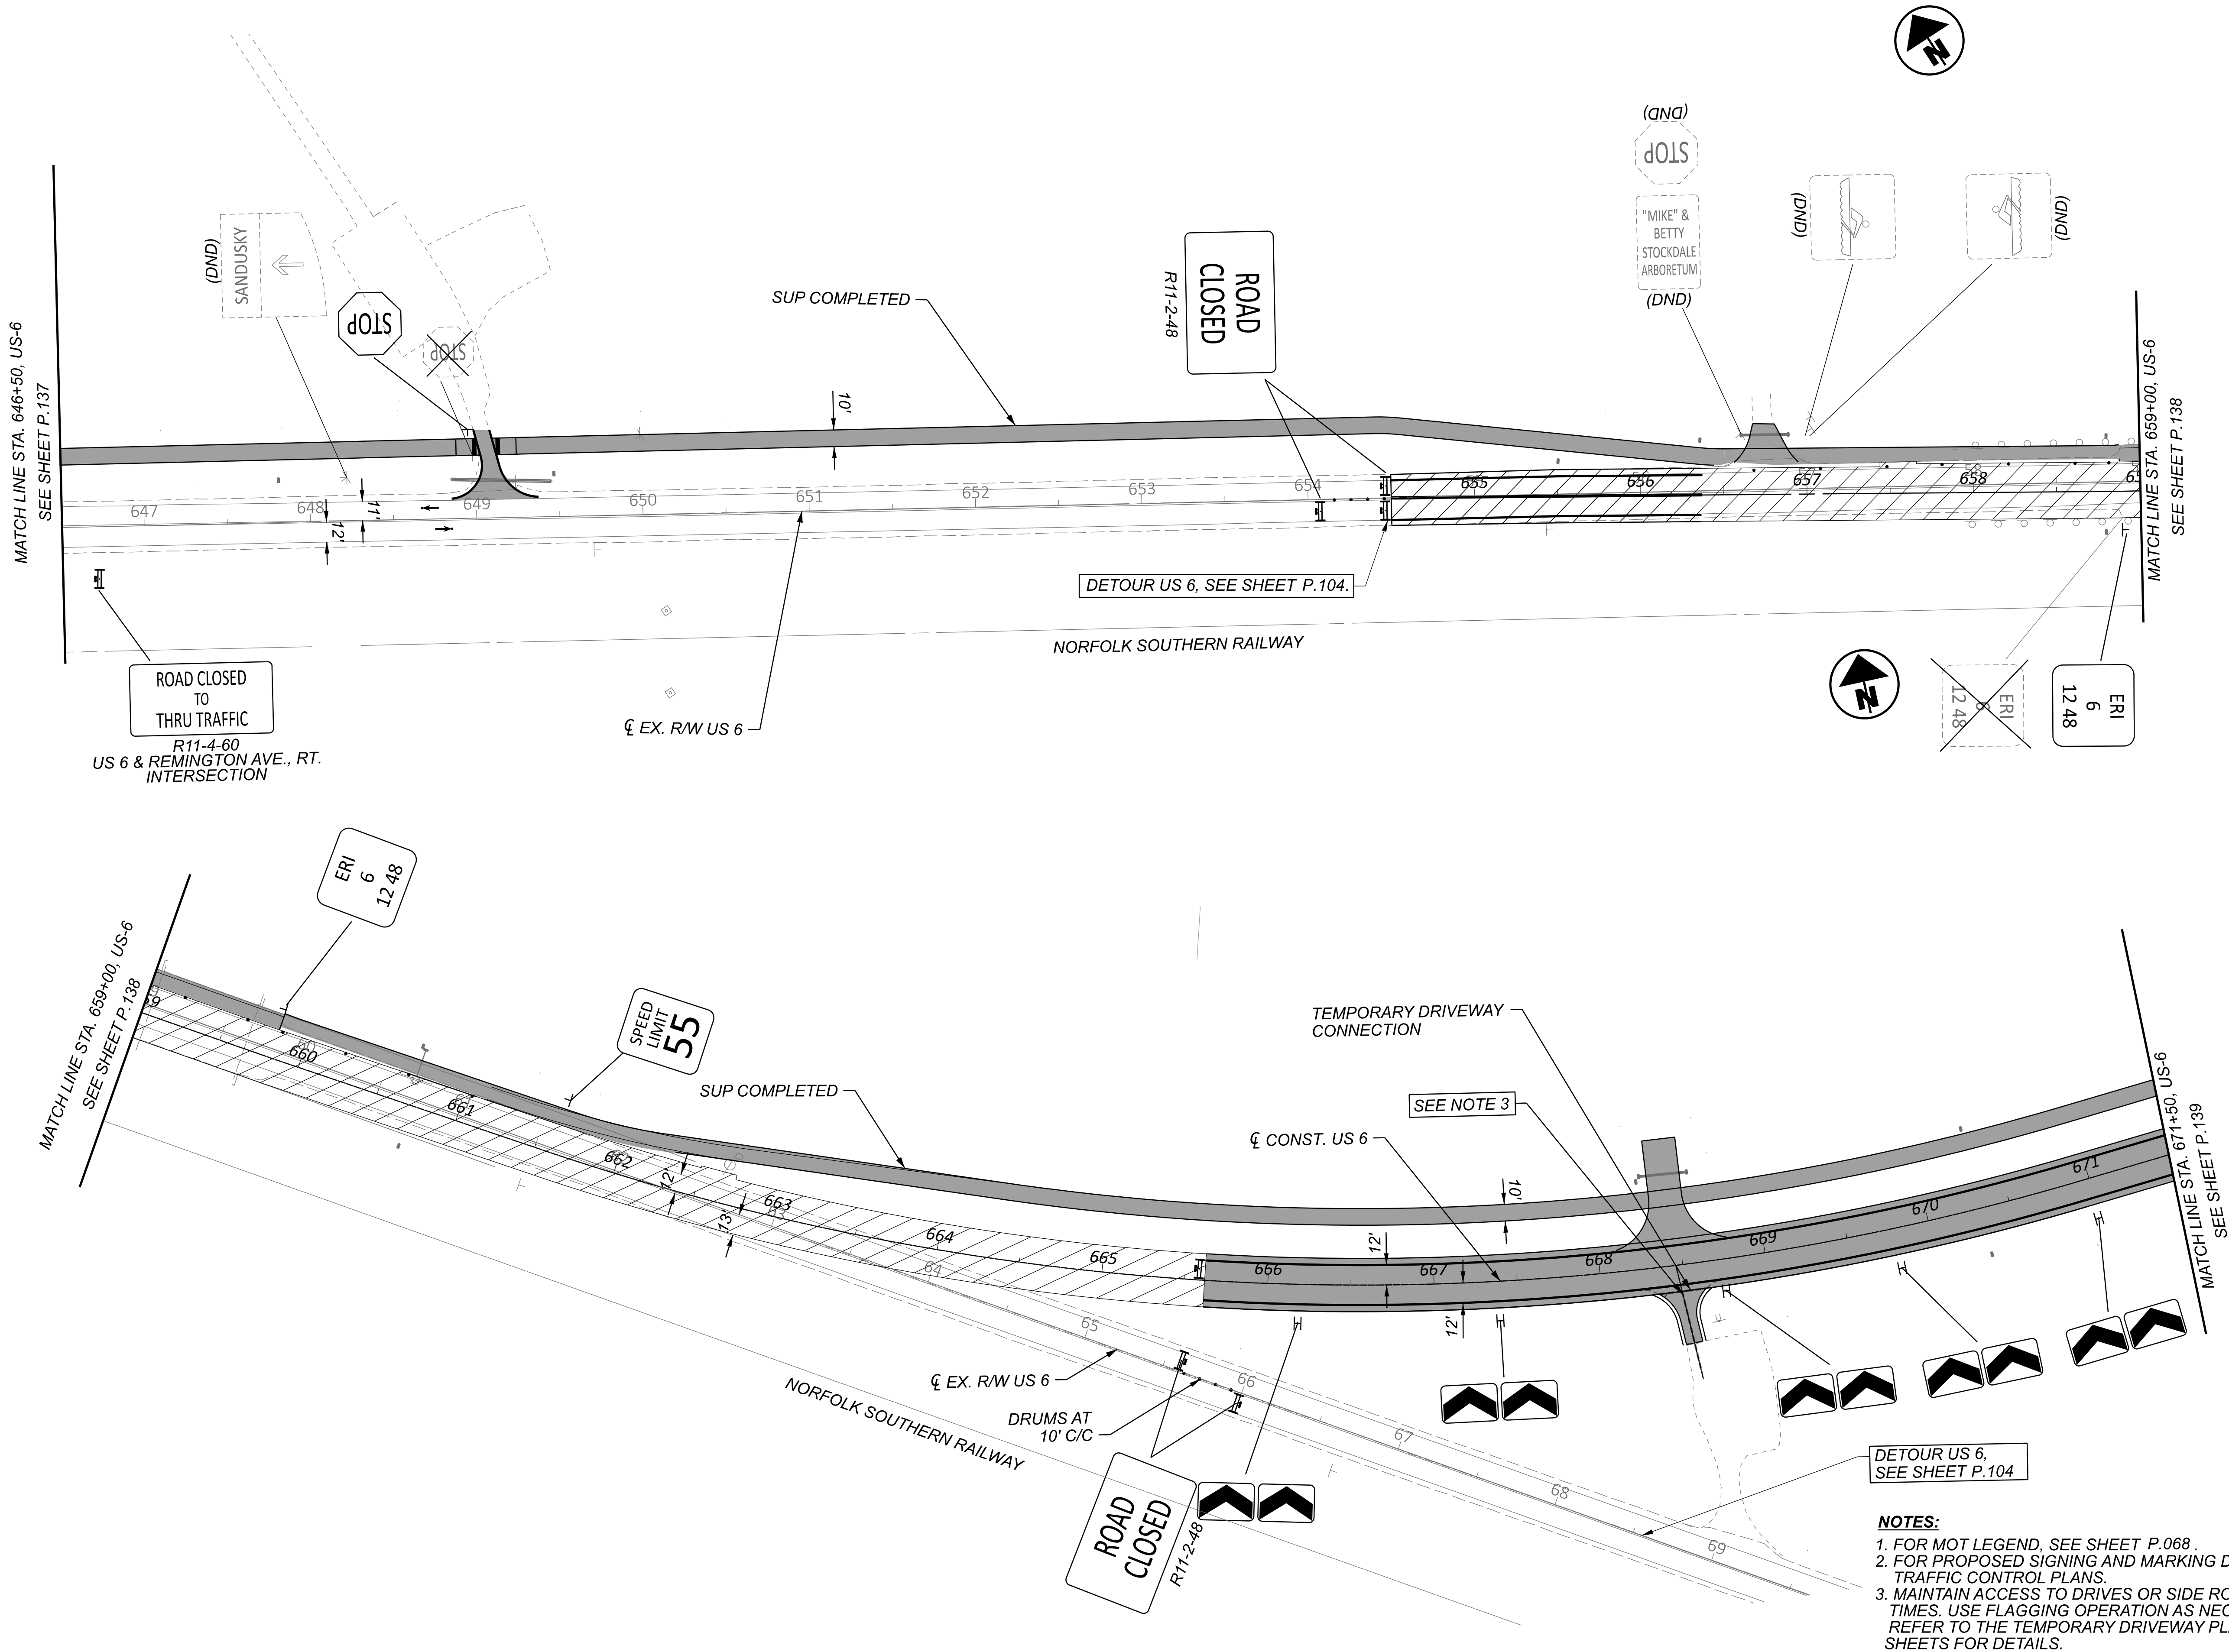


NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 646+50.00 TO STA. 671+50.00


DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.141	782

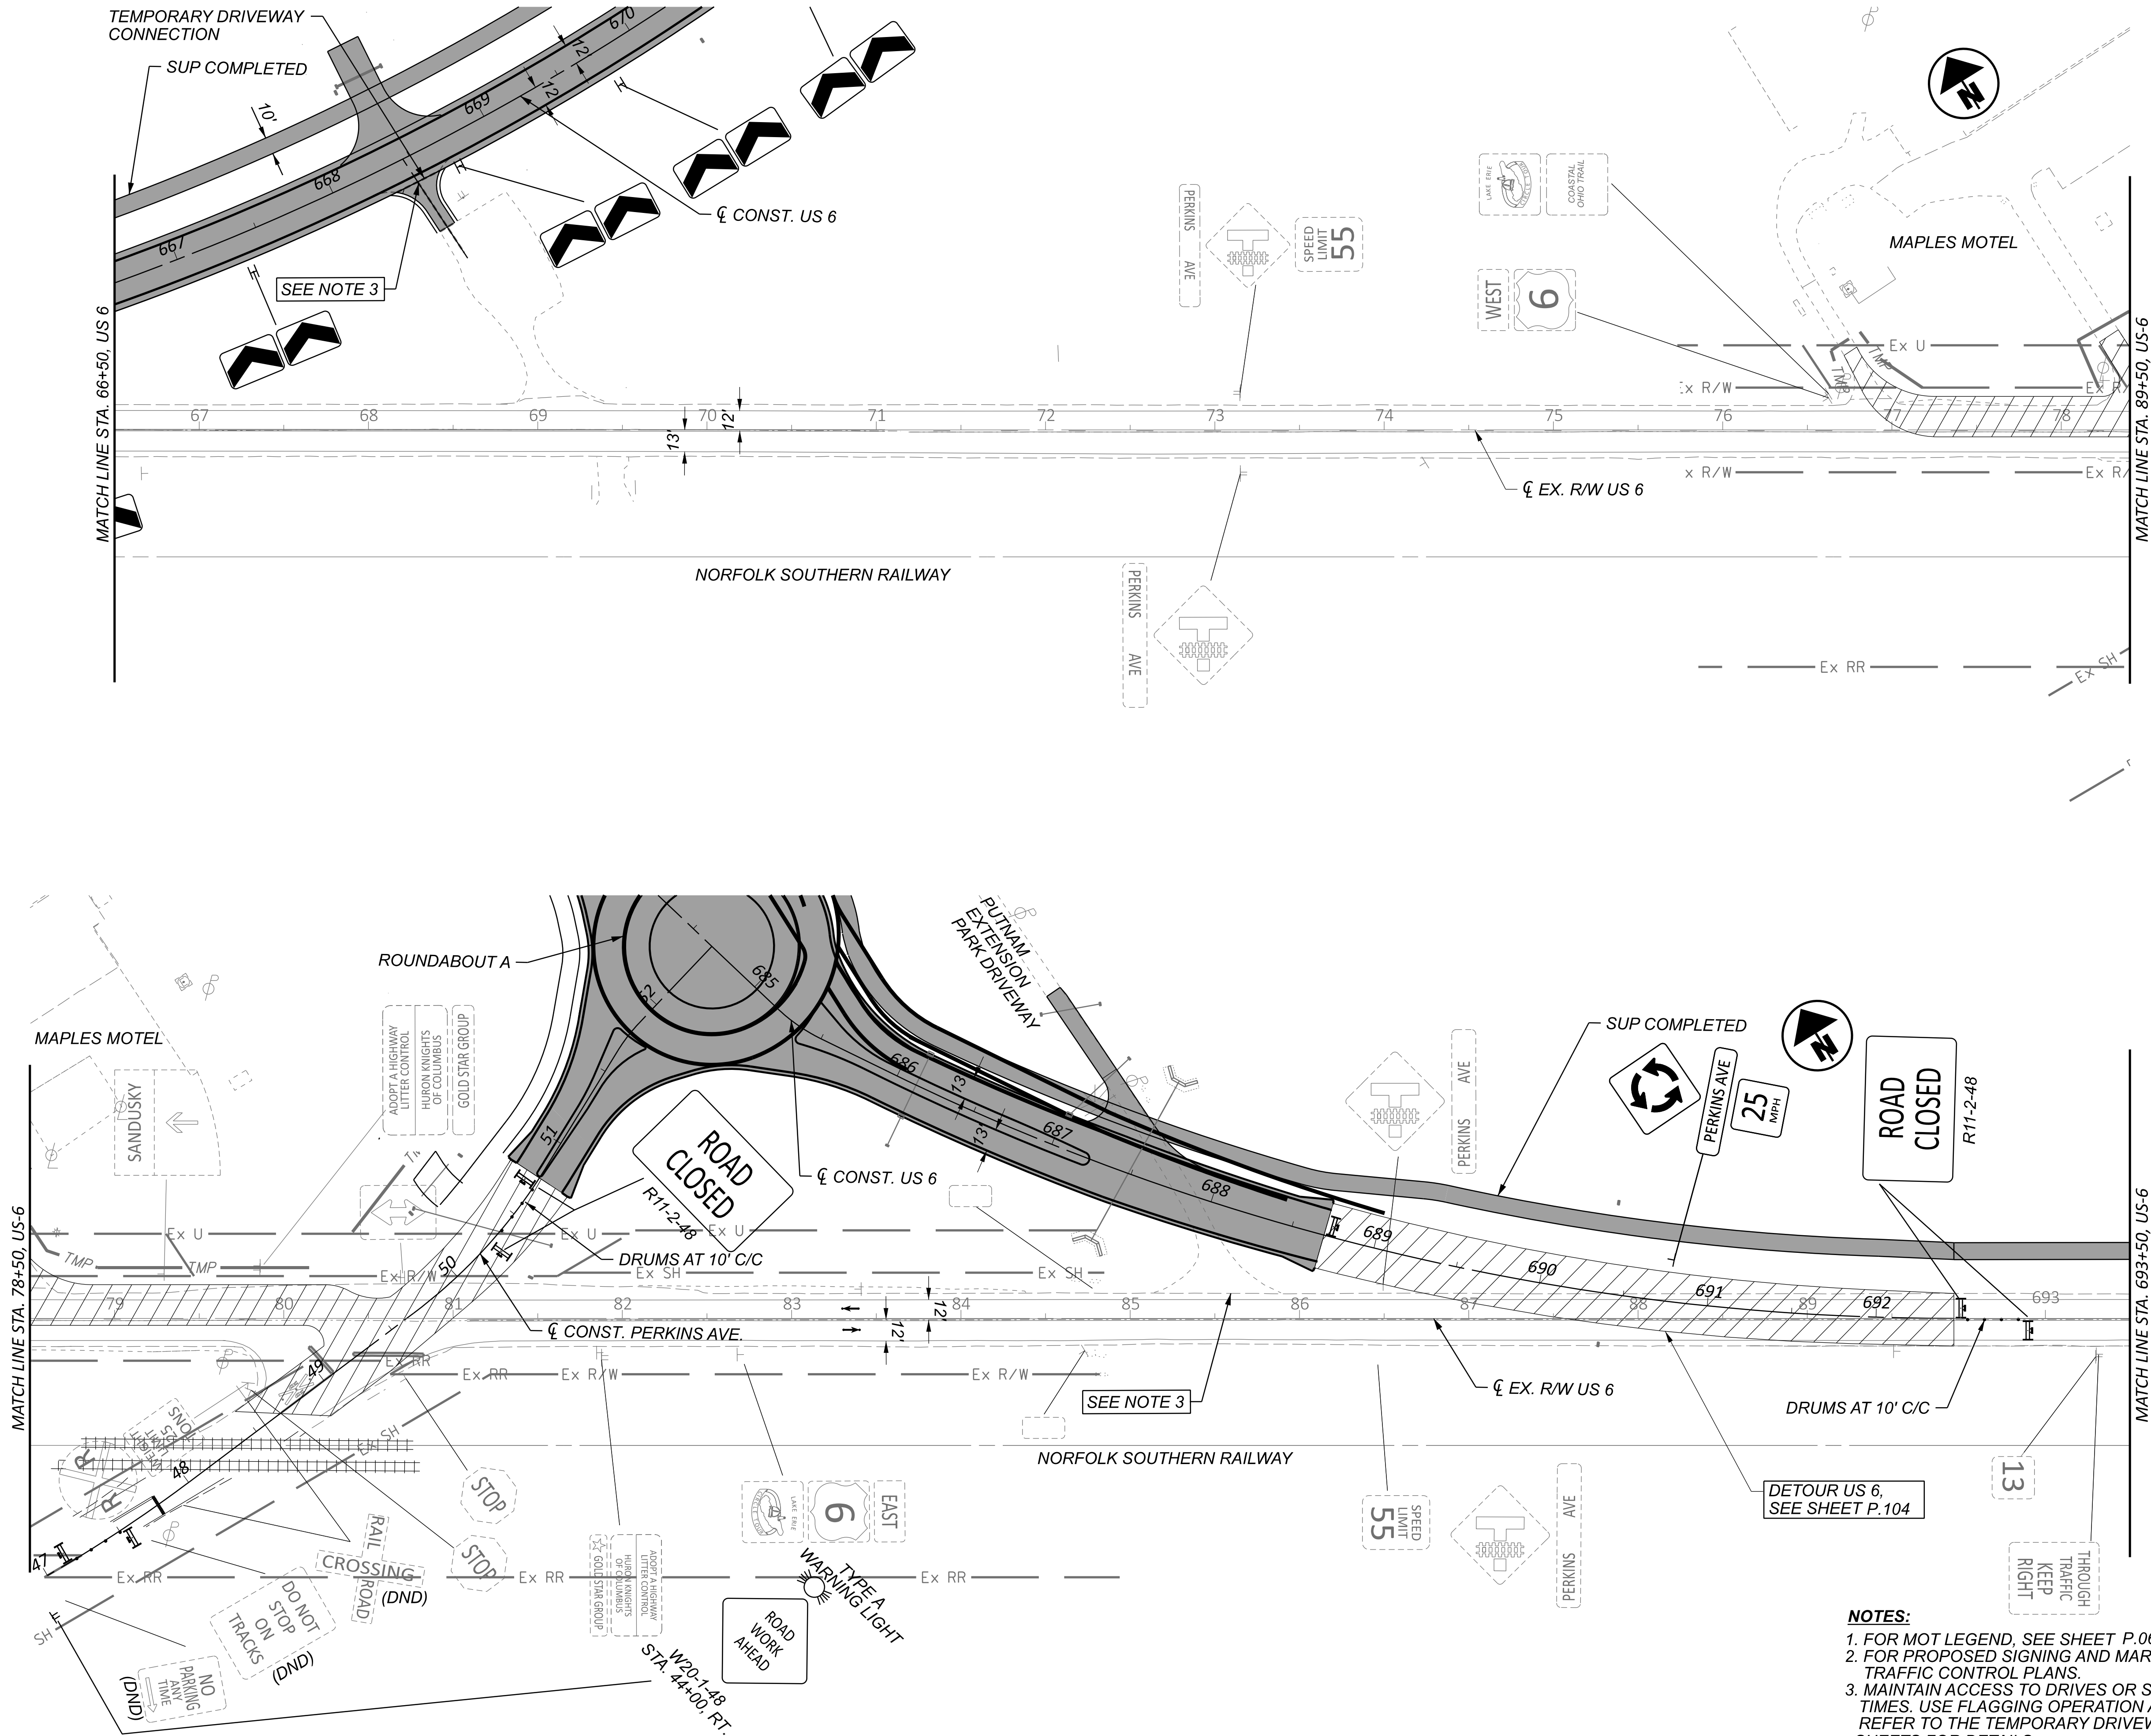

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 67+00.00 EX. US 6 TO 693+50.00 CONST. US 6 SUP



DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.142	782

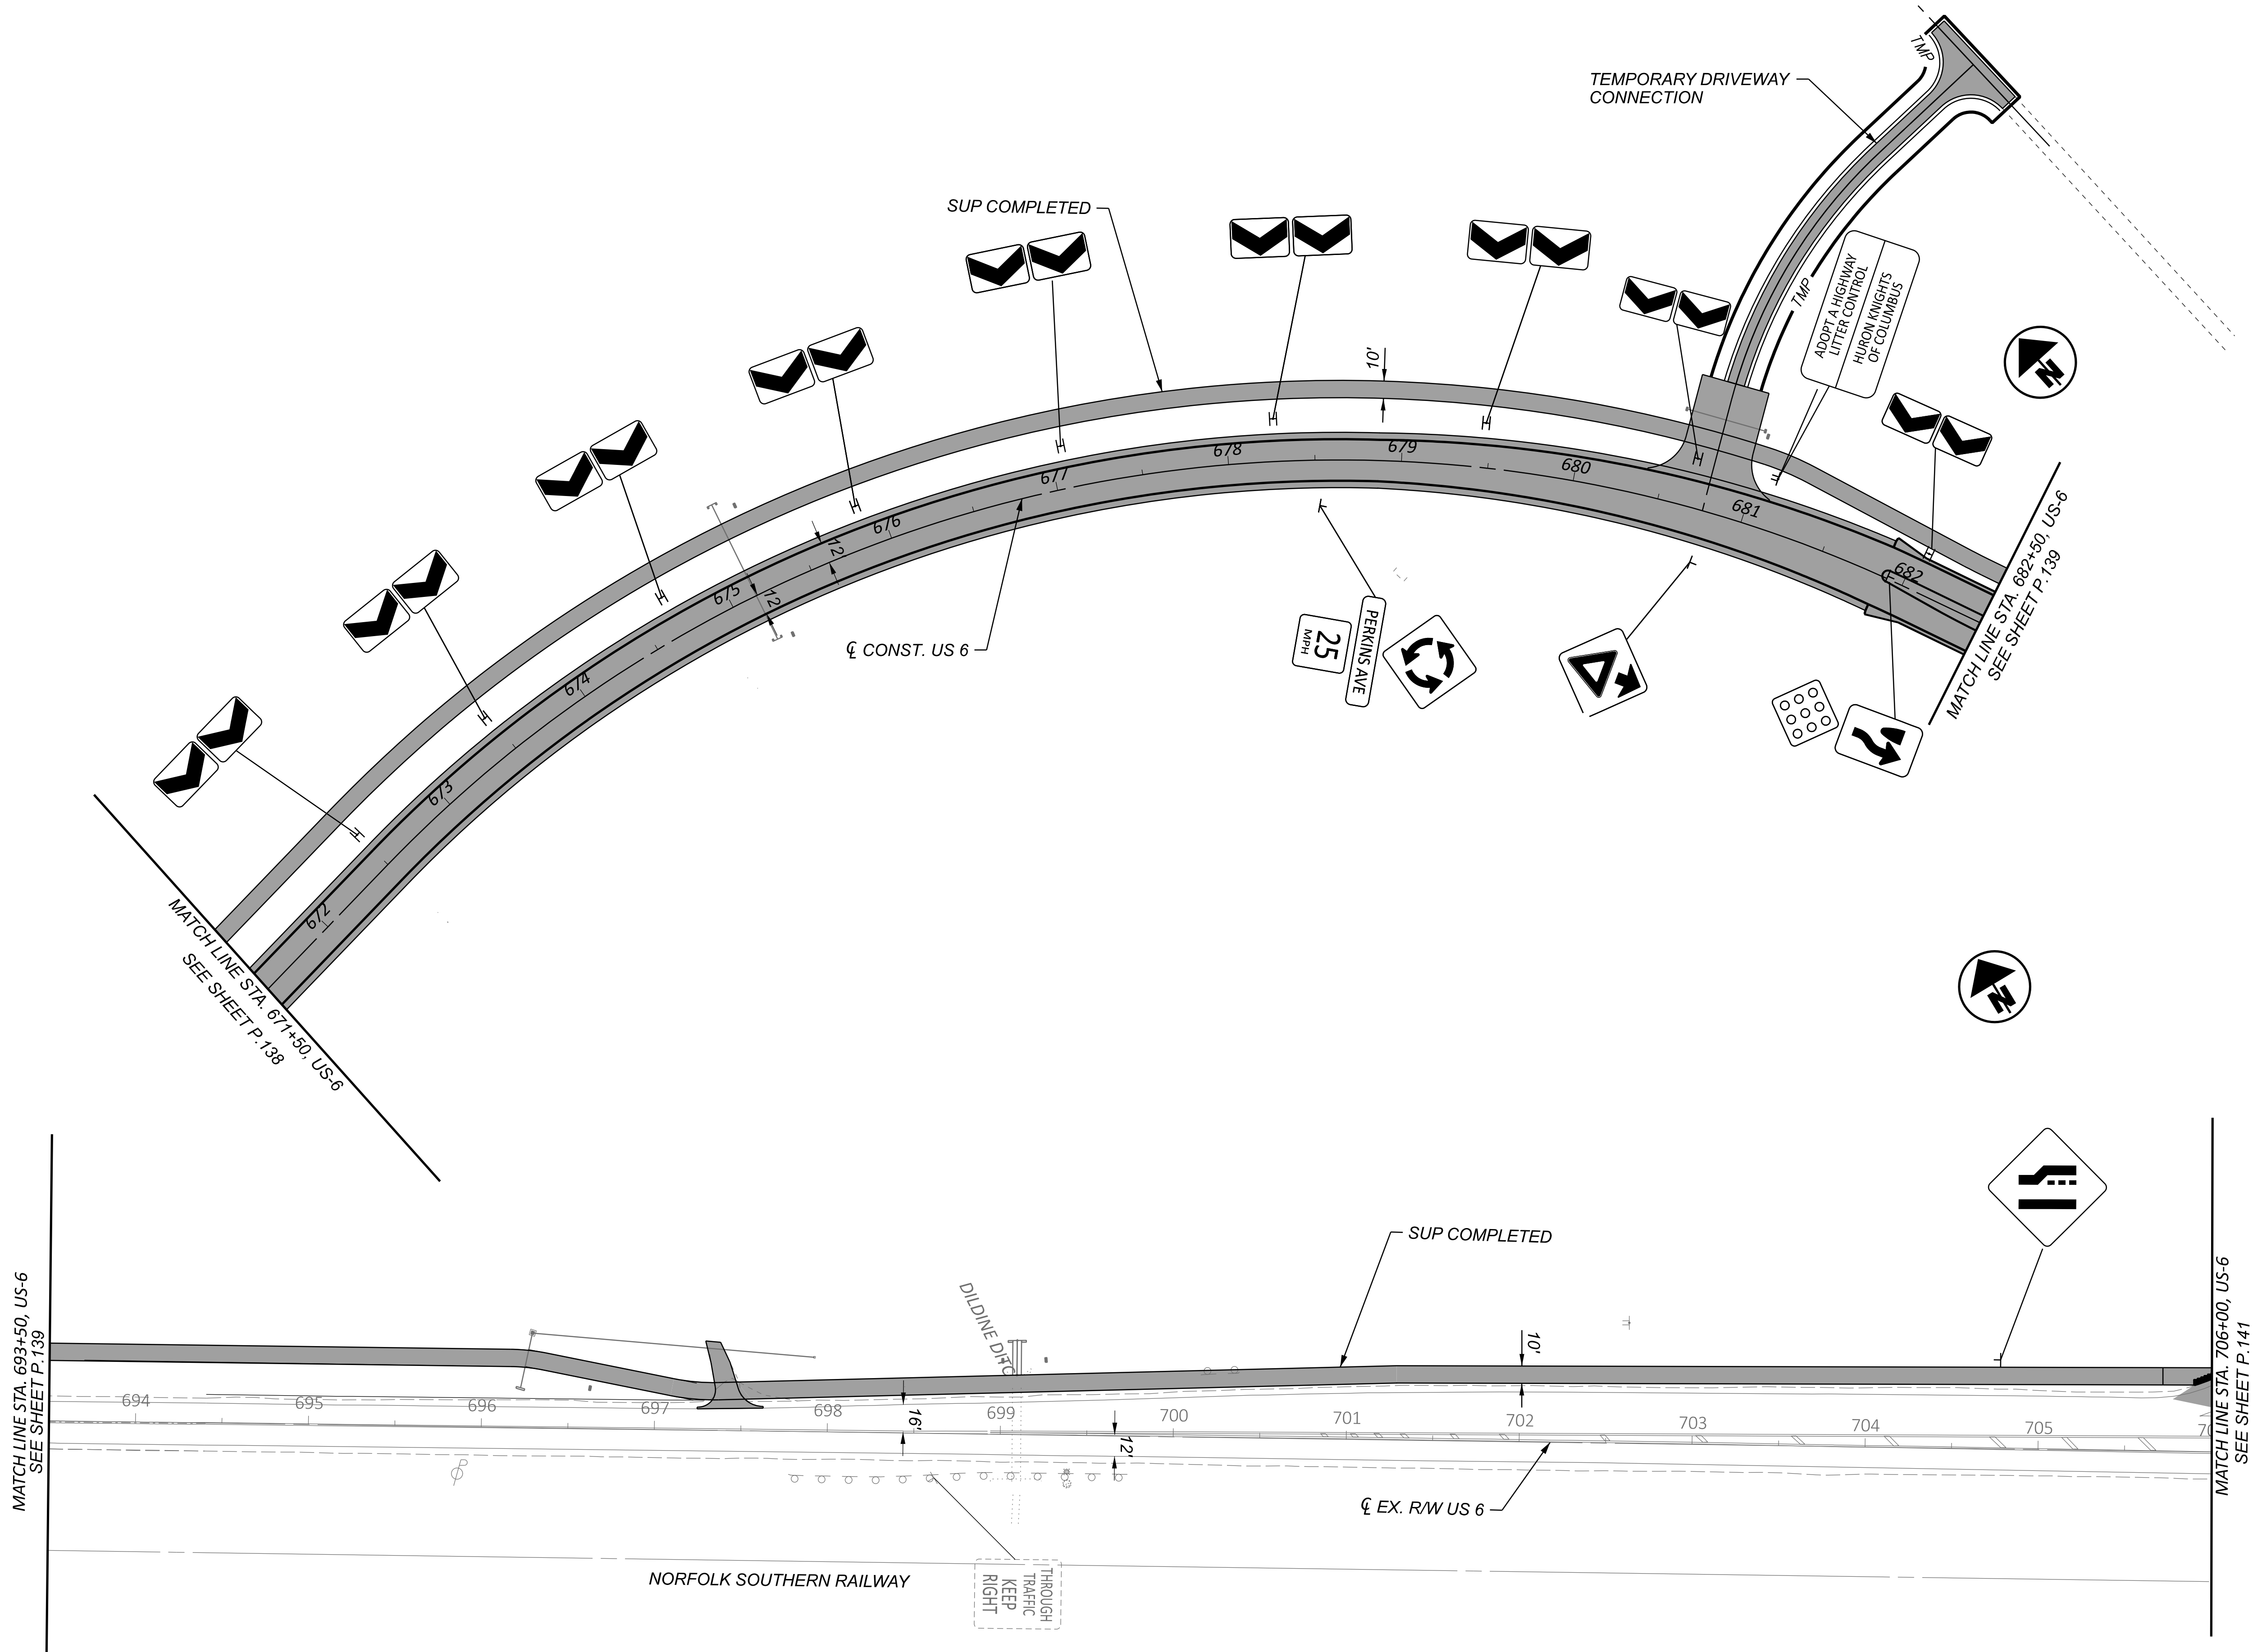

NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 671+50.00 TO STA. 706+00.00

DESIGNER
SSA

REVIEWER
SSA

PROJECT ID
116570

SHEET
P.143

TOTAL
782

2026 UTILITY RELOCATION WORK



- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.
REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 683+00.00 TO STA. 693+50.00

TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
SSA



REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.144 782




2026 UTILITY RELOCATION WORK

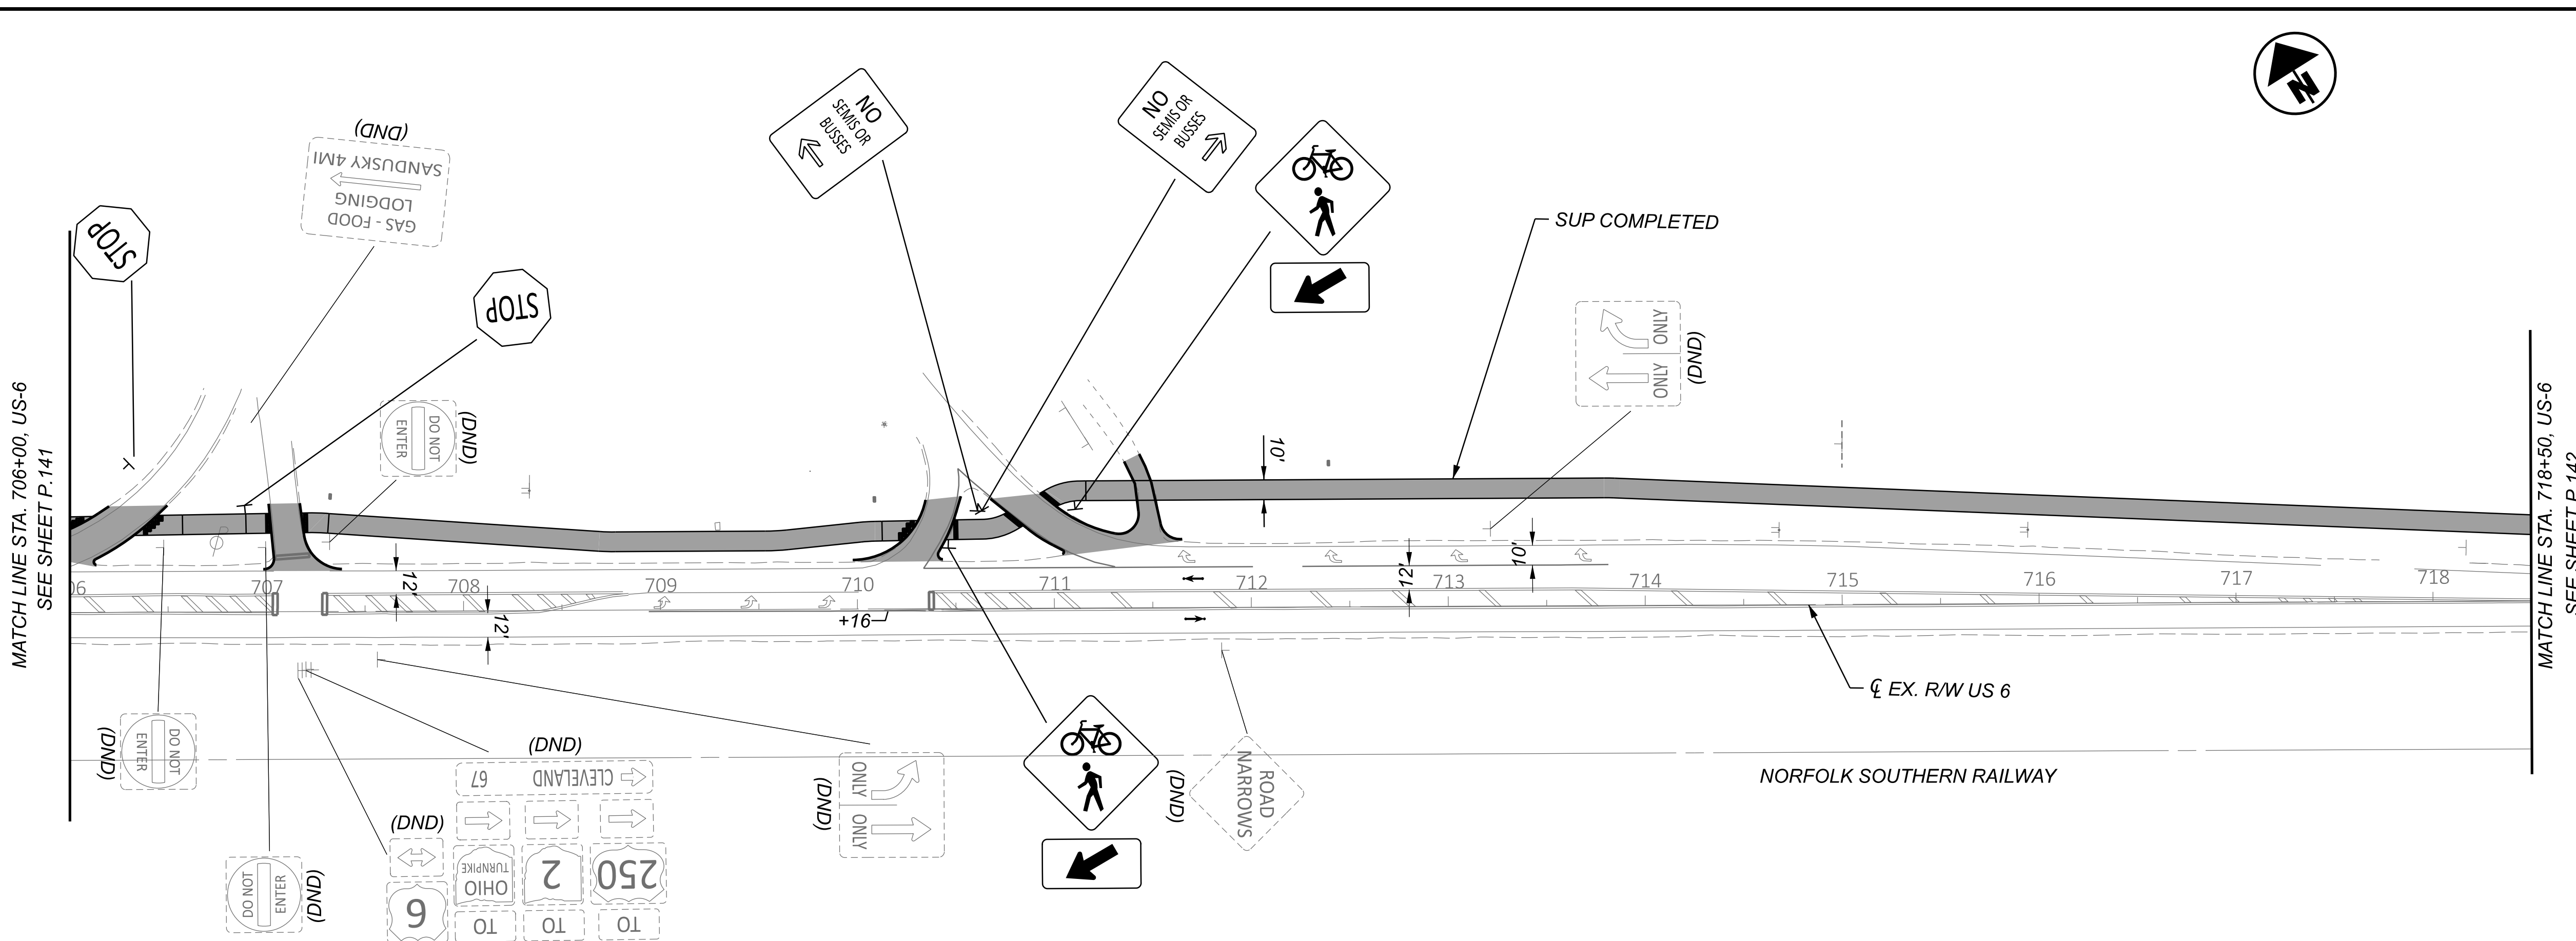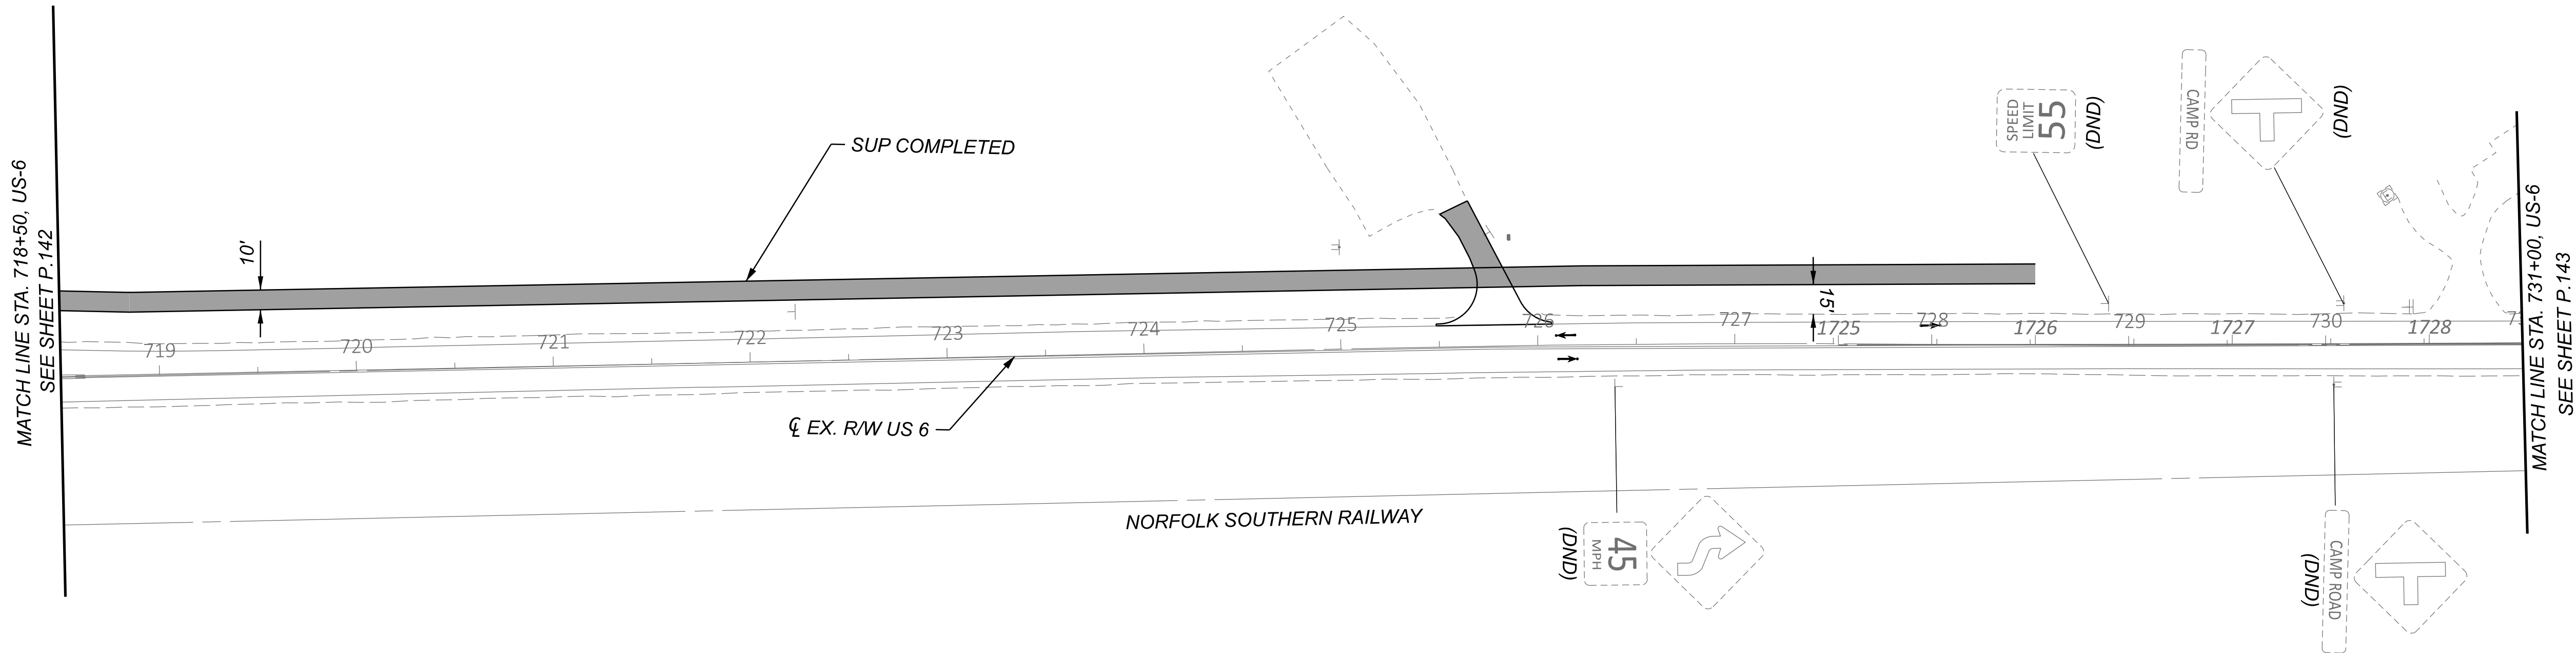


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.145	782

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 706+00.00 TO STA. 730+00.00



2026 UTILITY RELOCATION WORK

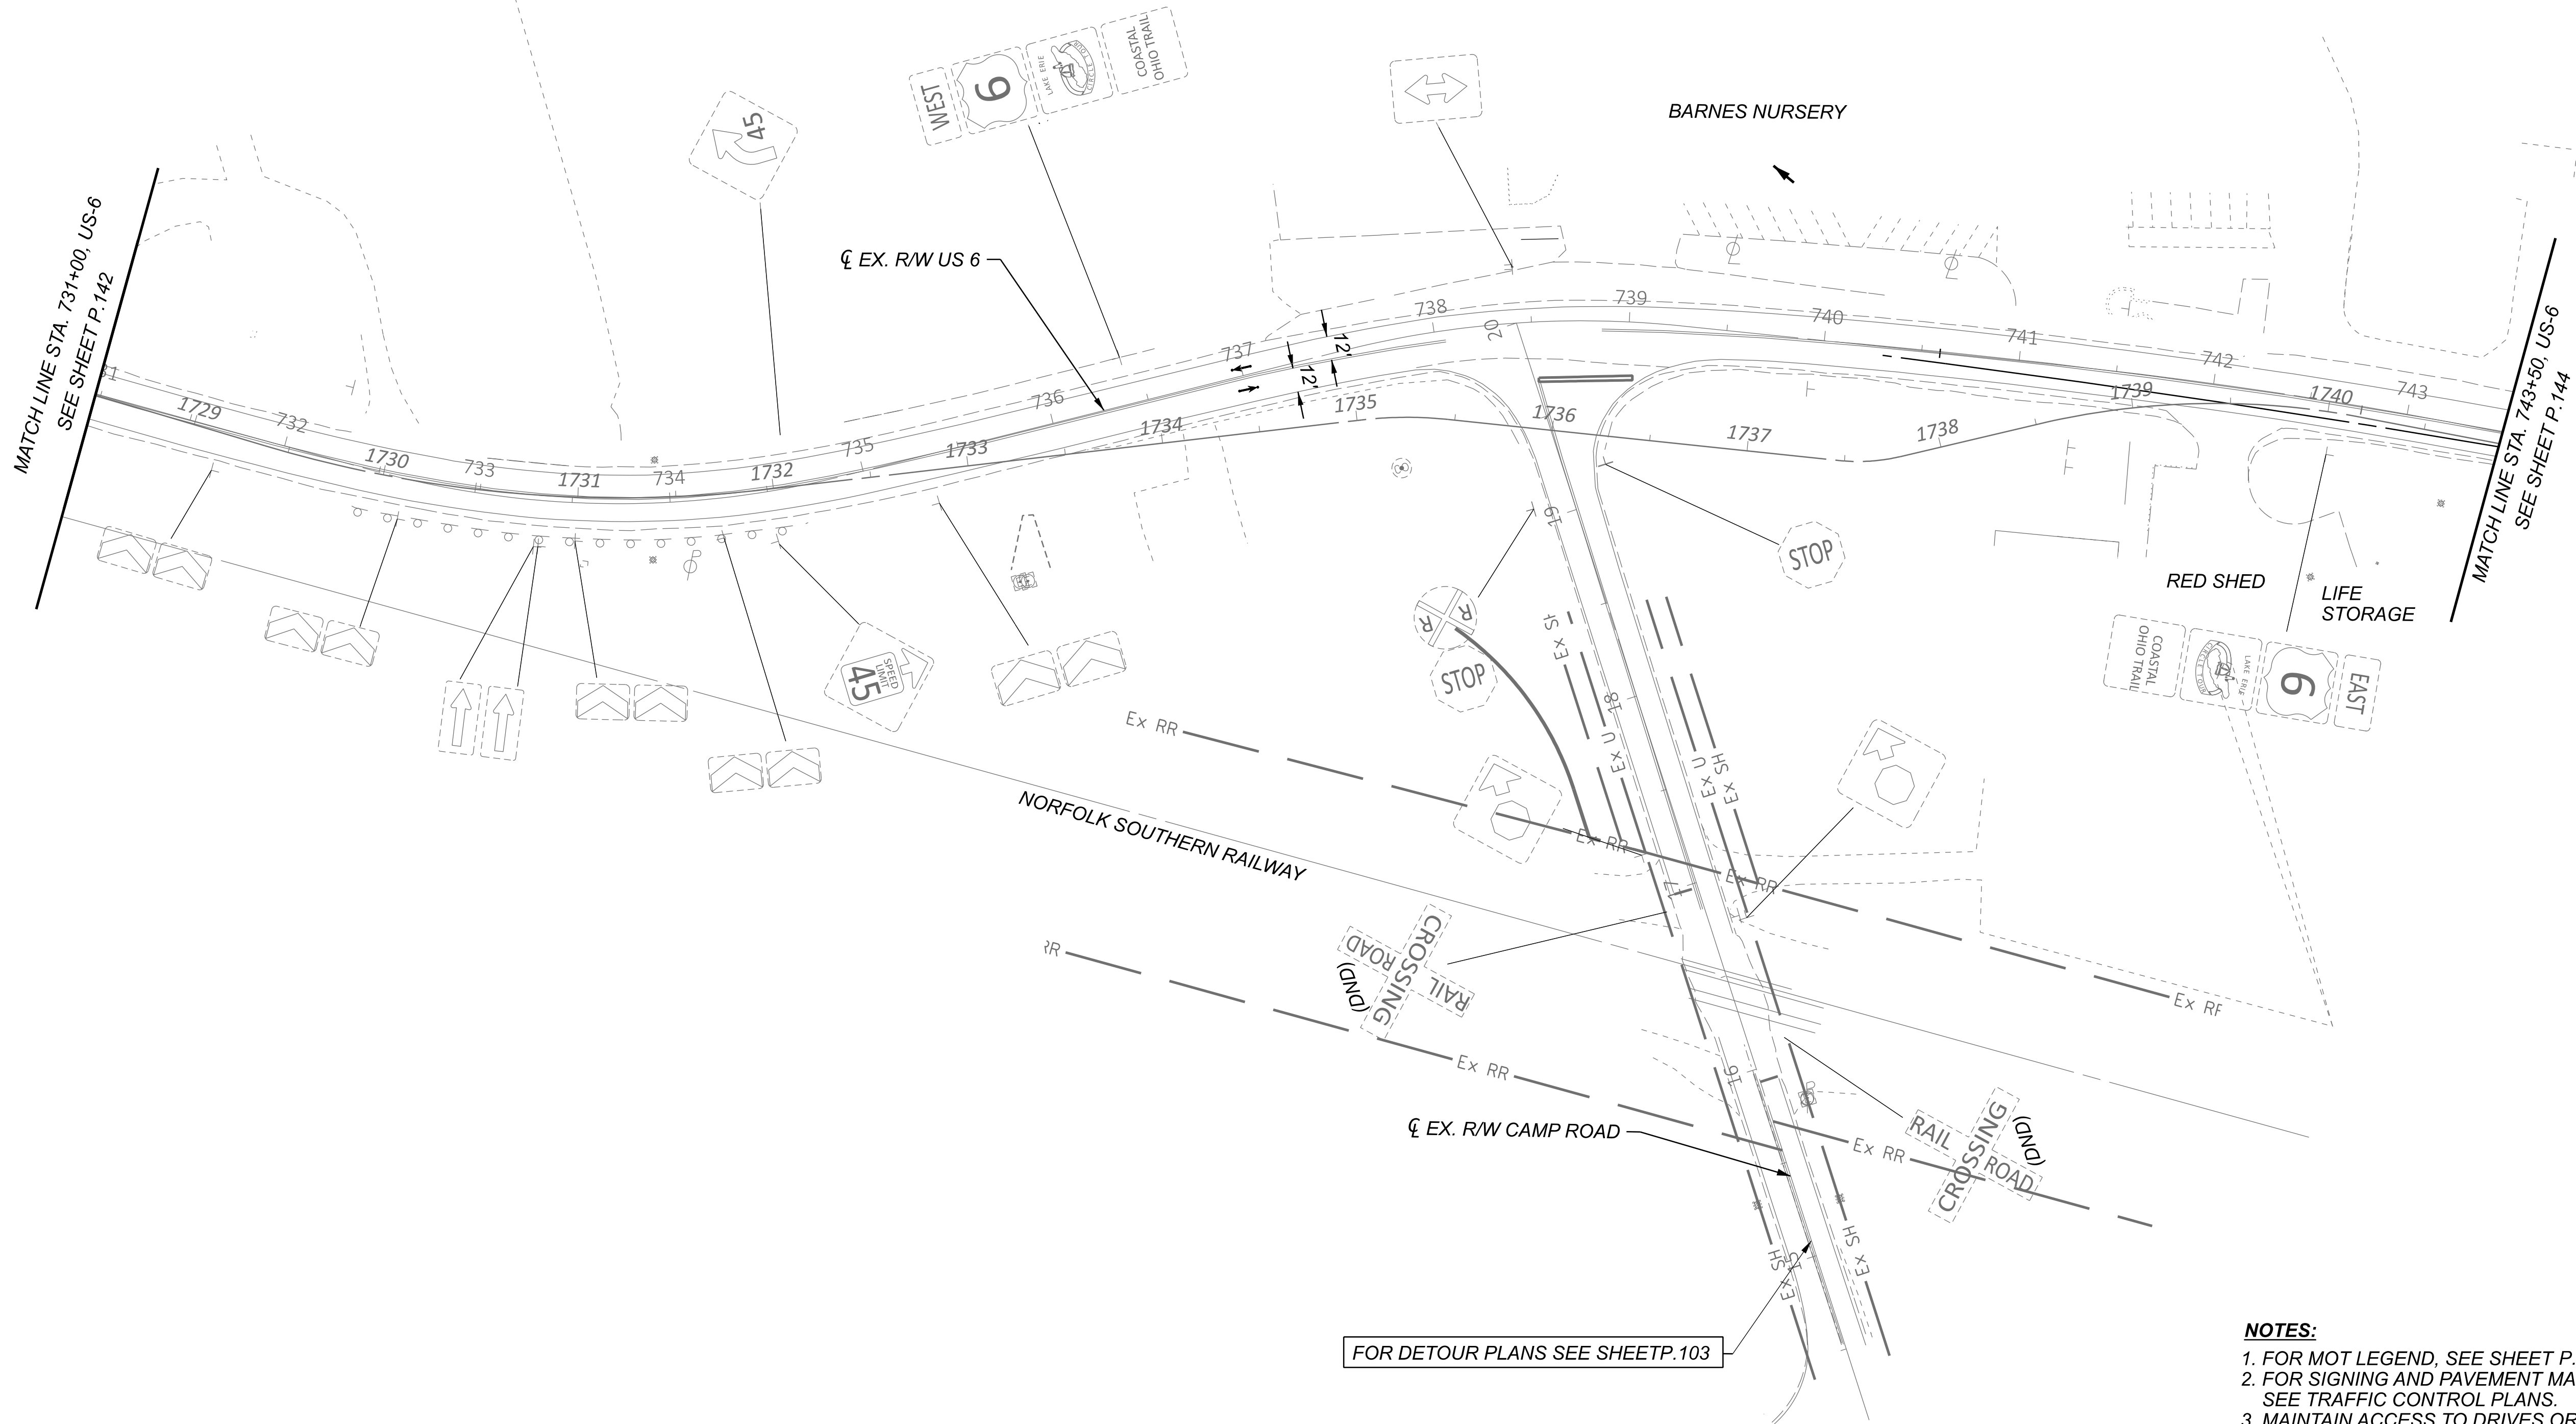

FOR DETOUR PLANS SEE SHEET P.103

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068 .
 - 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 731+00.00 TO STA. 743+50.00


DESIGN AGENCY
TRANSYSTEMS
400 W. WATKINSON BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA


REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.146 782



2026 UTILITY RELOCATION WORK

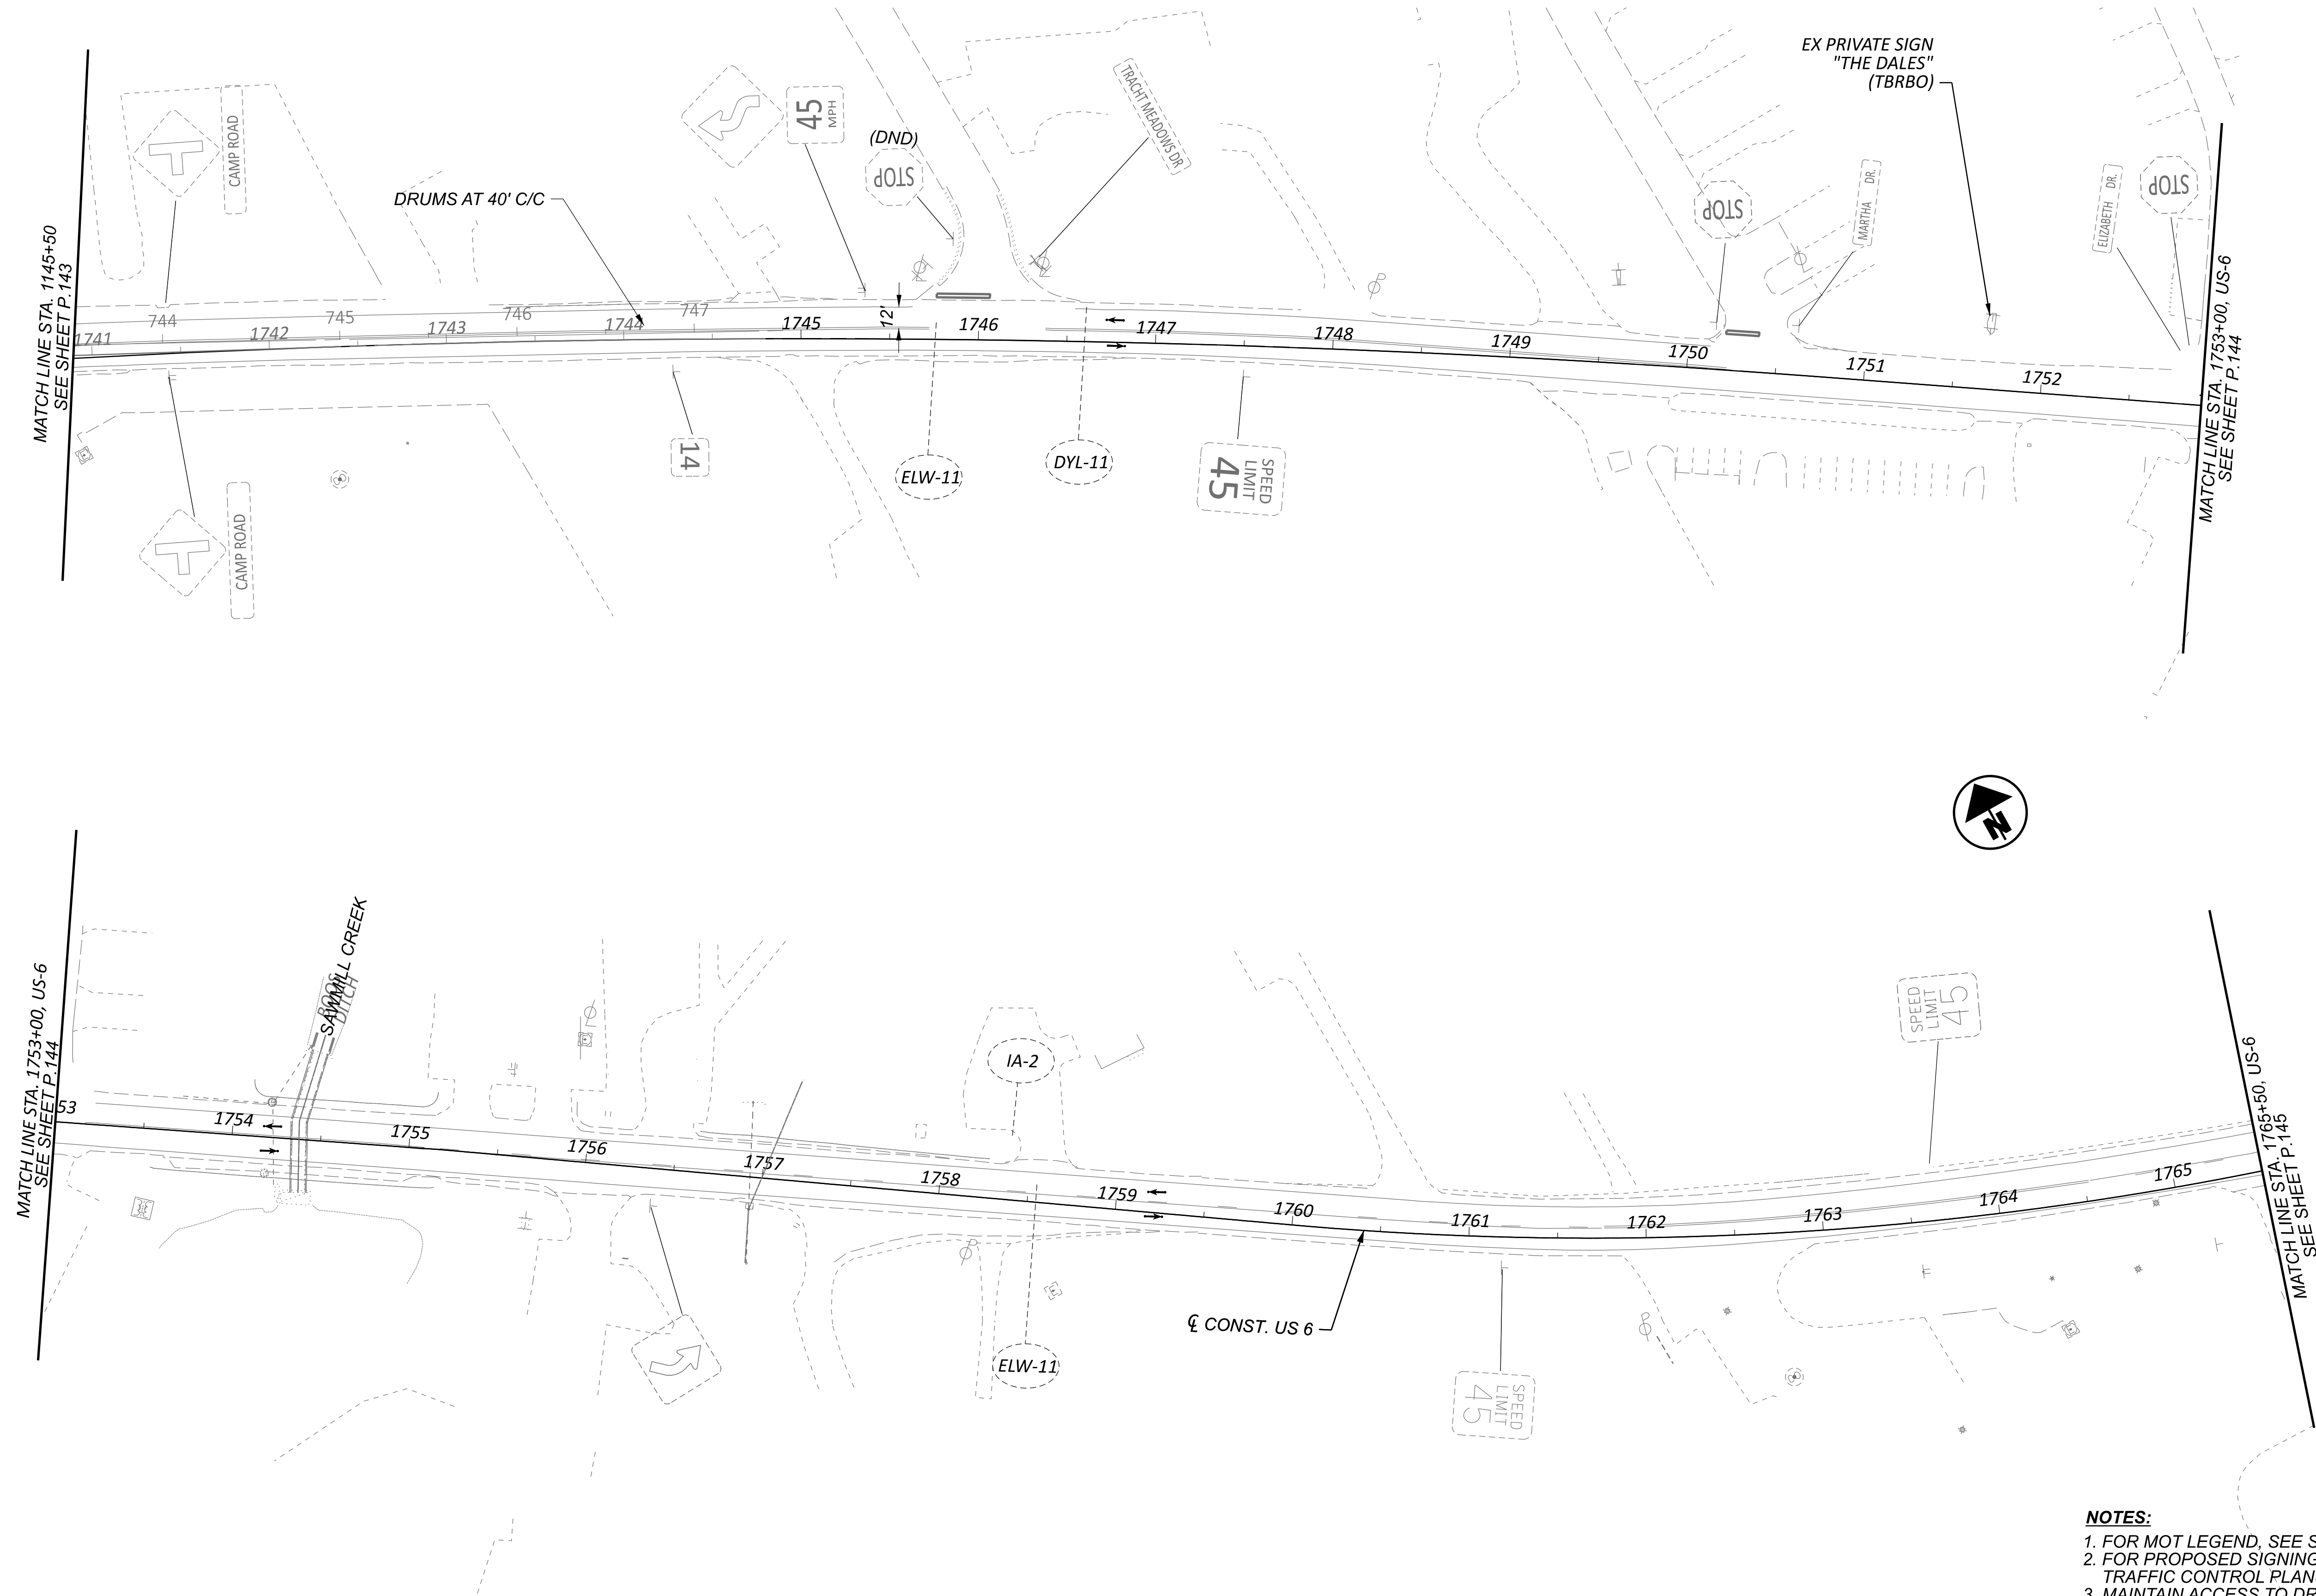

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 1 - Plan 17-18 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:22:05 PM USER: ssaduse1
pw:\\ohiodot-pw.bentley.com:ohiodot-pw-02\\Documents\\01 Active Projects\\District 03\\Erie\\116570\\402-Engineering


[illegible]

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.148	782


MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 1765+50.00 TO STA. 1790+50.00

2026 UTILITY RELOCATION WORK

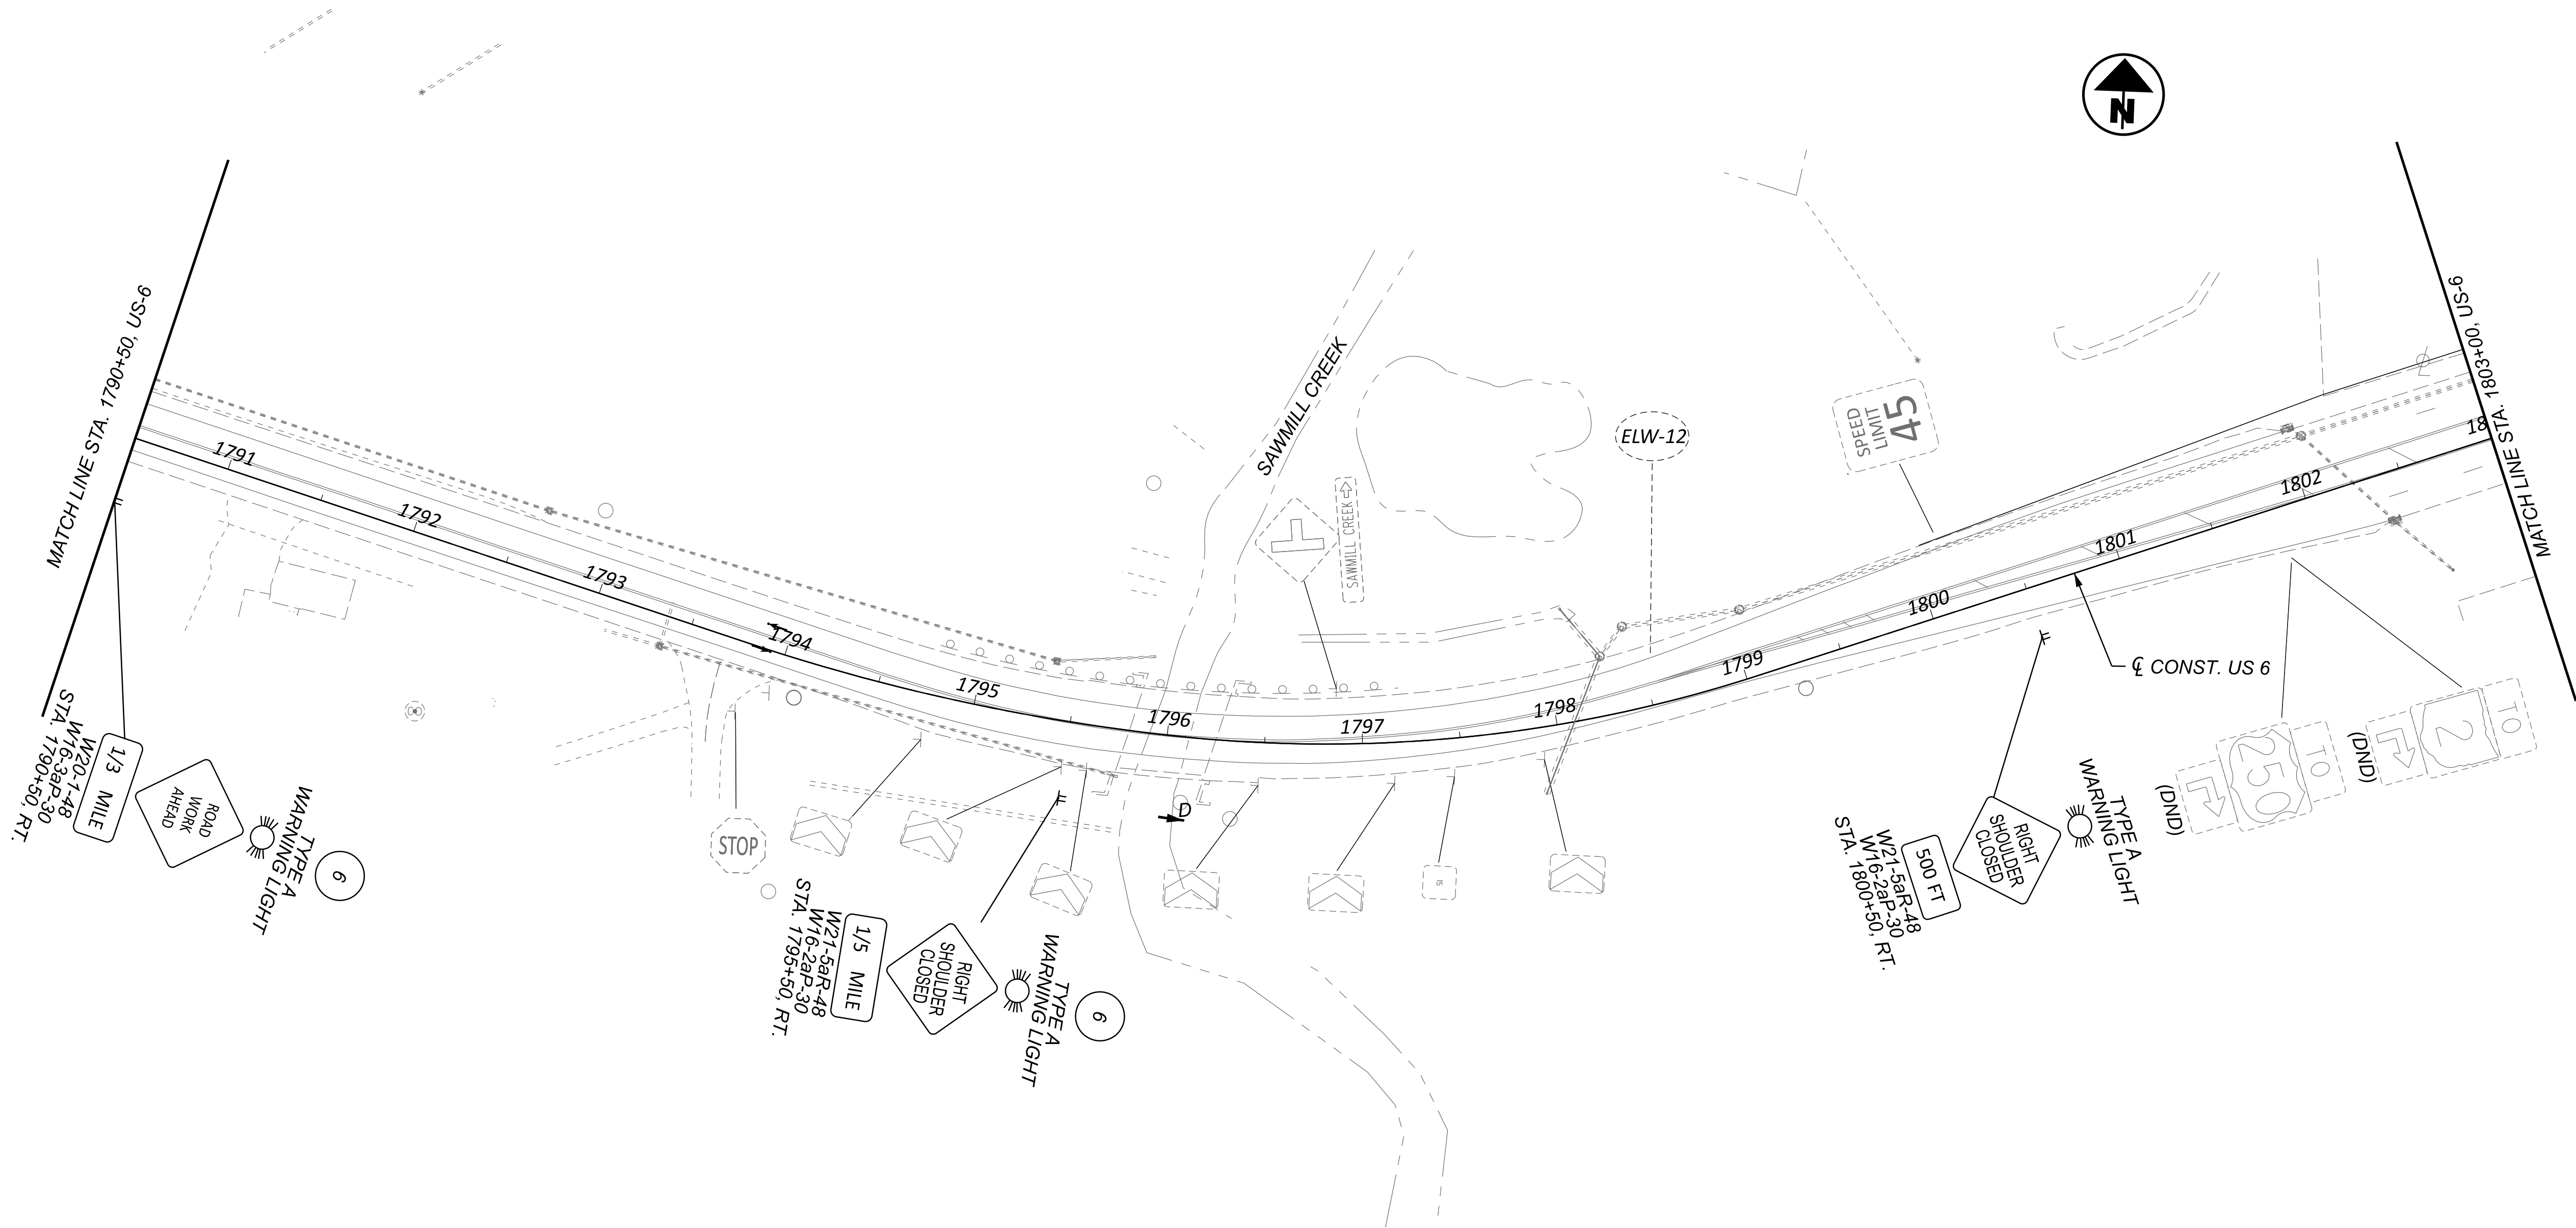


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. FOR SECTION D-D, SEE SHEET P.113 .
 4. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATIONS AS NECESSARY.


MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US - 6 STA. 1790+50.00 TO STA. 1803+00.00




DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.149	782

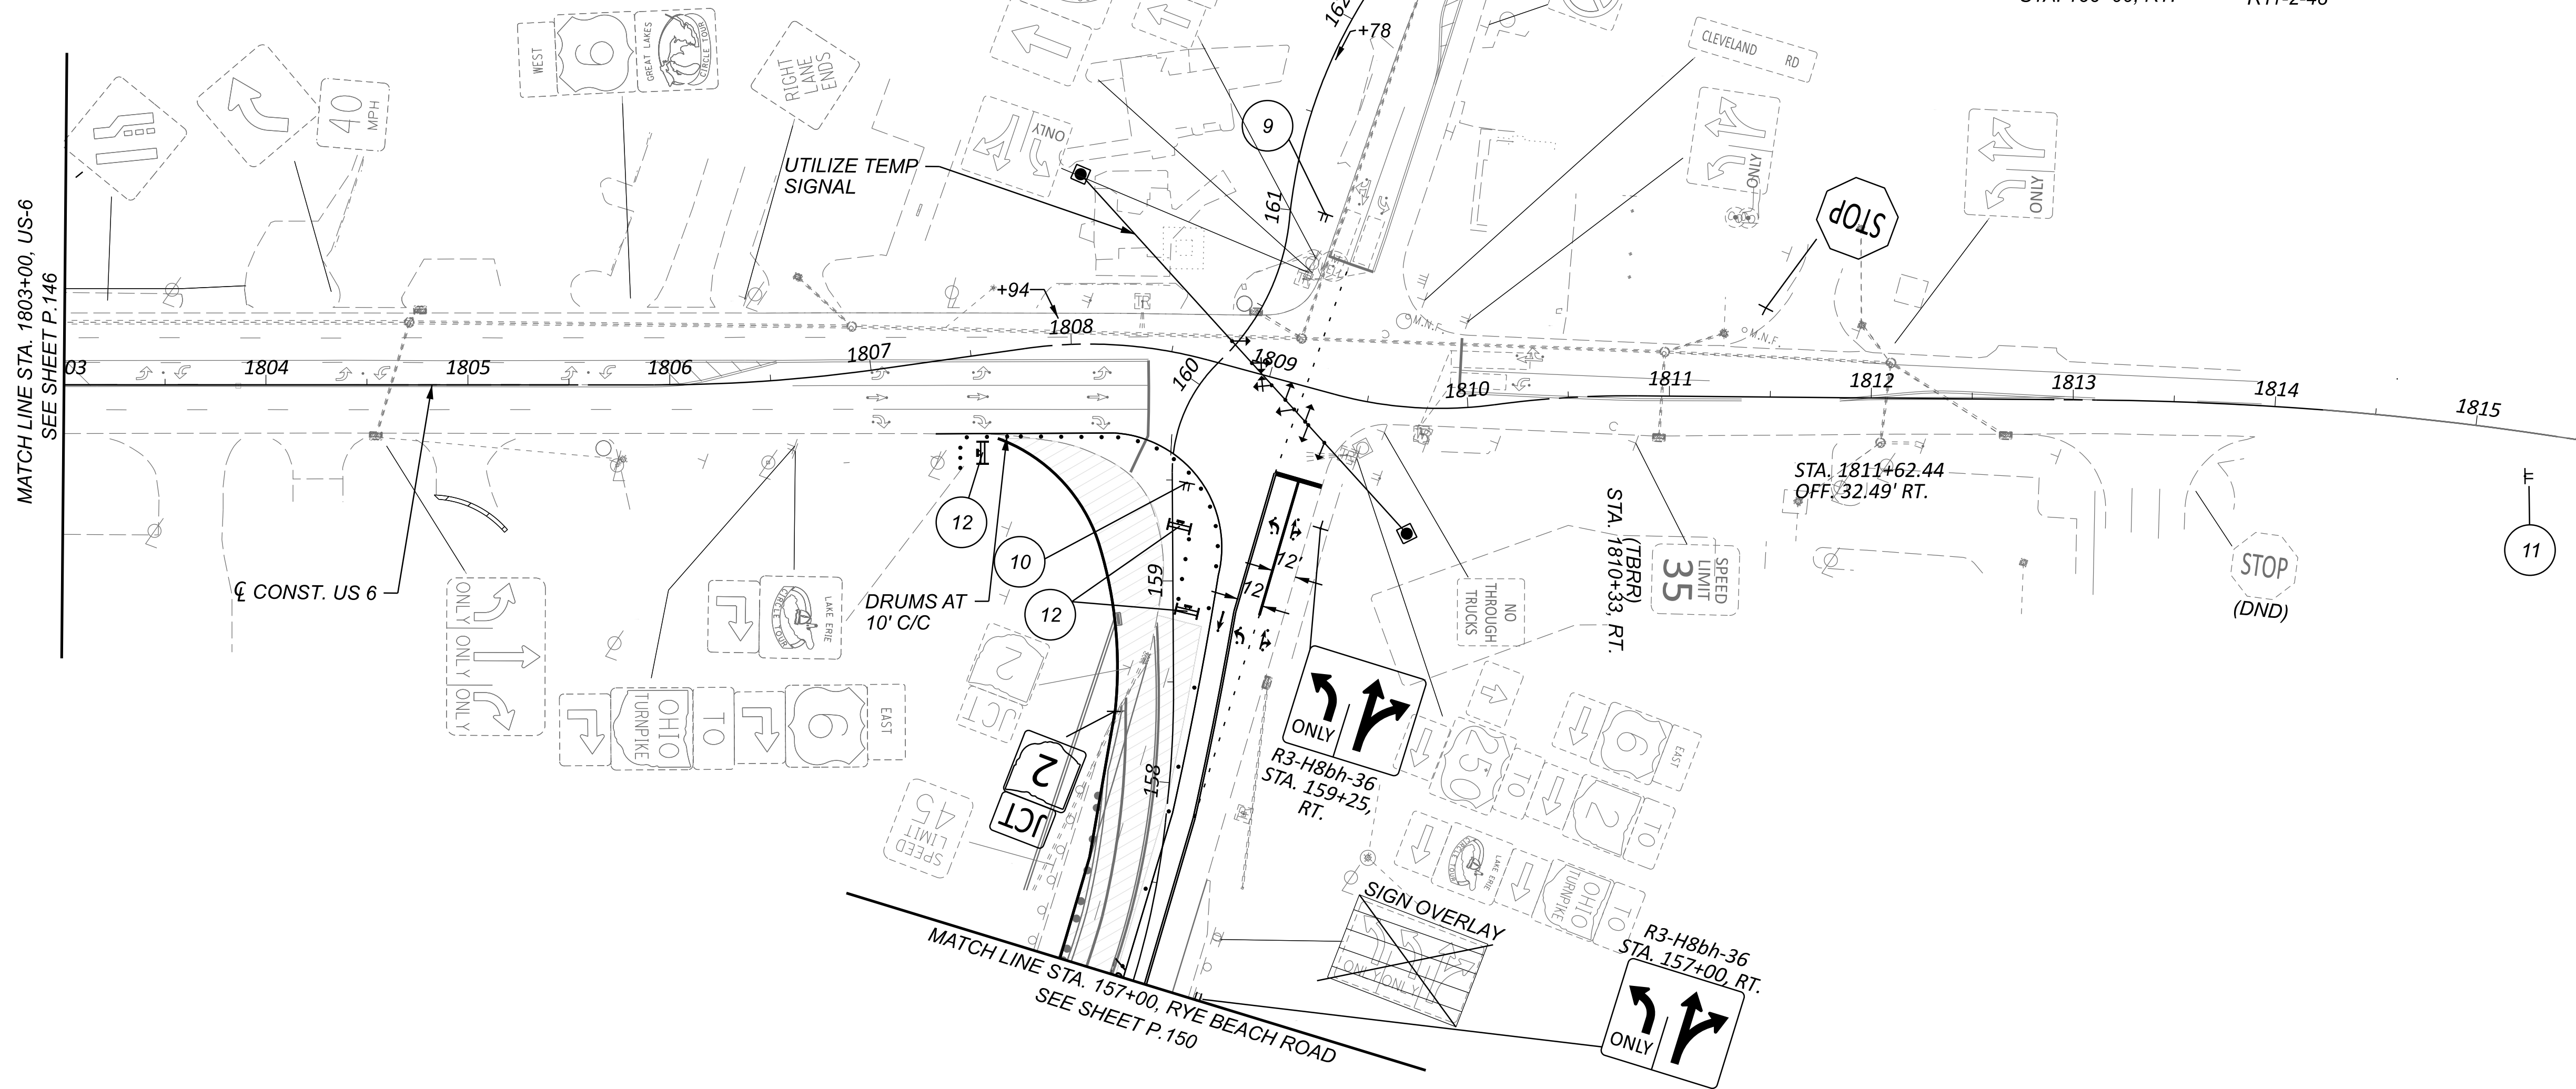


- | | | |
|--|------------|--|
| <p style="text-align: center;">MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)</p> <p style="text-align: center;">US 6 - STA. 1803+00.00 TO END PROJECT</p> | | |
| <p>DESIGN AGENCY</p> <p>TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 2025
COLUMBUS, OHIO 43215</p> | | |
| <p>DESIGNER</p> <p>SSA</p> | | |
| <p>REVIEWER</p> <p>SS 02/28/24</p> | | |
| <p>PROJECT ID</p> <p>116570</p> | | |
| SHEET | TOTAL | |
| P.150 | 782 | |

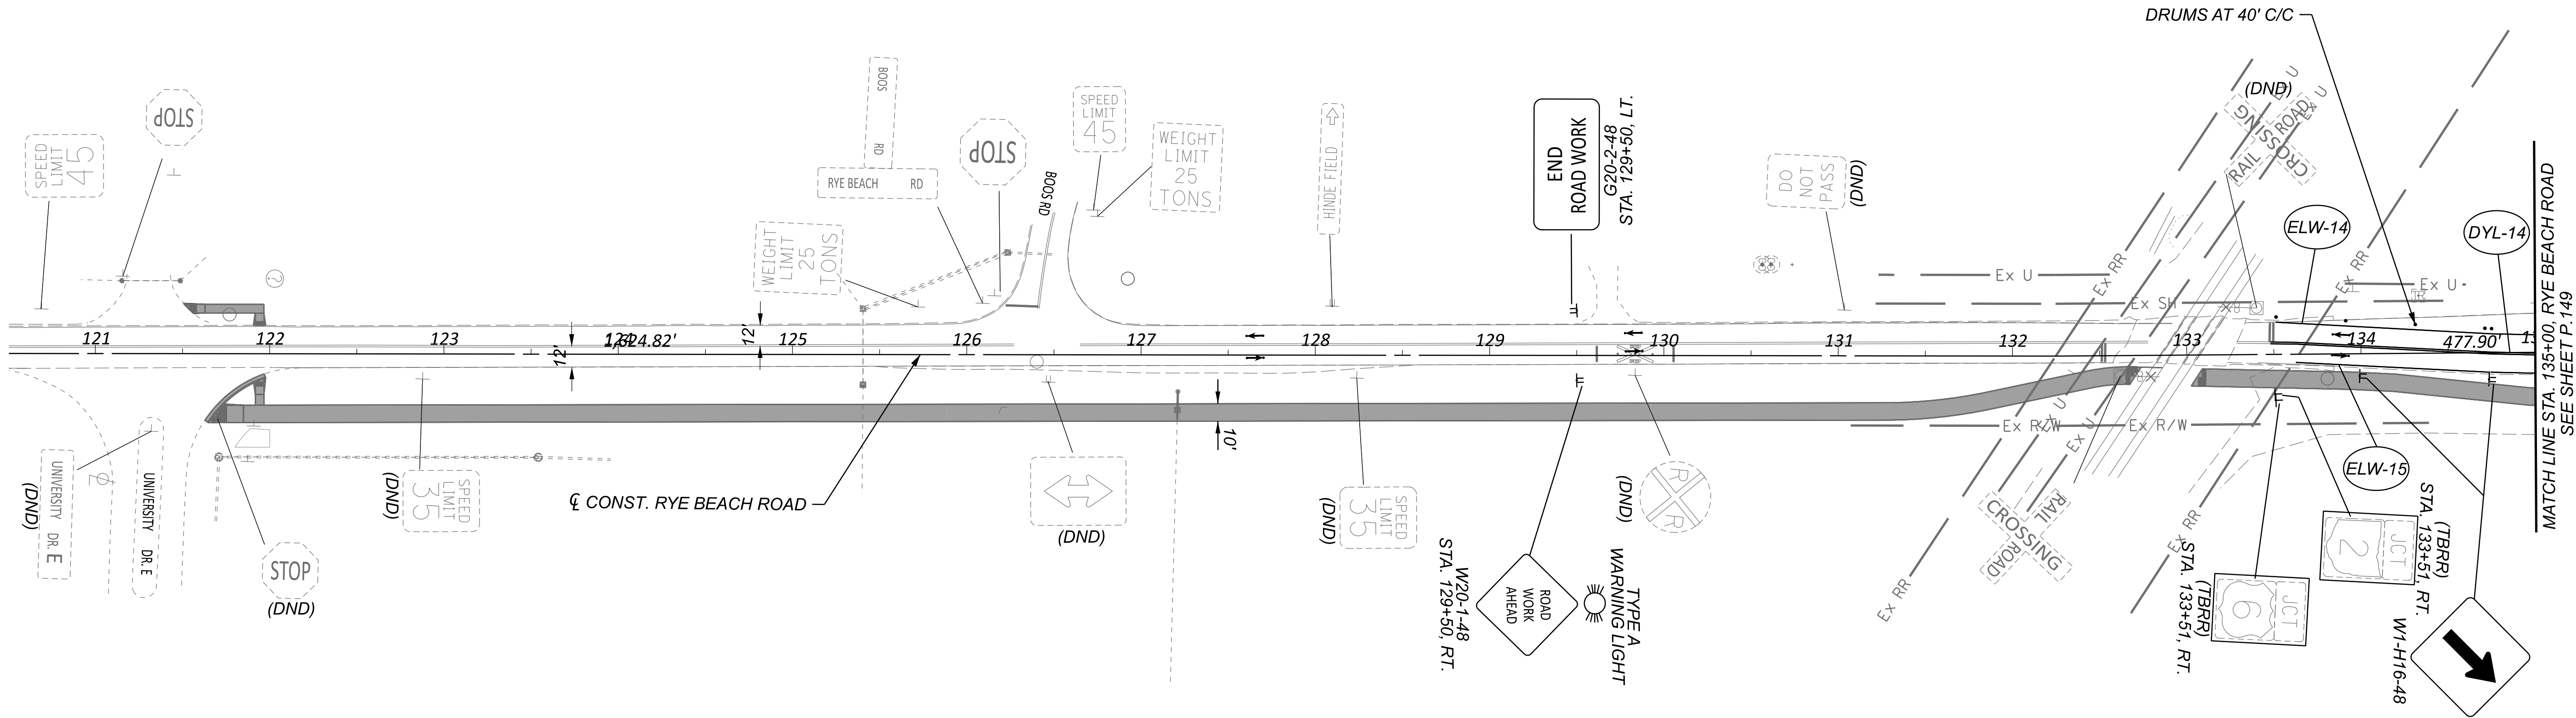


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.



MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
RYE BEACH ROAD - BEGIN PROJECT TO STA. 135+00.00



DESIGN AGENCY	
TRANSYSTEMS 400 W. WATKINS BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.151	782

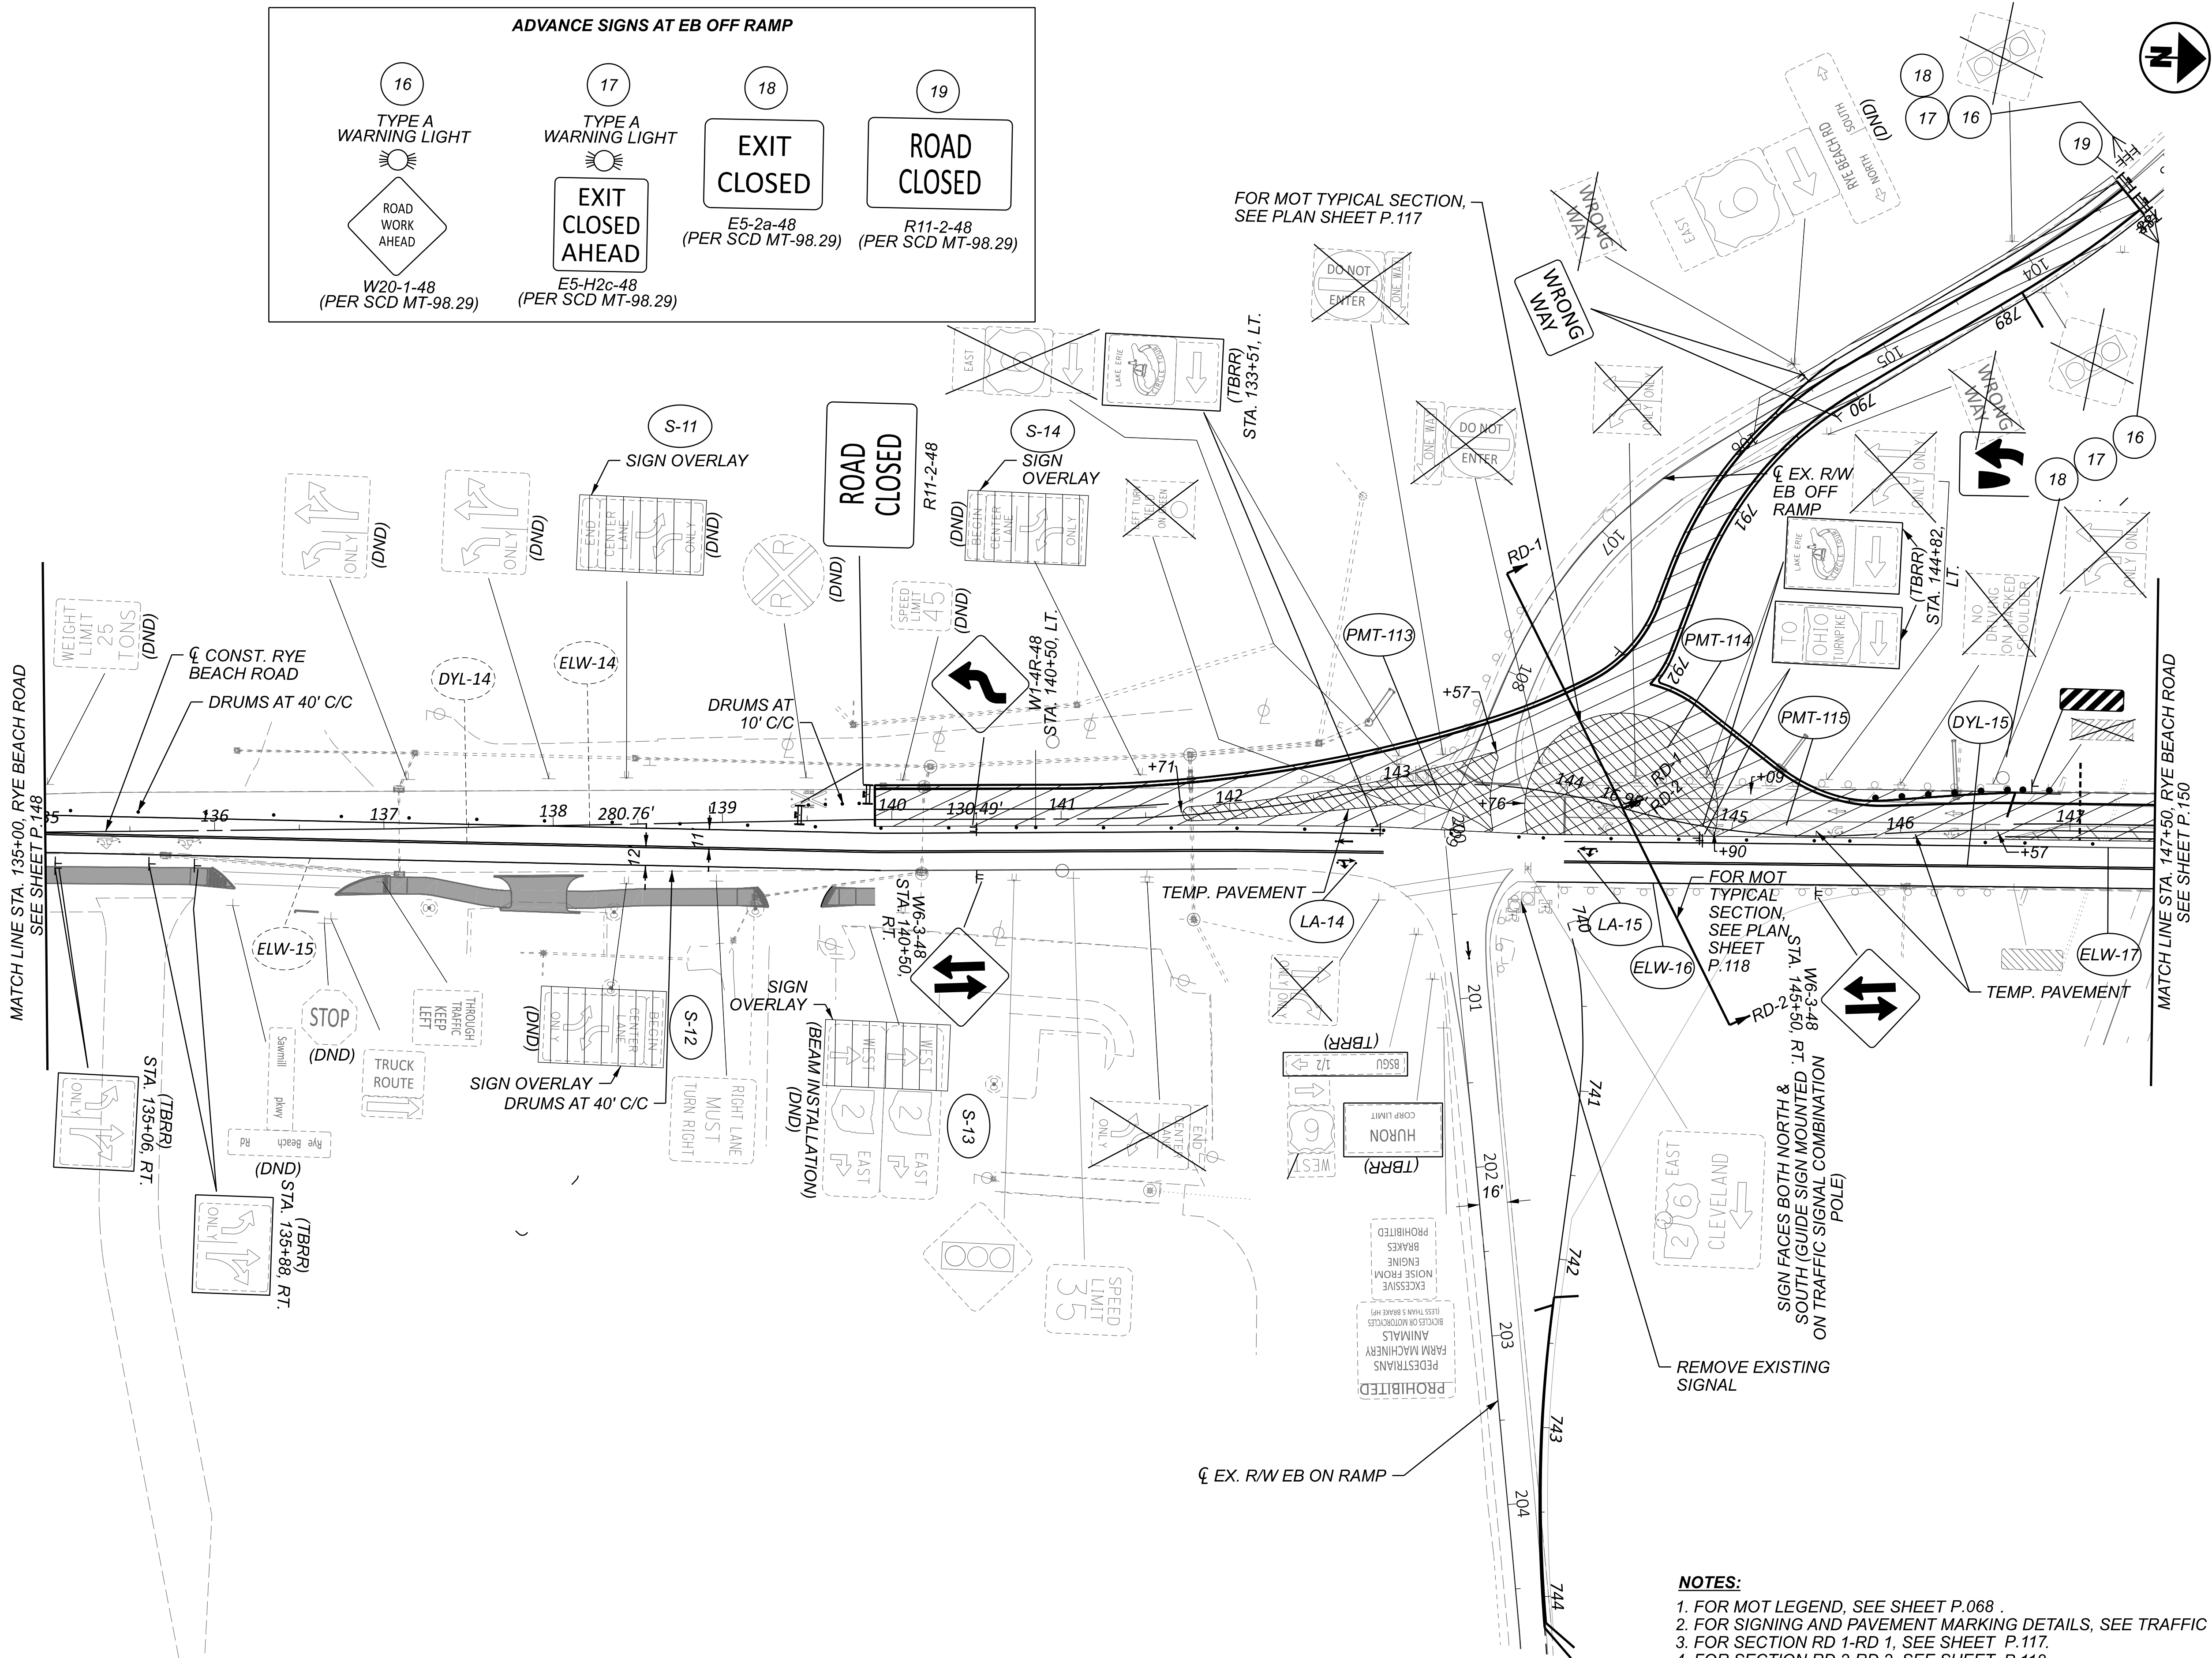


ADVANCE SIGNS AT EB OFF RAMP

16	17	18	19
TYPE A WARNING LIGHT	TYPE A WARNING LIGHT	EXIT CLOSED	ROAD CLOSED
ROAD WORK AHEAD	EXIT CLOSED AHEAD	E5-2a-48 (PER SCD MT-98.29)	R11-2-48 (PER SCD MT-98.29)
W20-1-48 (PER SCD MT-98.29)	E5-H2c-48 (PER SCD MT-98.29)		


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. FOR SECTION RD 1-RD 1, SEE SHEET P.117.
 4. FOR SECTION RD 2-RD 2, SEE SHEET P.118.
 5. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
RYE BEACH ROAD - STA. 135+00.00 TO STA. 147+50.00

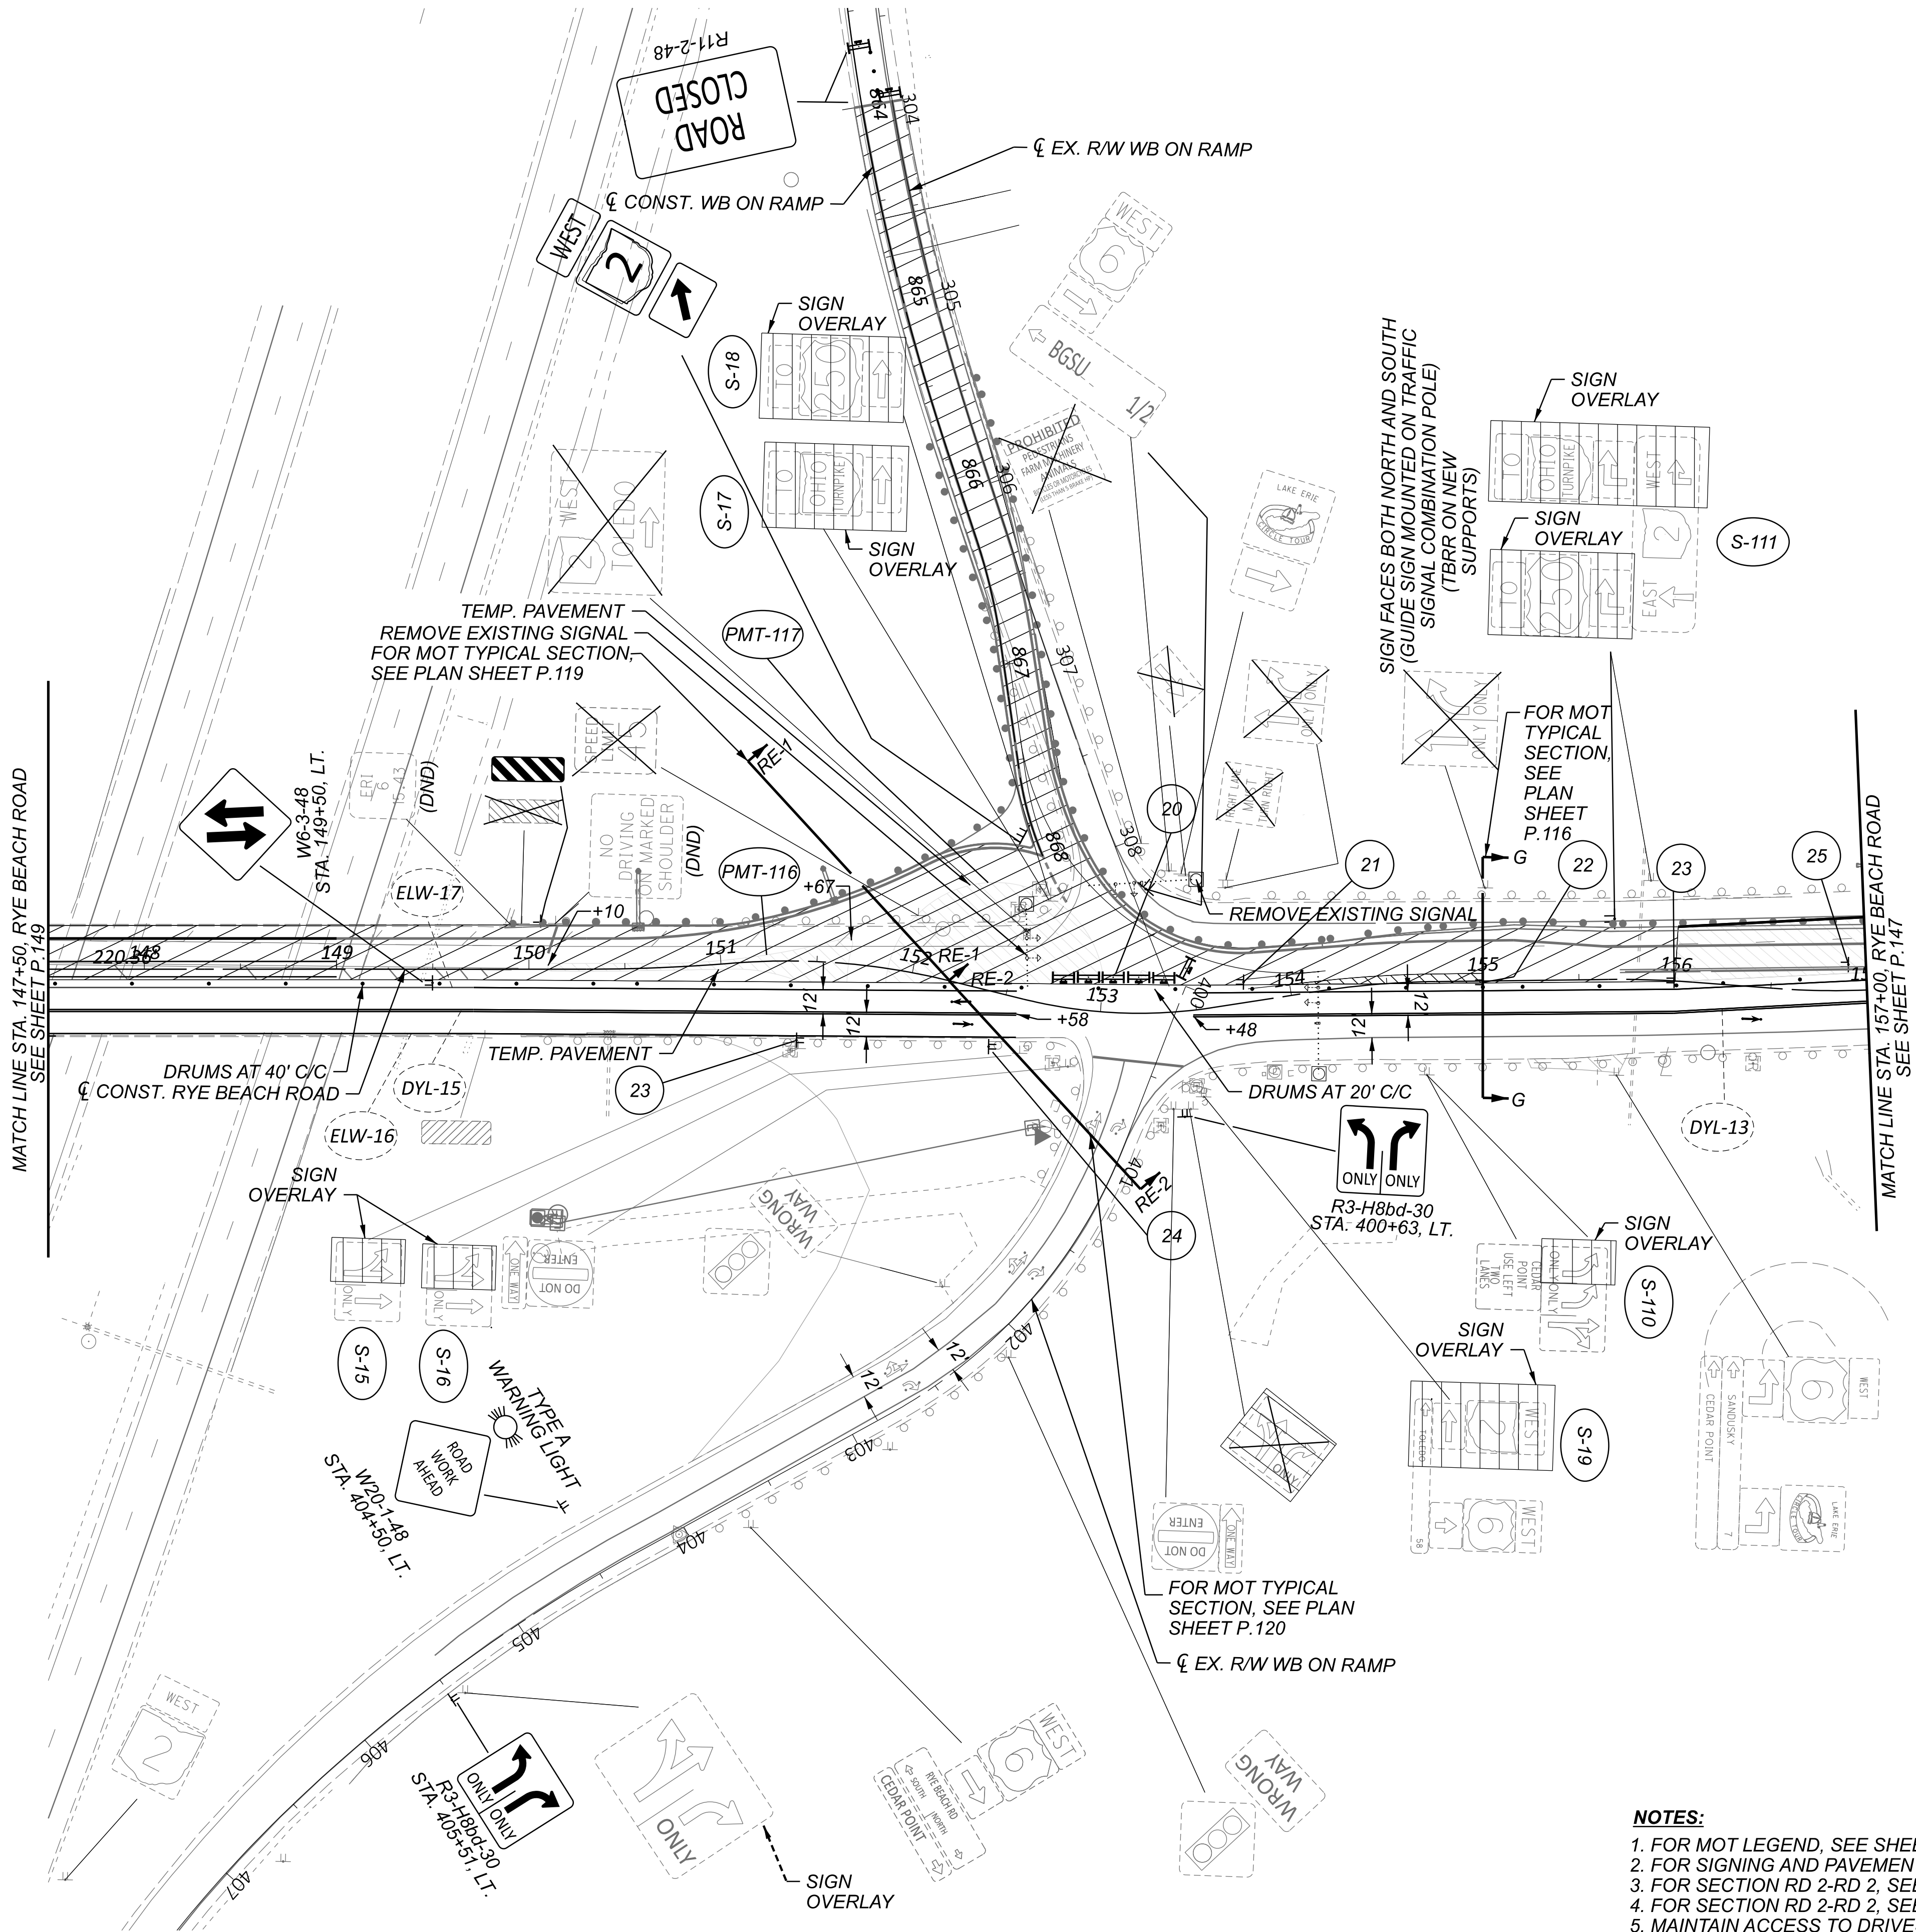

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. FOR SECTION RD 2-RD 2, SEE SHEET P.119.
 4. FOR SECTION RD 2-RD 2, SEE SHEET P.120.
 5. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

 20 TYPE B FLASHING (YELLOW) WARNING LIGHT 21 ROAD CLOSED R11-2-48 (PER SCD MT-98.30)	 22 TYPE A WARNING LIGHT 23 RAMP CLOSED AHEAD E5-H2f-48 STA. 151+40, RT. & STA. 156+00, LT. (PER MT-98.30)
 24 RAMP CLOSED E5-H2e-48 STA. 155+00, LT. (PER SCD MT-98.30)	 25 TYPE A WARNING LIGHT 26 ROAD WORK AHEAD W20-1-48 (PER SCD MT-98.30)



MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
RYE BEACH ROAD - STA. 147+50.00 TO STA. 157+00.00


DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570


SHEET TOTAL
P.153 782

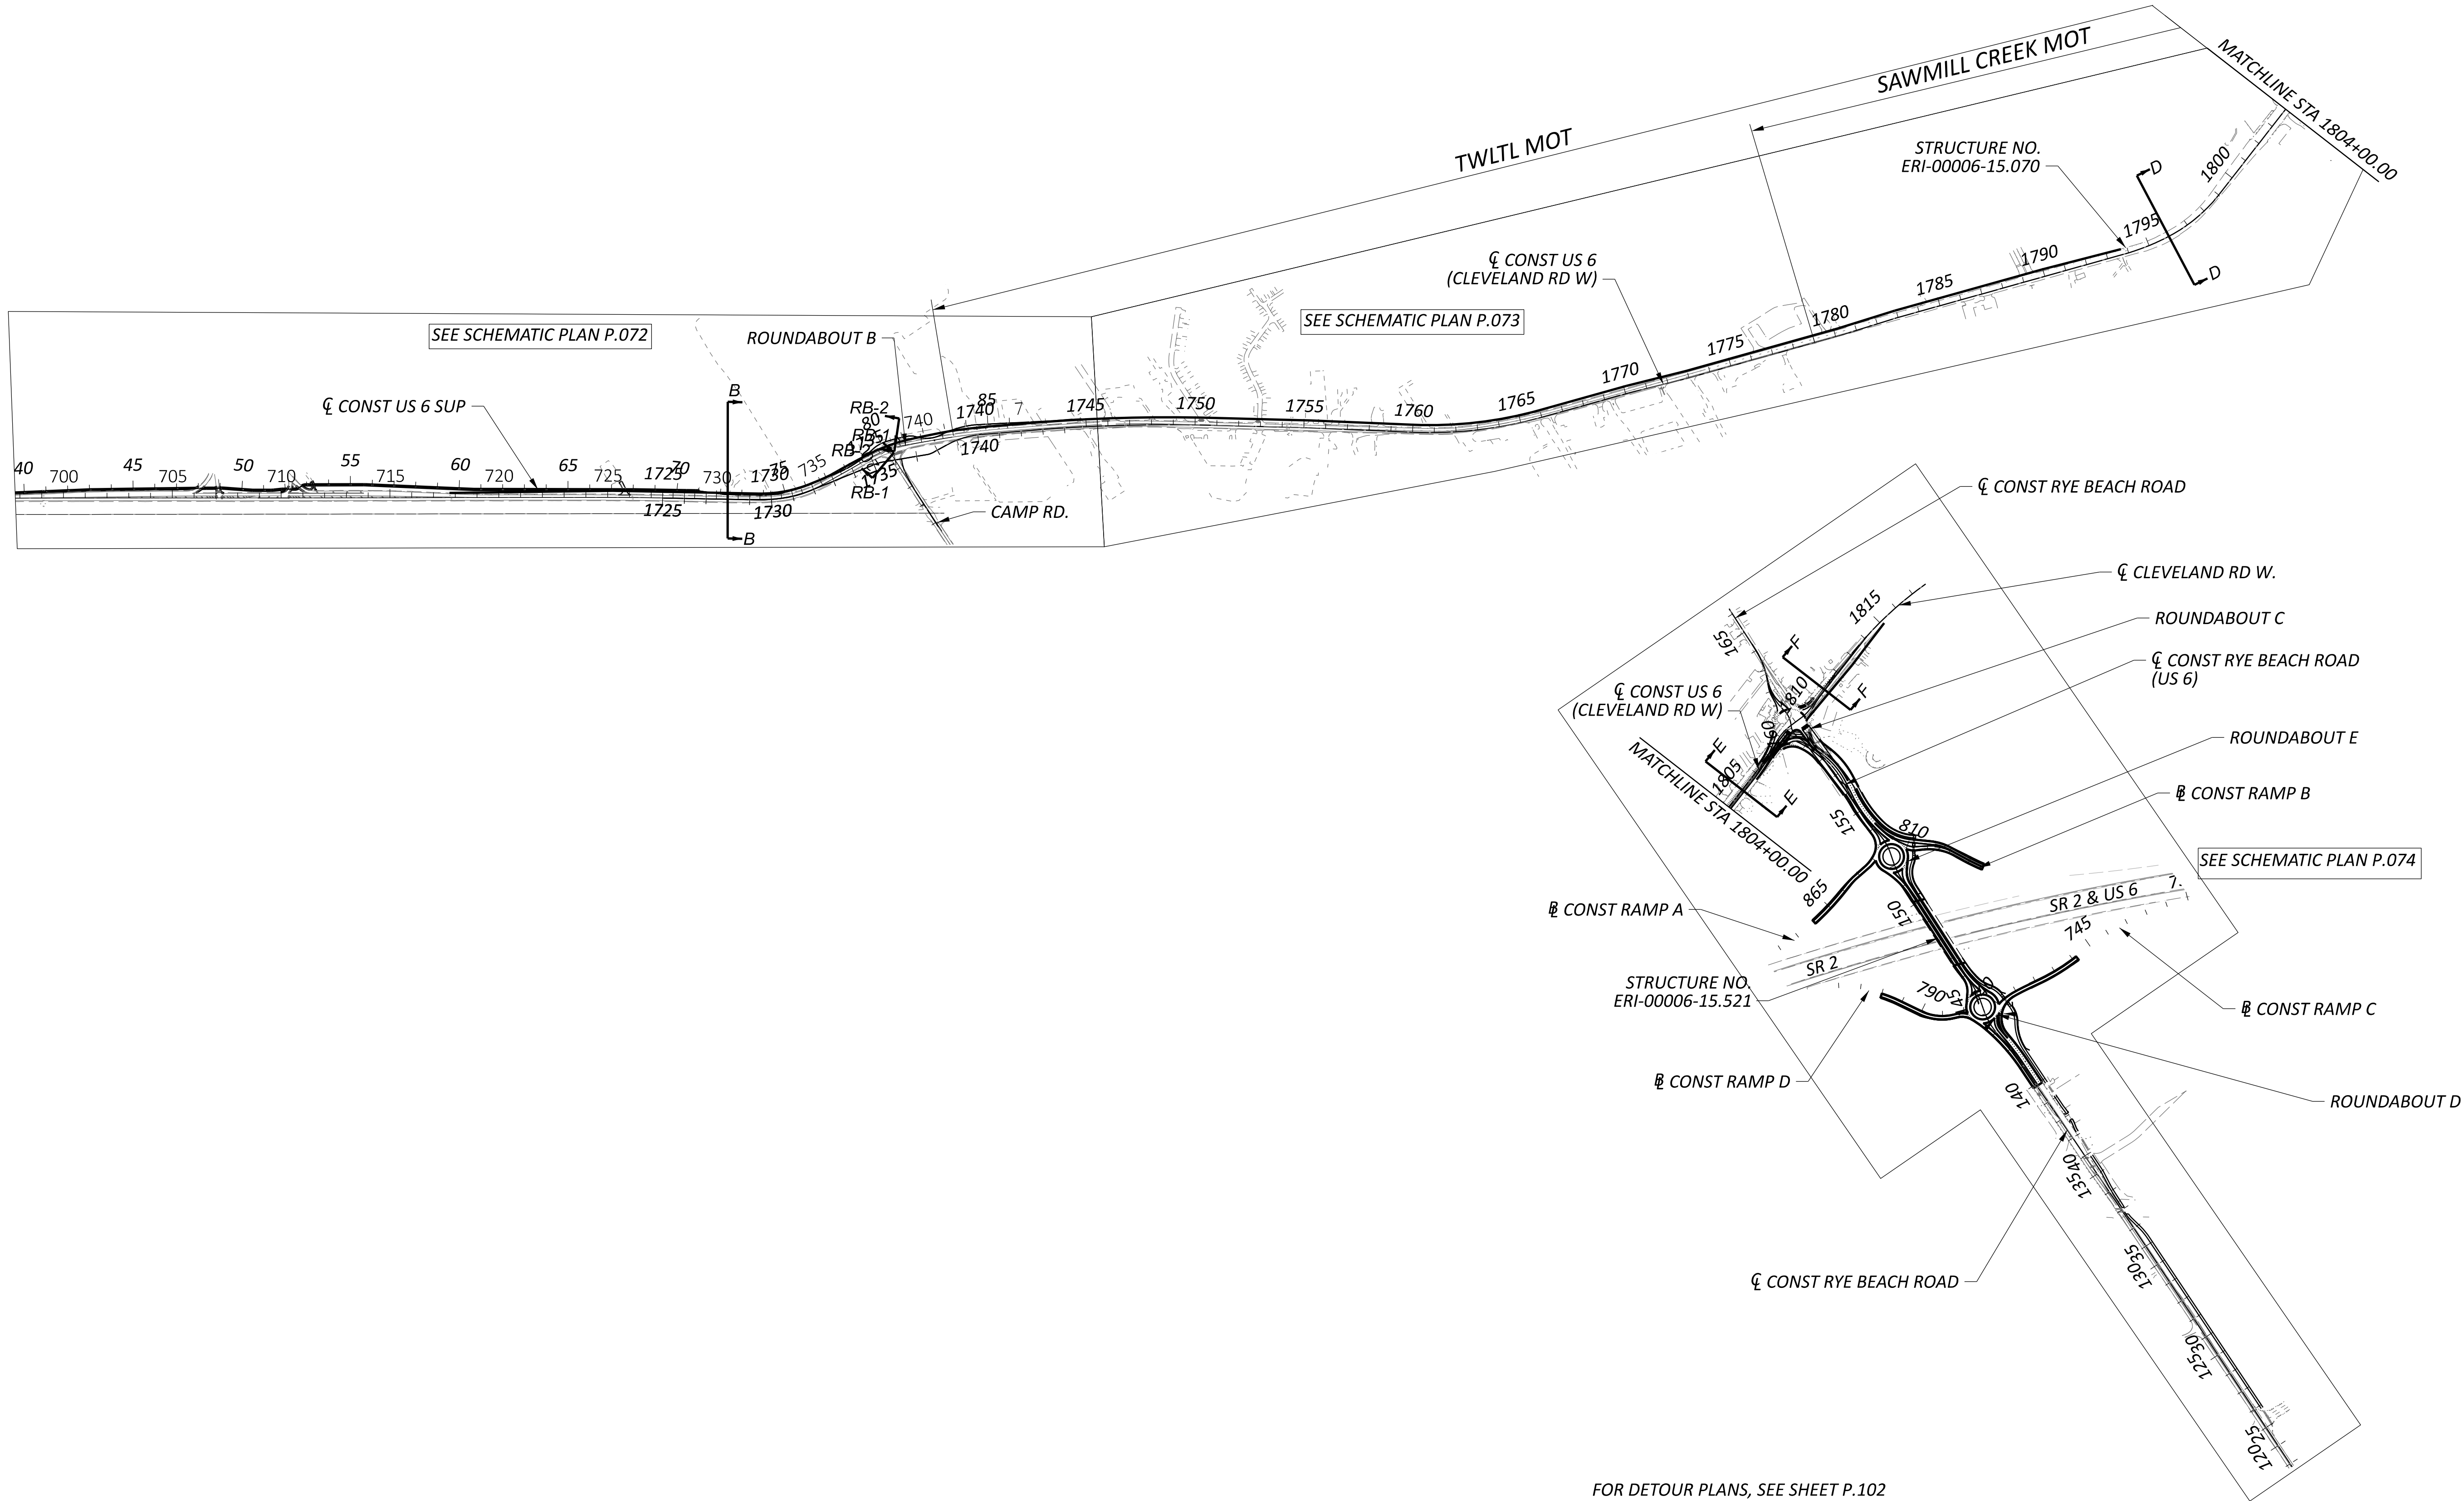

FOR DETOUR PLANS, SEE SHEET P.102

MOT OVERALL SCHEMATIC PLAN - PRE PHASE (2027/2028 CONSTRUCTION)


DESIGN AGENCY	
TRANSYSTEMS	
400 W. NATIONWIDE BLVD., STE. 225	
COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.071	TOTAL
	782

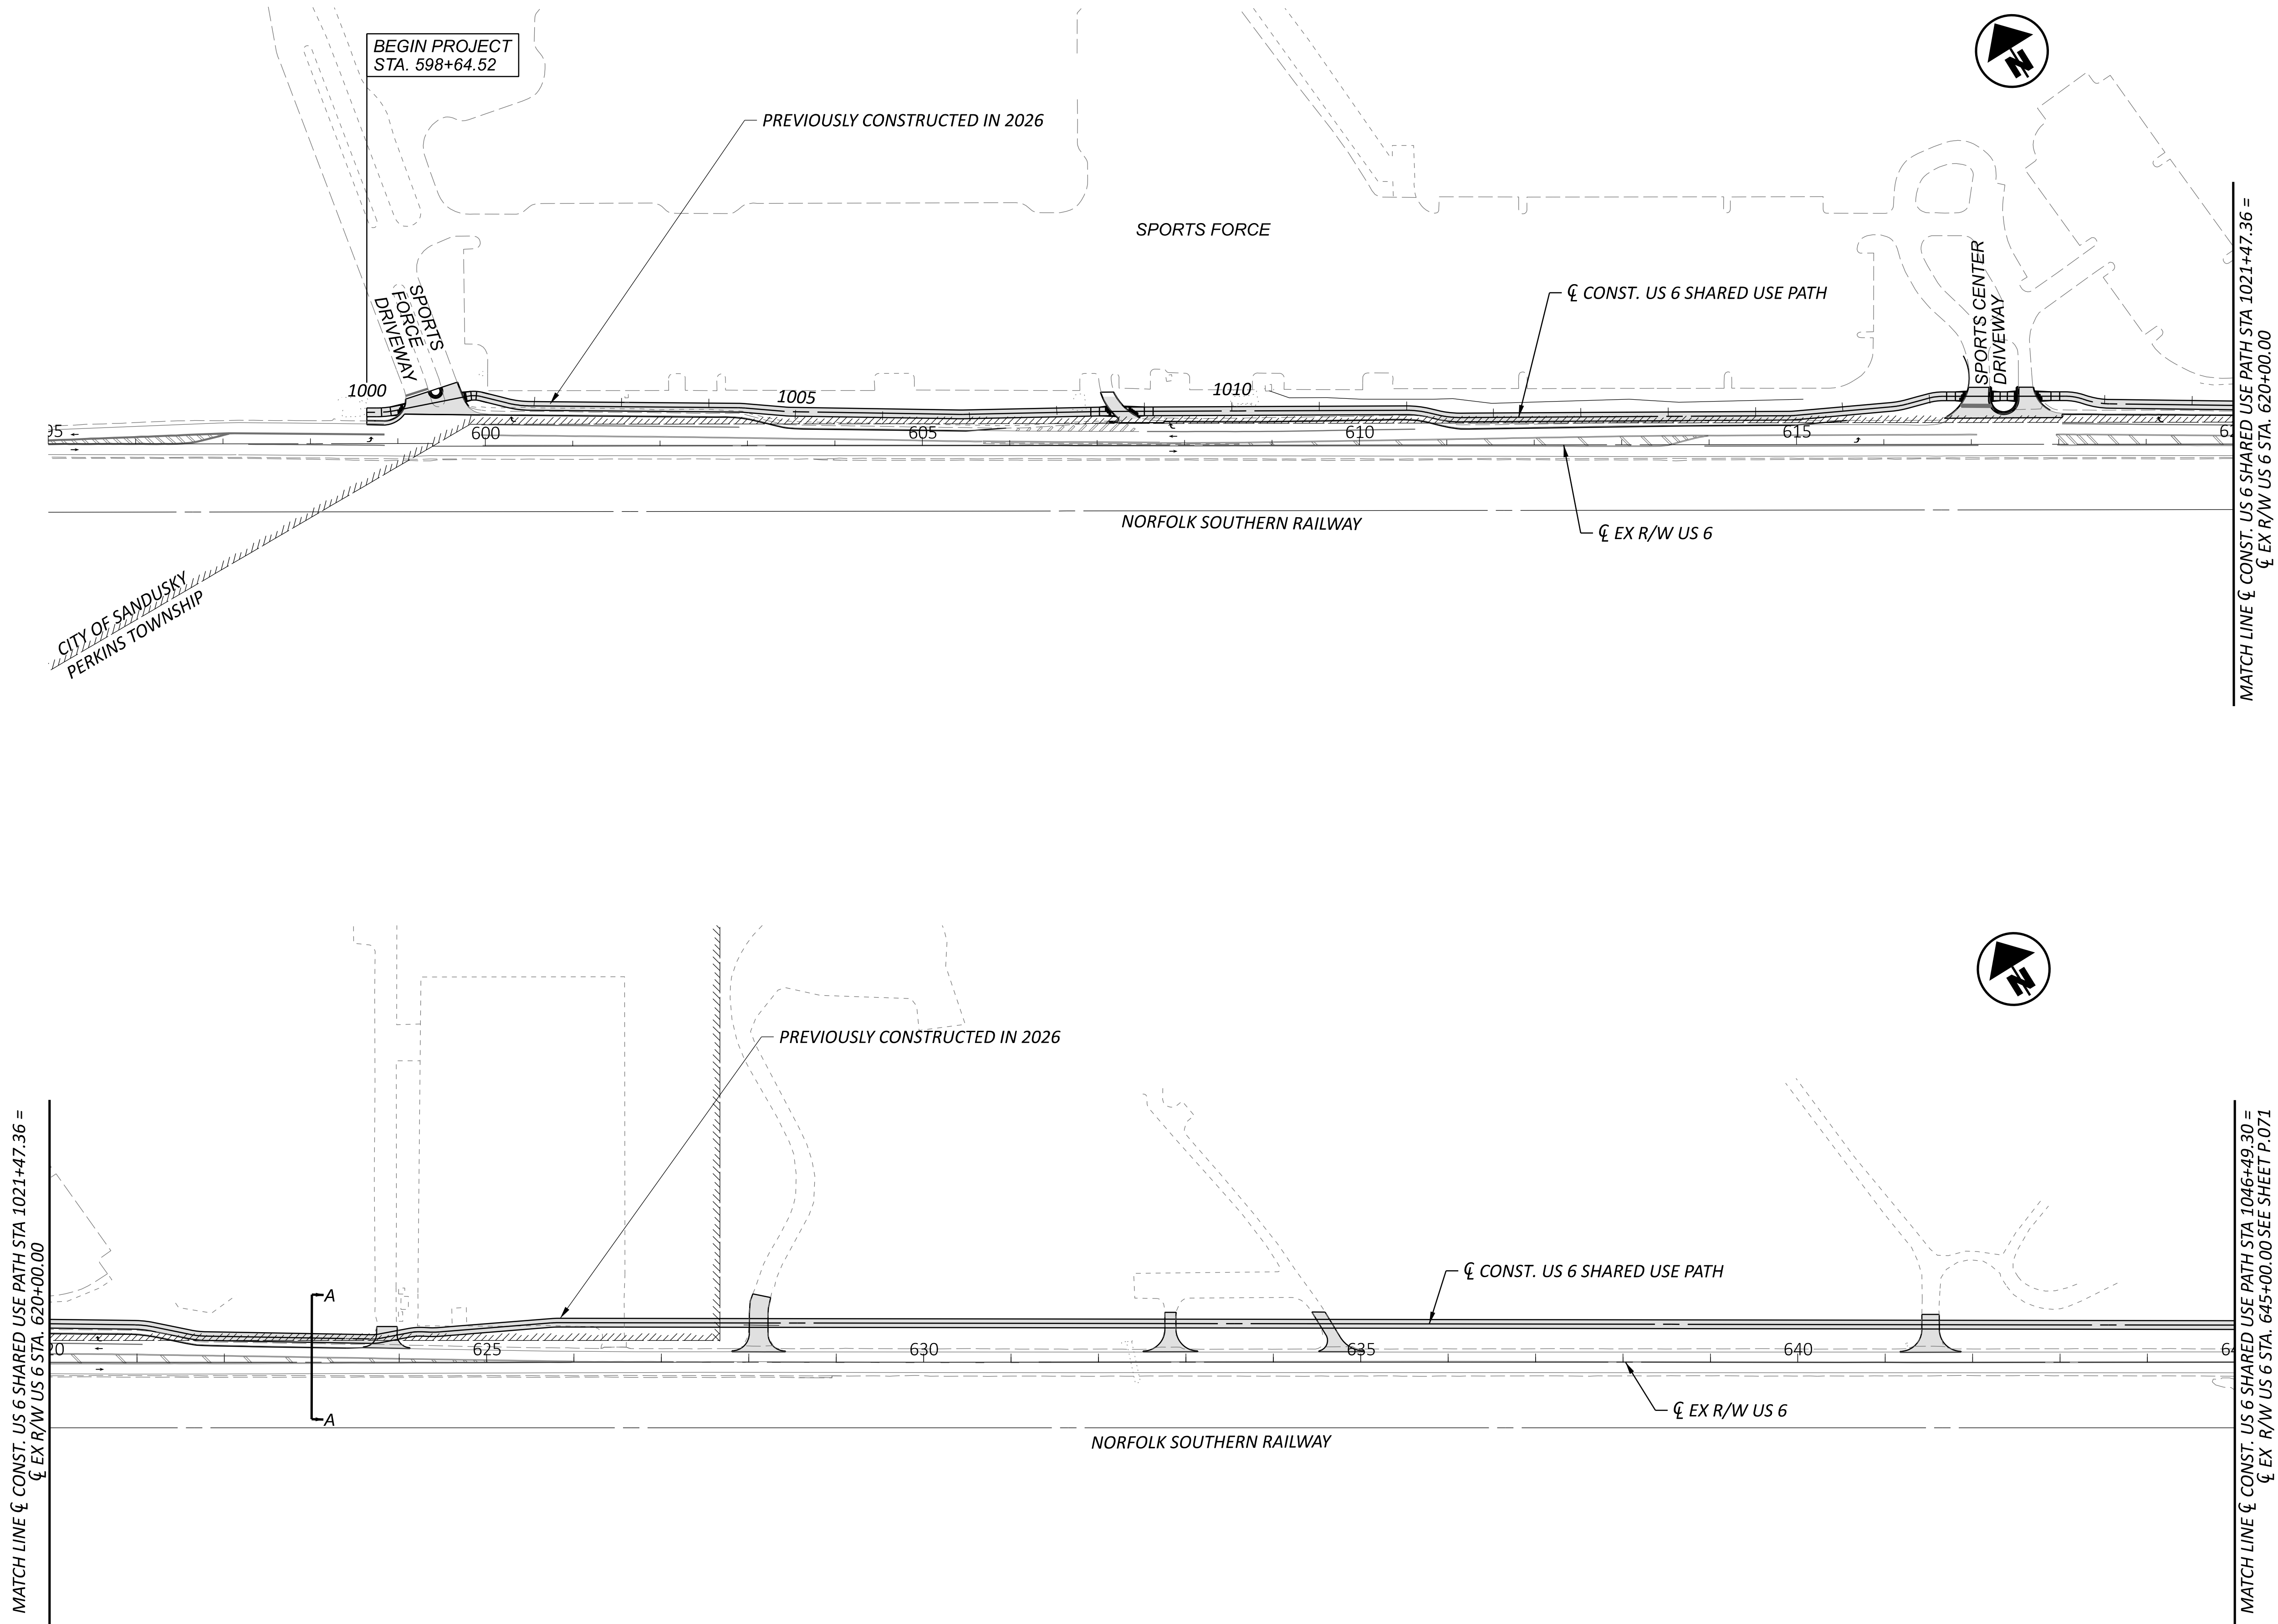

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075


MOT SCHEMATIC PLAN - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 BEGIN PROJECT TO STA 645+00

DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.072	782



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: GB102 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:22:43 PM USER: sadusei
 \\pw\vhohiodot-pw.dentley.com\chiodot-pw-02\Documents\01 Active Projects\District 03\03Eri\116570\402-Engineering_TransSystems\WOT\Sheets\116570_M8002_CV2027.dgn

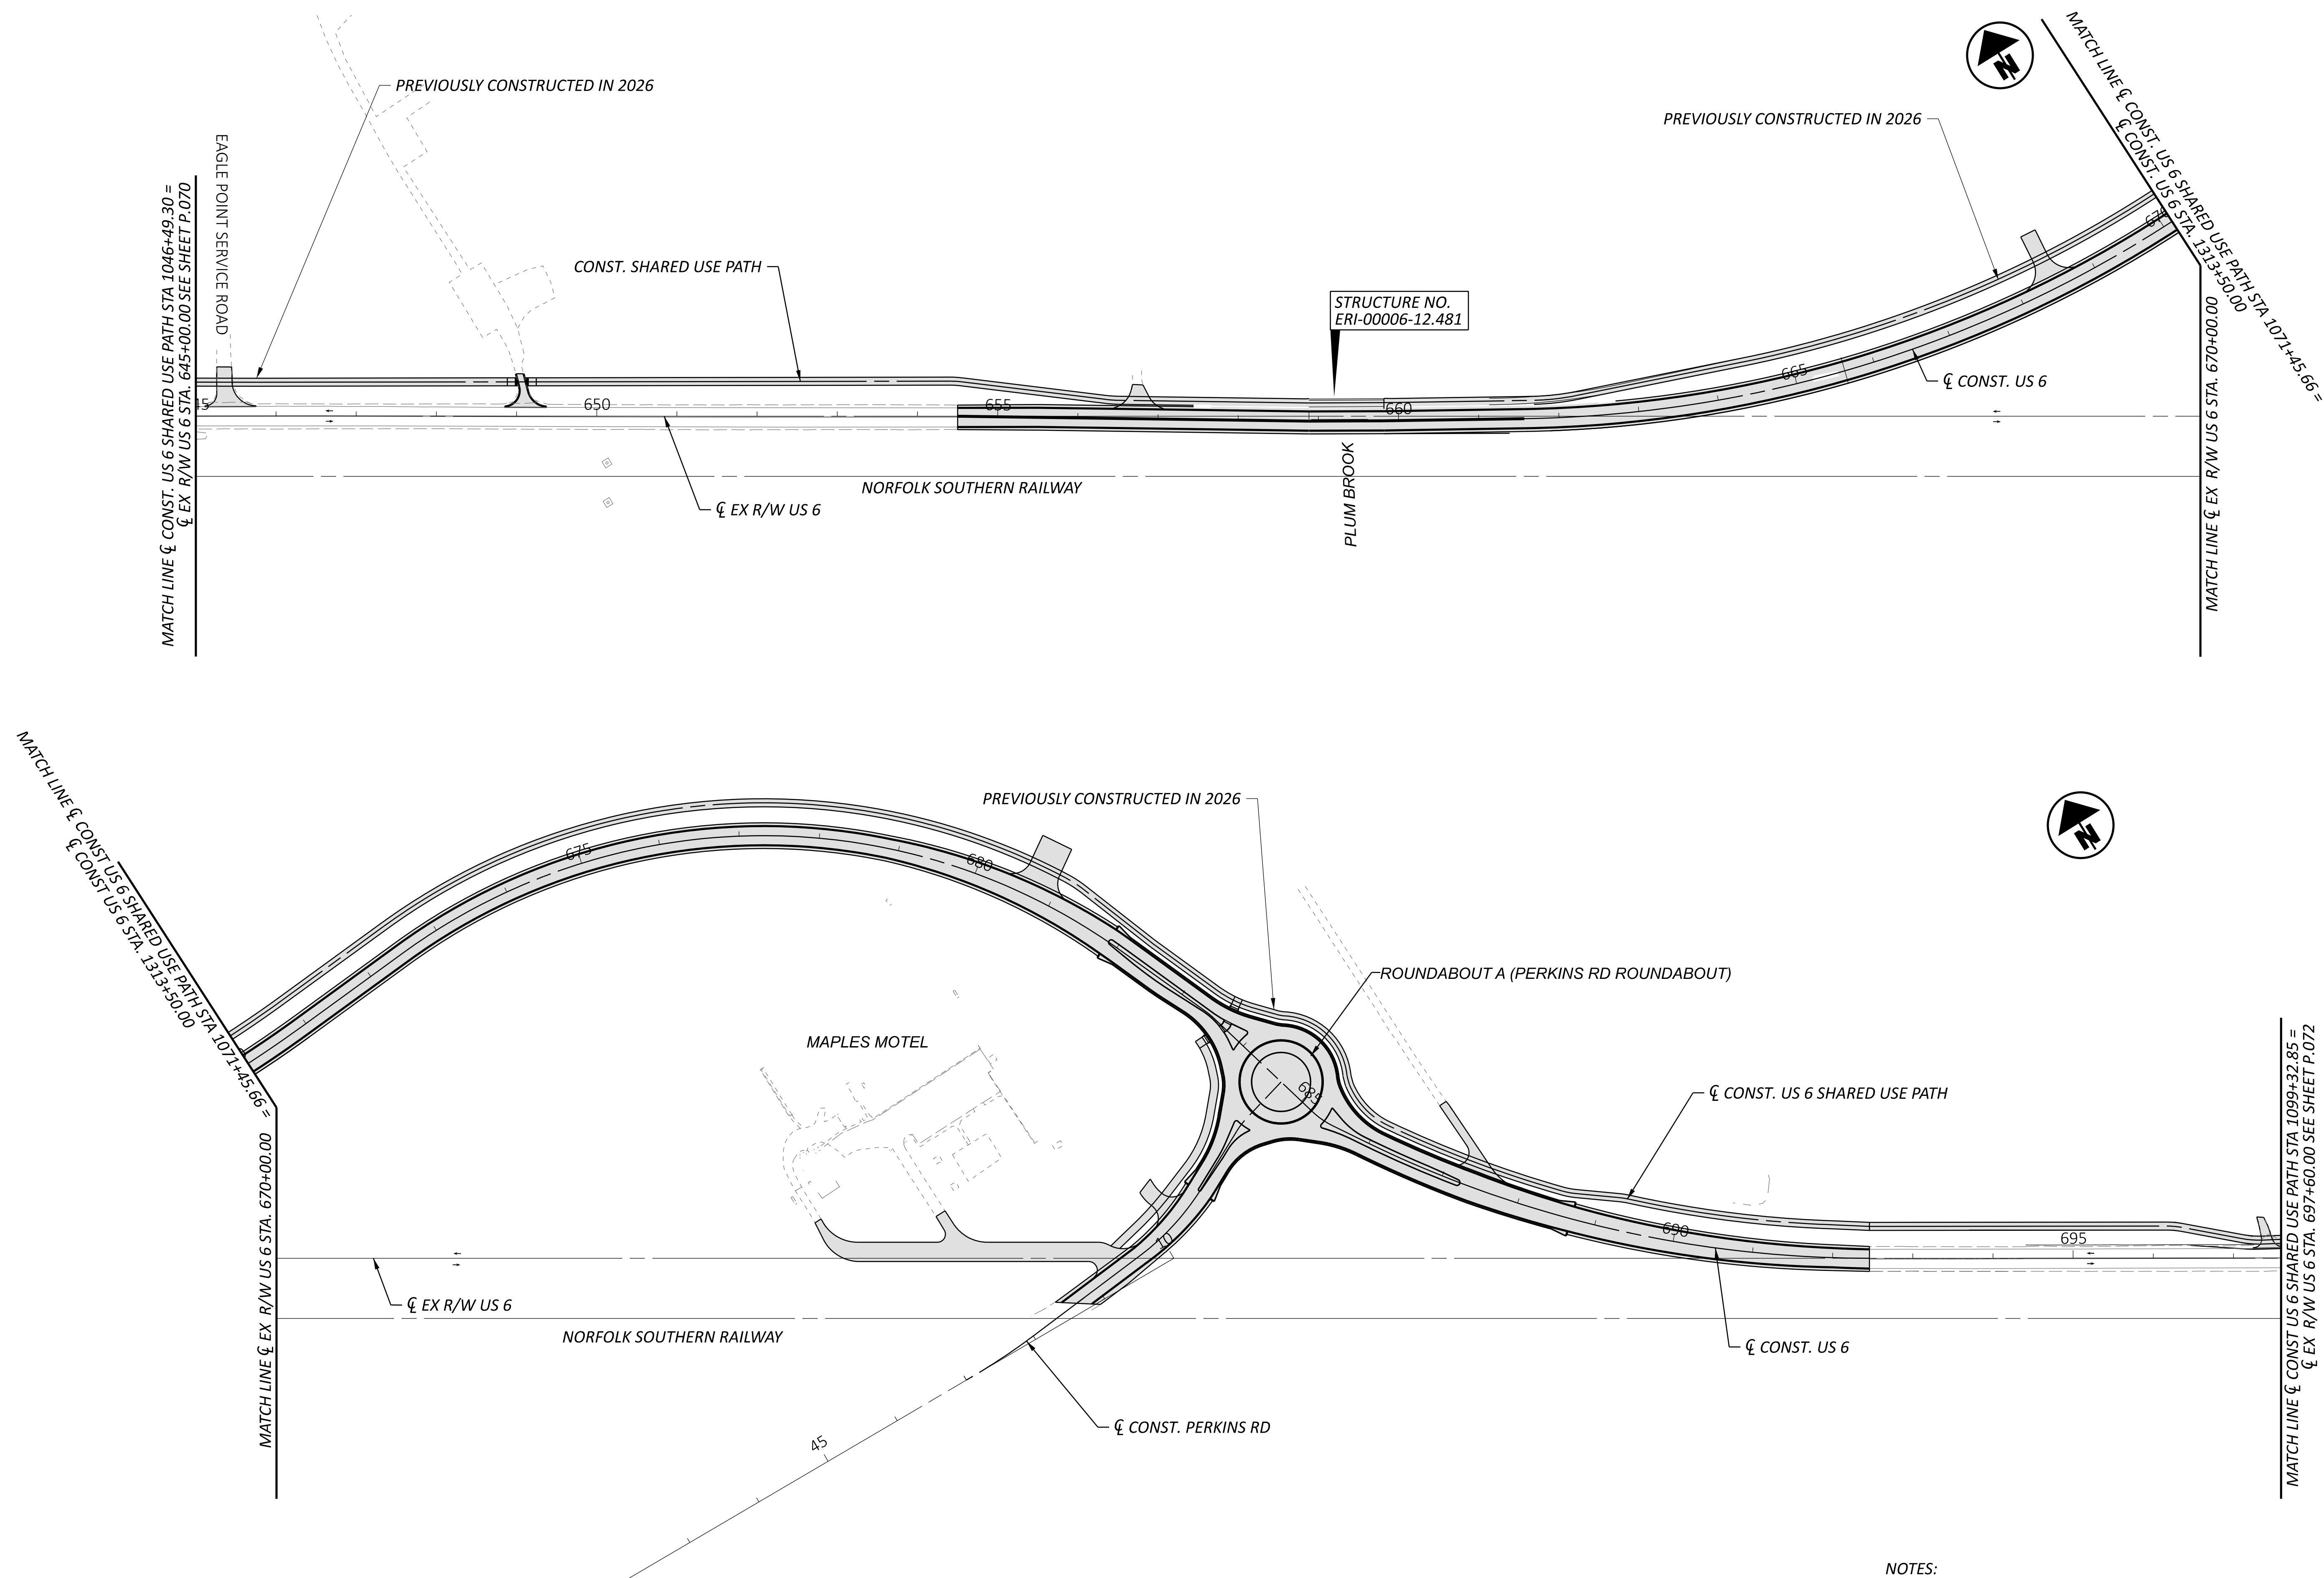

NOTES:

1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069.
2. FOR LEGEND, SEE SHEET P.068.

MOT SCHEMATIC PLAN - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 STA 645+00 TO STA 695+00

DESIGN AGENCY

TRANSYSTEMS

400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
SSA


REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.073 | 782

HORIZONTAL
SCALE IN FEET

A horizontal scale bar with a black and white checkerboard pattern. It is marked with '0' at the left end, '50' at the first black segment, '100' at the second white segment, and '200' at the right end.

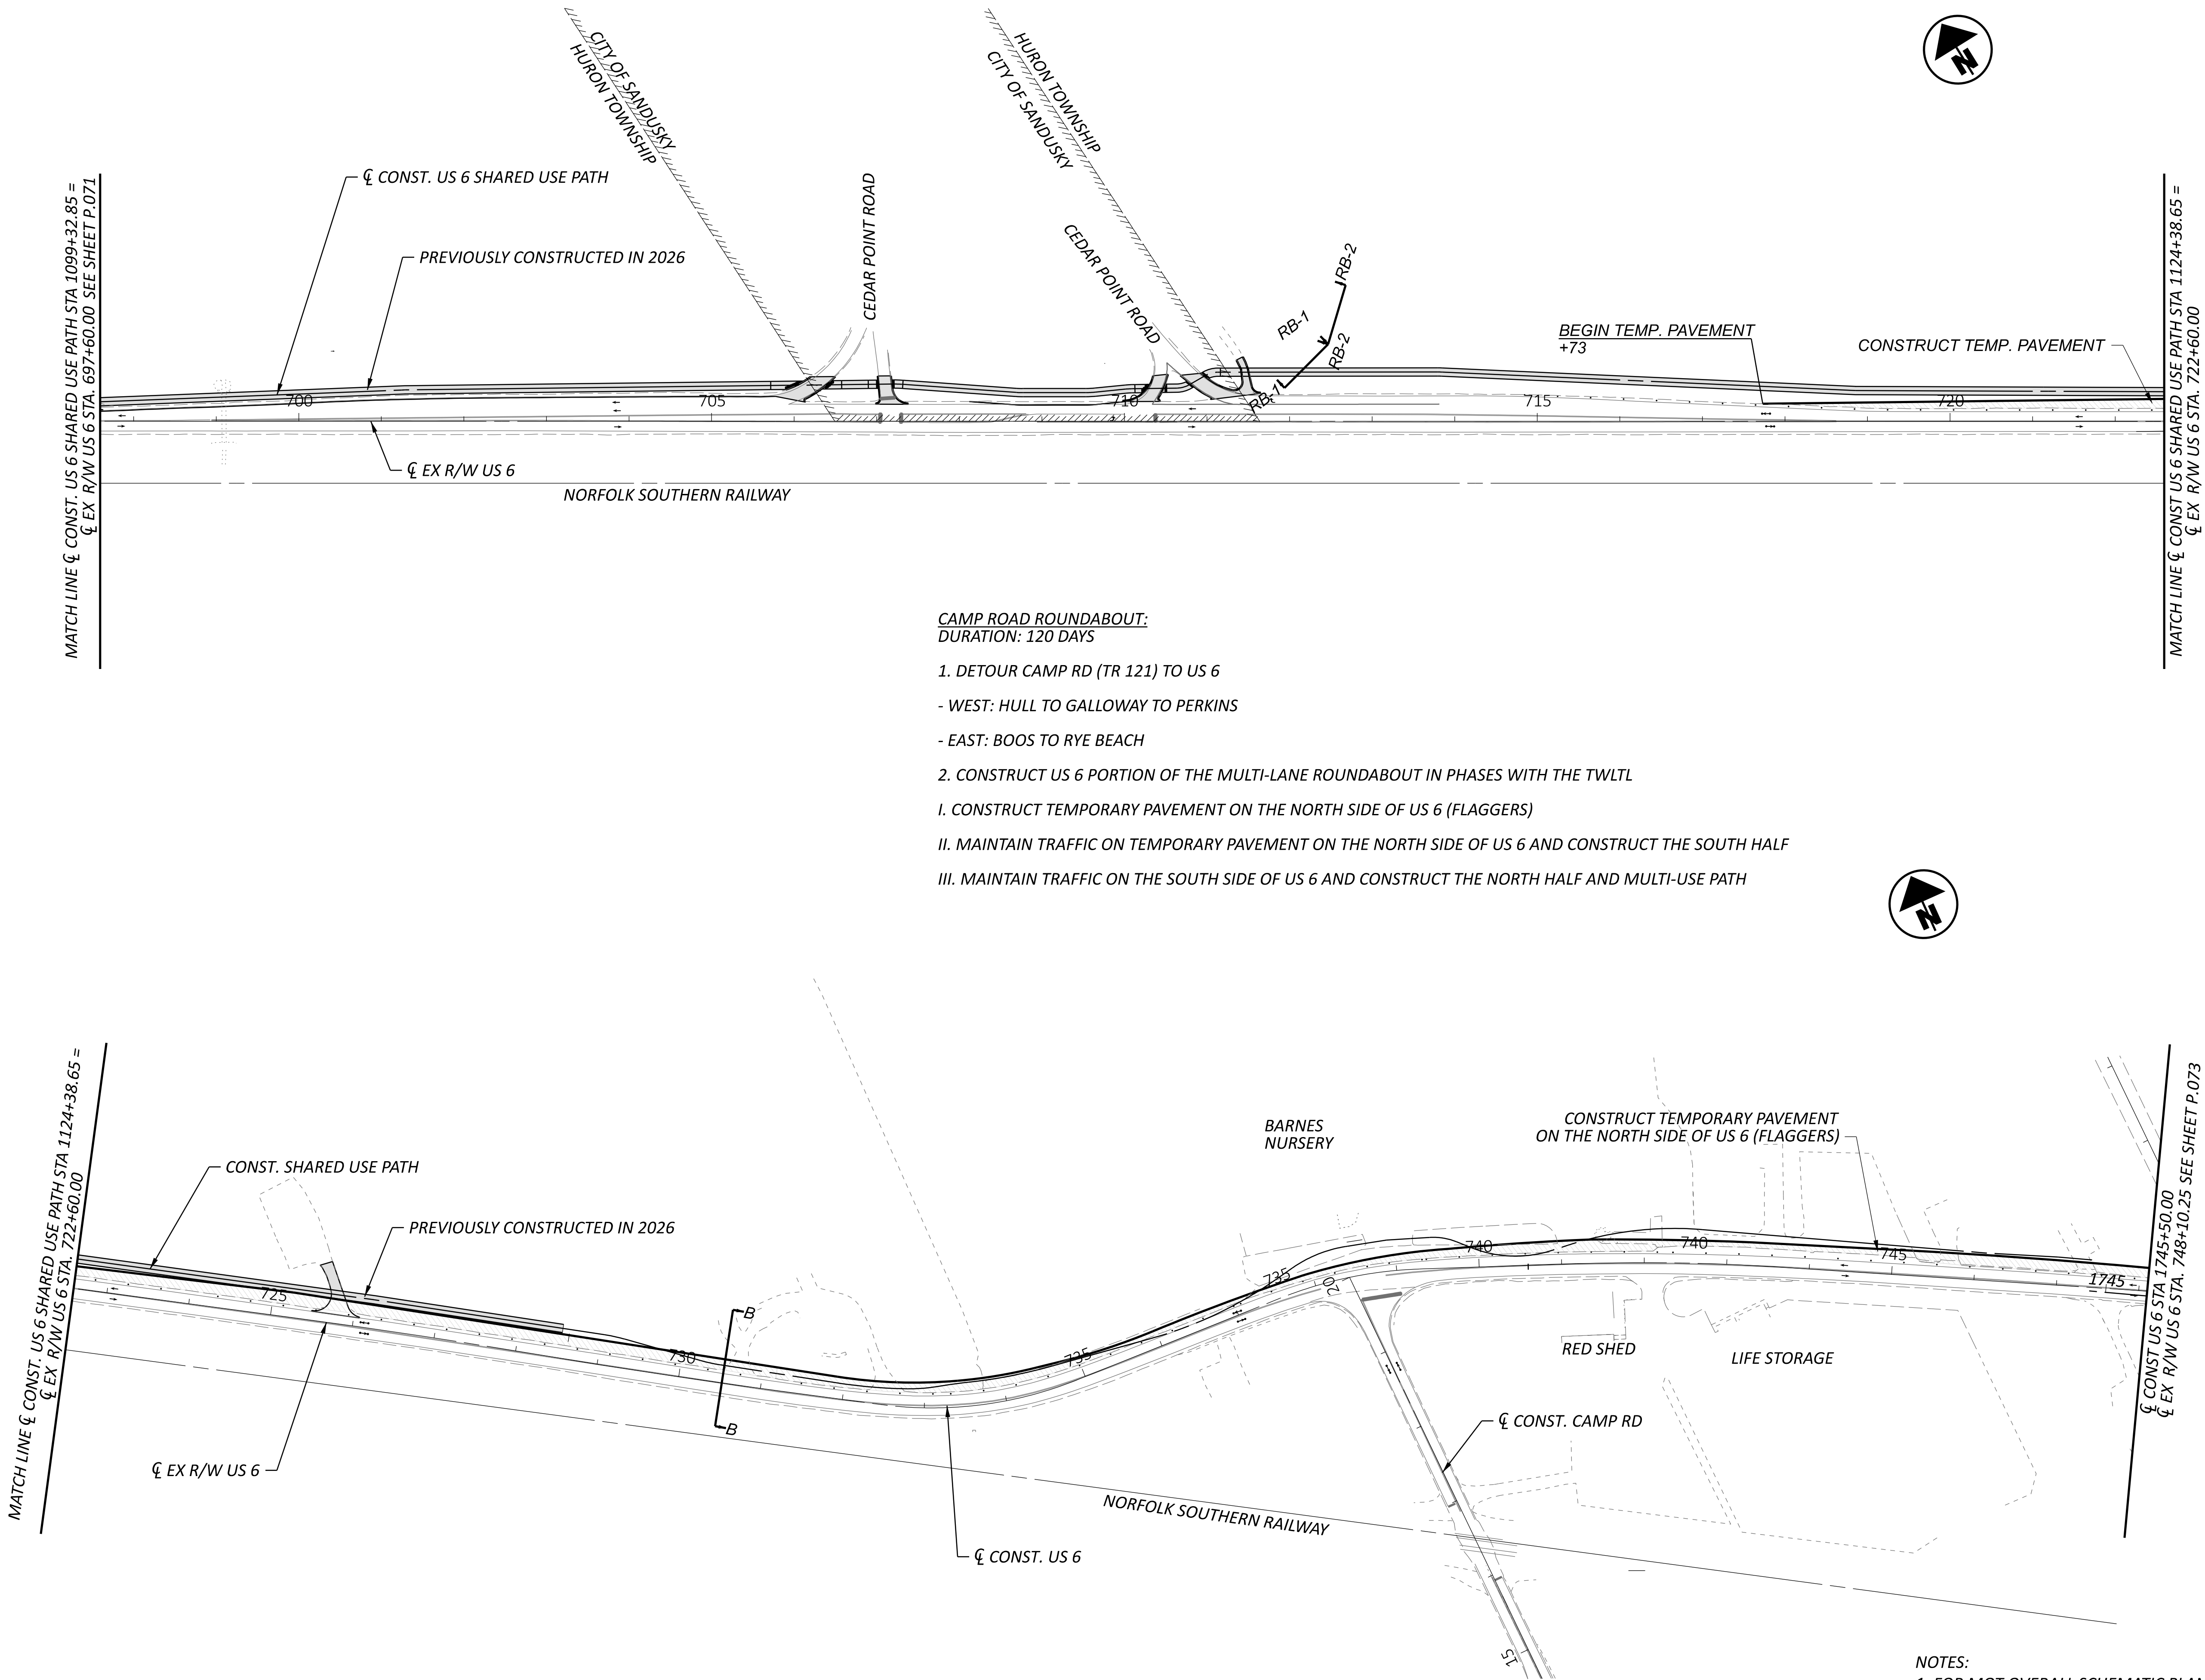

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

MOT SCHEMATIC PLAN - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 STA 695+00 TO STA 745+50


TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.074 782



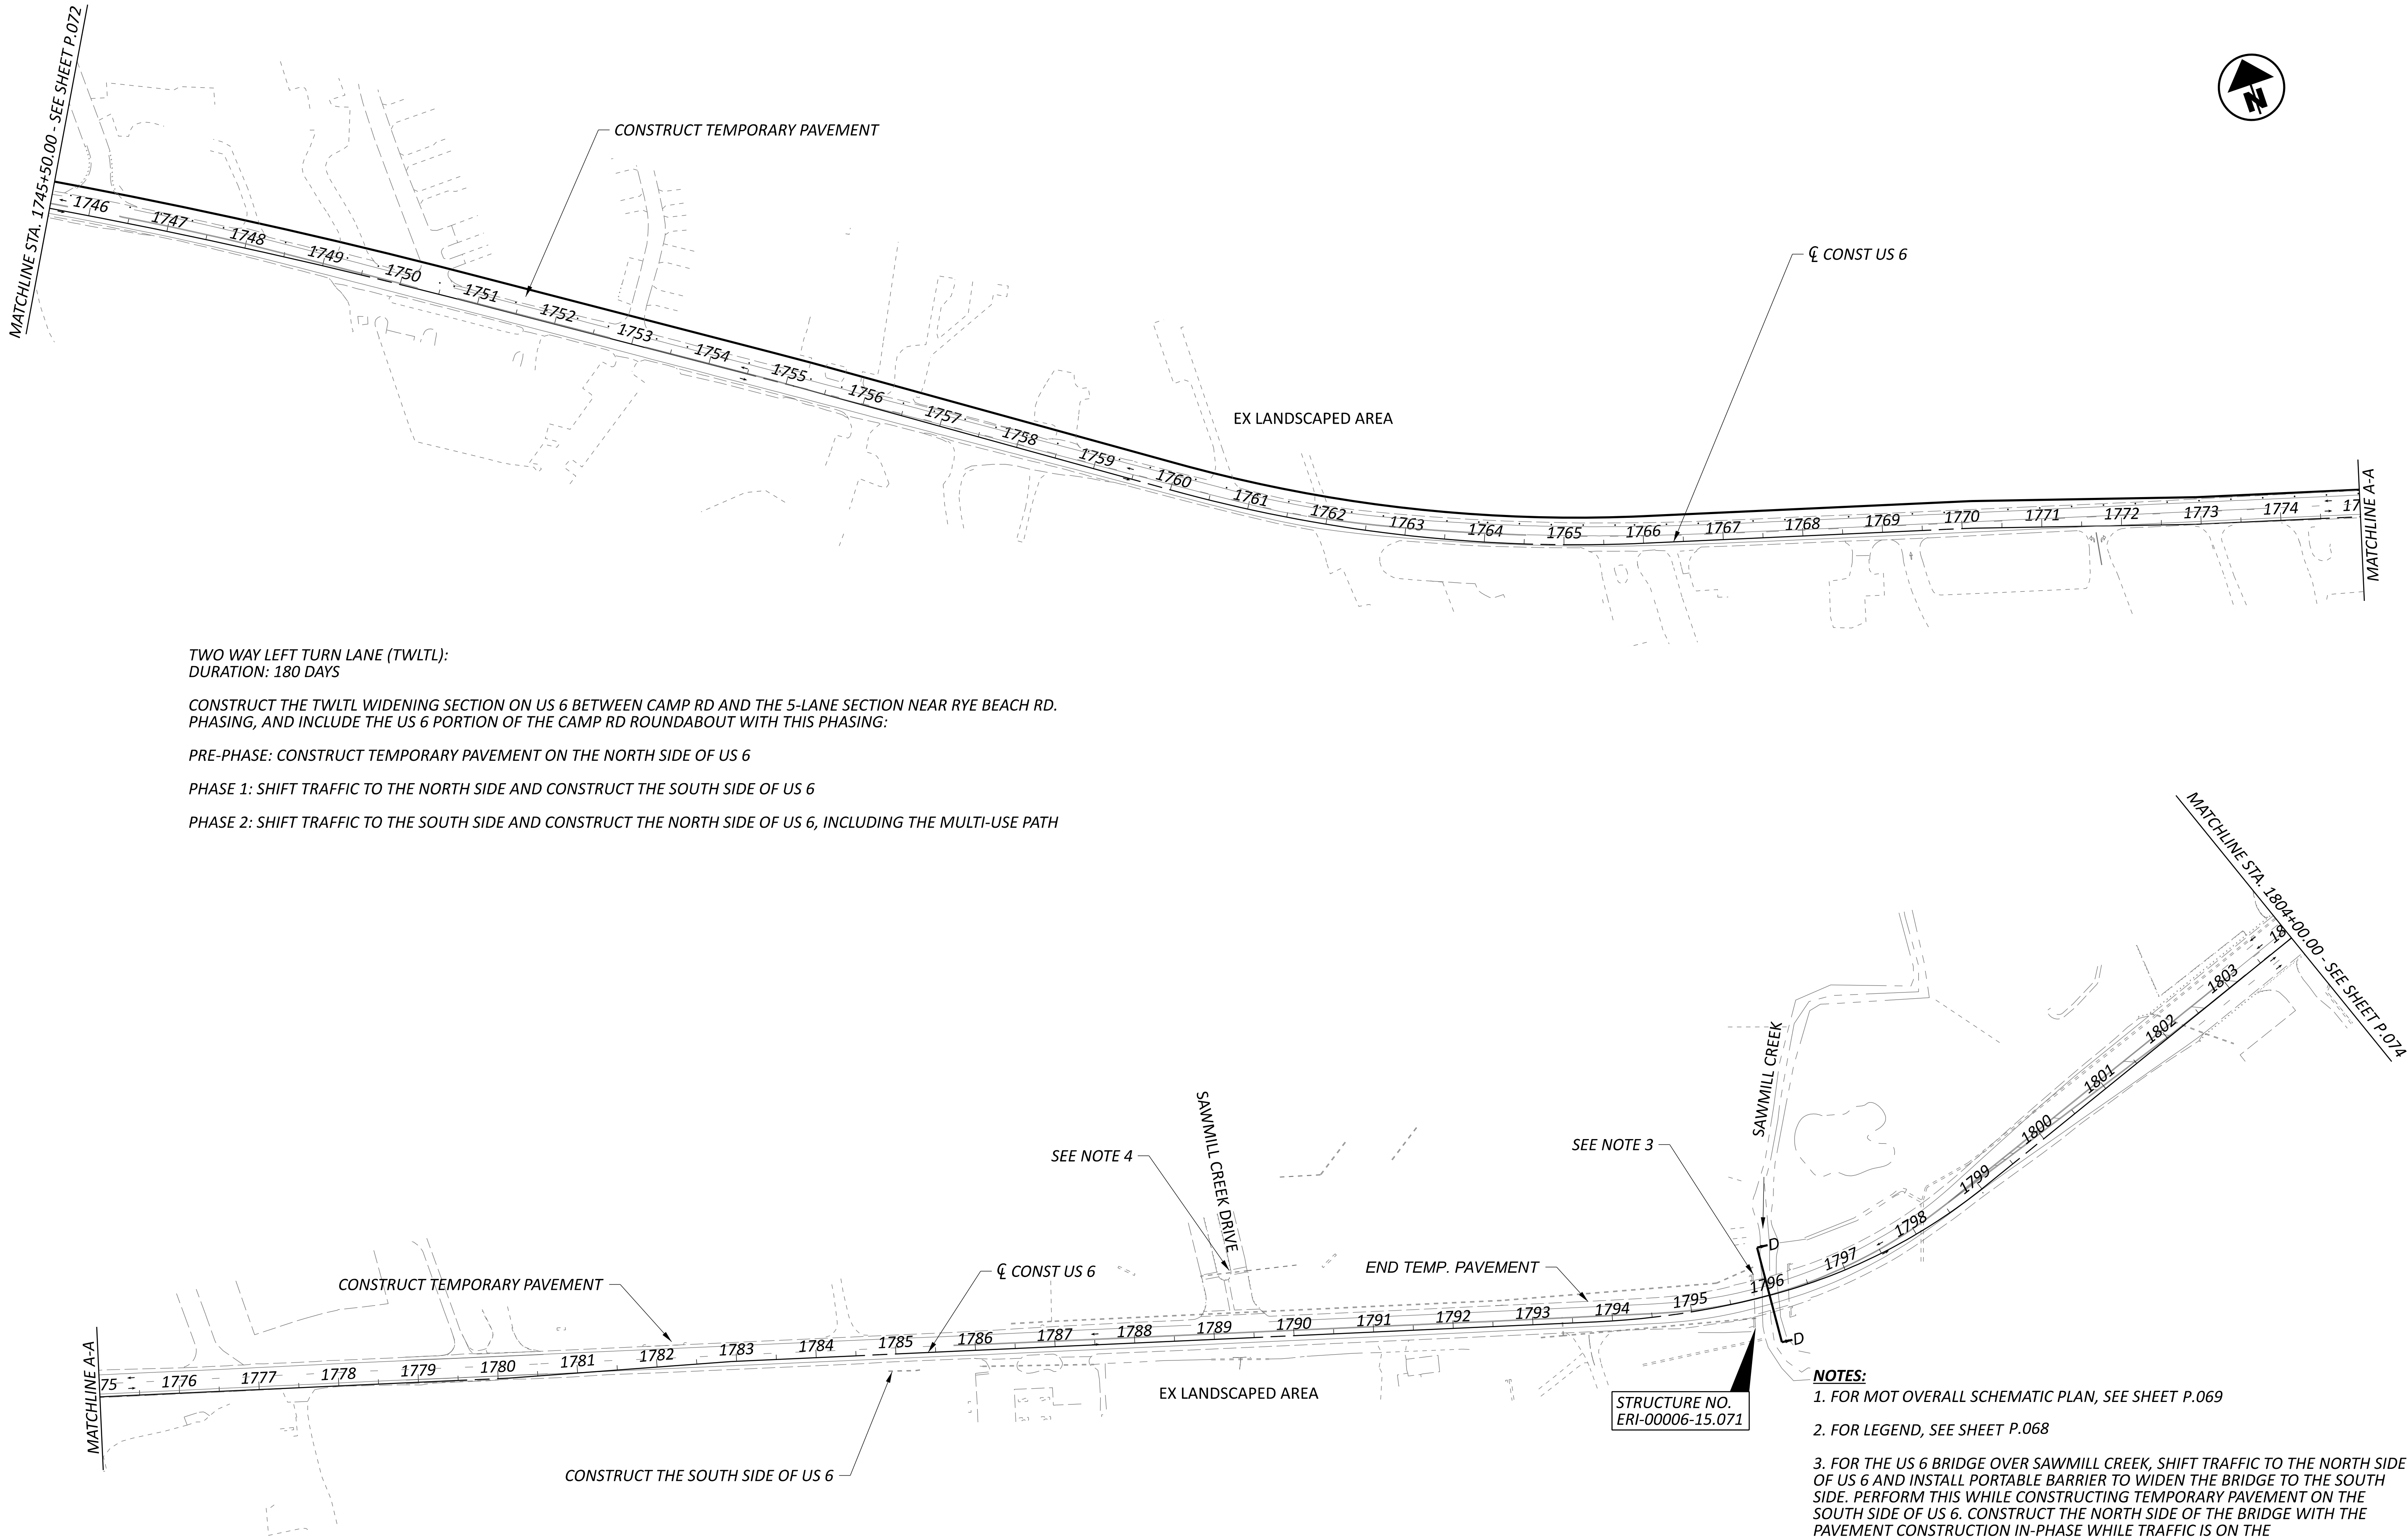

TWO WAY LEFT TURN LANE (TWLTL):
DURATION: 180 DAYS


CONSTRUCT THE TWLTL WIDENING SECTION ON US 6 BETWEEN CAMP RD AND THE 5-LANE SECTION NEAR RYE BEACH RD.
PHASING, AND INCLUDE THE US 6 PORTION OF THE CAMP RD ROUNDABOUT WITH THIS PHASING:

PRE-PHASE: CONSTRUCT TEMPORARY PAVEMENT ON THE NORTH SIDE OF US 6

PHASE 1: SHIFT TRAFFIC TO THE NORTH SIDE AND CONSTRUCT THE SOUTH SIDE OF US 6

PHASE 2: SHIFT TRAFFIC TO THE SOUTH SIDE AND CONSTRUCT THE NORTH SIDE OF US 6, INCLUDING THE MULTI-USE PATH

- NOTES:**
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
 2. FOR LEGEND, SEE SHEET P.068
 3. FOR THE US 6 BRIDGE OVER SAWMILL CREEK, SHIFT TRAFFIC TO THE NORTH SIDE OF US 6 AND INSTALL PORTABLE BARRIER TO WIDEN THE BRIDGE TO THE SOUTH SIDE. PERFORM THIS WHILE CONSTRUCTING TEMPORARY PAVEMENT ON THE SOUTH SIDE OF US 6. CONSTRUCT THE NORTH SIDE OF THE BRIDGE WITH THE PAVEMENT CONSTRUCTION IN-PHASE WHILE TRAFFIC IS ON THE NEWLY-CONSTRUCTED SOUTH SIDE OF THE BRIDGE. ASSUME CONSTRUCTION DURATION OF 60 DAYS.
 4. MAINTAIN THIS DRIVE PART-WIDTH DURING CONSTRUCTION TO RE-BUILD THE DRIVE AND TURN LANES IN THE TWLTL SECTION. SHIFT TRAFFIC TO ONE SIDE AND CONSTRUCT THE OTHER FOR BOTH PHASES. ASSUME CONSTRUCTION DURATION OF 120 DAYS.

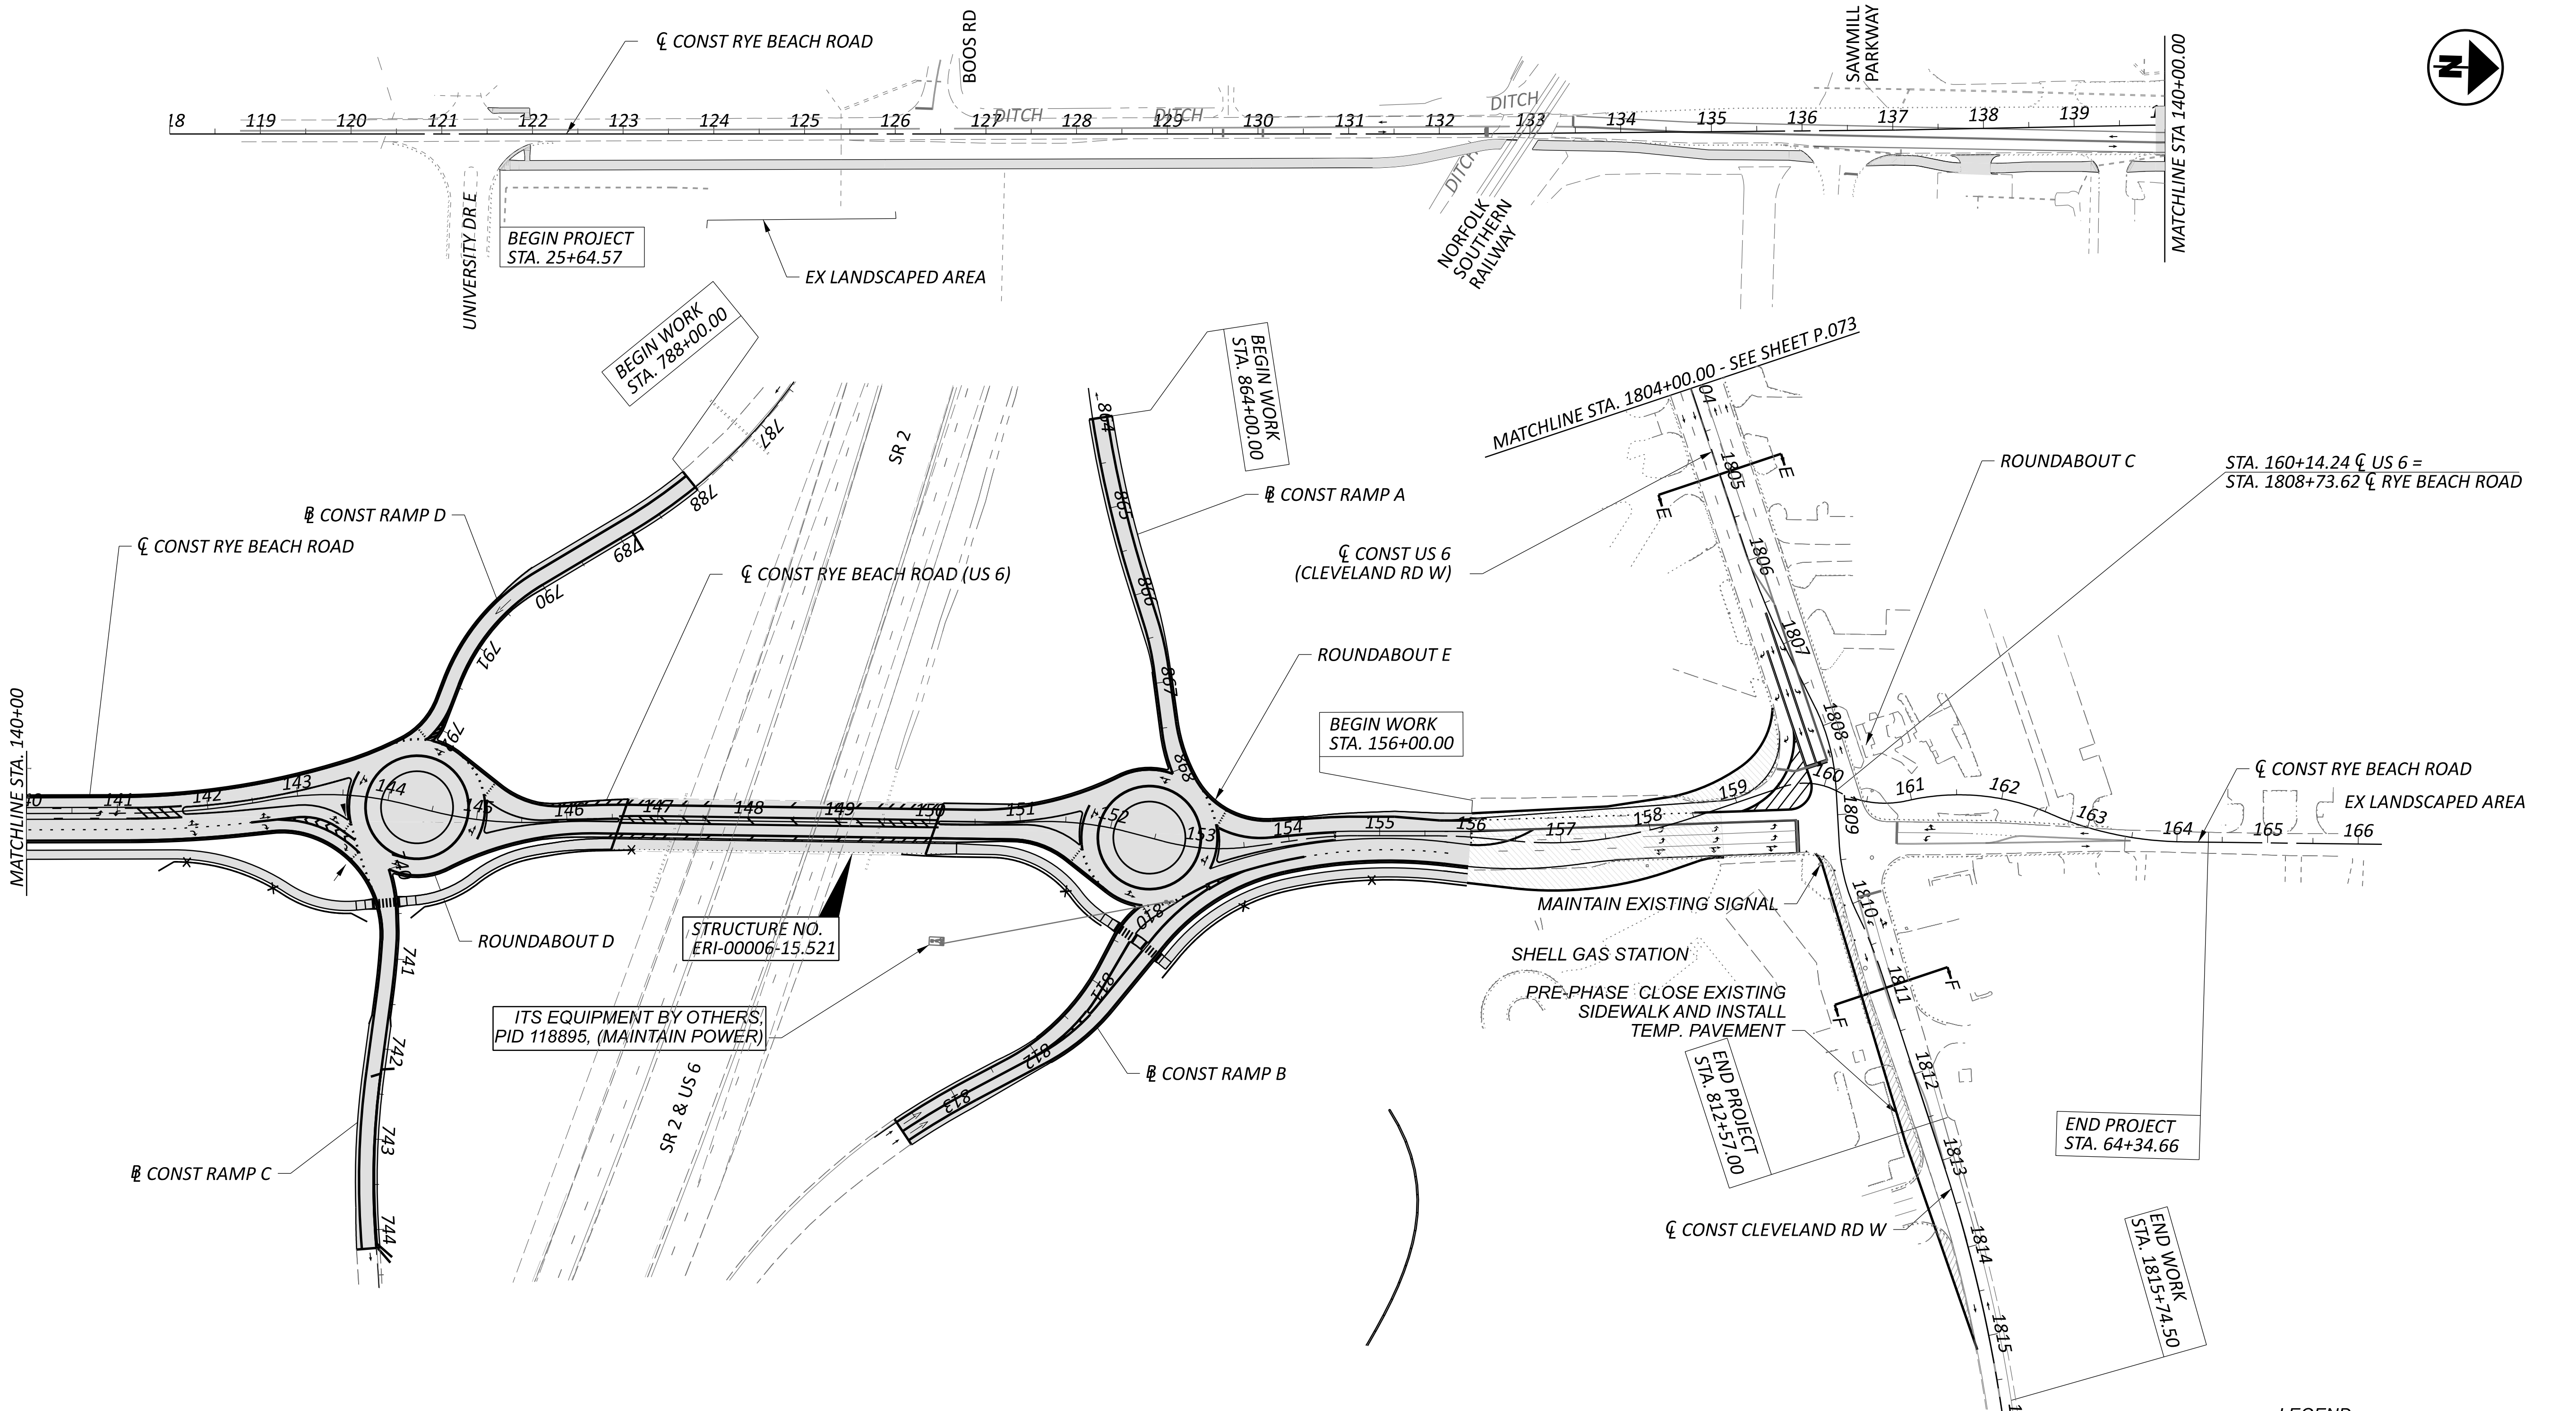

RYE BEACH ROUNDABOUTS:
DURATION: 180 DAYS
CEDAR POINT: NO ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER


PRE-PHASE:
CONSTRUCT TEMPORARY ROAD AND GRADING WITH MINIMAL IMPACTS TO EXISTING TRAFFIC.

LEGEND:


	EMBANKMENT AND GRADING CONSTRUCTED IN PRE-PHASE
	PAVEMENT CONSTRUCTED IN PREVIOUS PHASE
	WORK ZONE
	TEMPORARY PAVEMENT
	DIRECTION OF TRAFFIC DRUMS

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

MOT SCHEMATIC PLAN - PRE PHASE (2027/2028 CONSTRUCTION)
RYE BEACH ROAD STA 118+00.00 TO STA 166+00.00

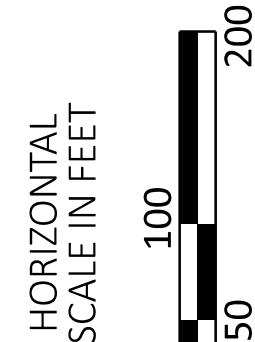

DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.076	782

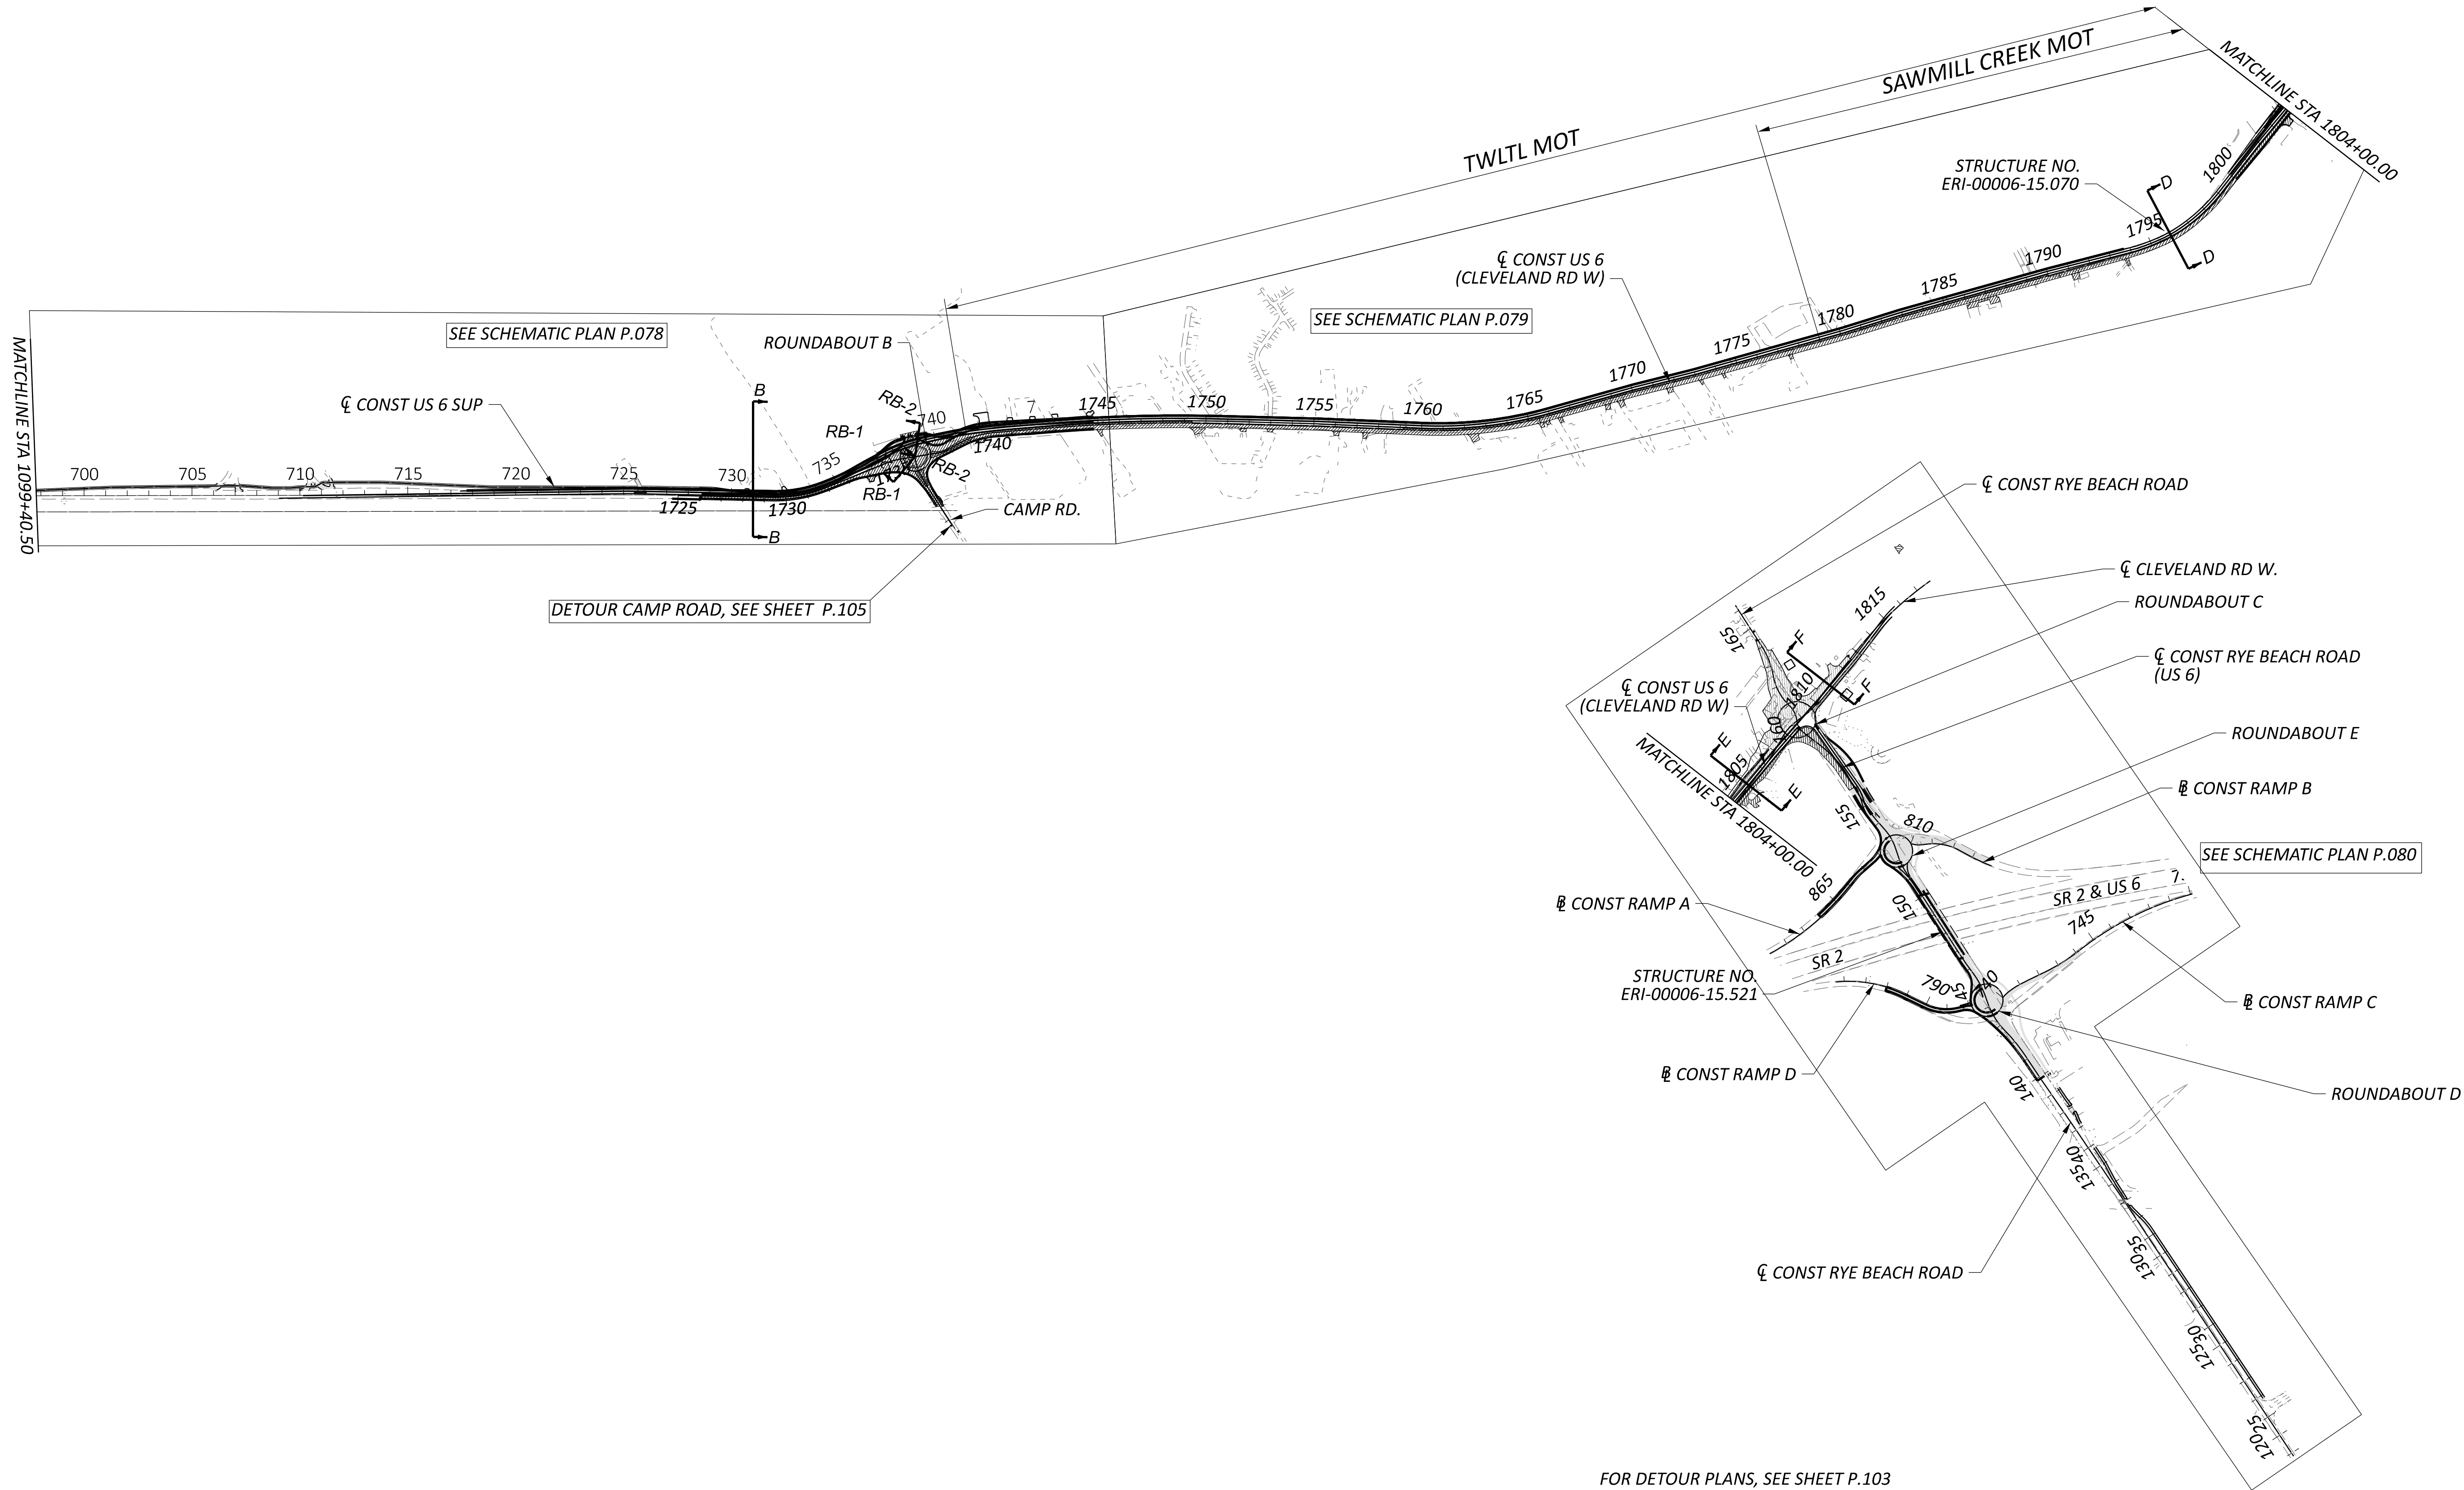

FOR DETOUR PLANS, SEE SHEET P.103

MOT OVERALL SCHEMATIC PLAN - PHASE 1 (2027/2028 CONSTRUCTION)

TRANSYSTEMS
400 W. WATSON BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGN AGENCY

DESIGNER
SSA

REVIEWER
SS 02/28/24


PROJECT ID
116570

SHEET TOTAL
P.077 782

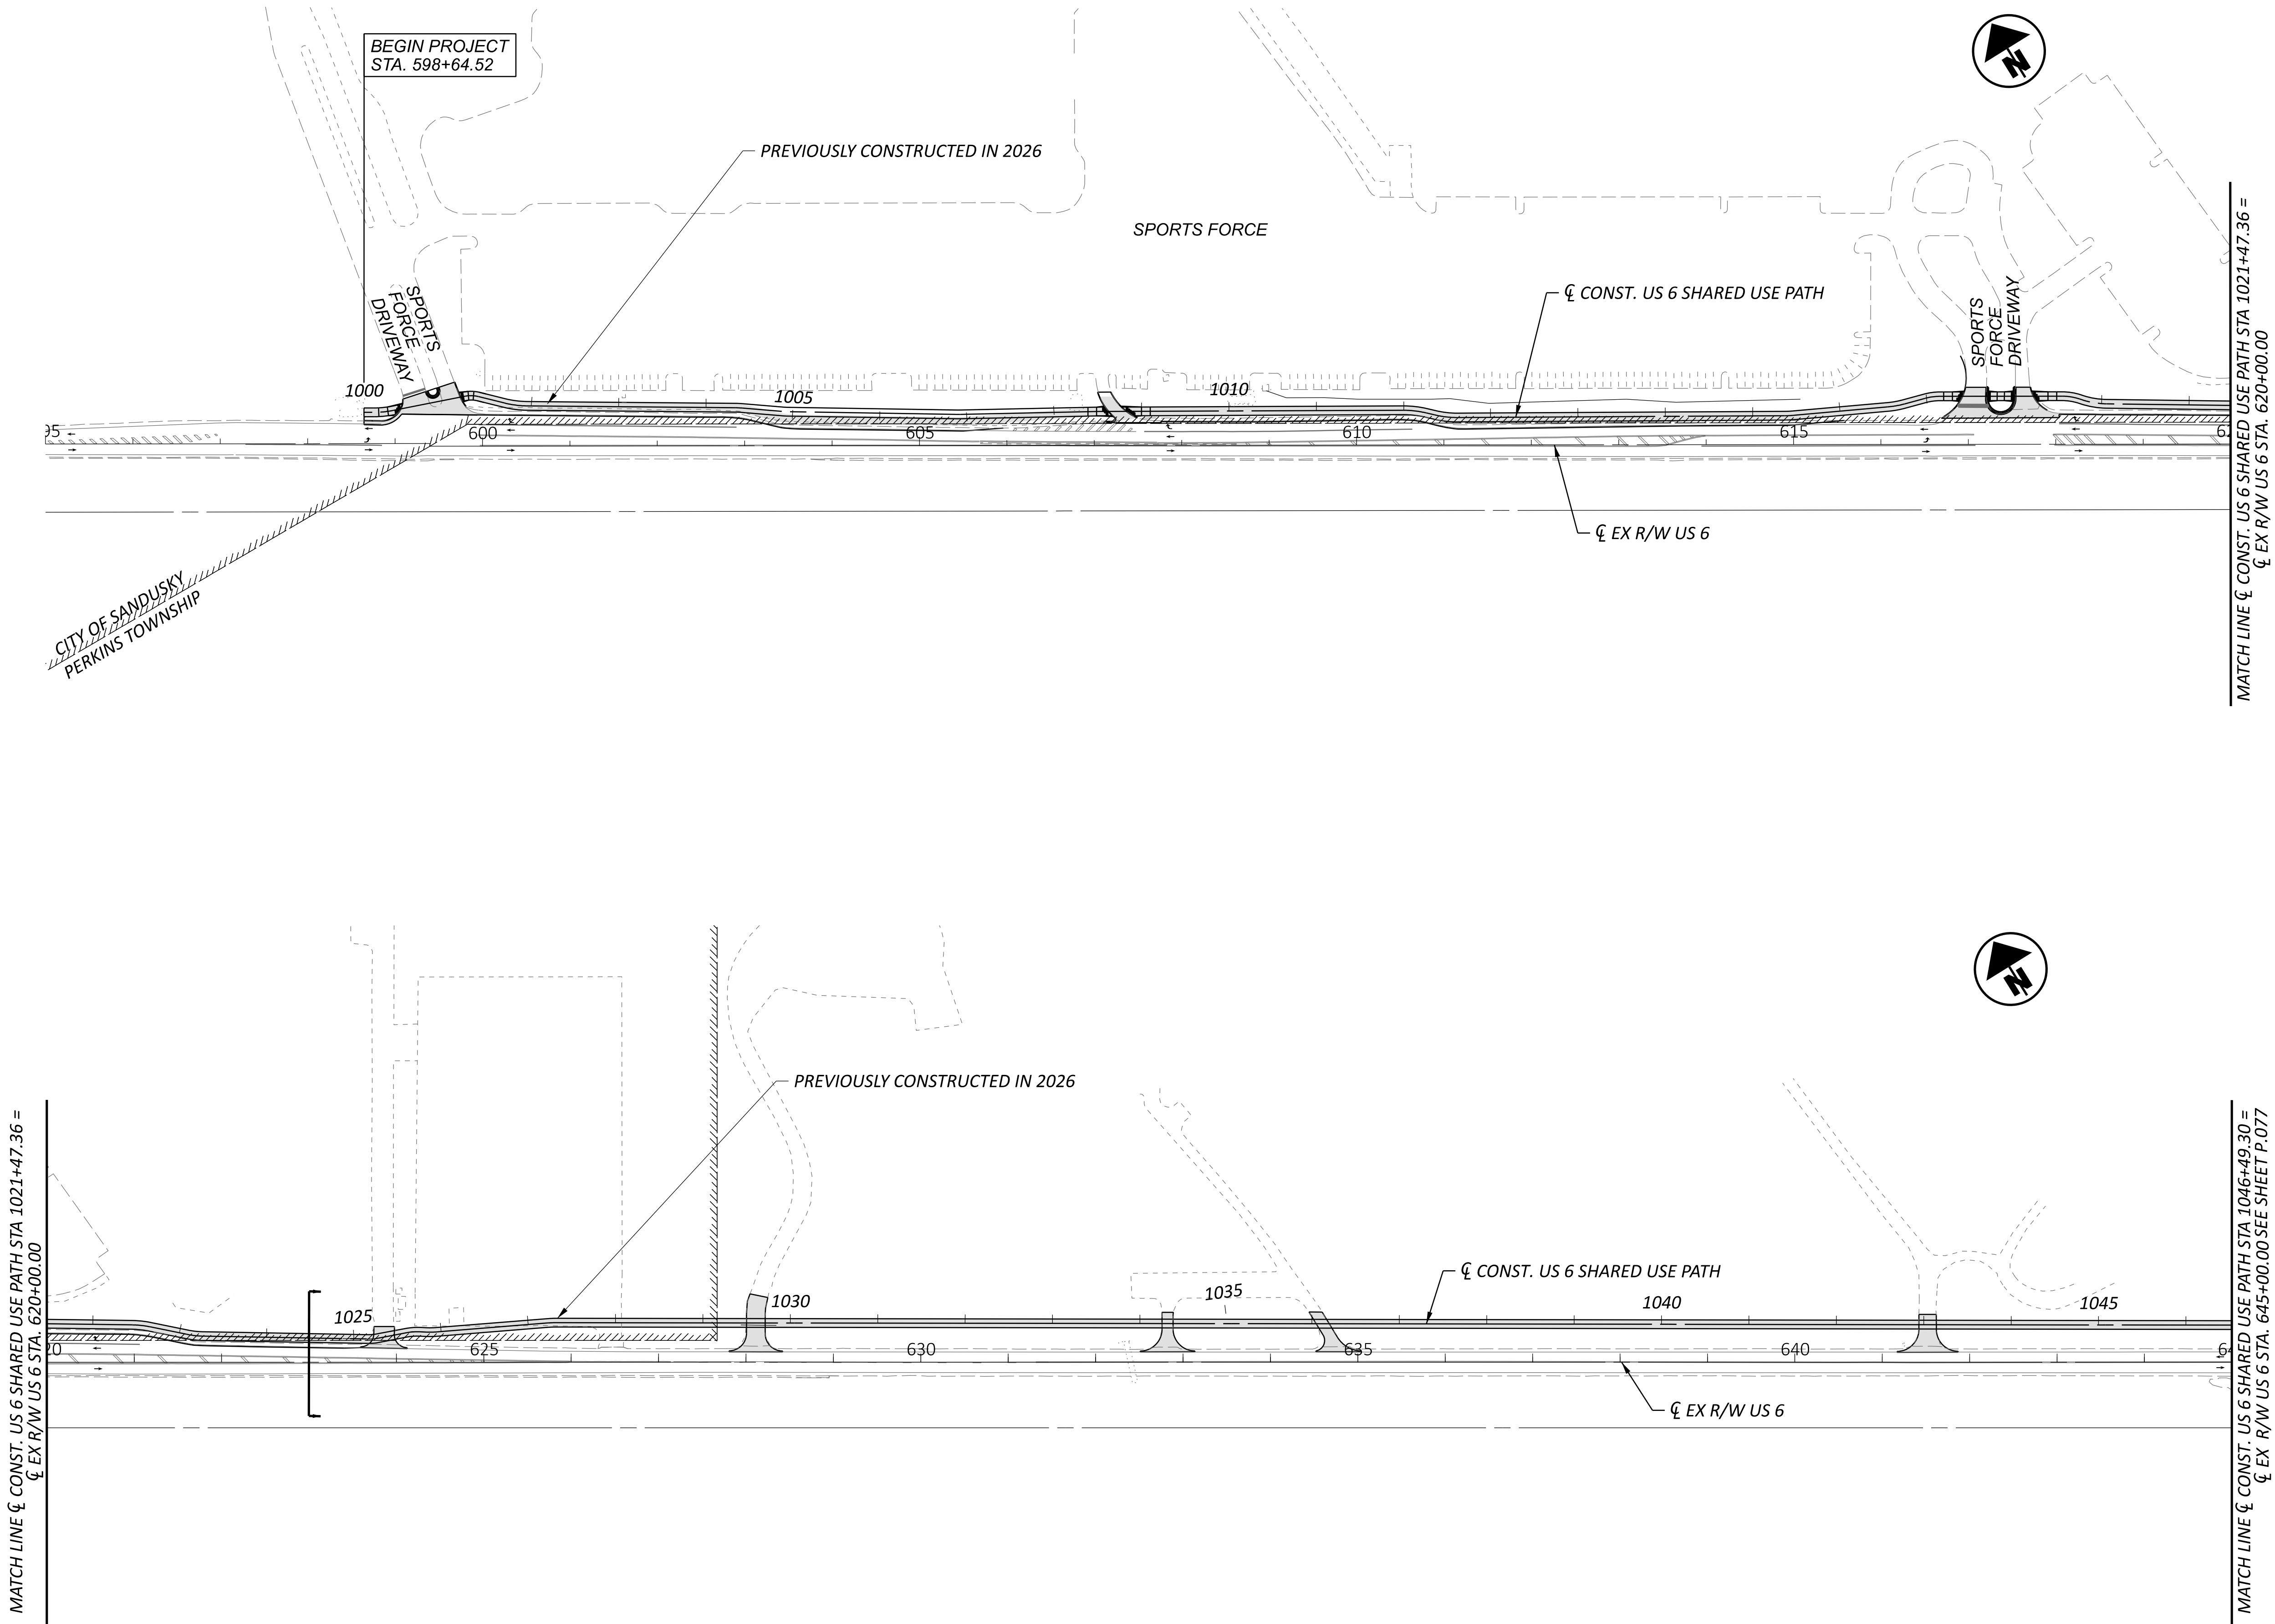

- NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
 2. FOR LEGEND, SEE SHEET P.076

HORIZONTAL SCALE IN FEET 0 50 100 200	
MOT SCHEMATIC PLAN - PHASE 1 (2027/2028 CONSTRUCTION) US 6 BEGIN PROJECT TO STA 645+00	
DESIGN AGENCY TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.078	782

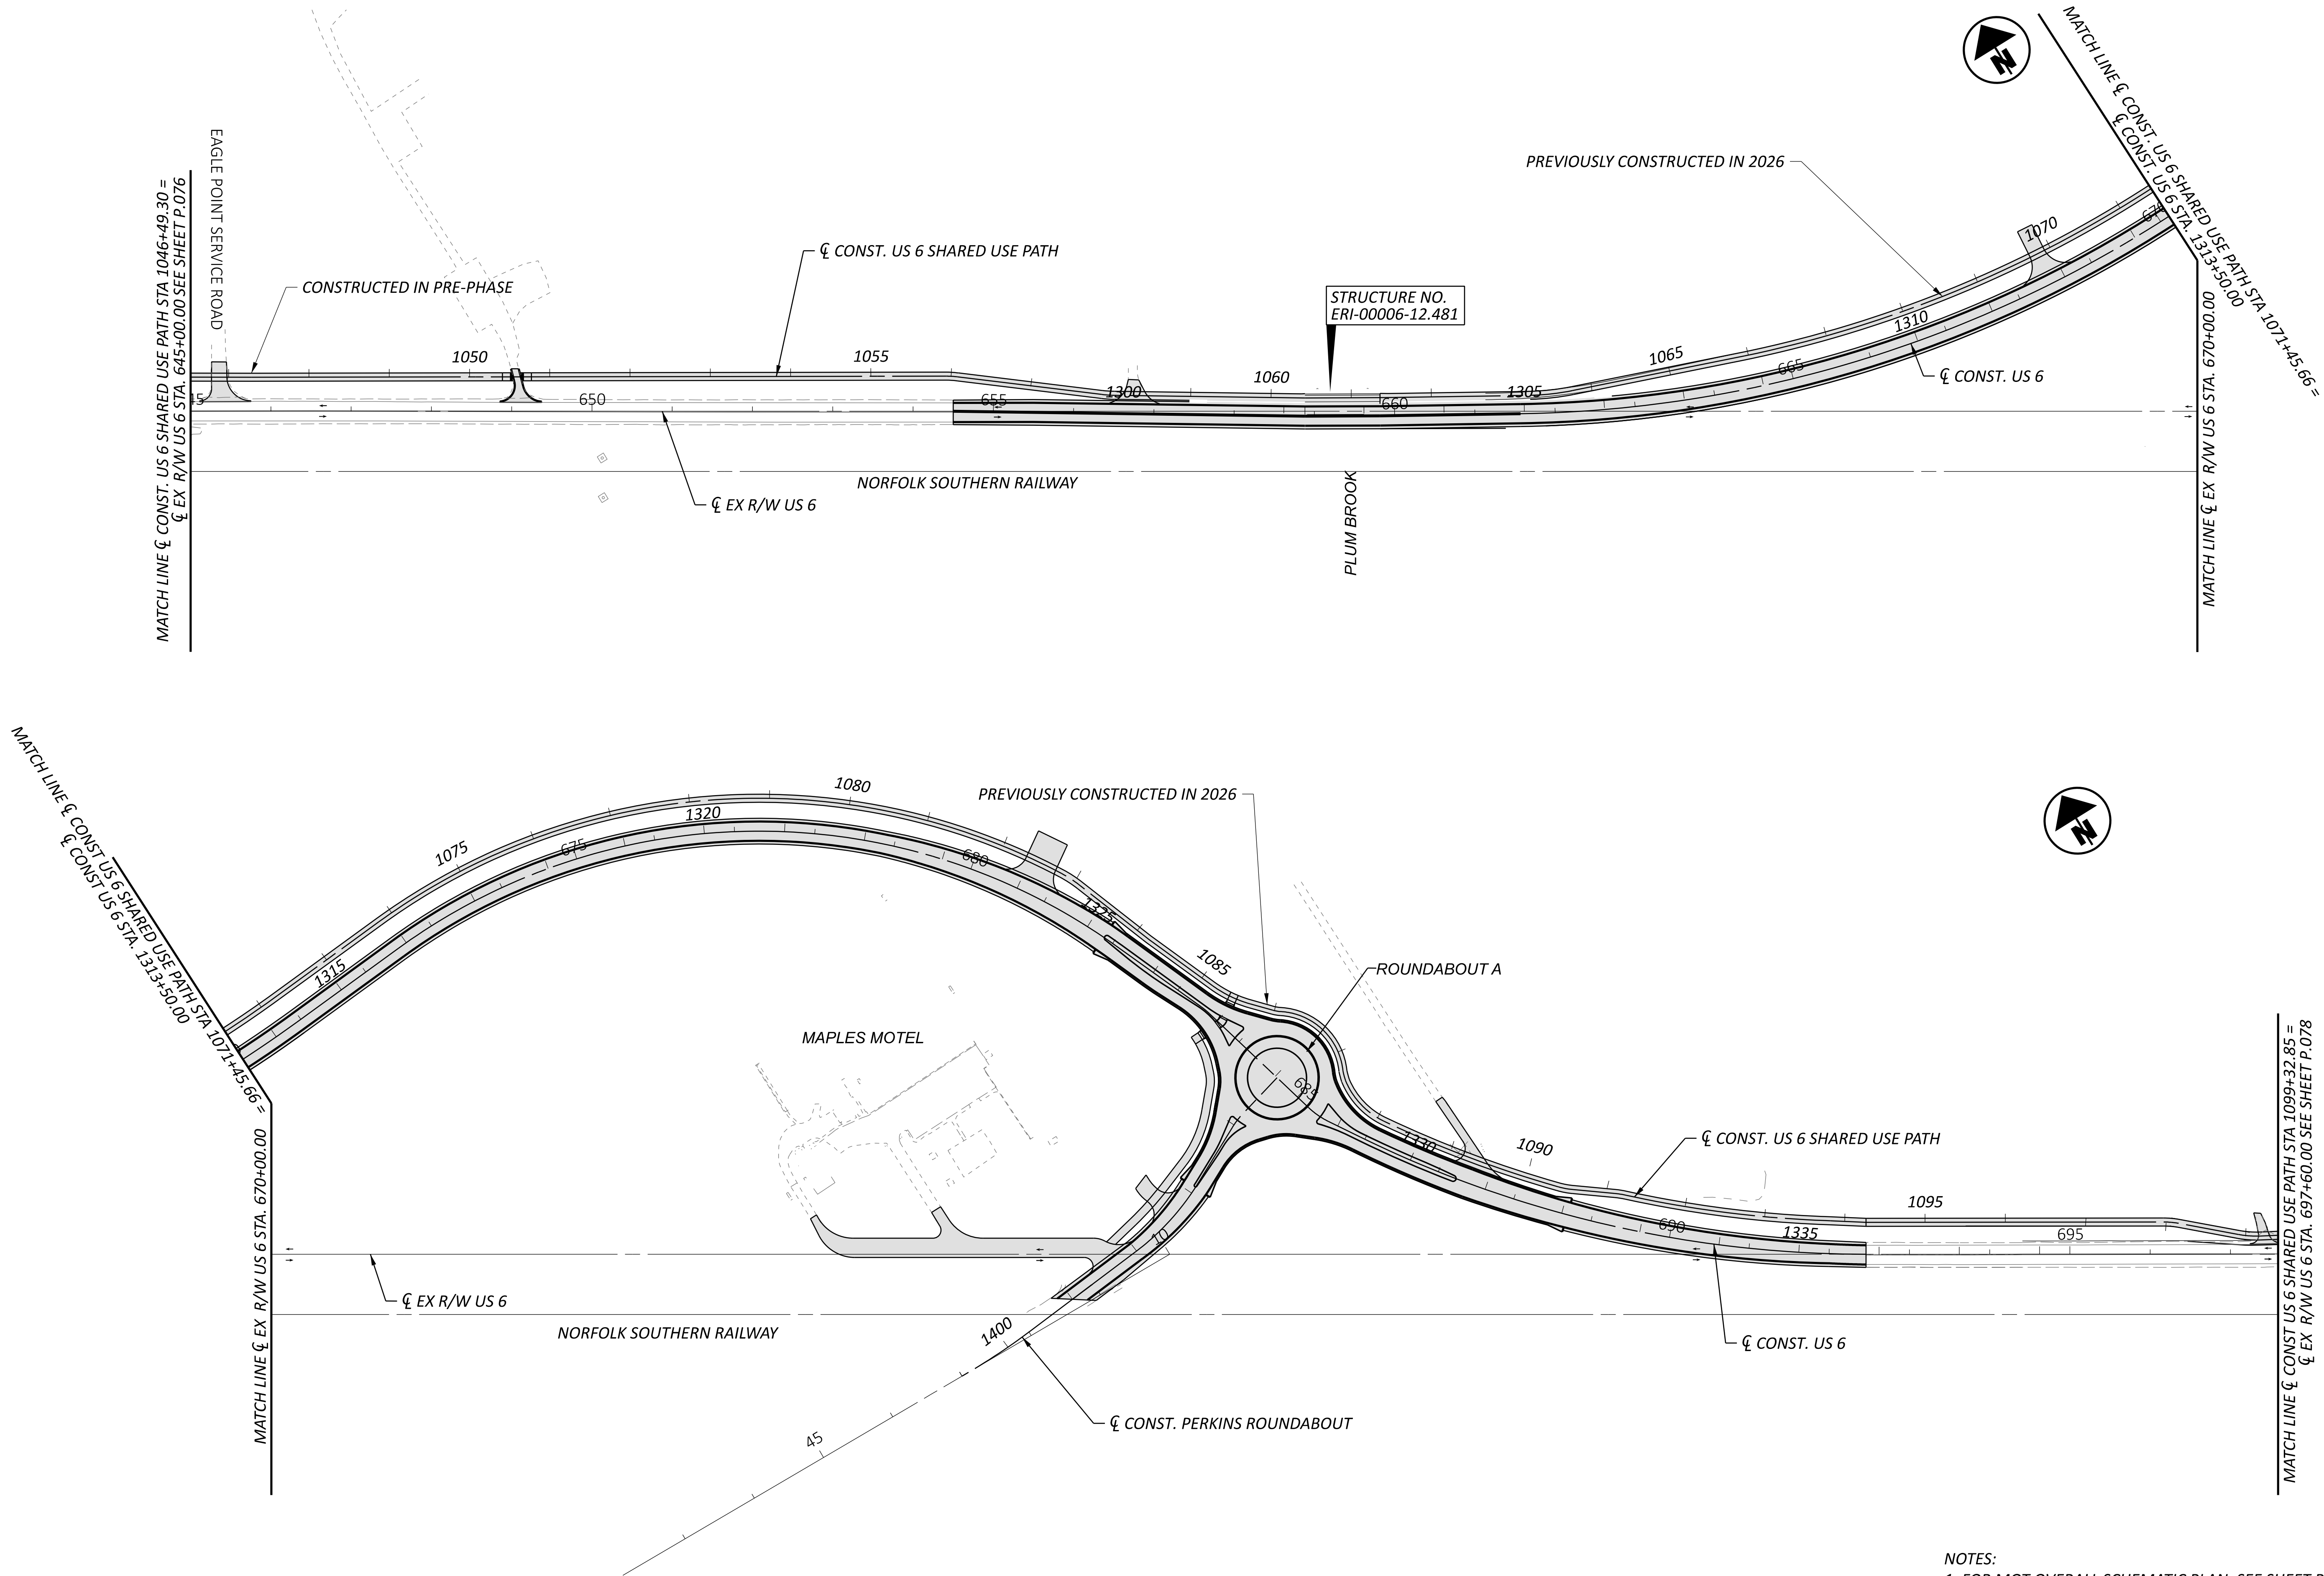

- NOTES:
- FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
 - FOR LEGEND, SEE SHEET P.076 .

MOT SCHEMATIC PLAN - PHASE 1 (2027/2028 CONSTRUCTION)
US 6 STA 645+00 TO STA 695+00

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA


REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.079 782

HORIZONTAL
SCALE IN FEET
0 50 100 200

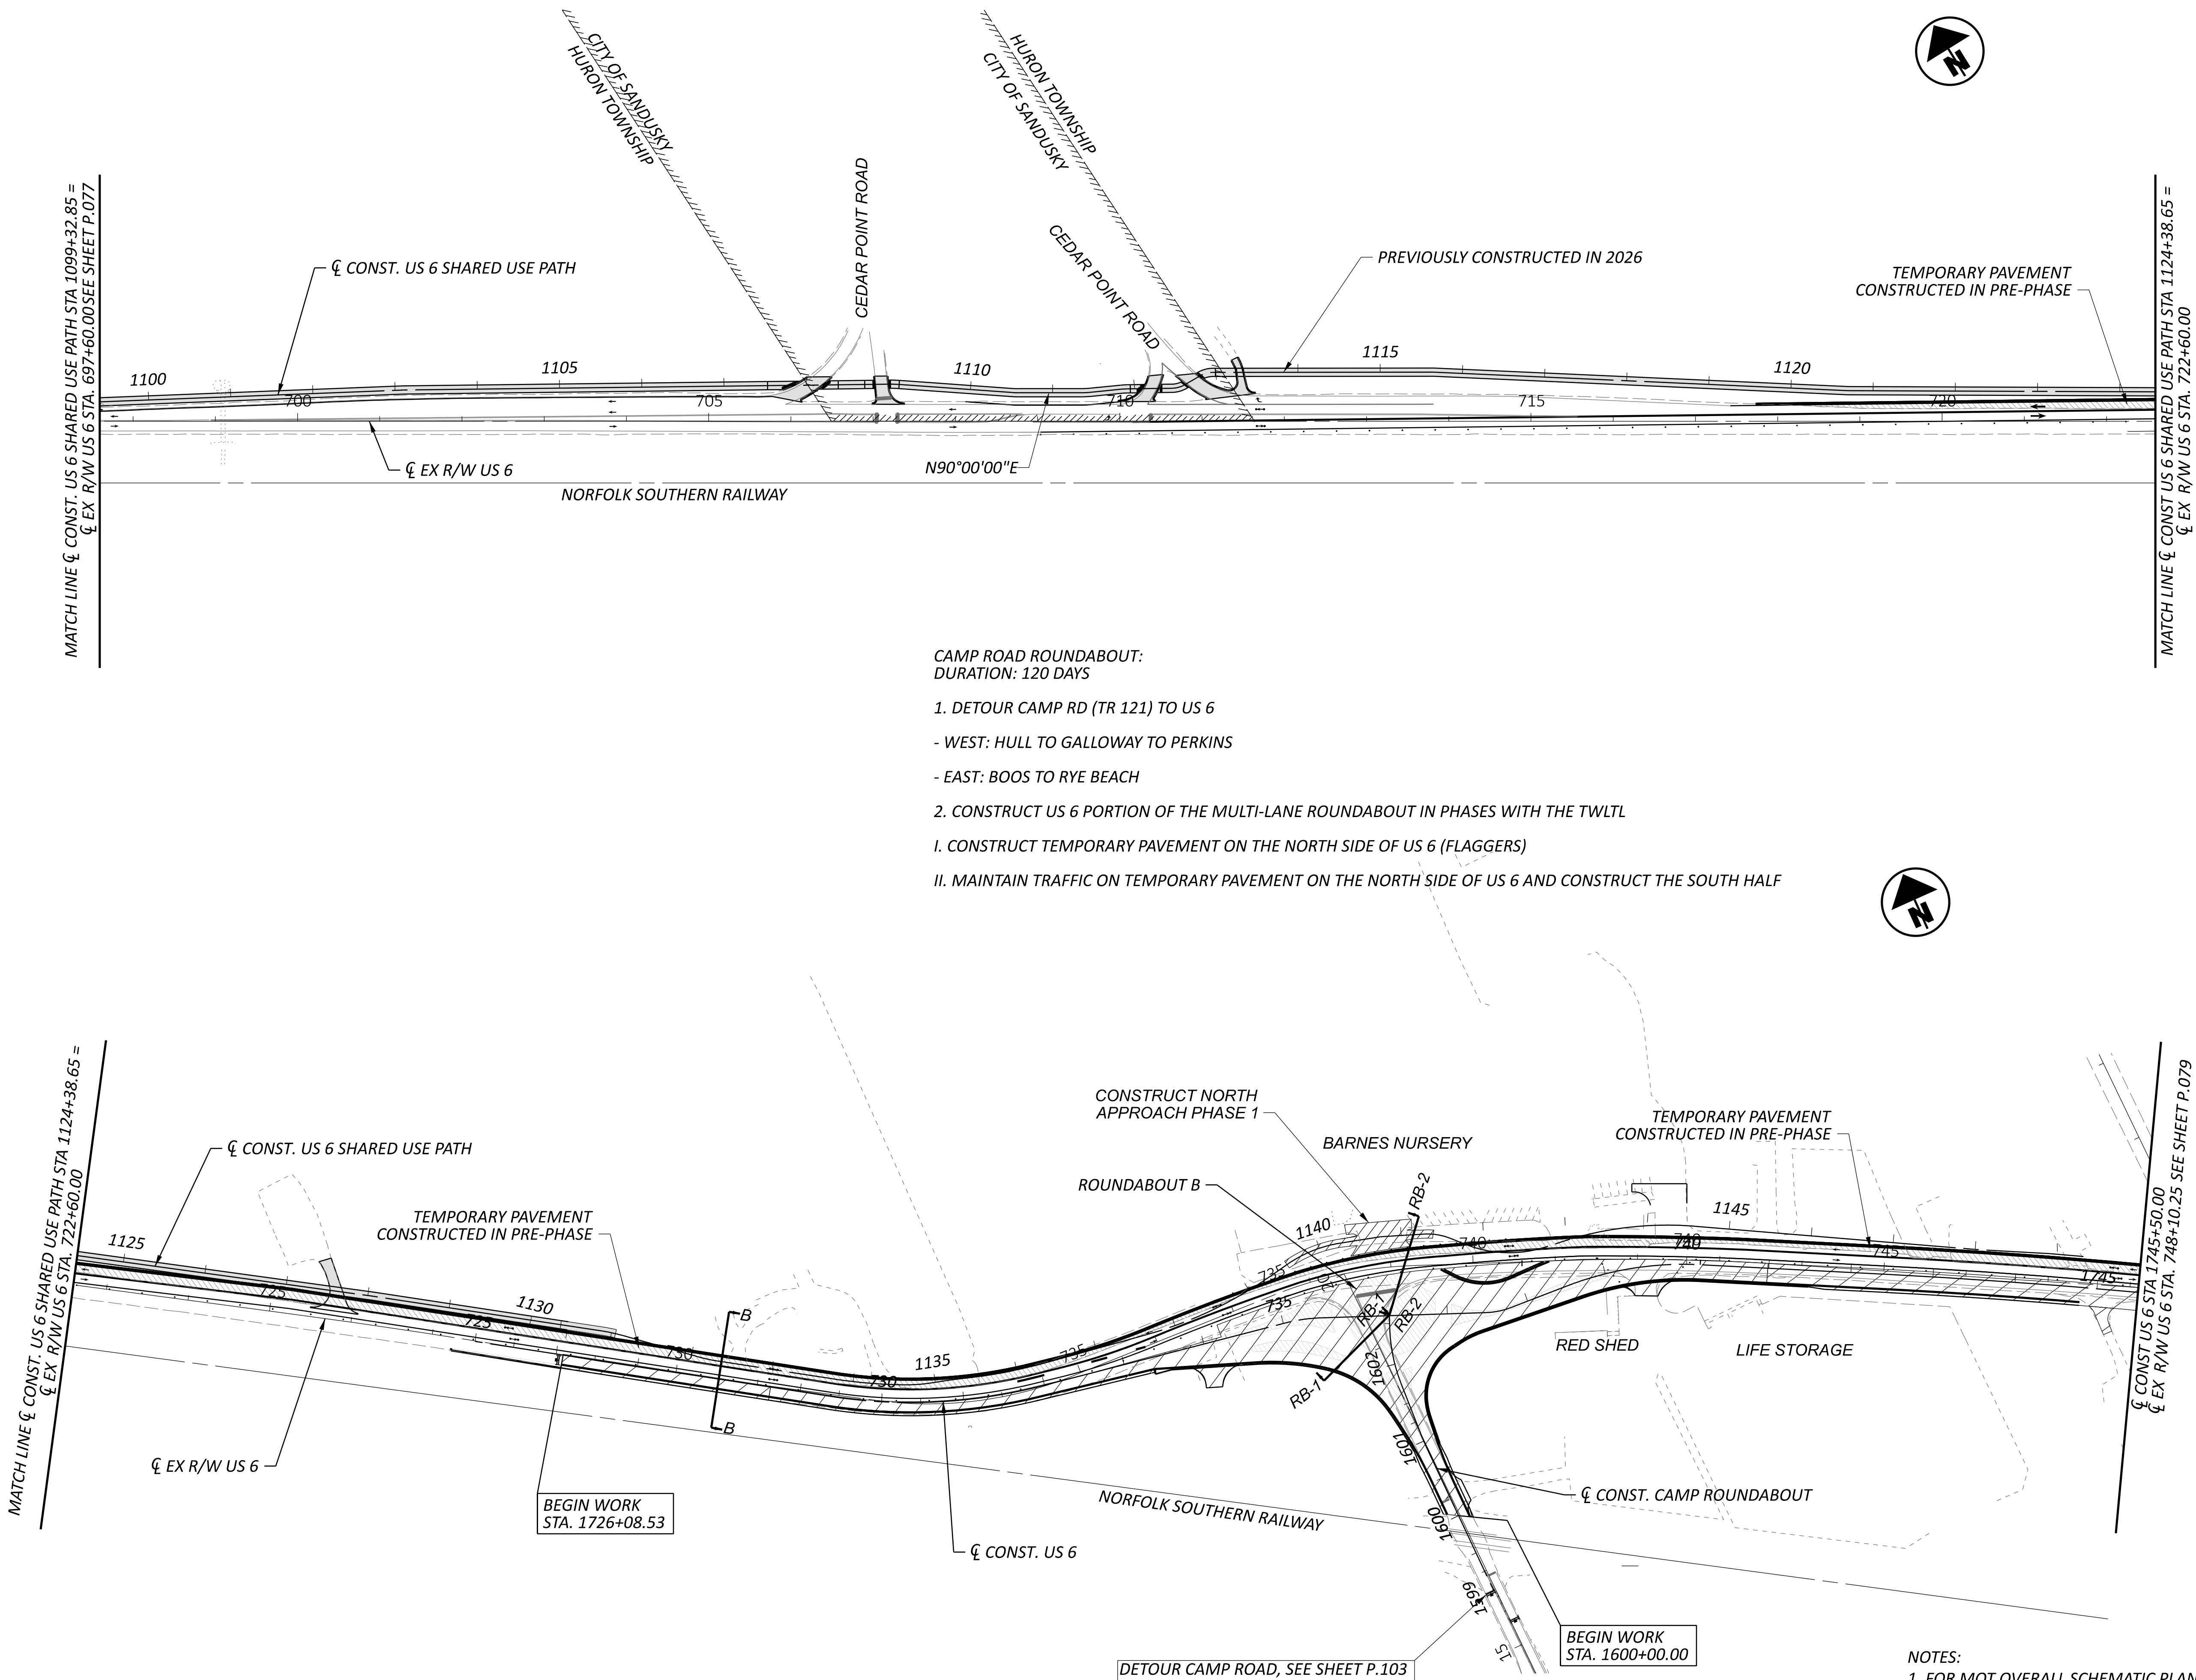

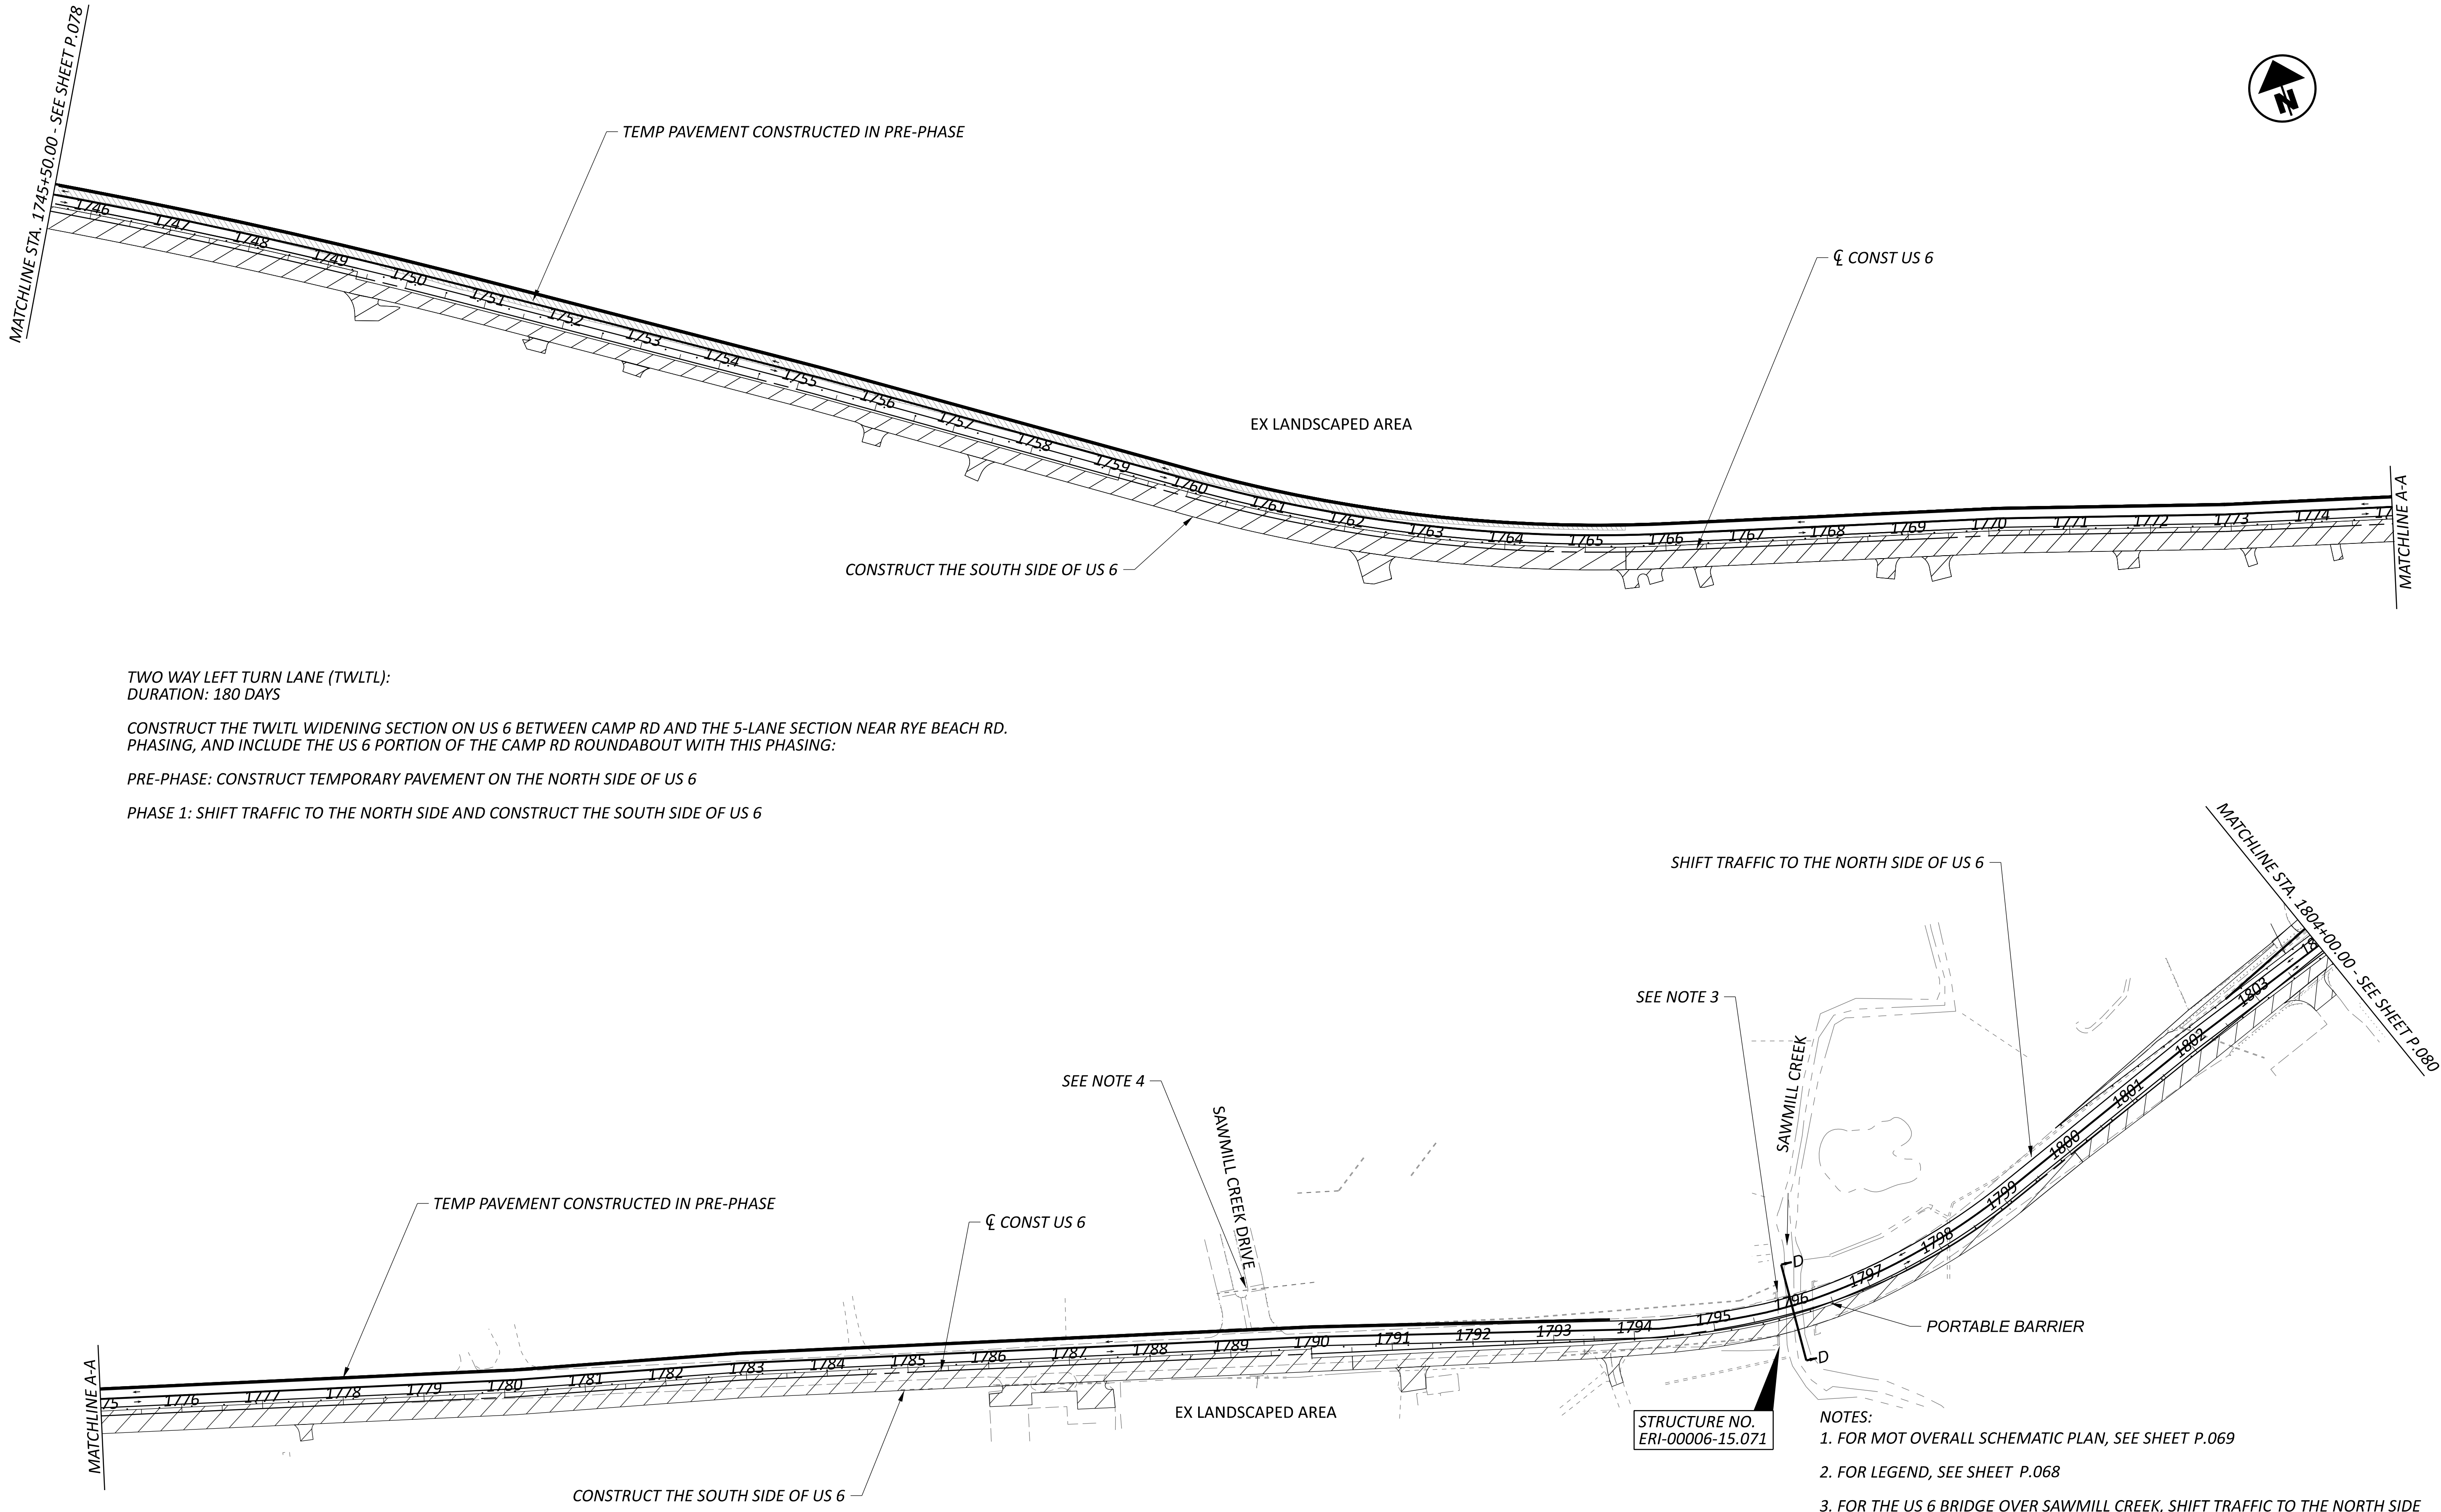

HORIZONTAL
SCALE IN FEET
0 50 100 200

MOT SCHEMATIC PLAN - PHASE 1 (2027/2028 CONSTRUCTION)
WIDENING SECTION STA 745+50.00 TO STA 804+00.00

TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGN AGENCY


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570


SHEET
P.081

TOTAL
782





DESIGN AGENCY	
TRANSYSTEMS	400 W. NATIONWIDE BLVD., STE 225 COLUMBUS, OHIO 43215
DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.082	782

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

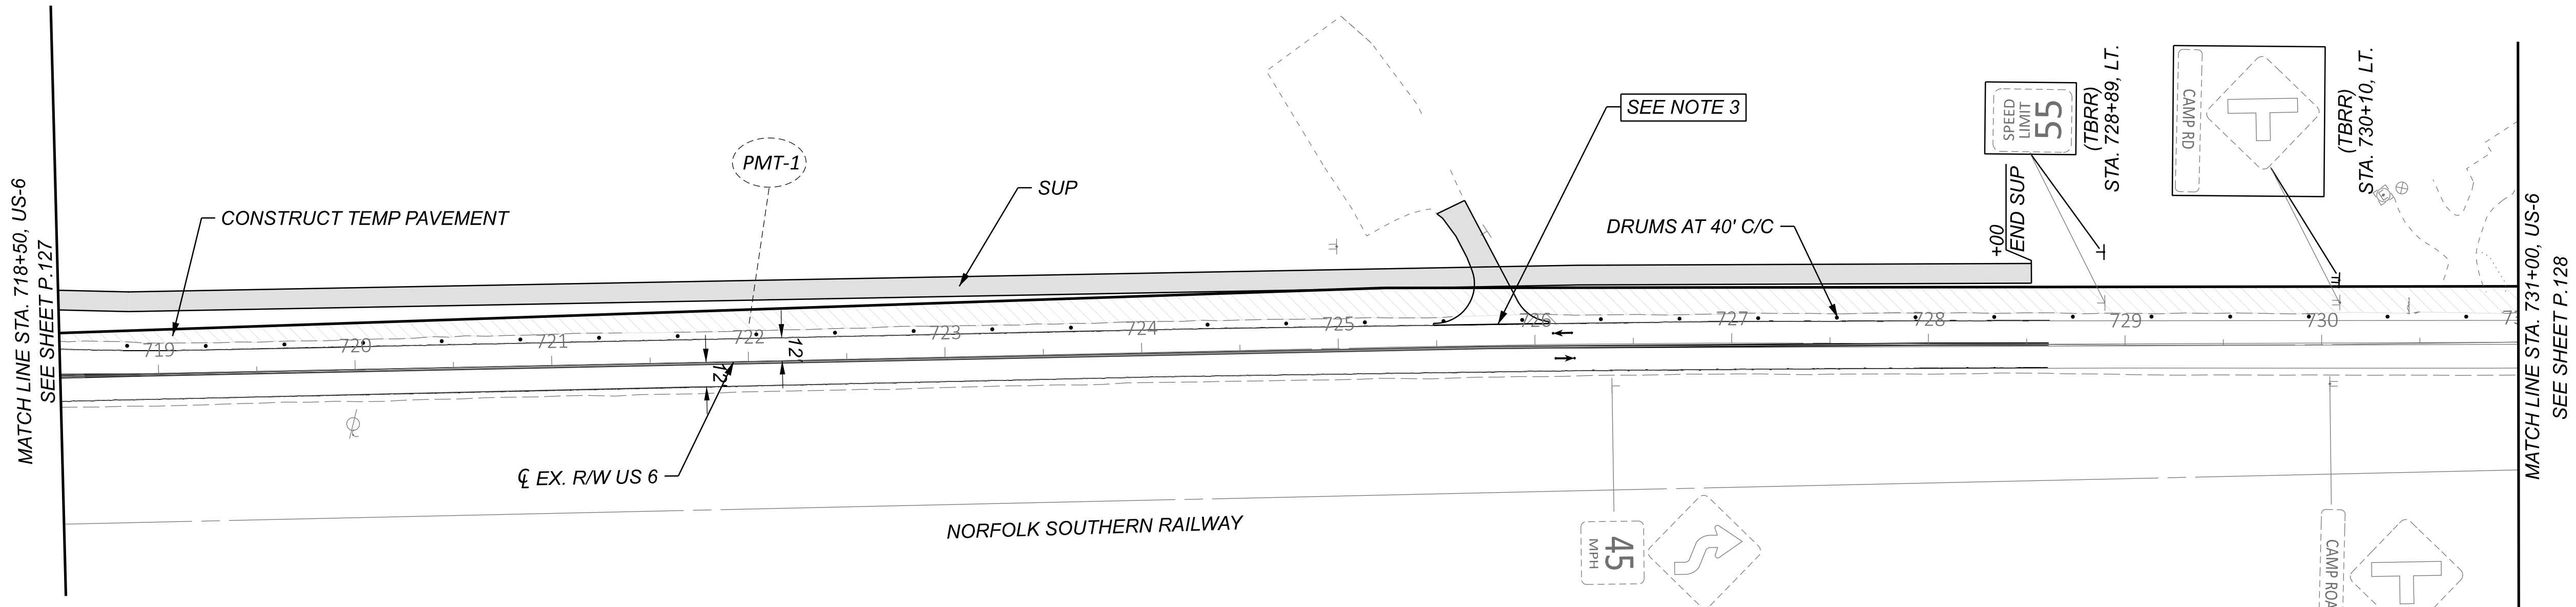


NOTE: UTILITIES RELOCATED IN CY 2026

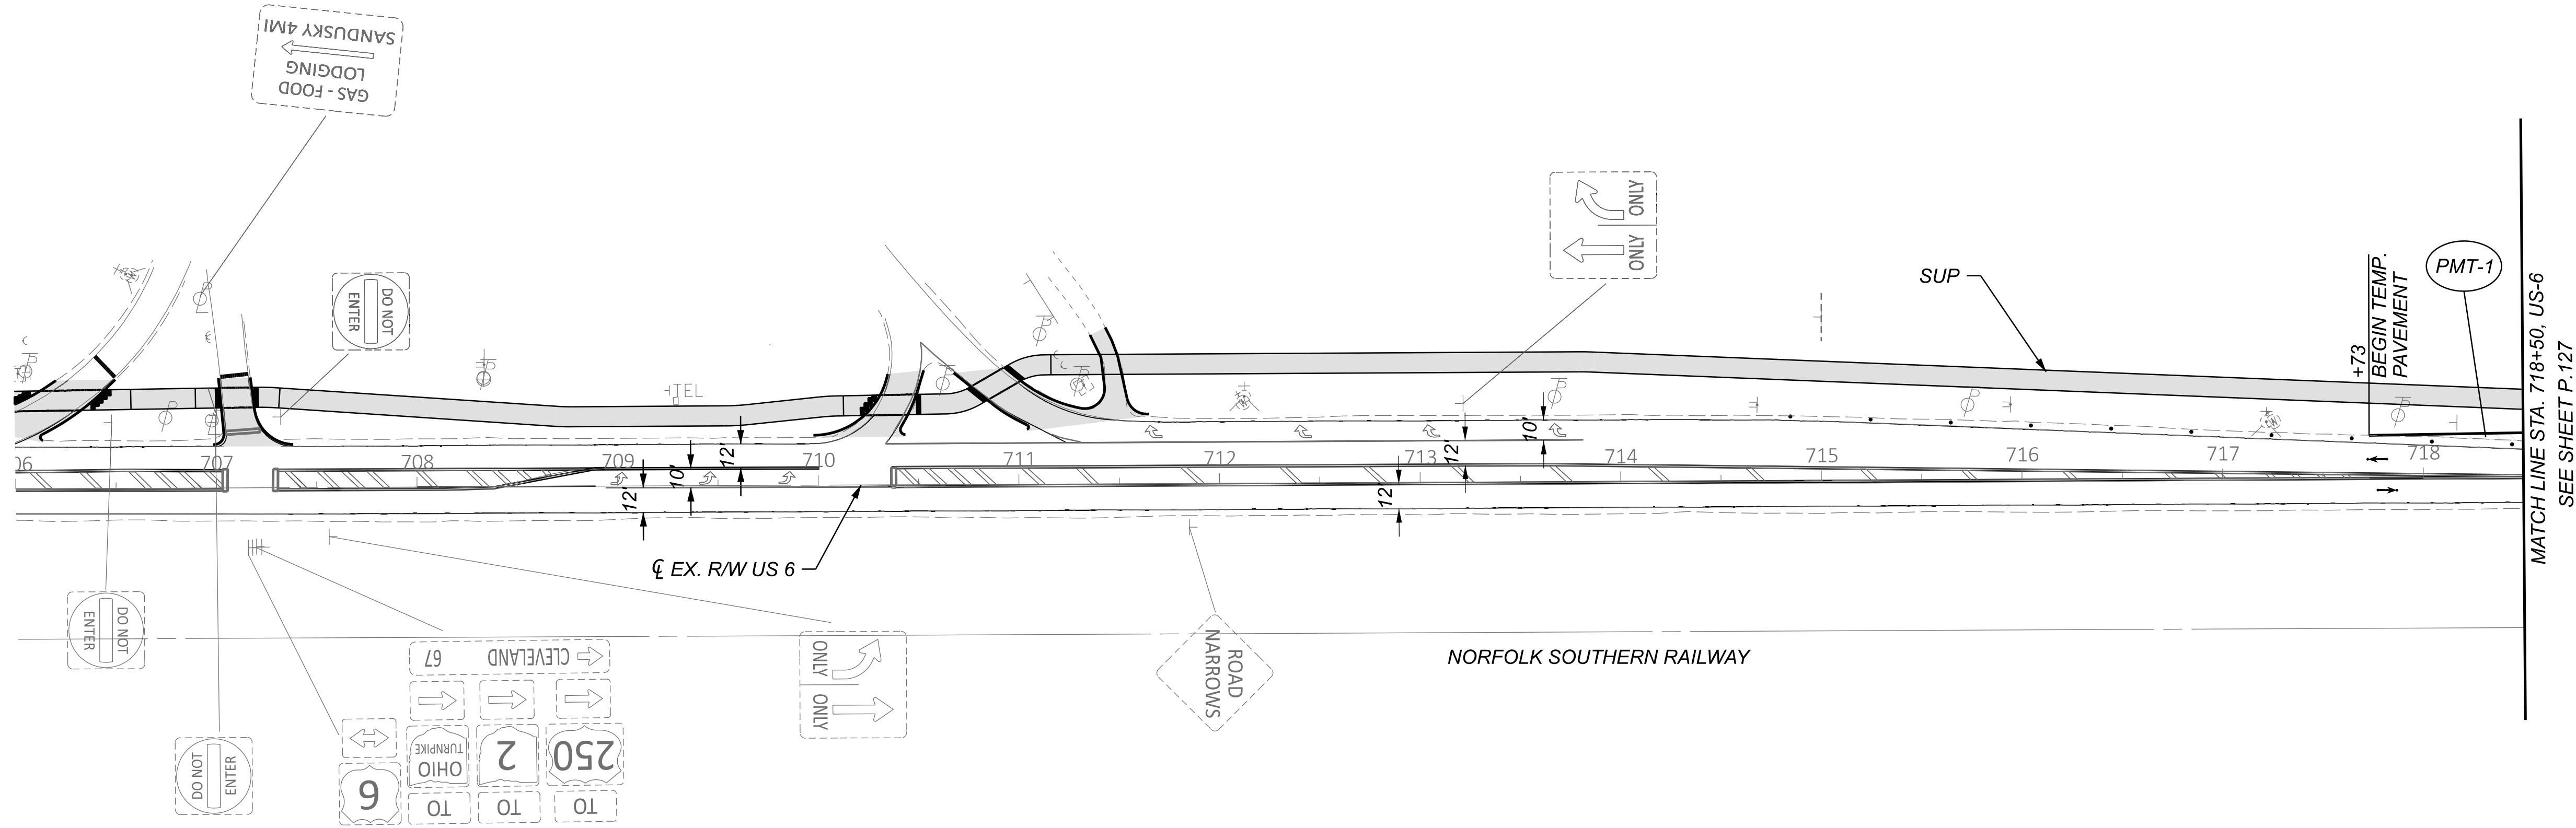

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

HORIZONTAL SCALE IN FEET 0 25 50 100	
MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION) US 6 - STA. 706+00.00 TO STA. 730+00.00	
DESIGNER SSA	
REVIEWER SS 02/28/24	
PROJECT ID 116570	
SHEET P.130	TOTAL 782

NOTE: UTILITIES RELOCATED IN CY 2026

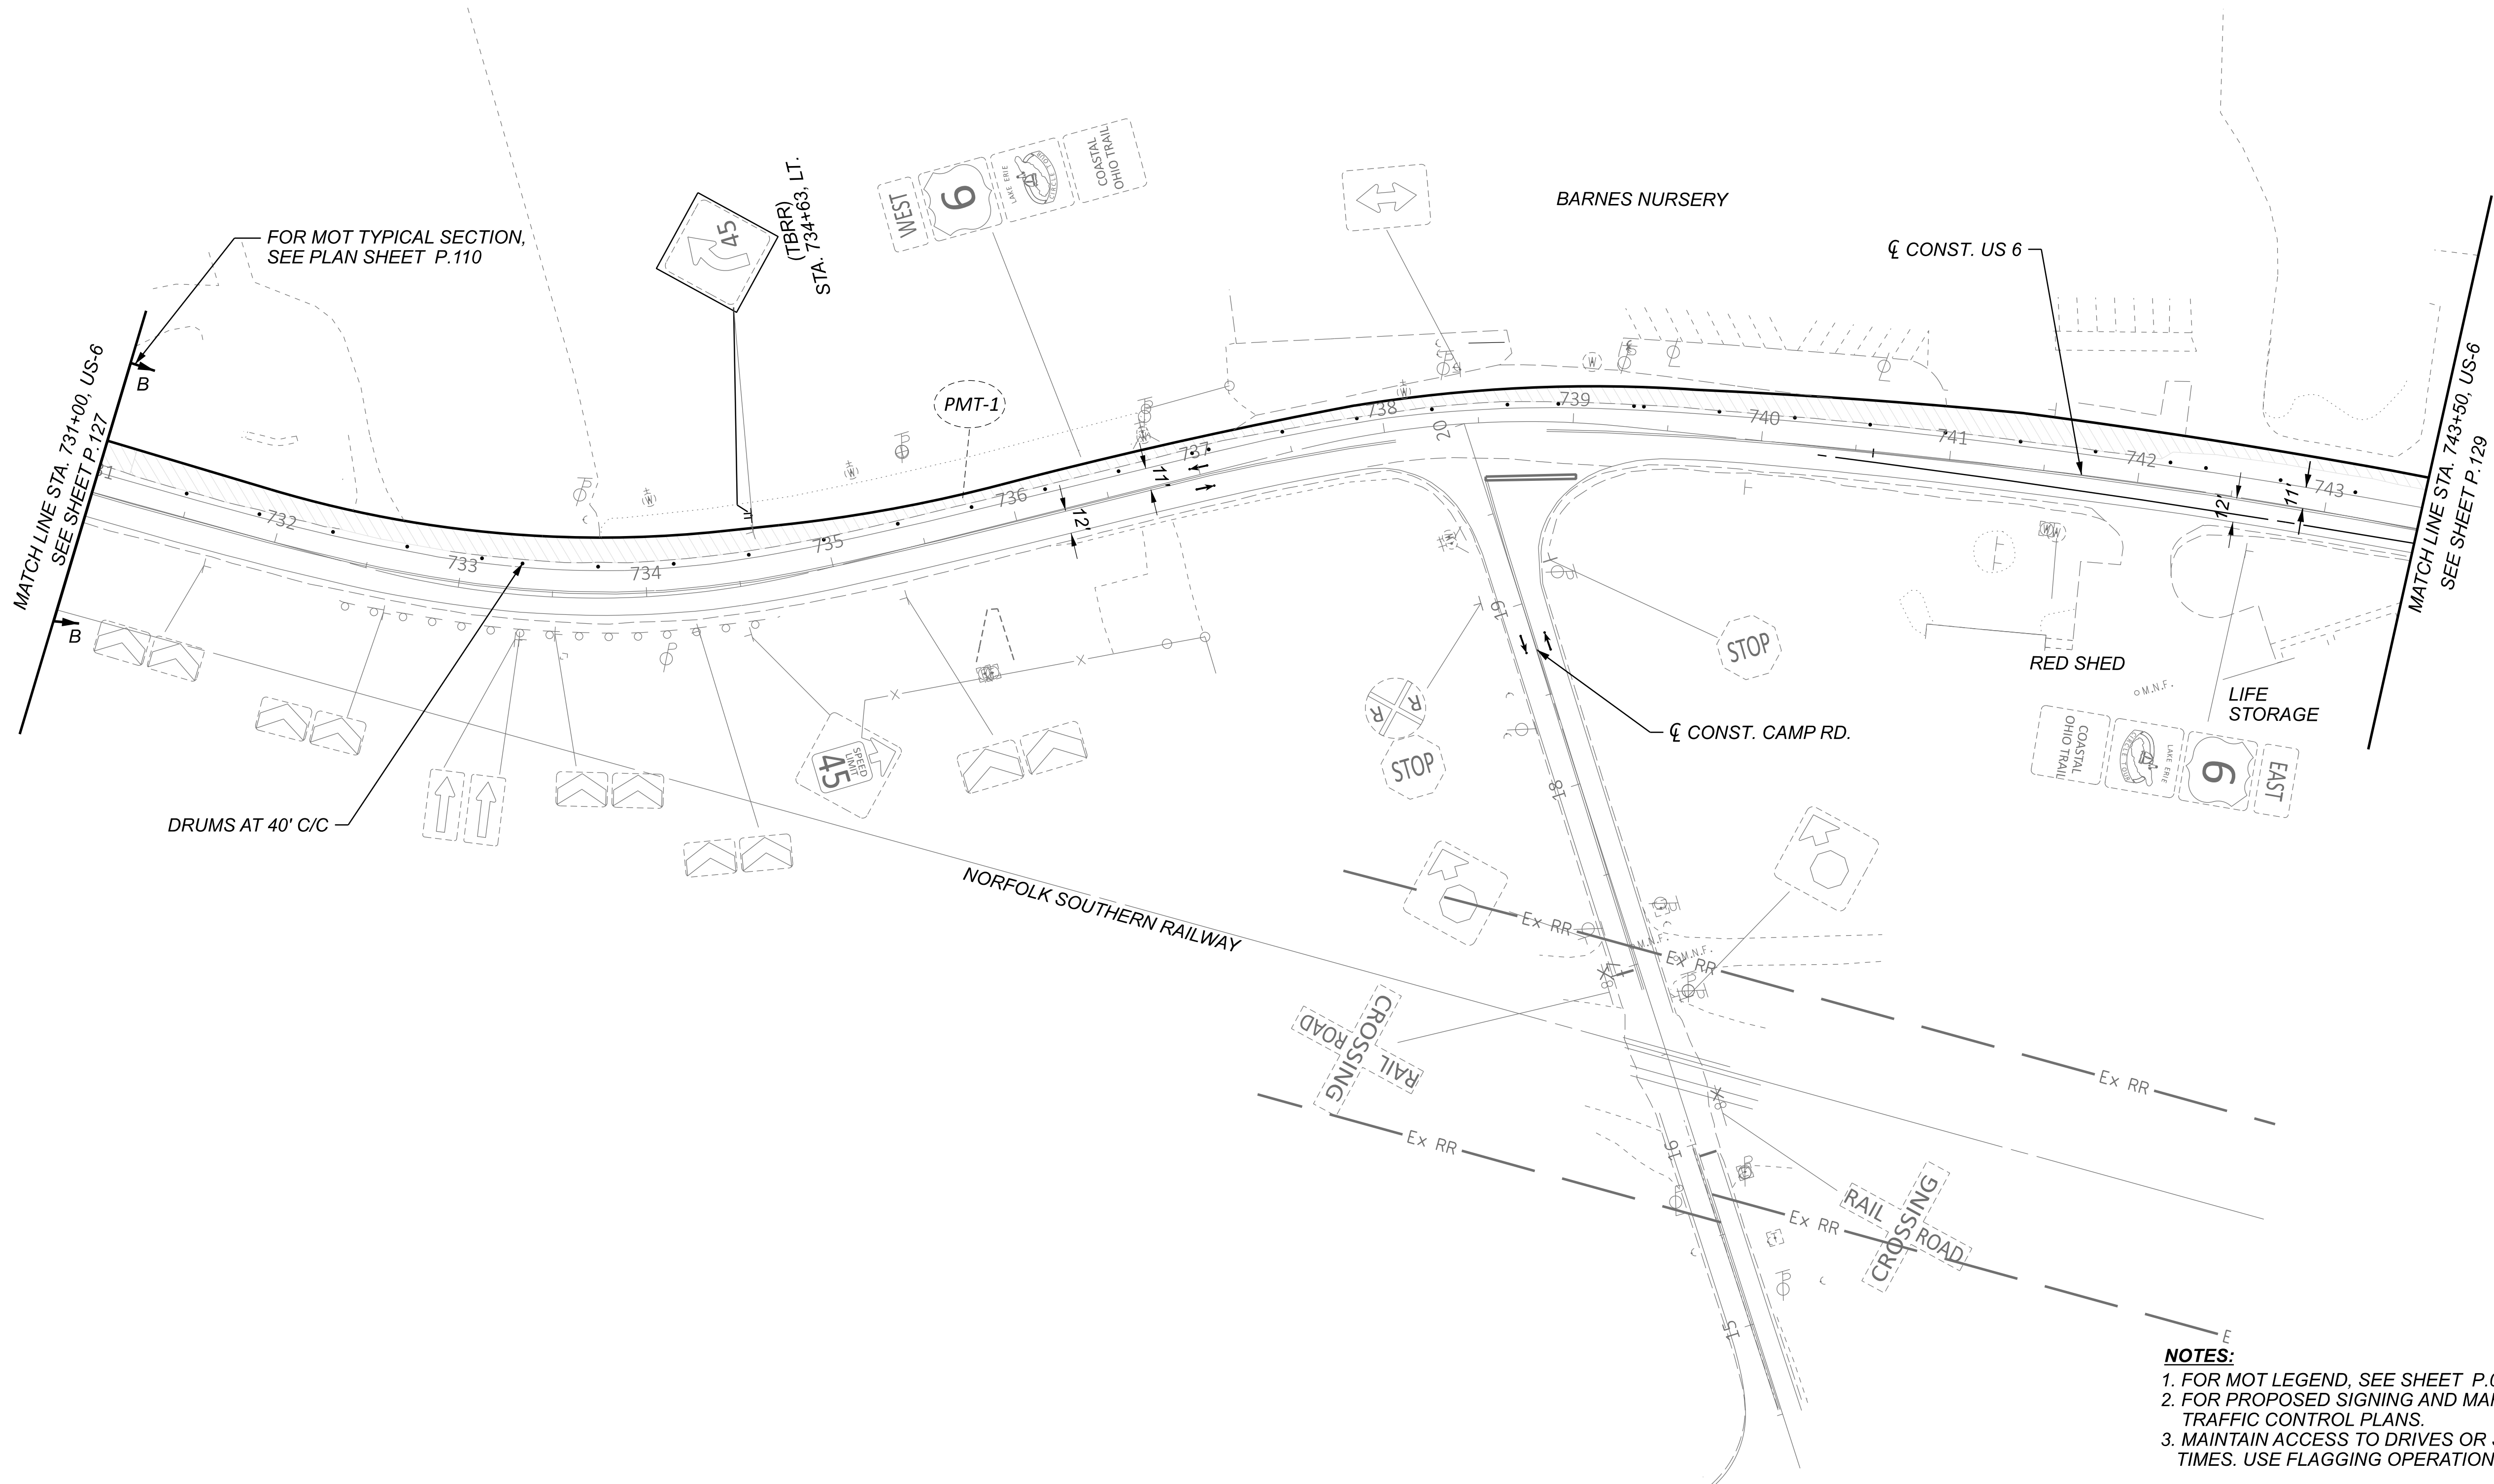

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 - STA. 731+00.00 TO STA. 743+50.00


DESIGN AGENCY
TRANSYSTEMS
400 W. WATKINSON BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET	TOTAL
P.131	782

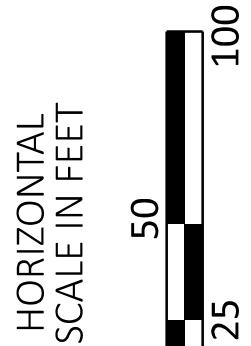

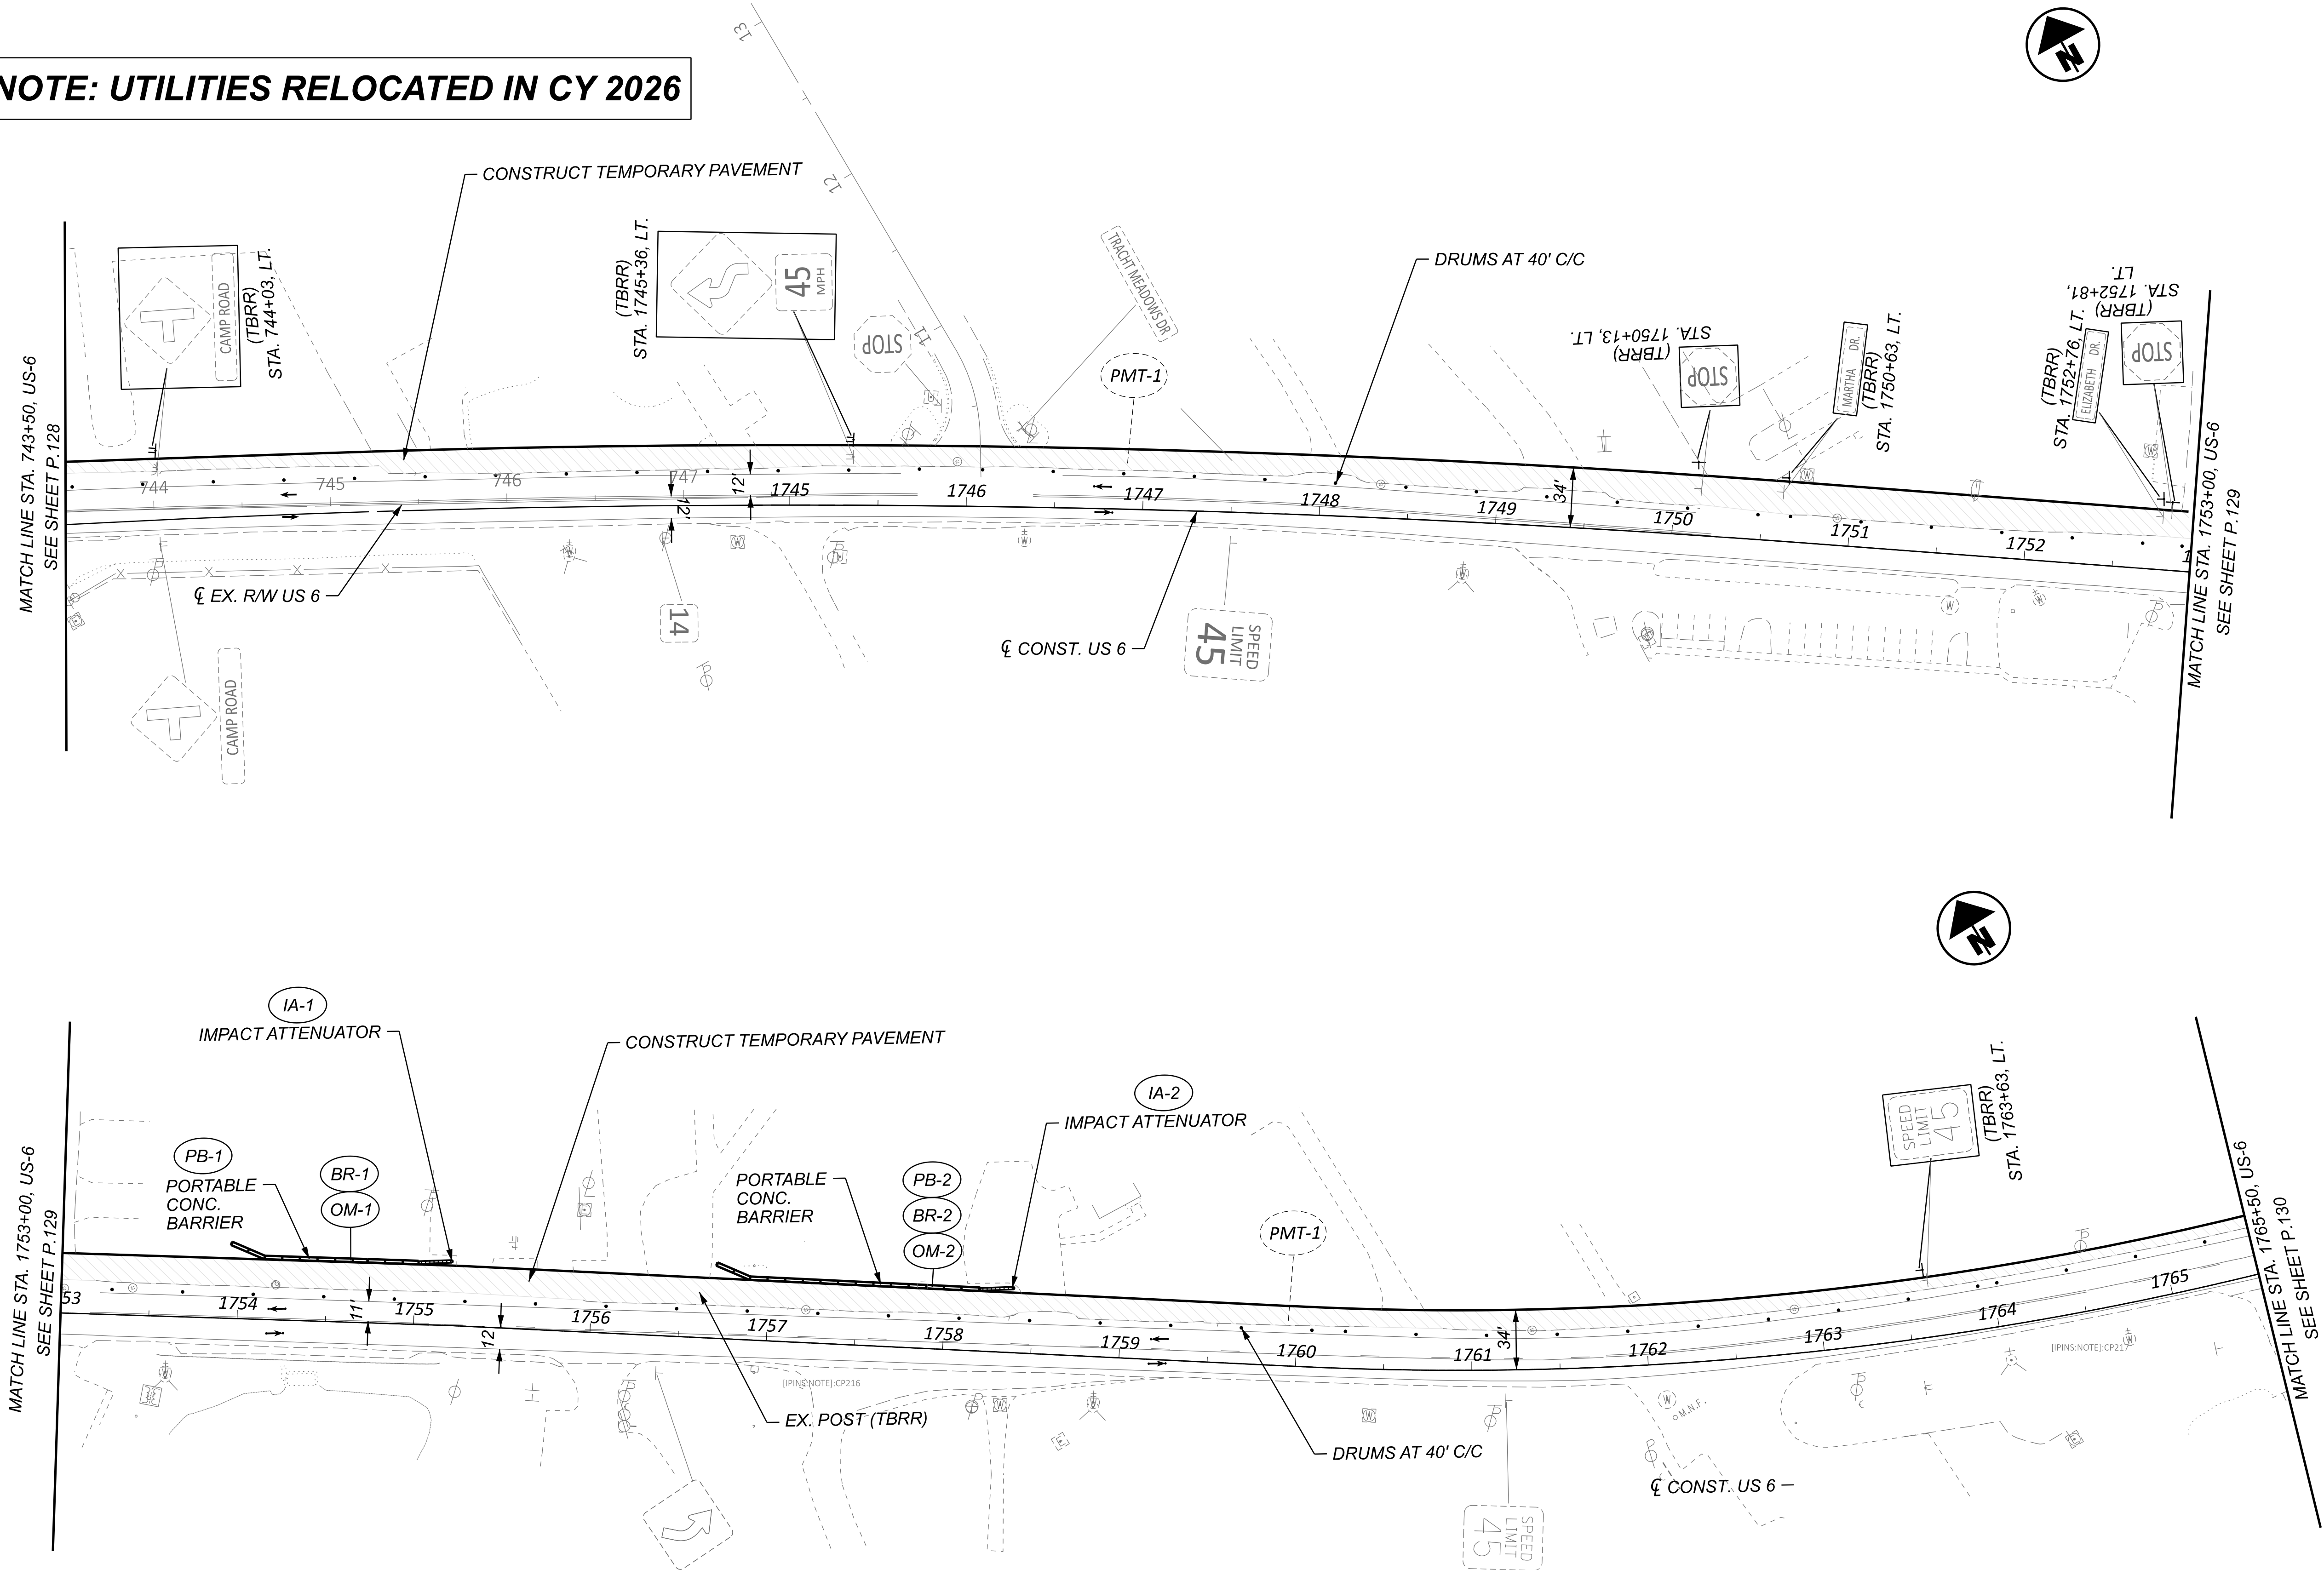

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 - EX. US 6 STA. 743+50.00 TO CONST. US 6 STA. 1765+50.00

DESIGN AGENCY
TRANSYSTEMS
400 W. WATKINSON BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570


SHEET TOTAL
P.132 782



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP_1 - Plan 17-18 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:23:53 PM USER: ssadusei
 www:\vhohodot-pw.bentley.com:\vhohodot-pw-02\Documents\01 Active Projects\District 03\Erle\116570\402-Engineering_TransSystems\MOT\Sheets\116570_MP000_CV2027.dgn

NOTE: UTILITIES RELOCATED IN CY 2026

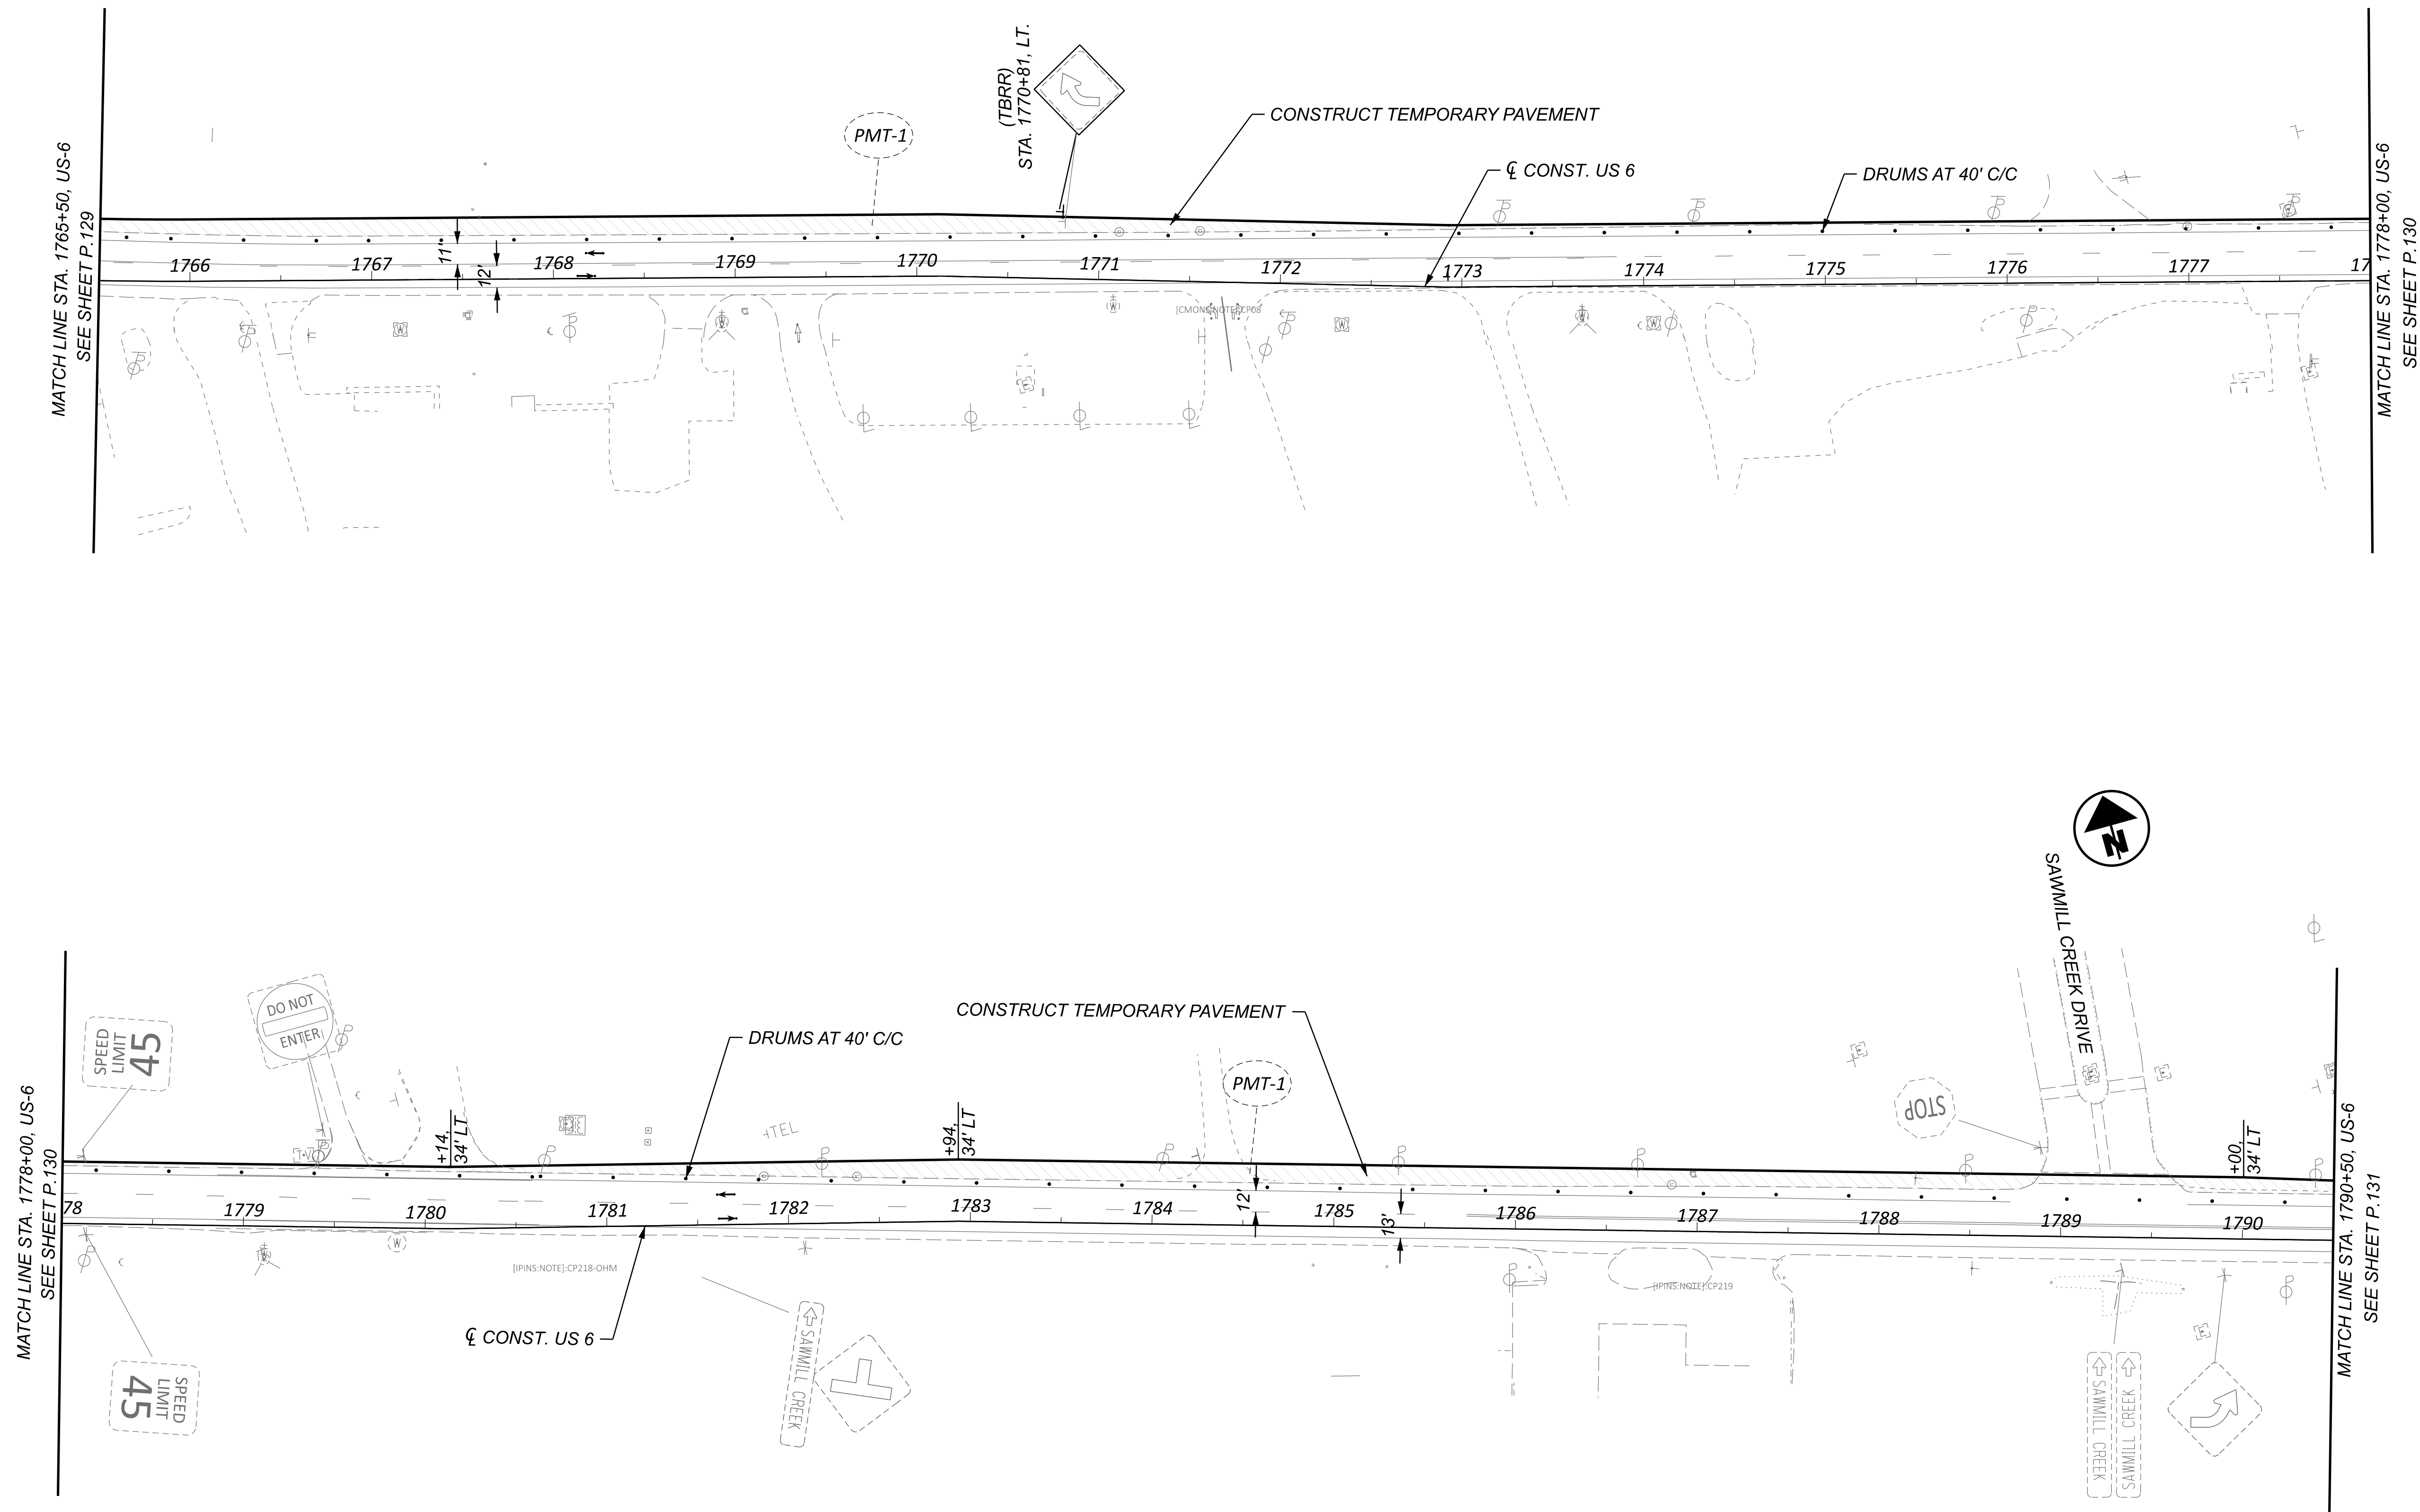

NOTES:


1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 - STA. 1765+50.00 TO STA. 1790+50.00


DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.133	782



NOTE: UTILITIES RELOCATED IN CY 2026

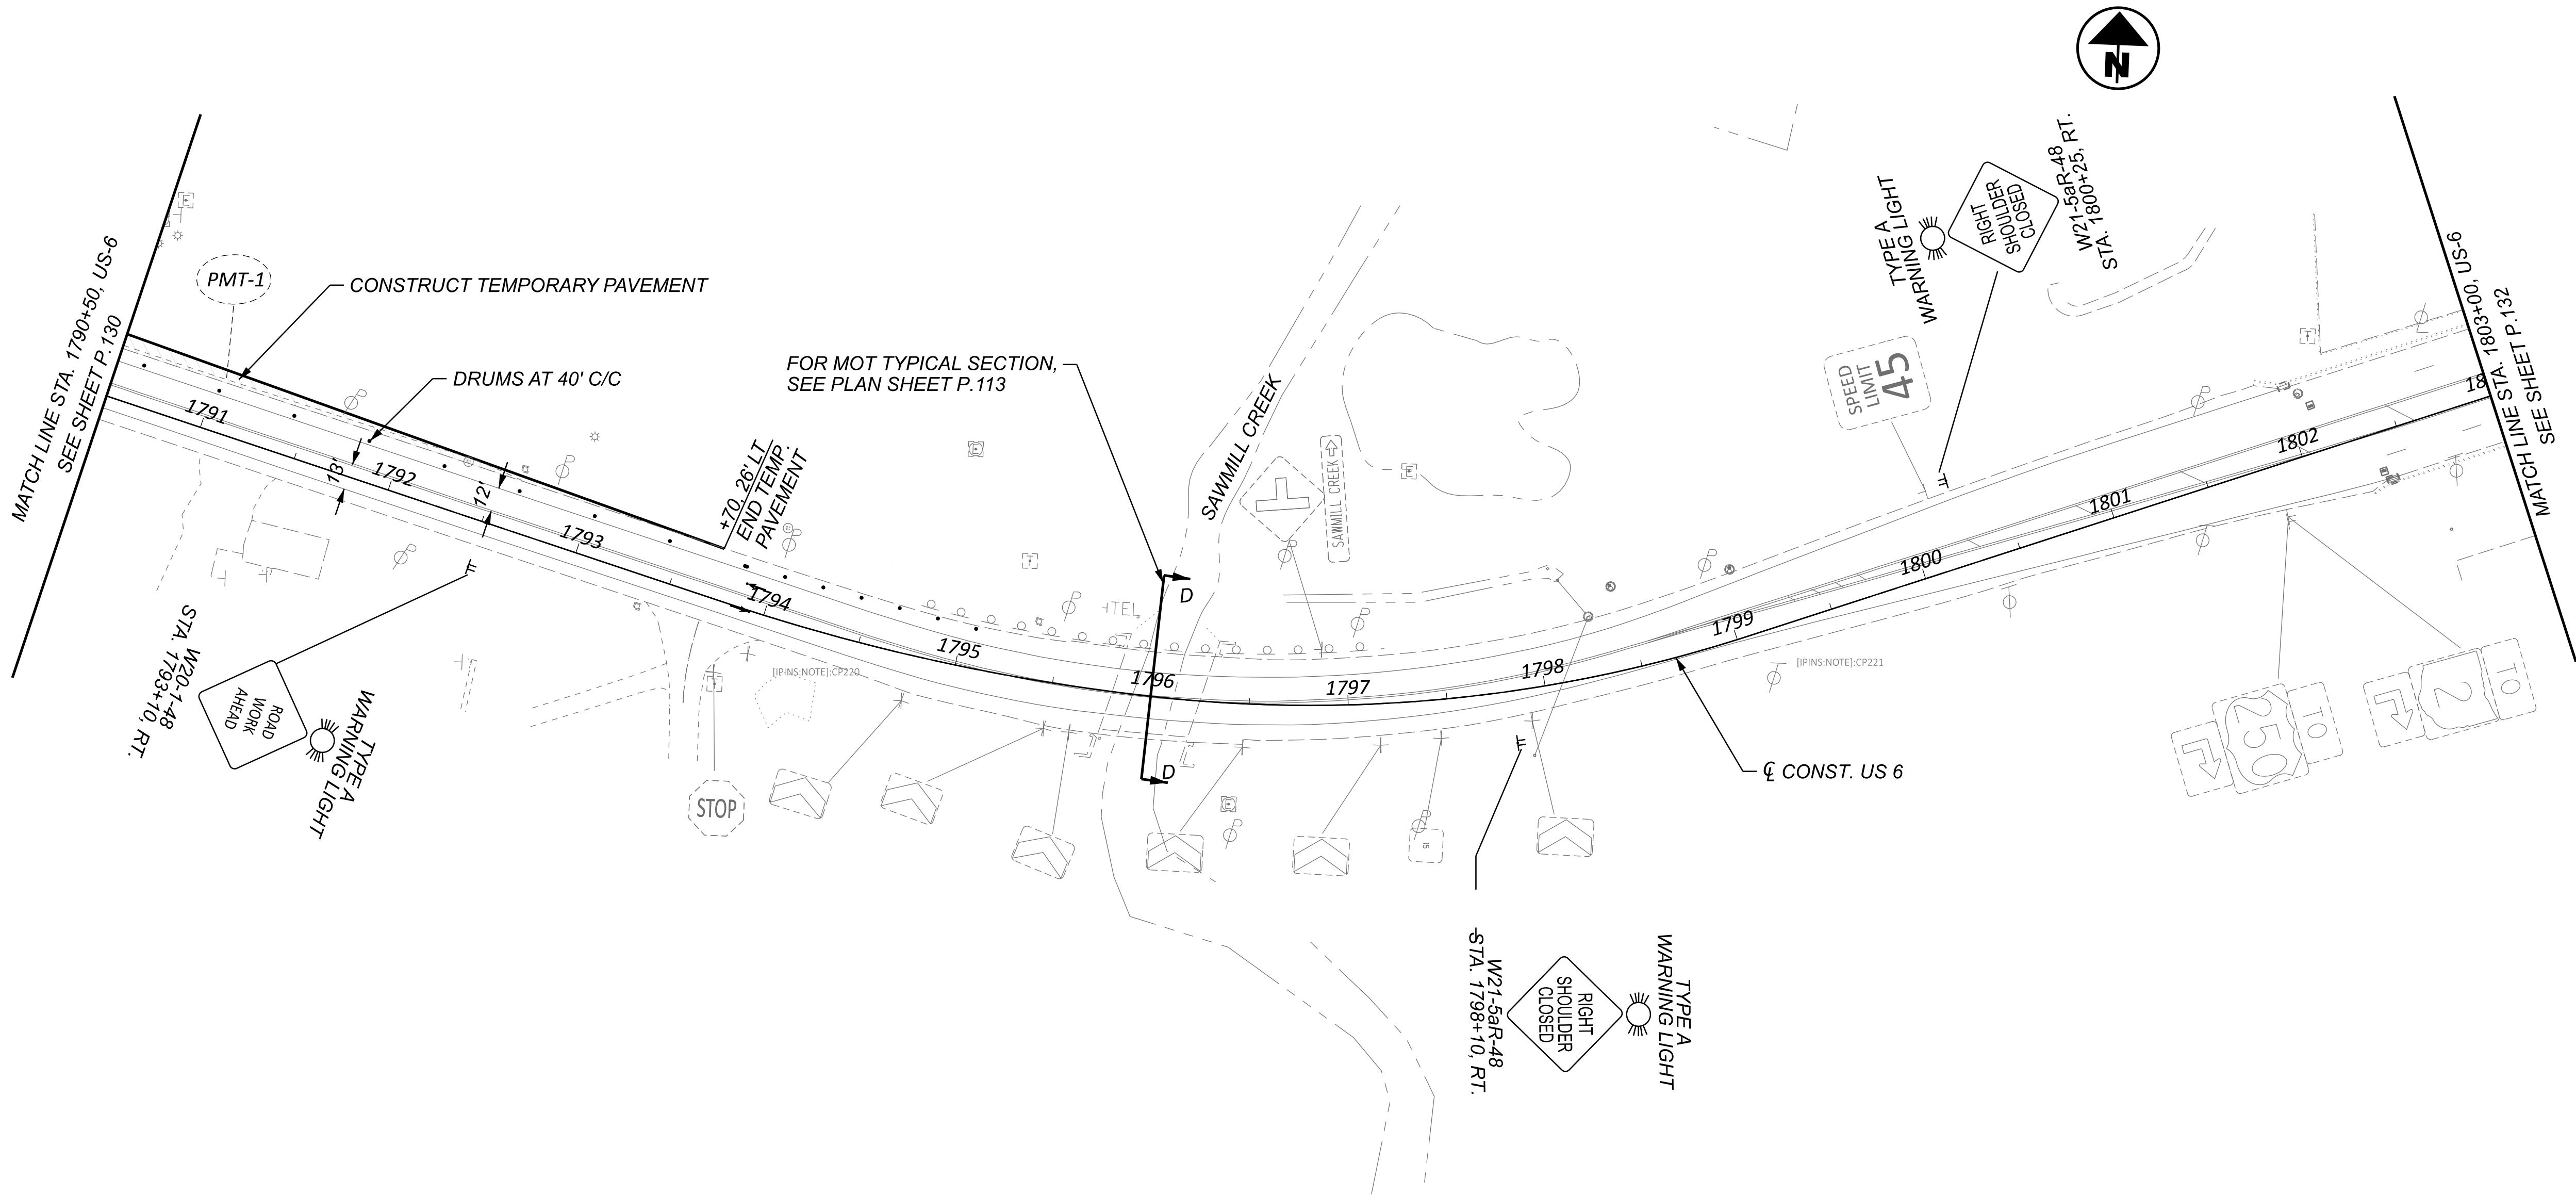

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 - STA. 1790+50.00 TO STA. 1803+00.00


DESIGN AGENCY
TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET	TOTAL
P.134	782




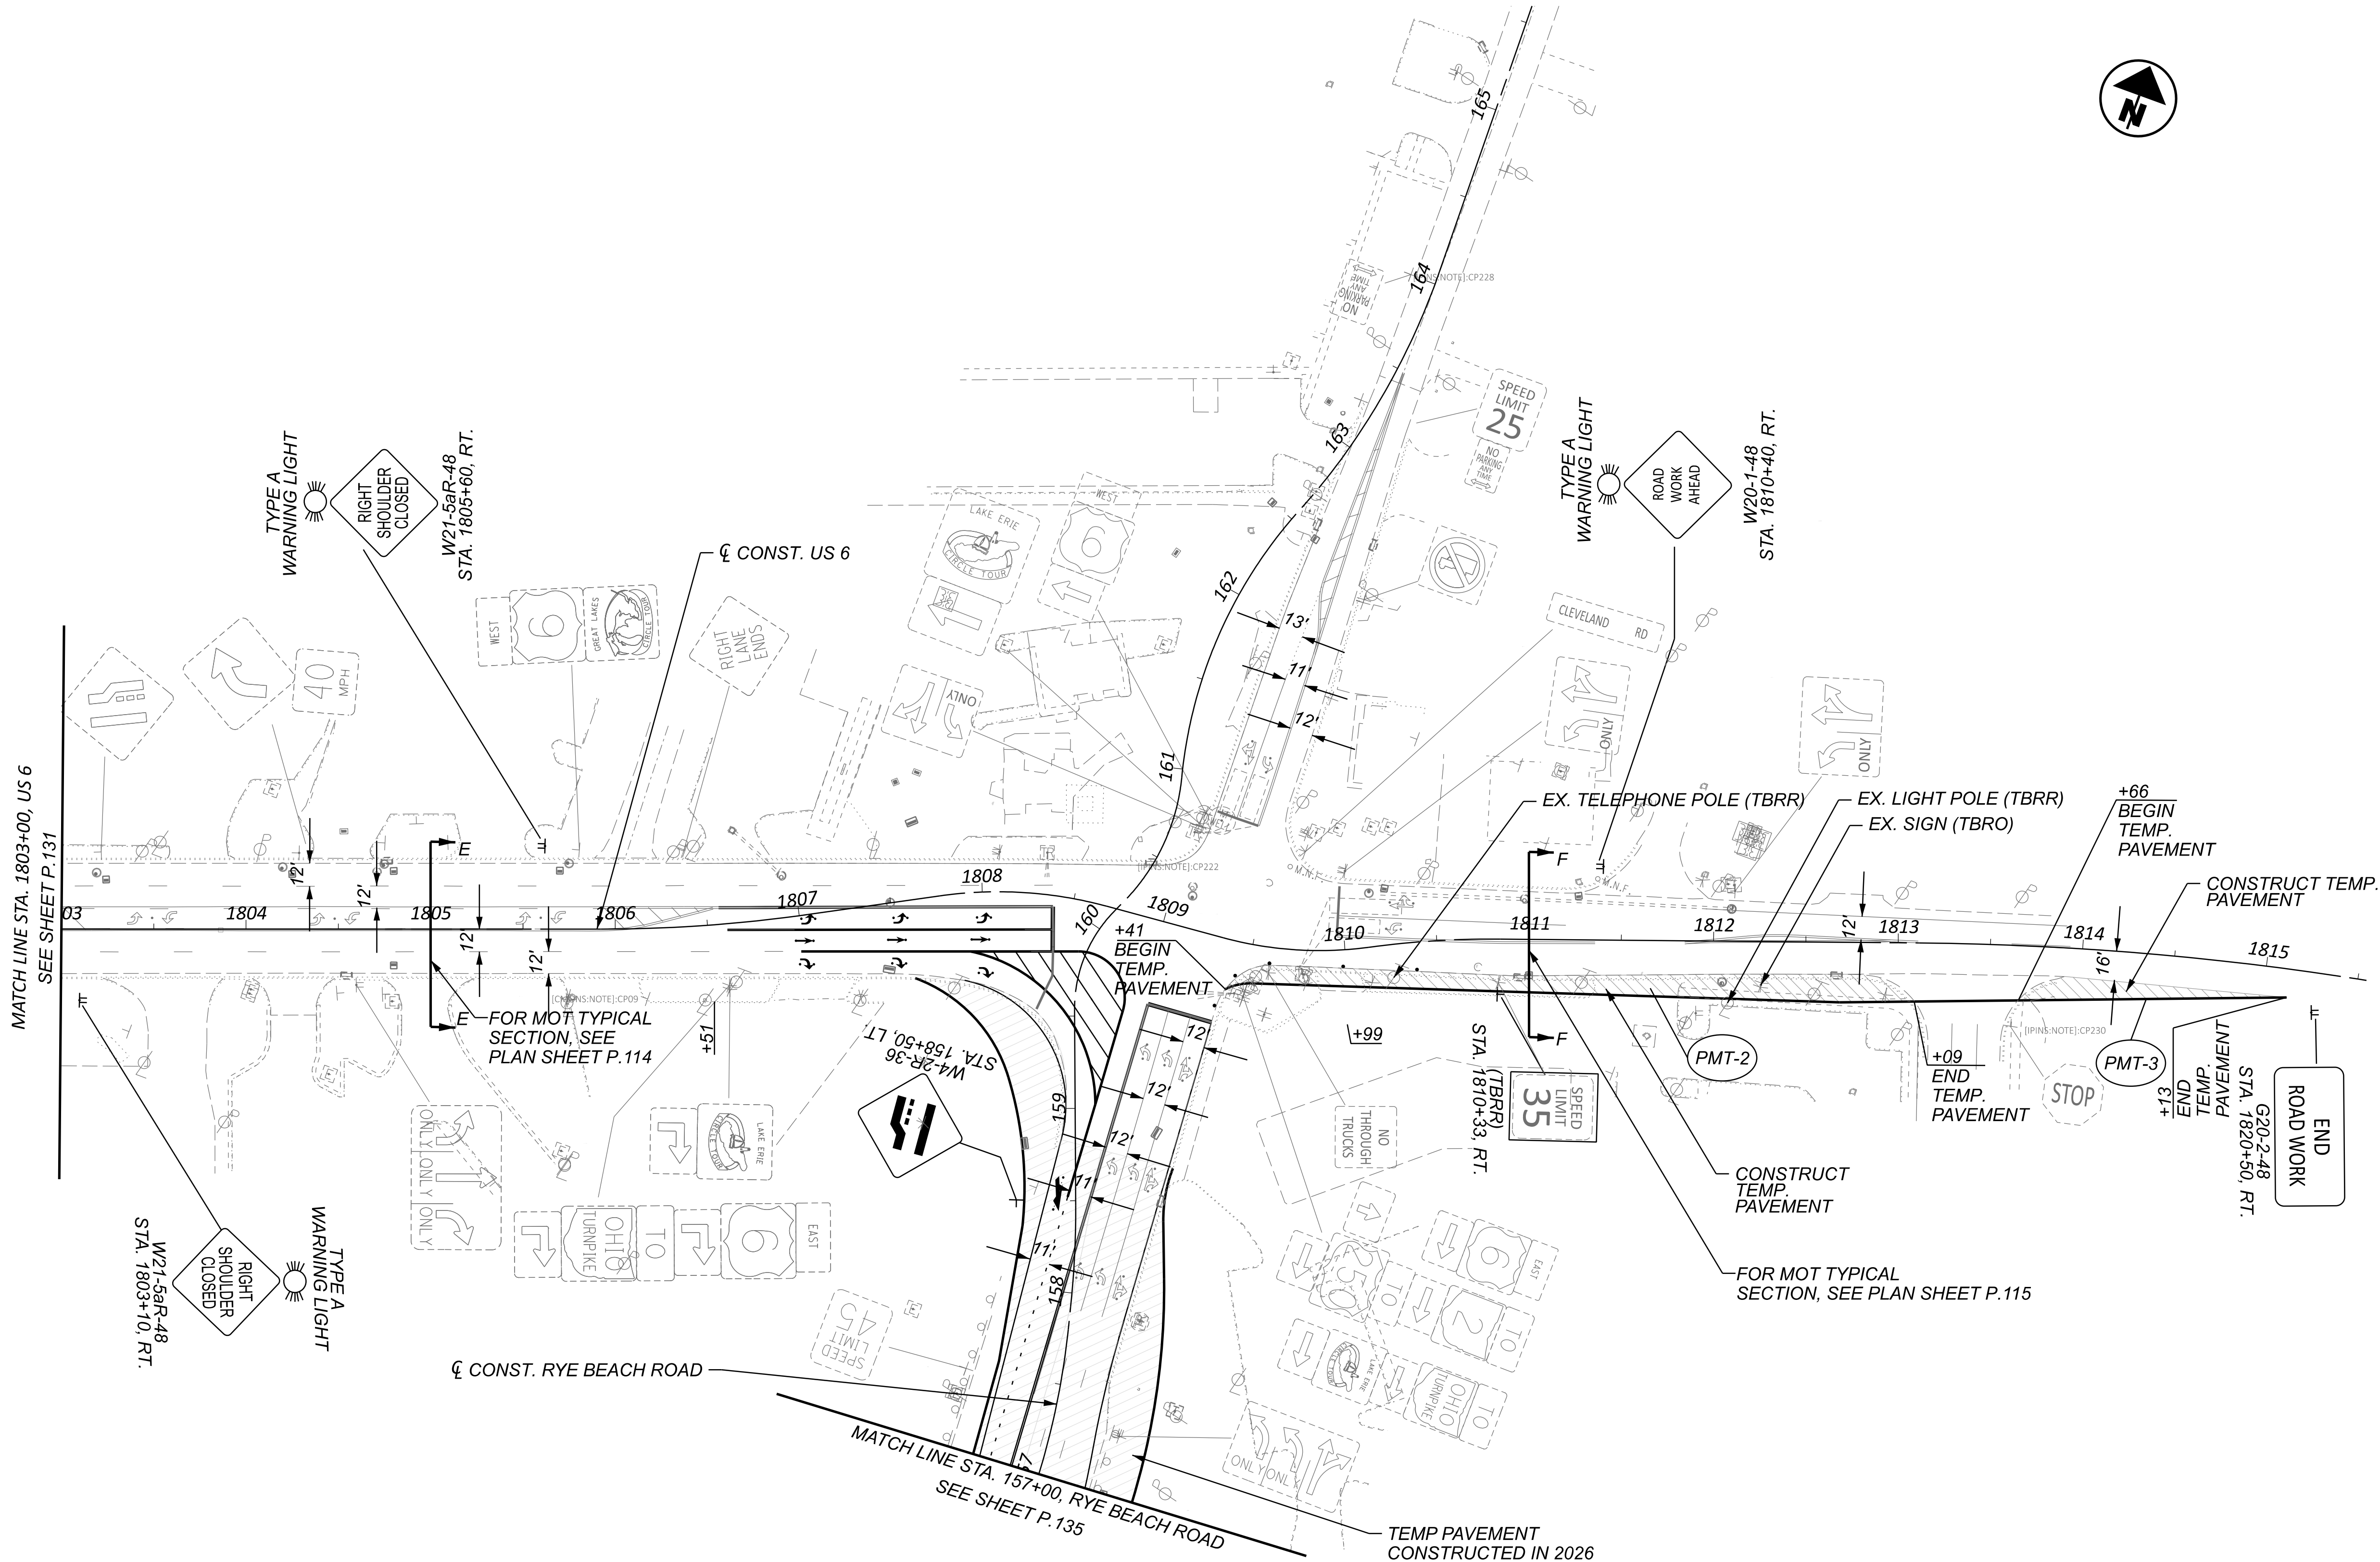


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
US 6 - STA. 1803+00.00 TO END PROJECT

DESIGN AGENCY	
TRANSYSTEMS	
400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS
PROJECT ID	02/28/24
SHEET	116570
TOTAL	782



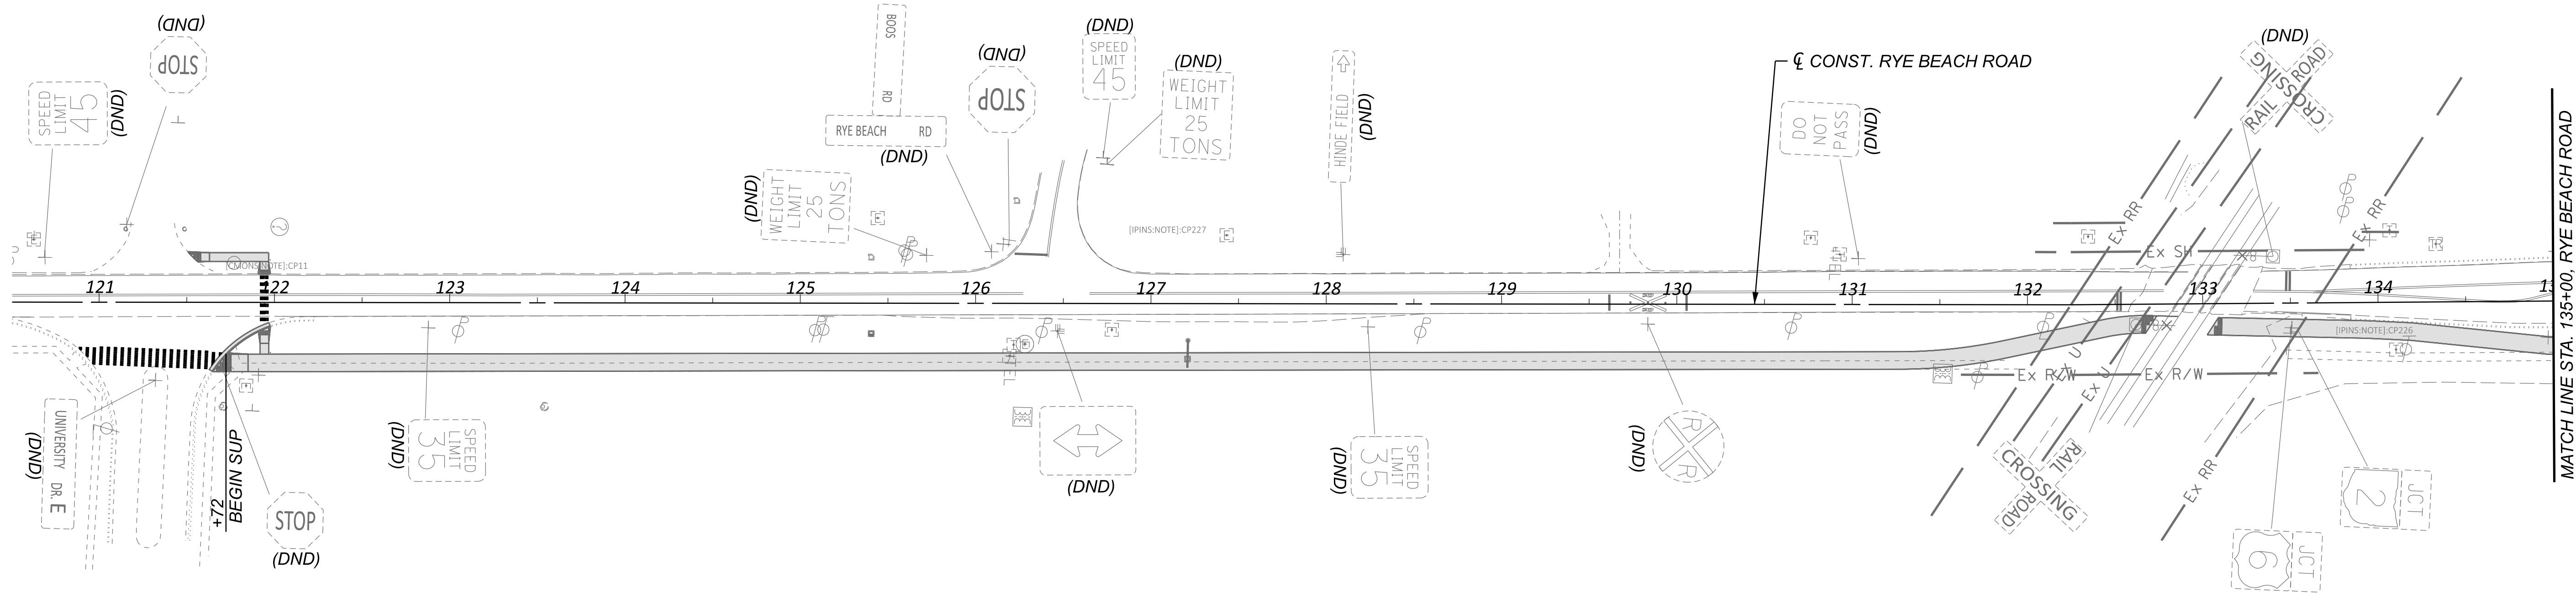

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


DESIGN AGENCY	
TRANSYSTEMS 400 W. WATKINSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	TOTAL
P.136	782

MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
RYE BEACH ROAD - BEGIN PROJECT TO STA. 135+00.00



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 2 - Plan 22 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:24:01 PM USER: ssadusei
\\vohiodor-pw.bentley.com:ohiodor-pw-02\Documents\01 Active Projects\District 03\Errie\116570\402-Engineering_TransSystems\MOT\Sheets\116570_MP000_C\2027.dgn

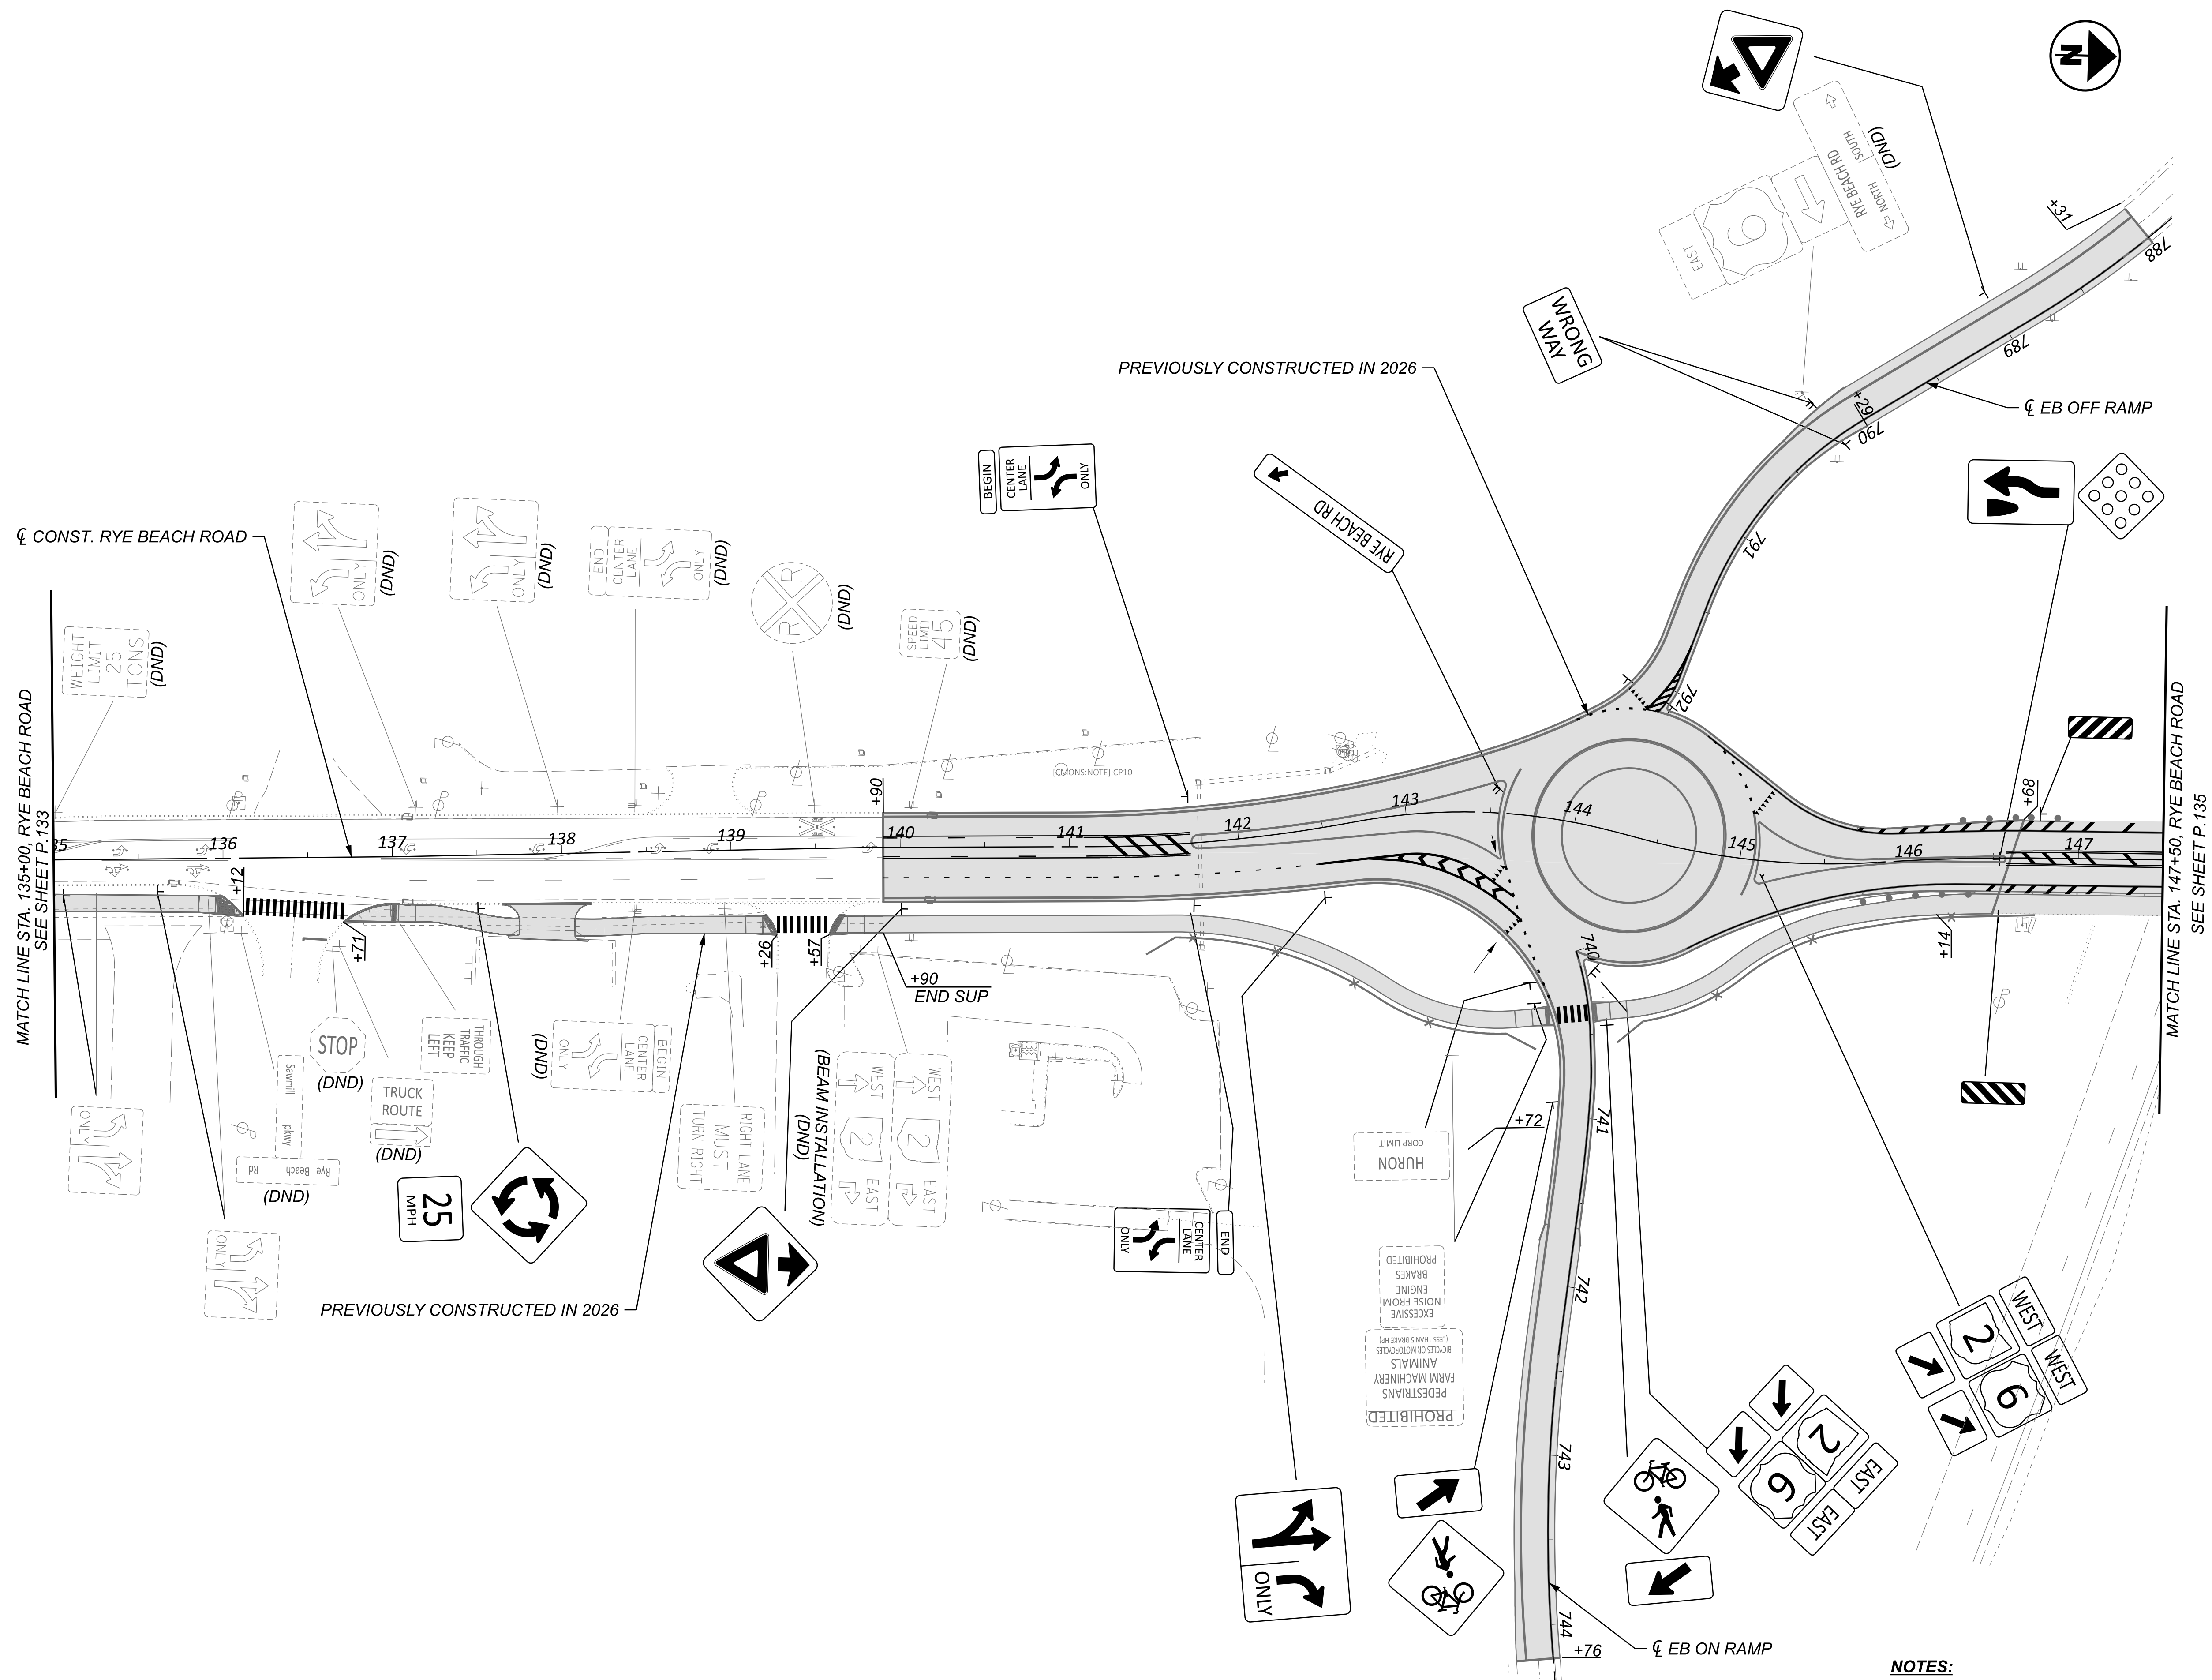

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.


MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
 RYE BEACH ROAD - STA. 135+00.00 TO STA. 147+50.00

DESIGN AGENCY

TRANSYSTEMS


400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.137	782

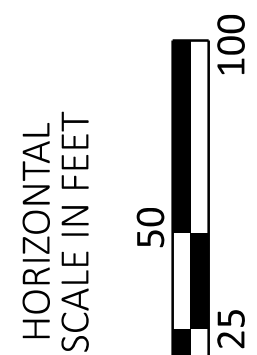


ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 2 - Plan 23 [Sheet] PAPER SIZE: 34x22 [in.] DATE: 6/16/2025 TIME: 5:24:04 PM USER: ssadusei
pw:\vhobdodot-pw.bentley.com:chiodot-pw-02\Documents\01 Active Projects\District 03 Erie\116570\402-Engineering TransSystems\WOT\Sheets\116570 MP000 CV2027.dgn

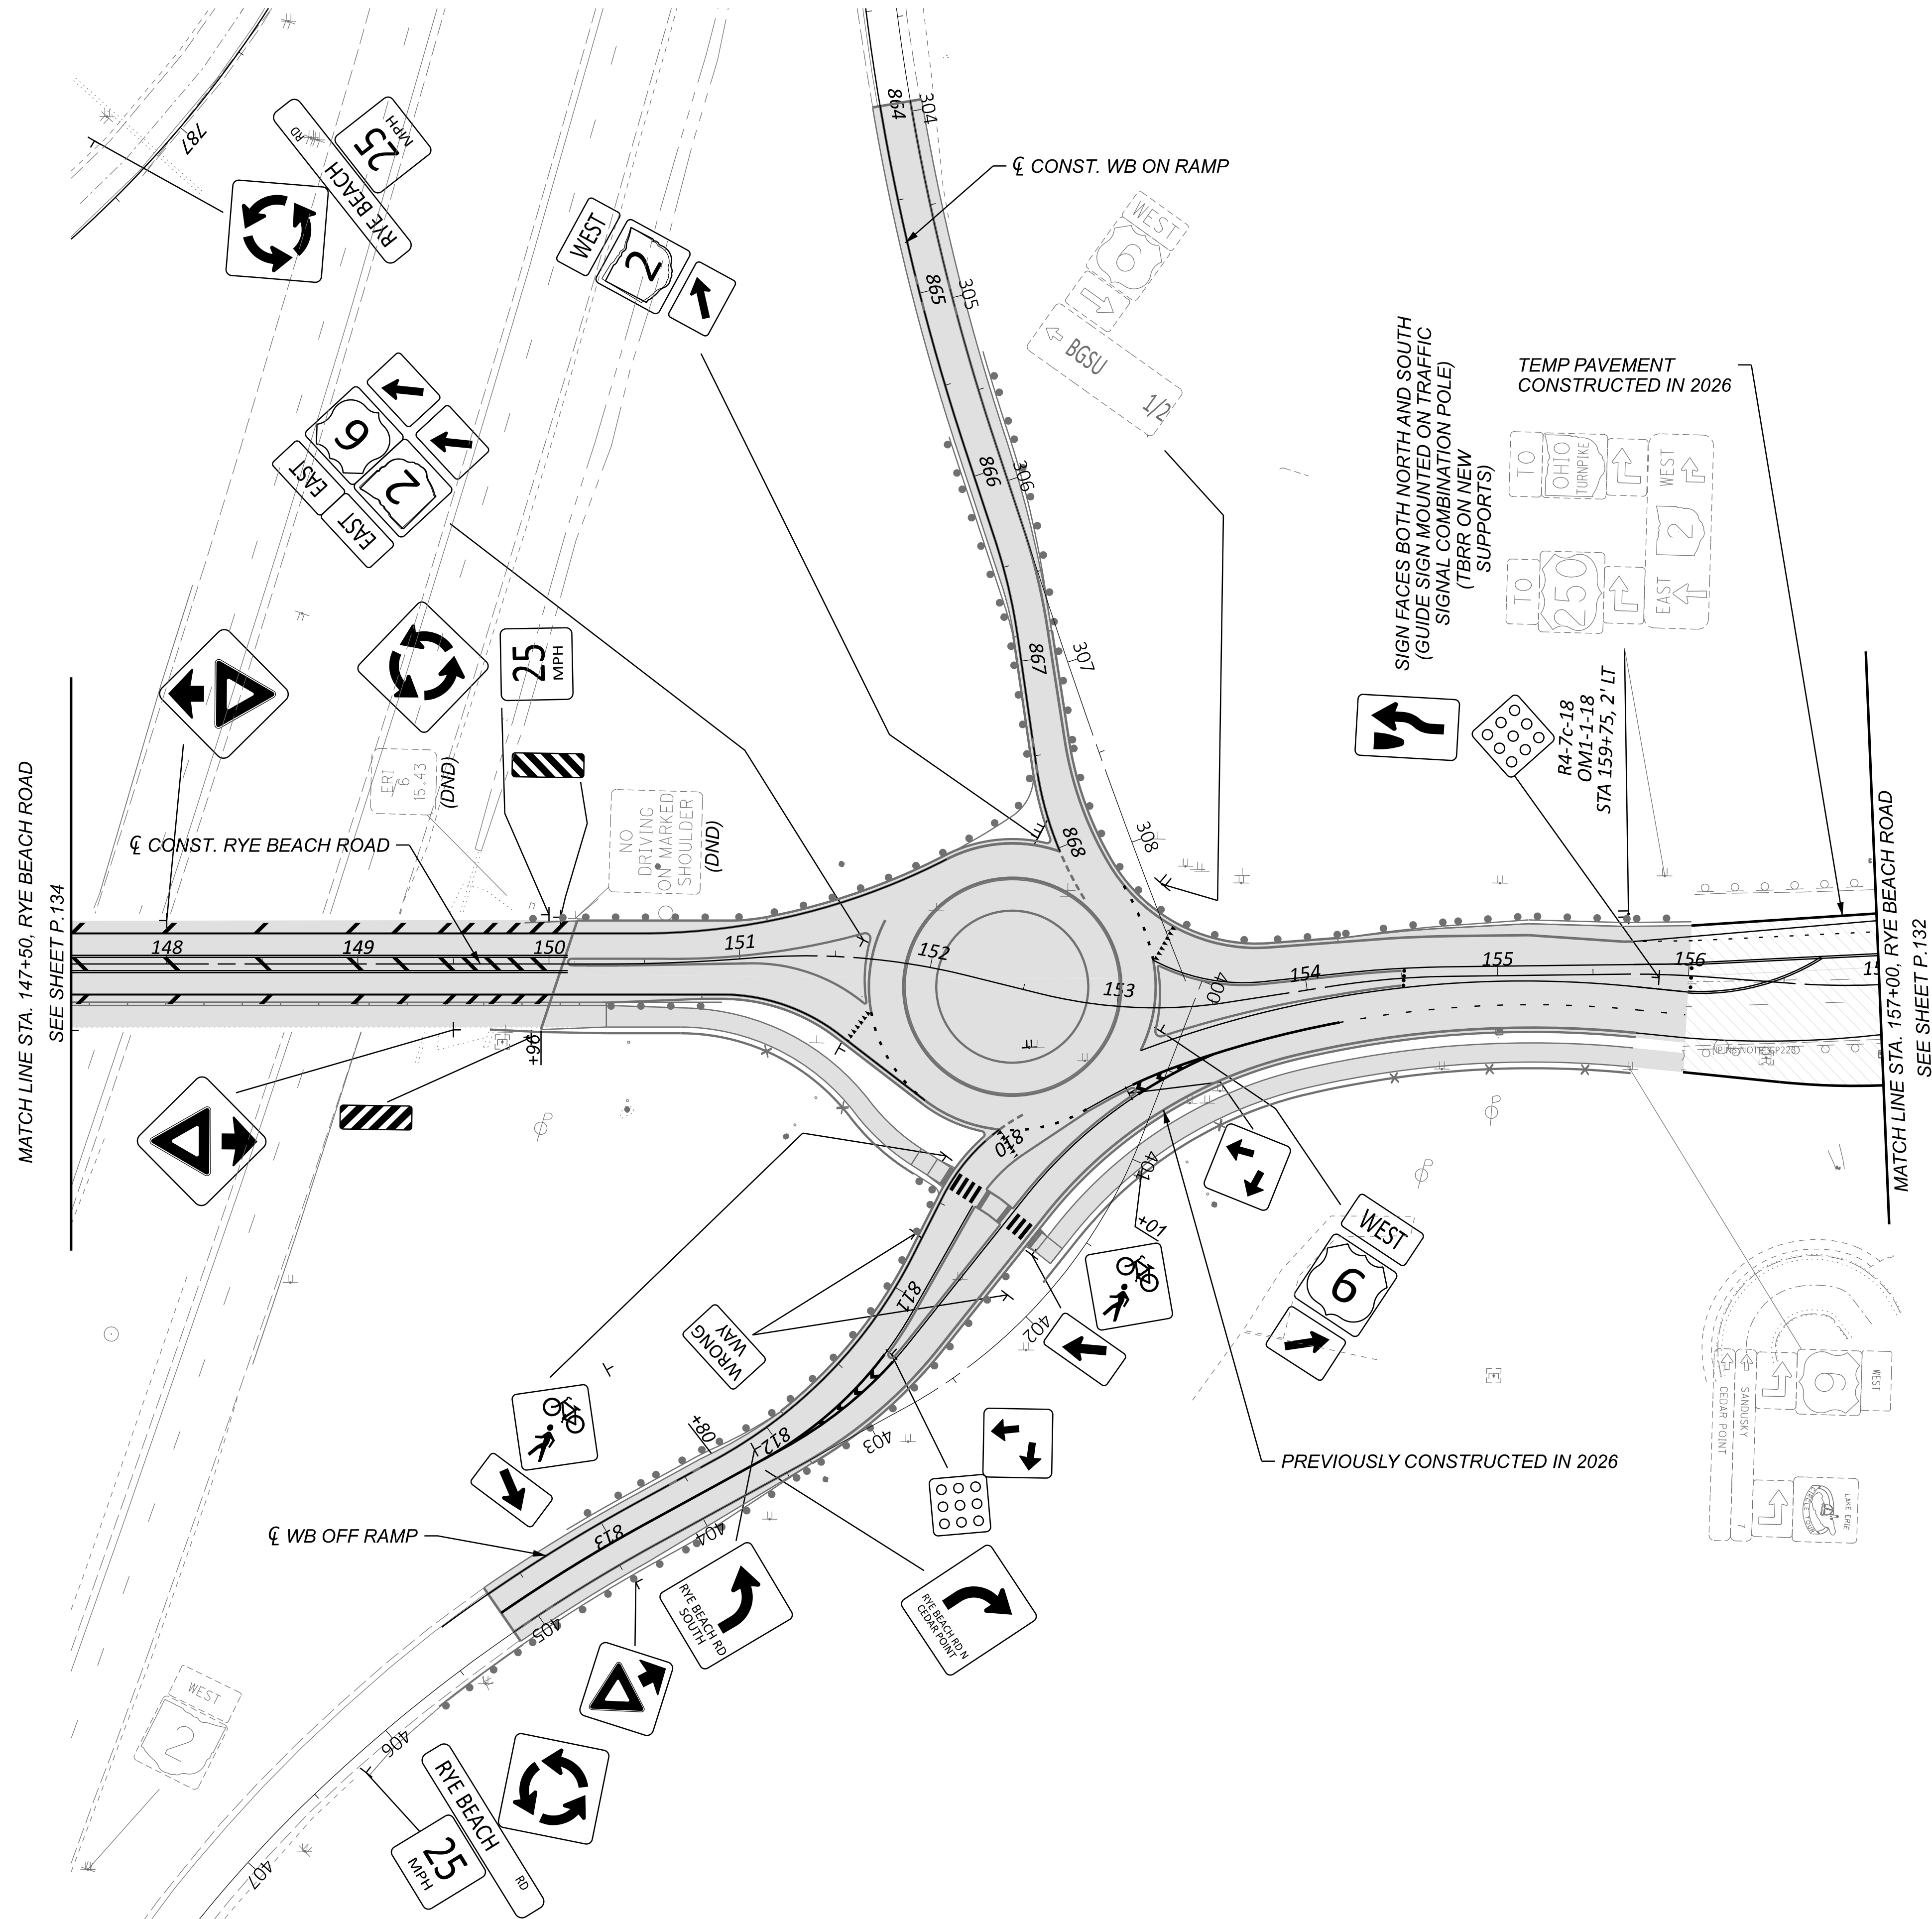

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.



MAINTENANCE OF TRAFFIC - PRE PHASE (2027/2028 CONSTRUCTION)
 RYE BEACH ROAD - STA. 147+50.00 TO STA. 157+00.00

DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28,



PROJECT ID	116570
------------	--------


SHEET	TOTAL
P.138	78

HORIZONTAL
SCALE IN FEET



25 50 100

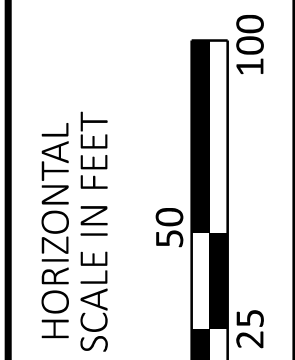


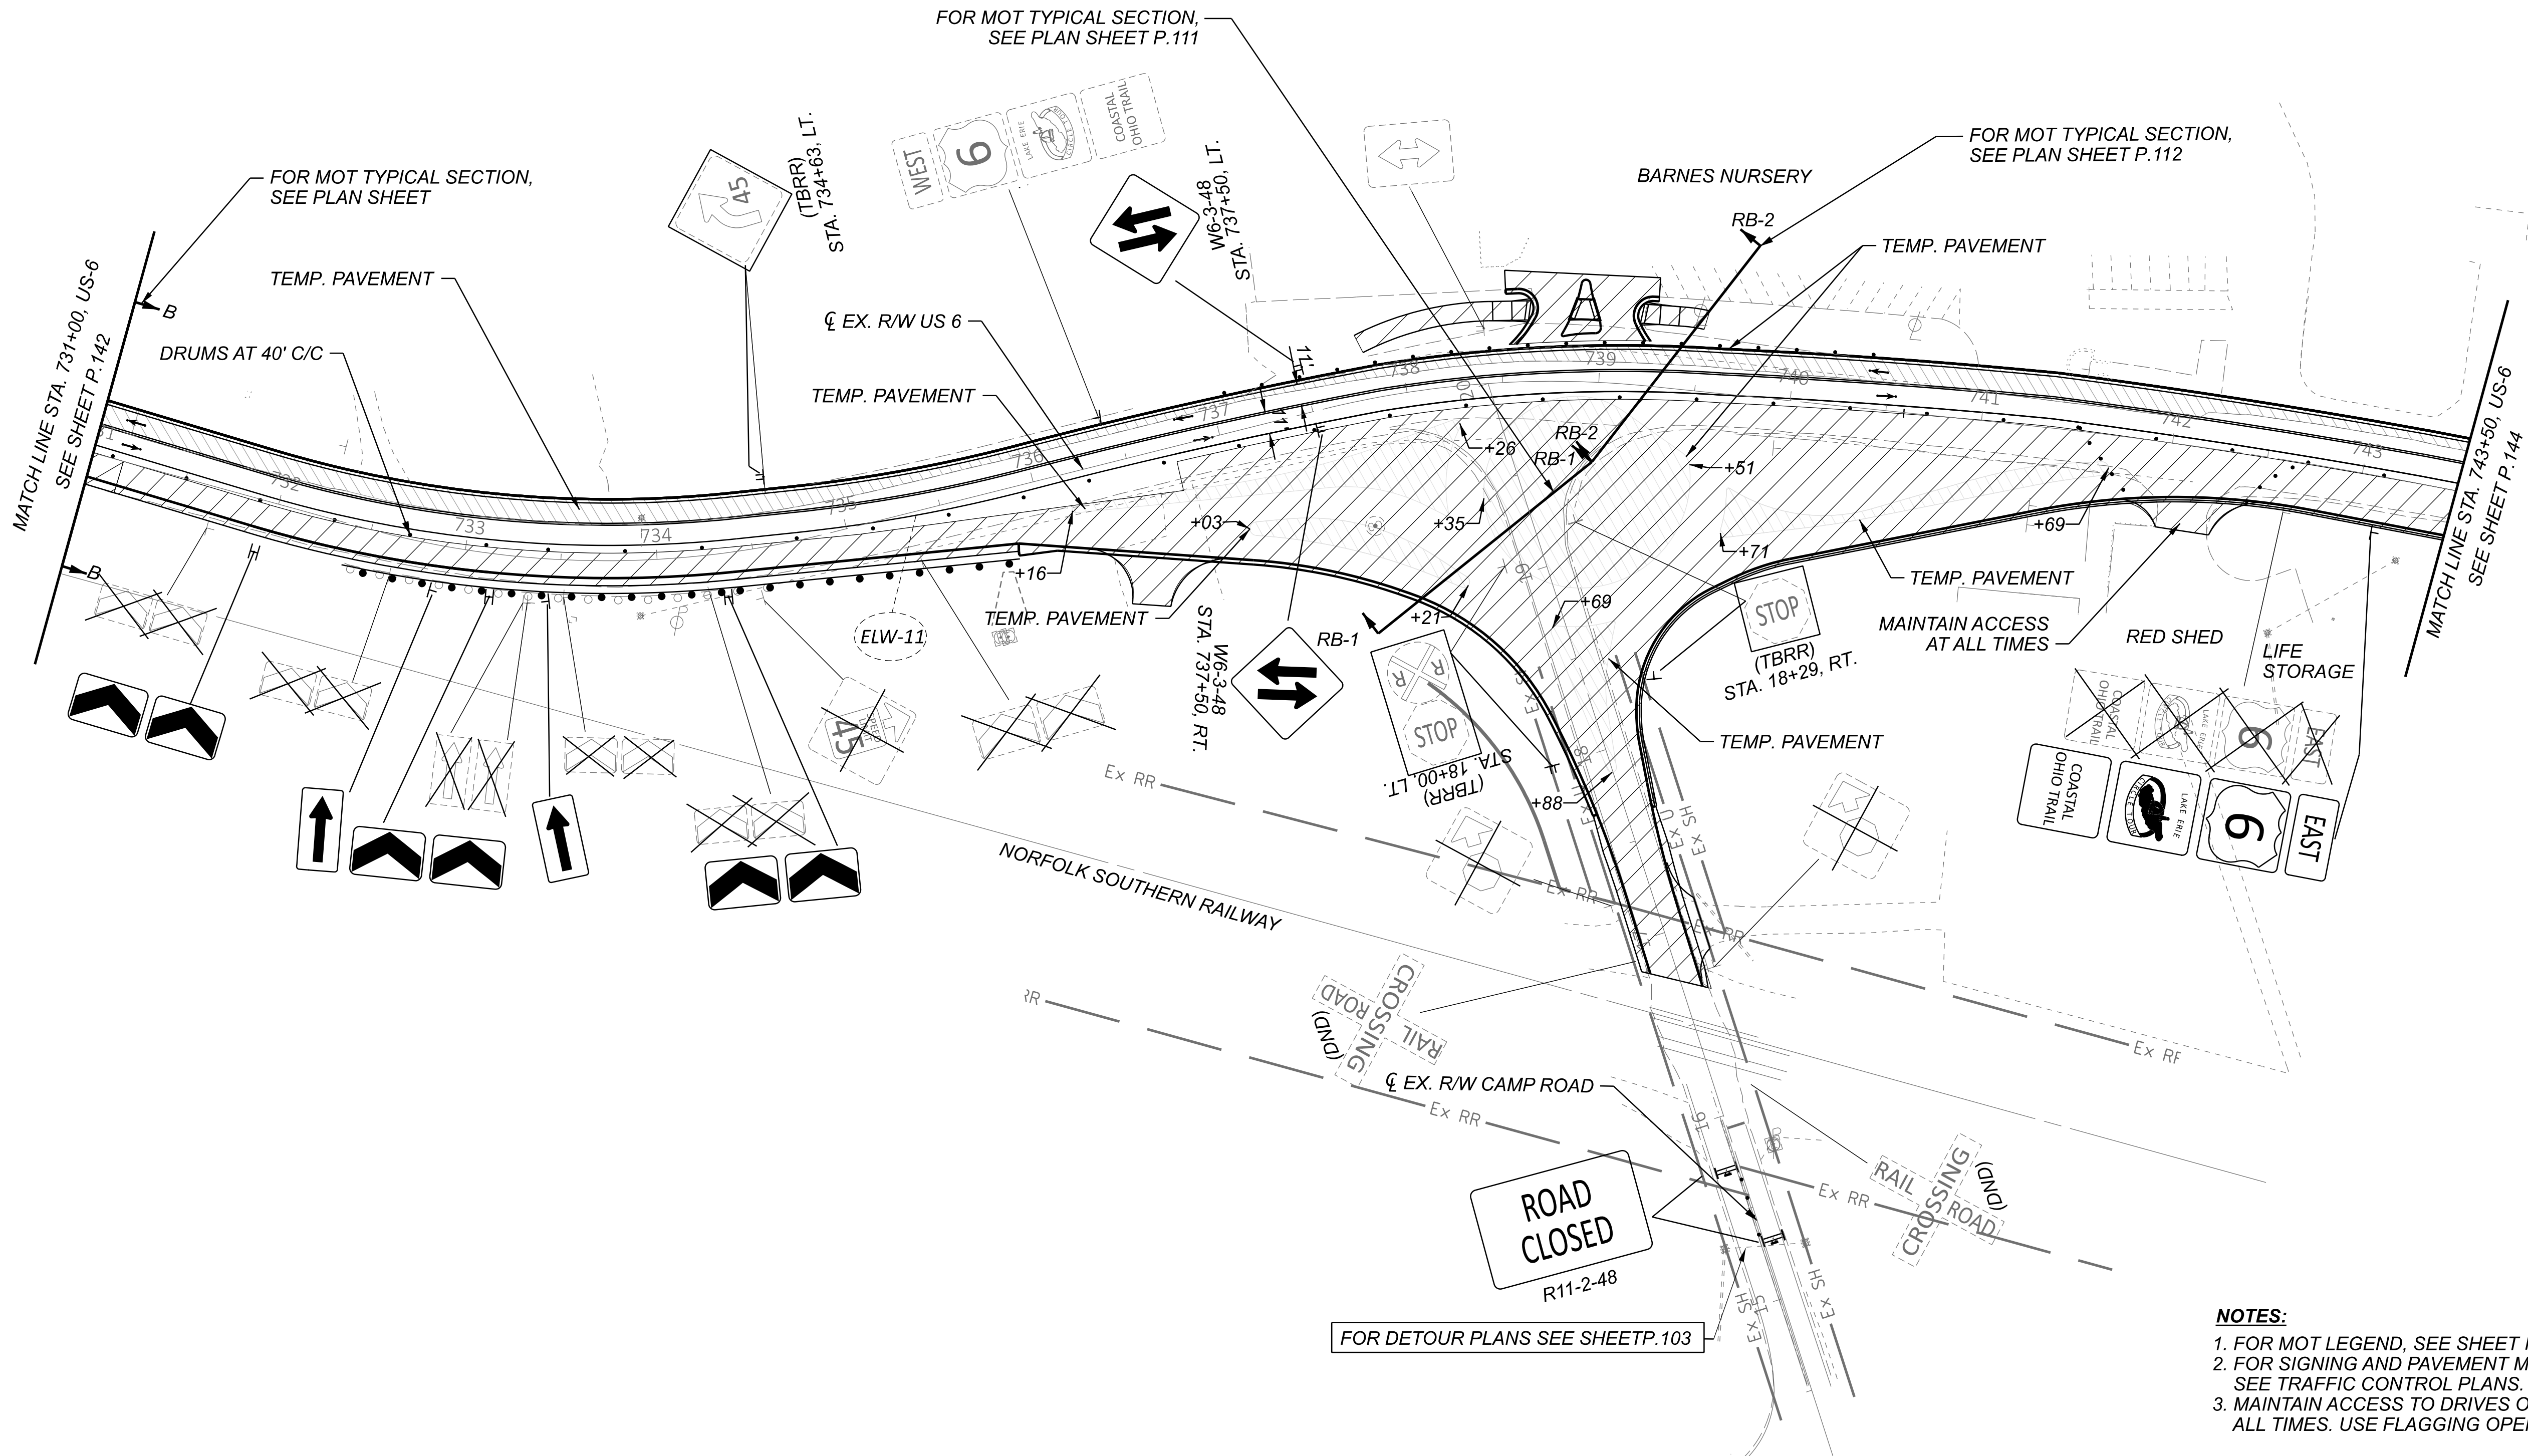

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
US 6 - STA. 731+00.00 TO STA. 743+50.00

TRANSYSTEMS
400 W. WATSON BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGN AGENCY	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.146	782



- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

ERI-US 0006-CONNECTIVITY CORRIDOR


MODEL: CLP_SUP 1 - Plan 15-16 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/16/2025 TIME: 5:58:45 PM USER: ssadusei
pw:\ohiodot-pw.bentley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\Erre\116570\402-Engineering_TransSystems\MOT\Sheets\116570_MP001_CY2027.dgn

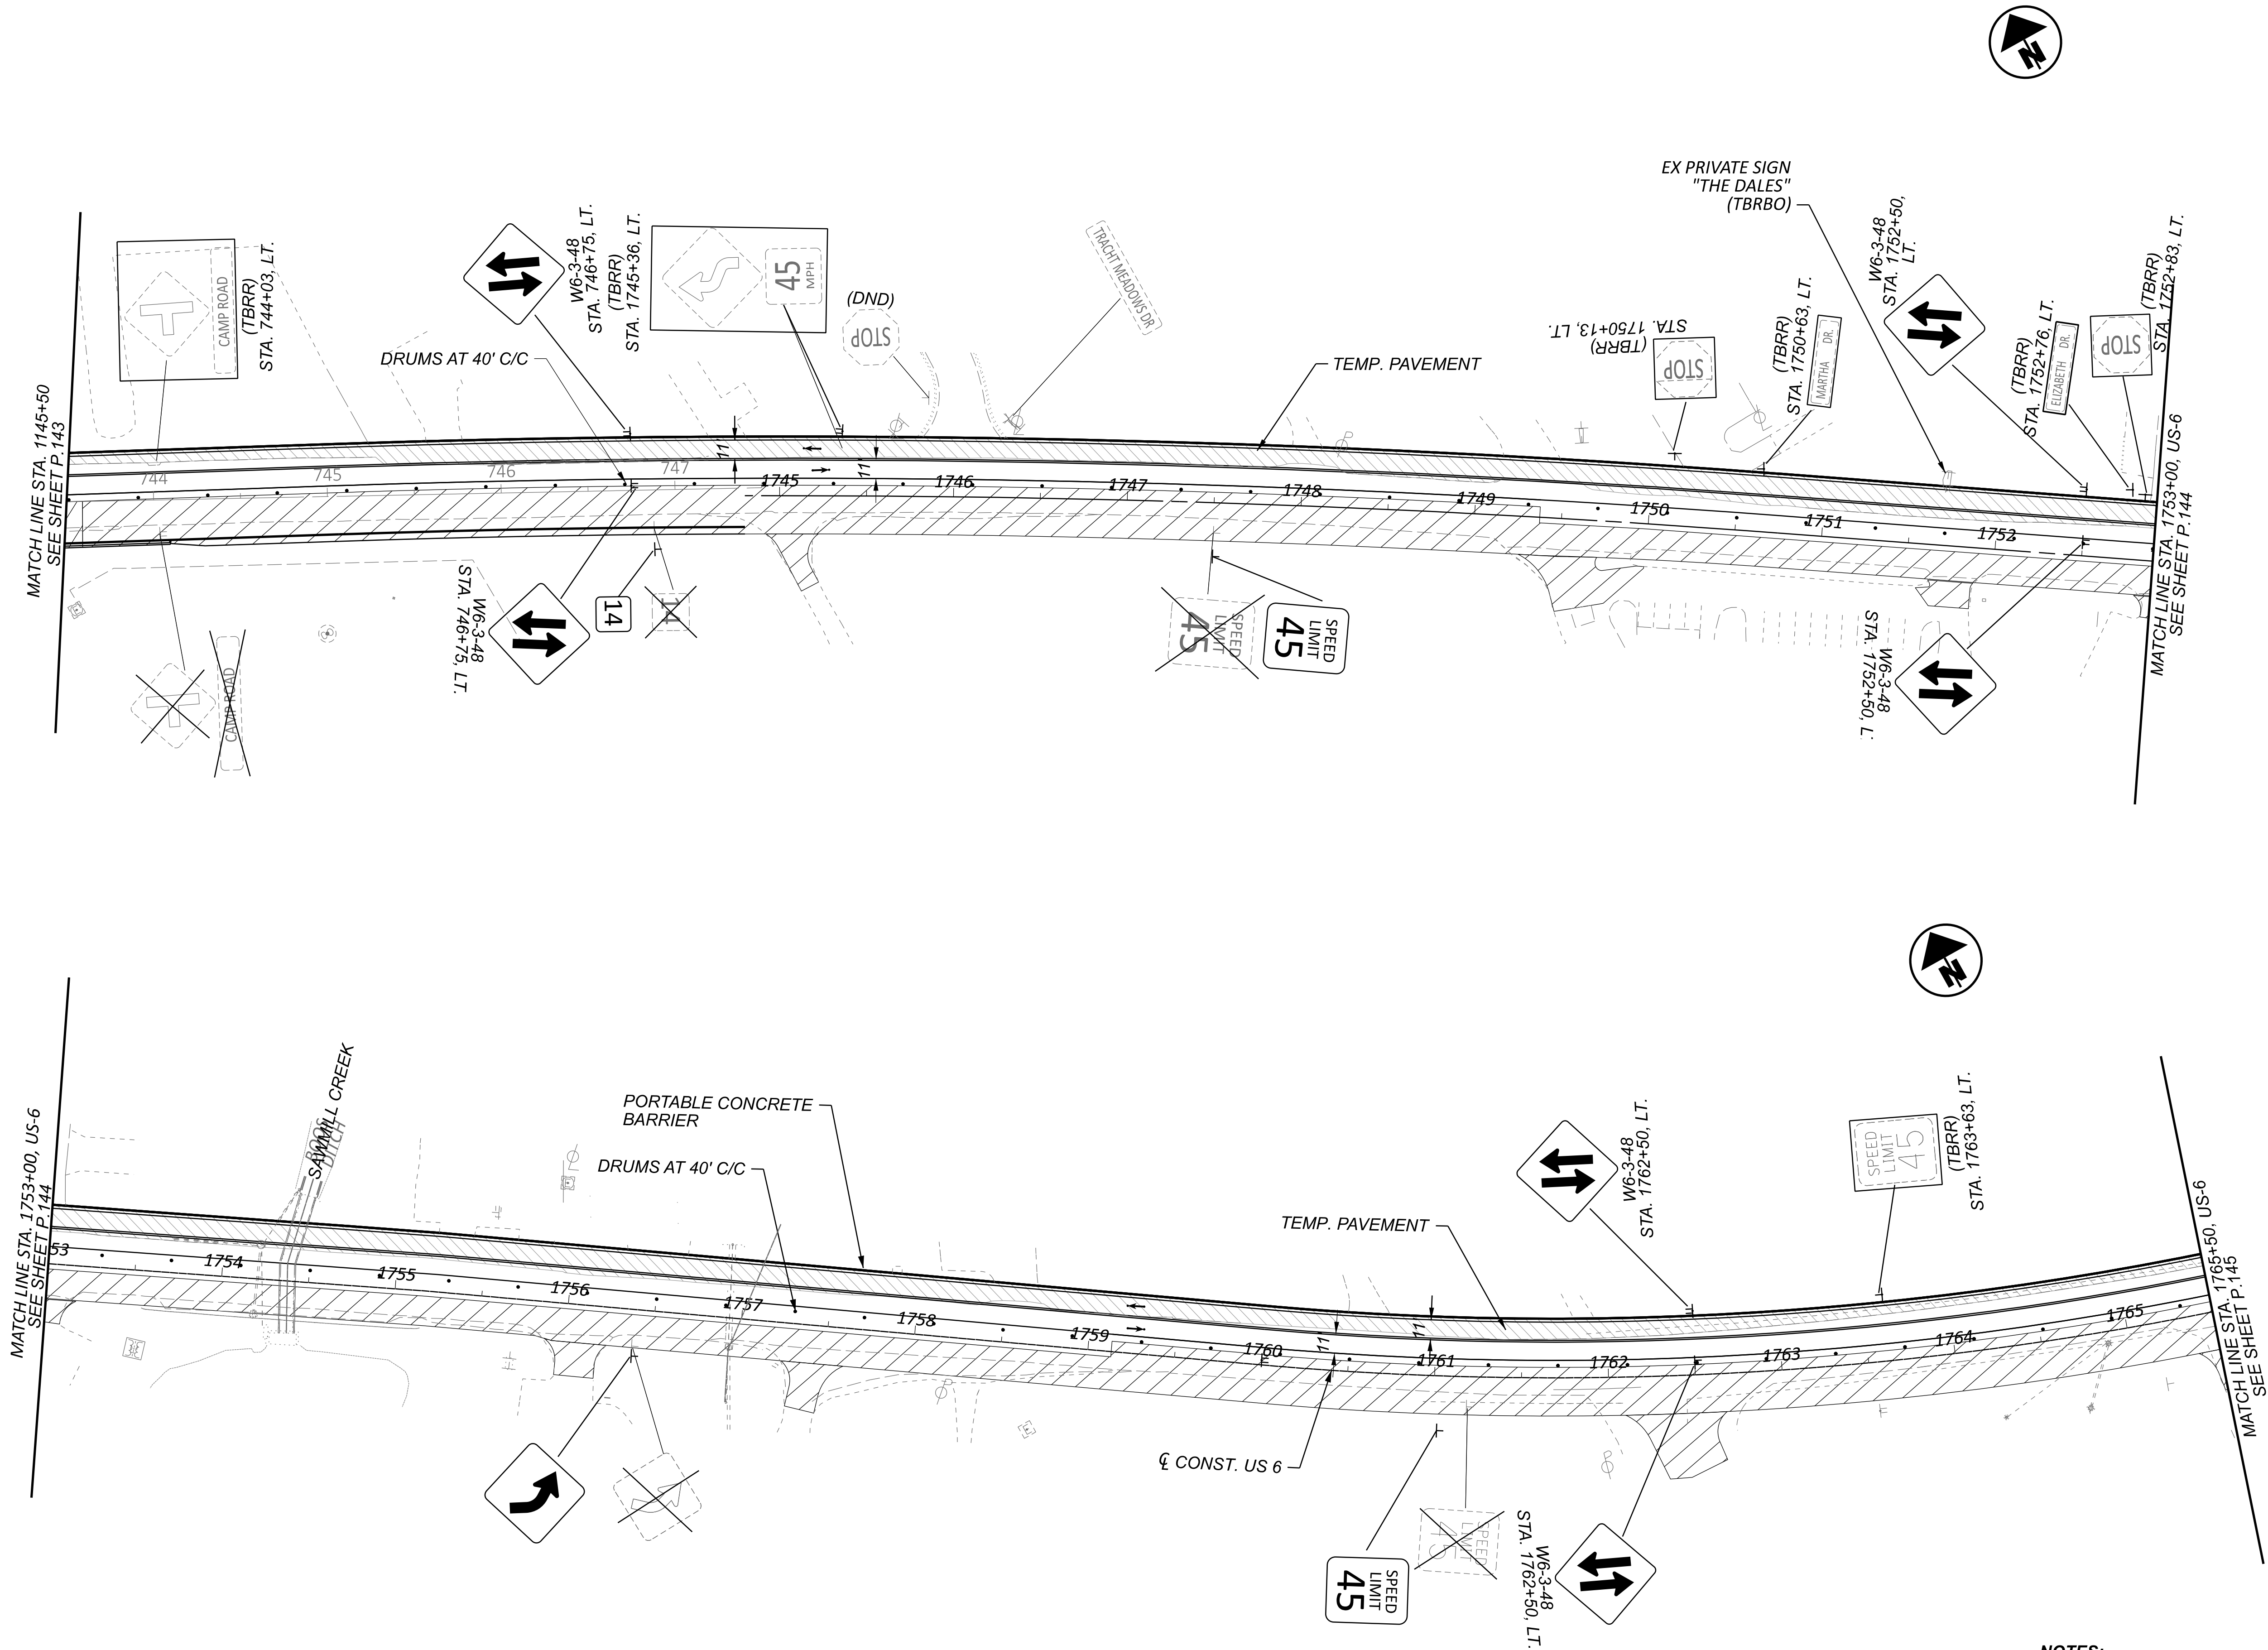


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.147	782

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
US 6 - EX. US 6 STA. 743+50.00 TO CONST. US 6 STA. 1765+50.00



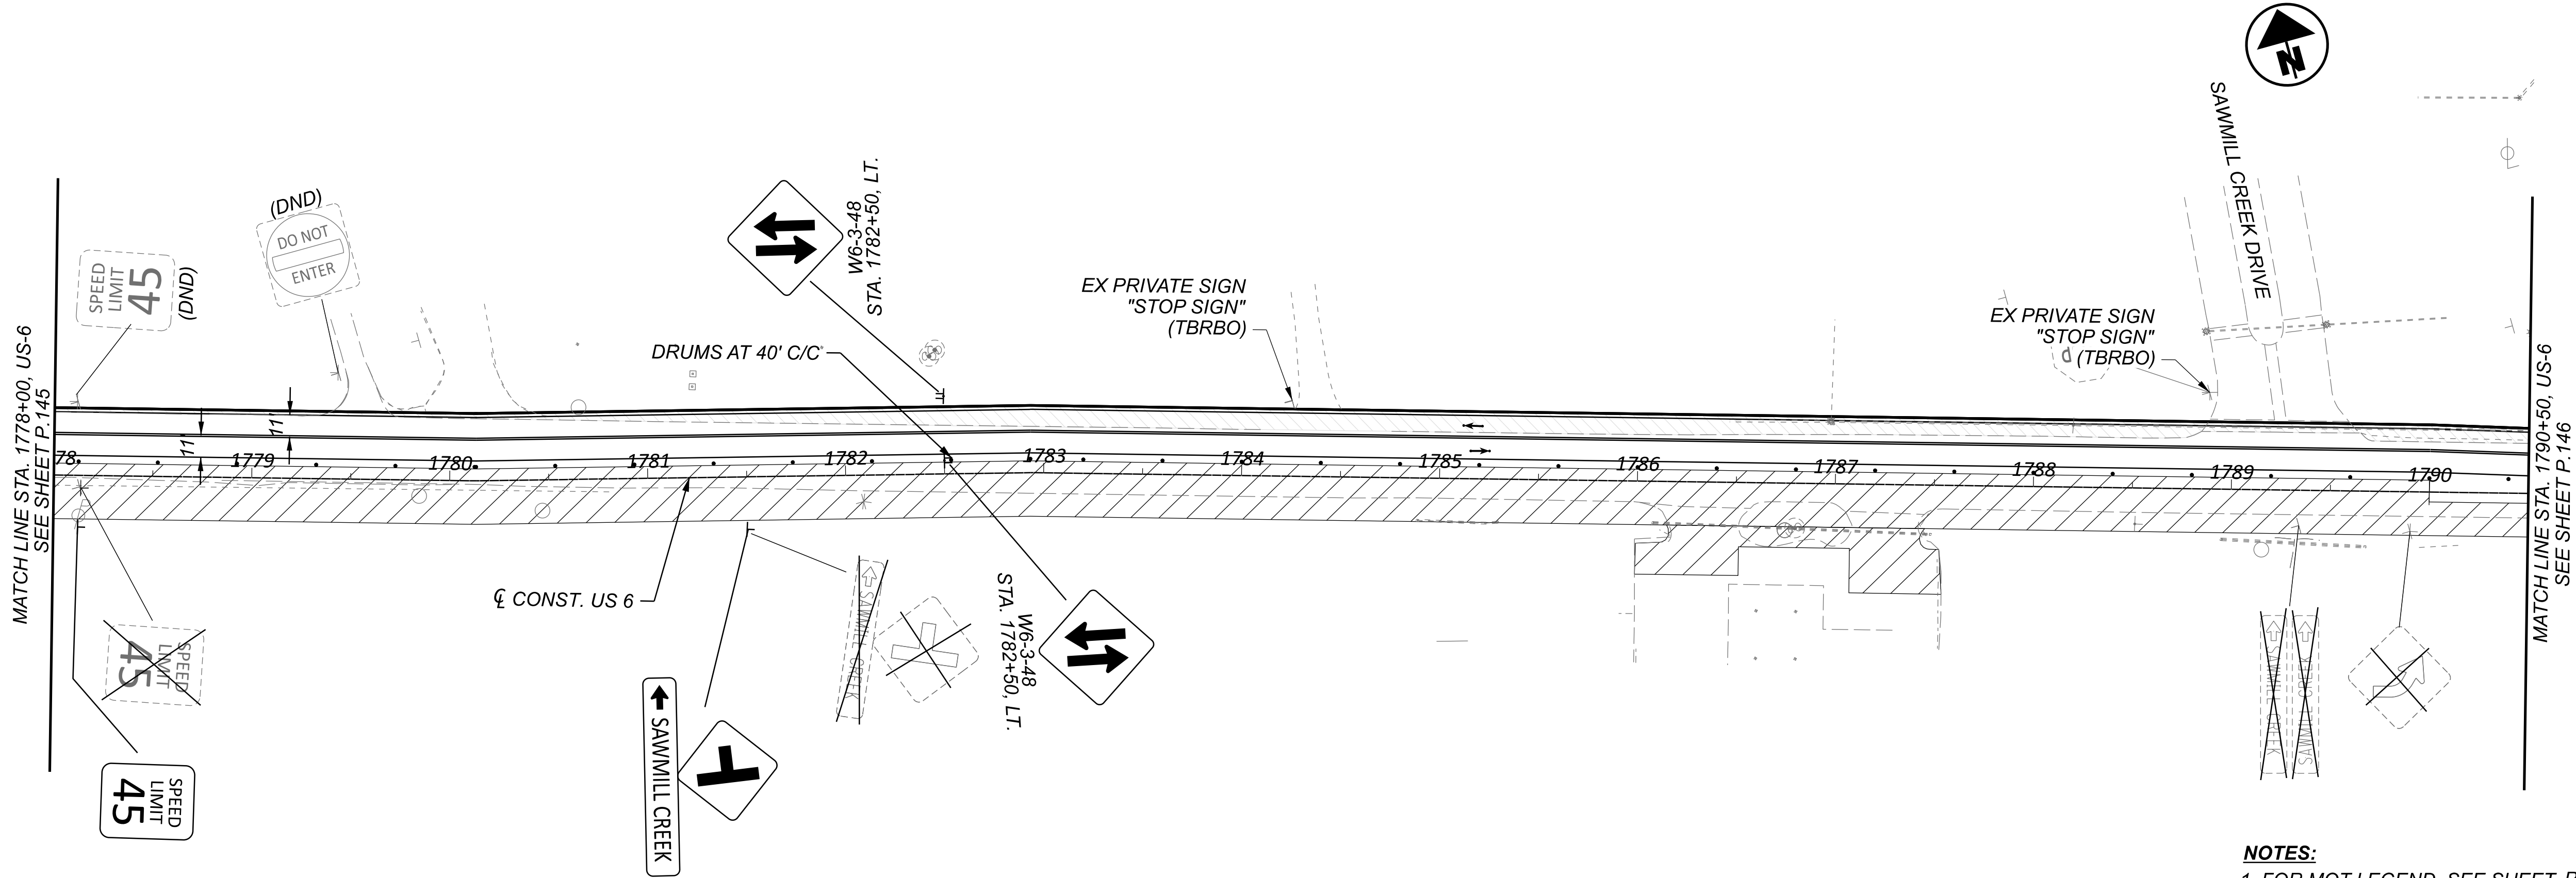

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

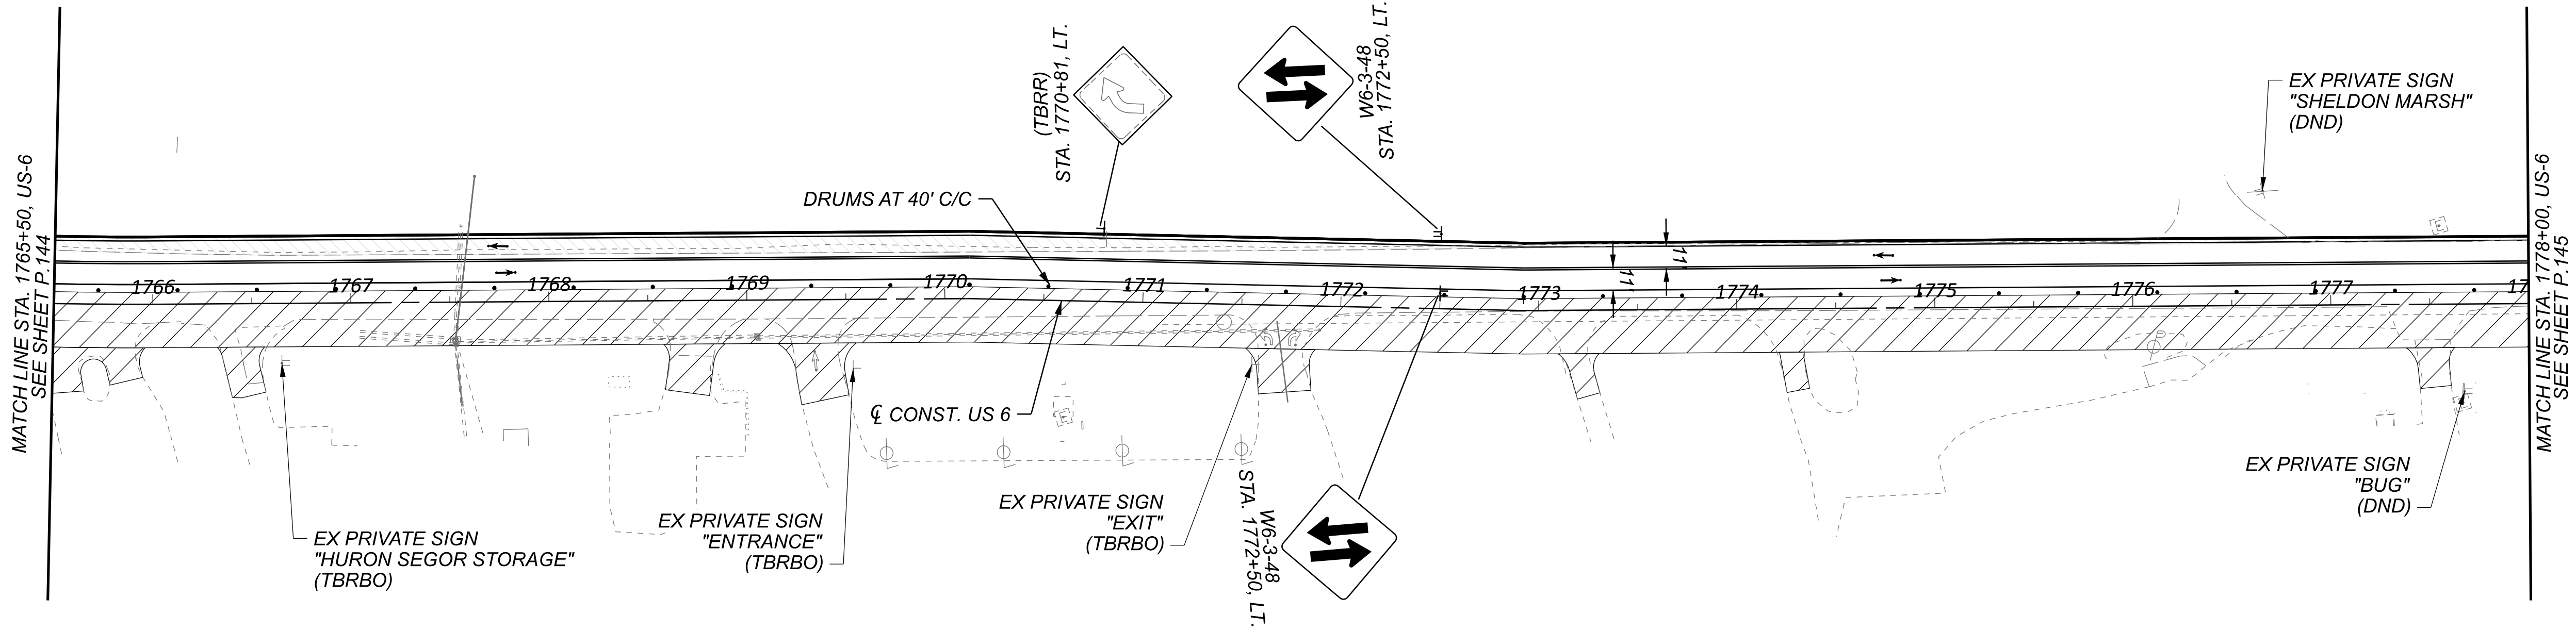

TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID

116570

SHEET



P.148


TOTAL

782

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
US 6 - STA. 1765+50.00 TO STA. 1790+50.00

HORIZONTAL
SCALE IN FEET



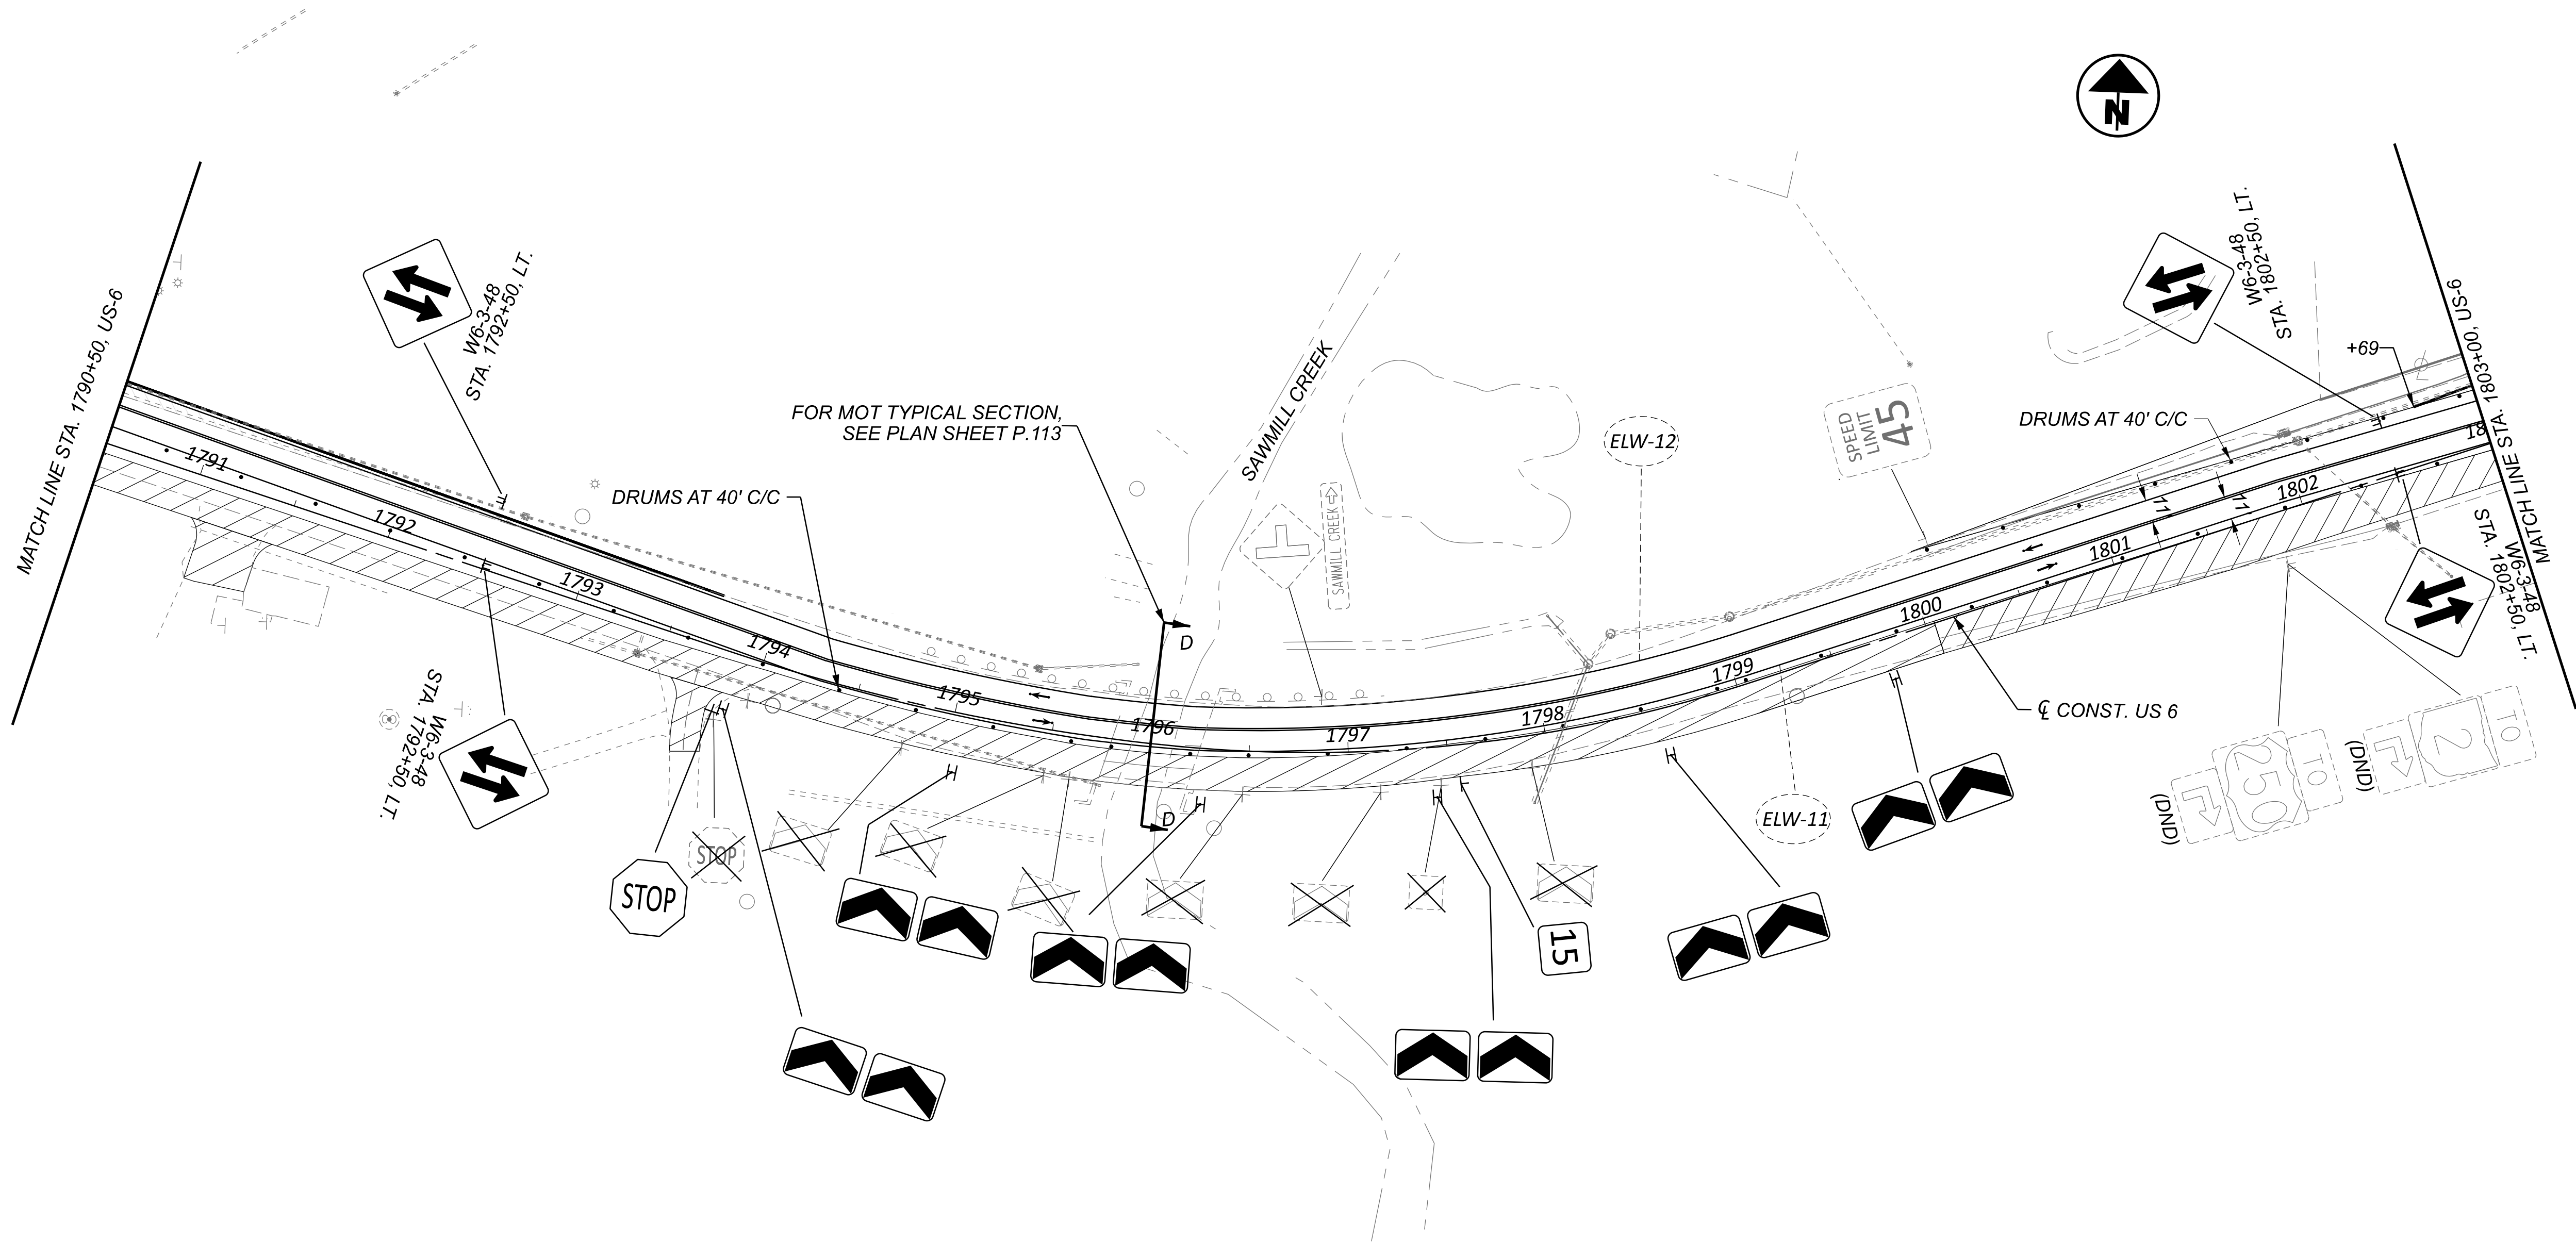


- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068 .
 - 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. FOR SECTION D-D, SEE SHEET P.113 .
 - 4. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATIONS AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
US - 6 STA. 1790+50.00 TO STA. 1803+00.00


TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.149	782

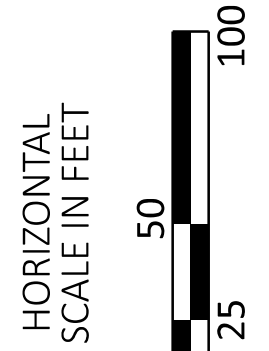



1. FOR MOT LEGEND, SEE SHEET P.068 .
2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. FOR SECTION E-E, SEE SHEET P.114 .
4. FOR SECTION D-D, SEE SHEET P.115 .
5. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

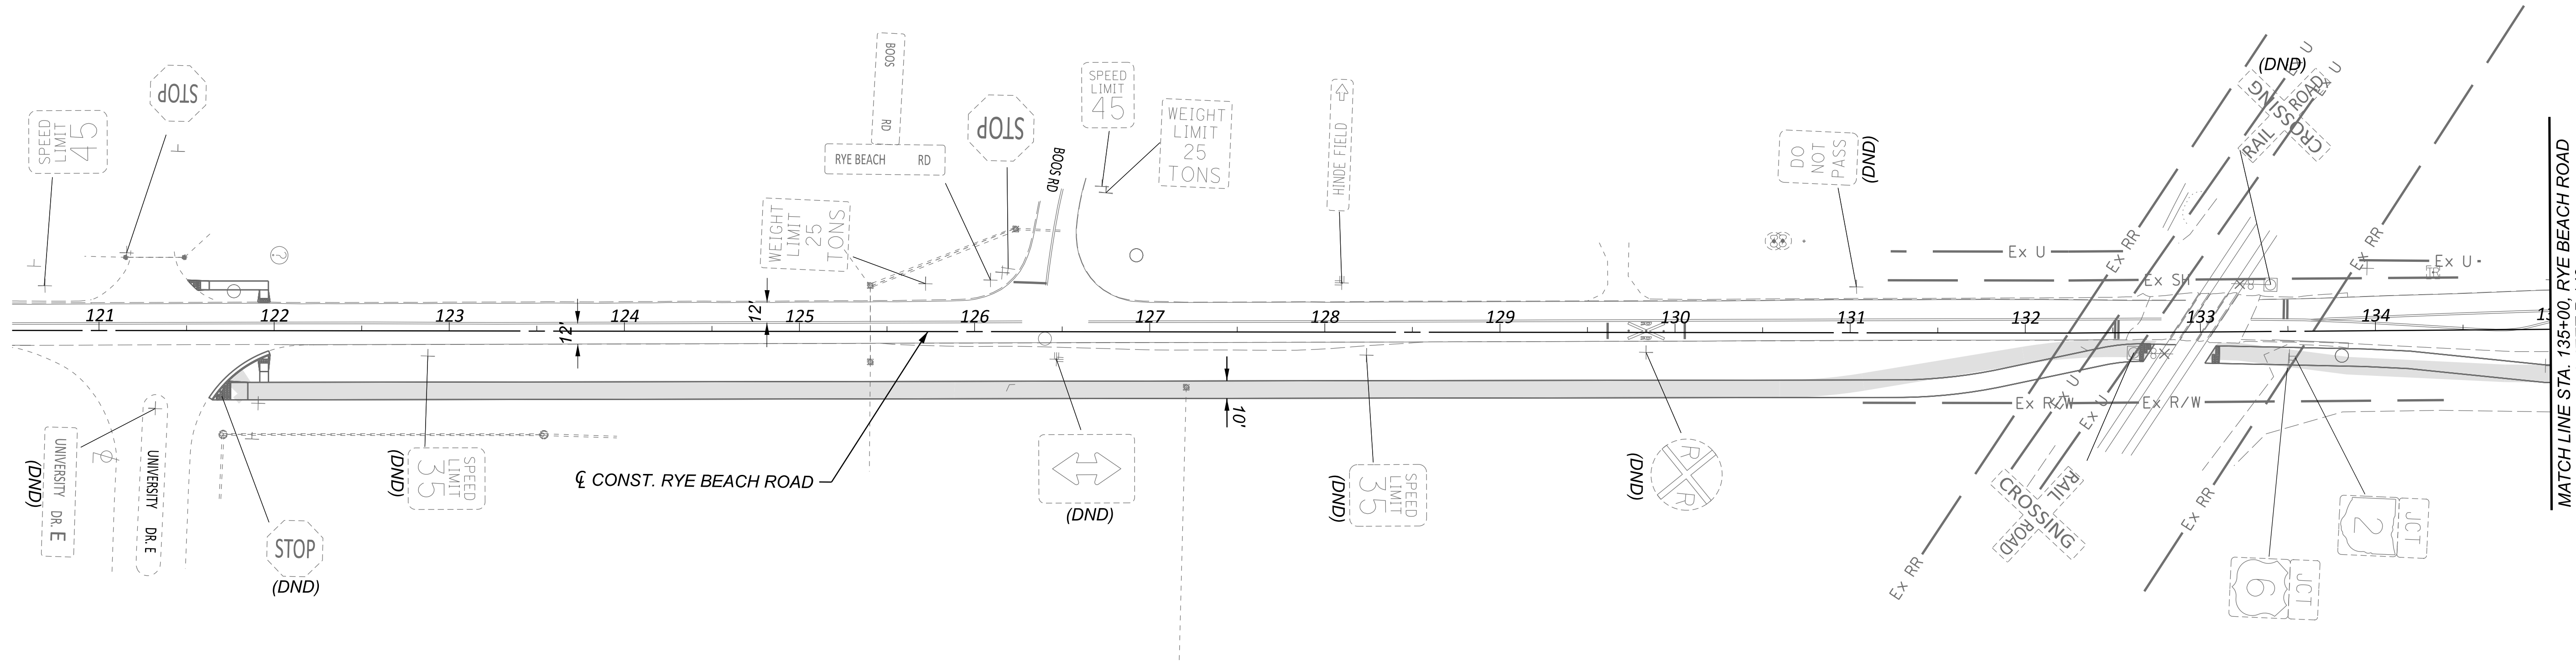


- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.151	782

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
RYE BEACH ROAD - BEGIN PROJECT TO STA. 135+00.00




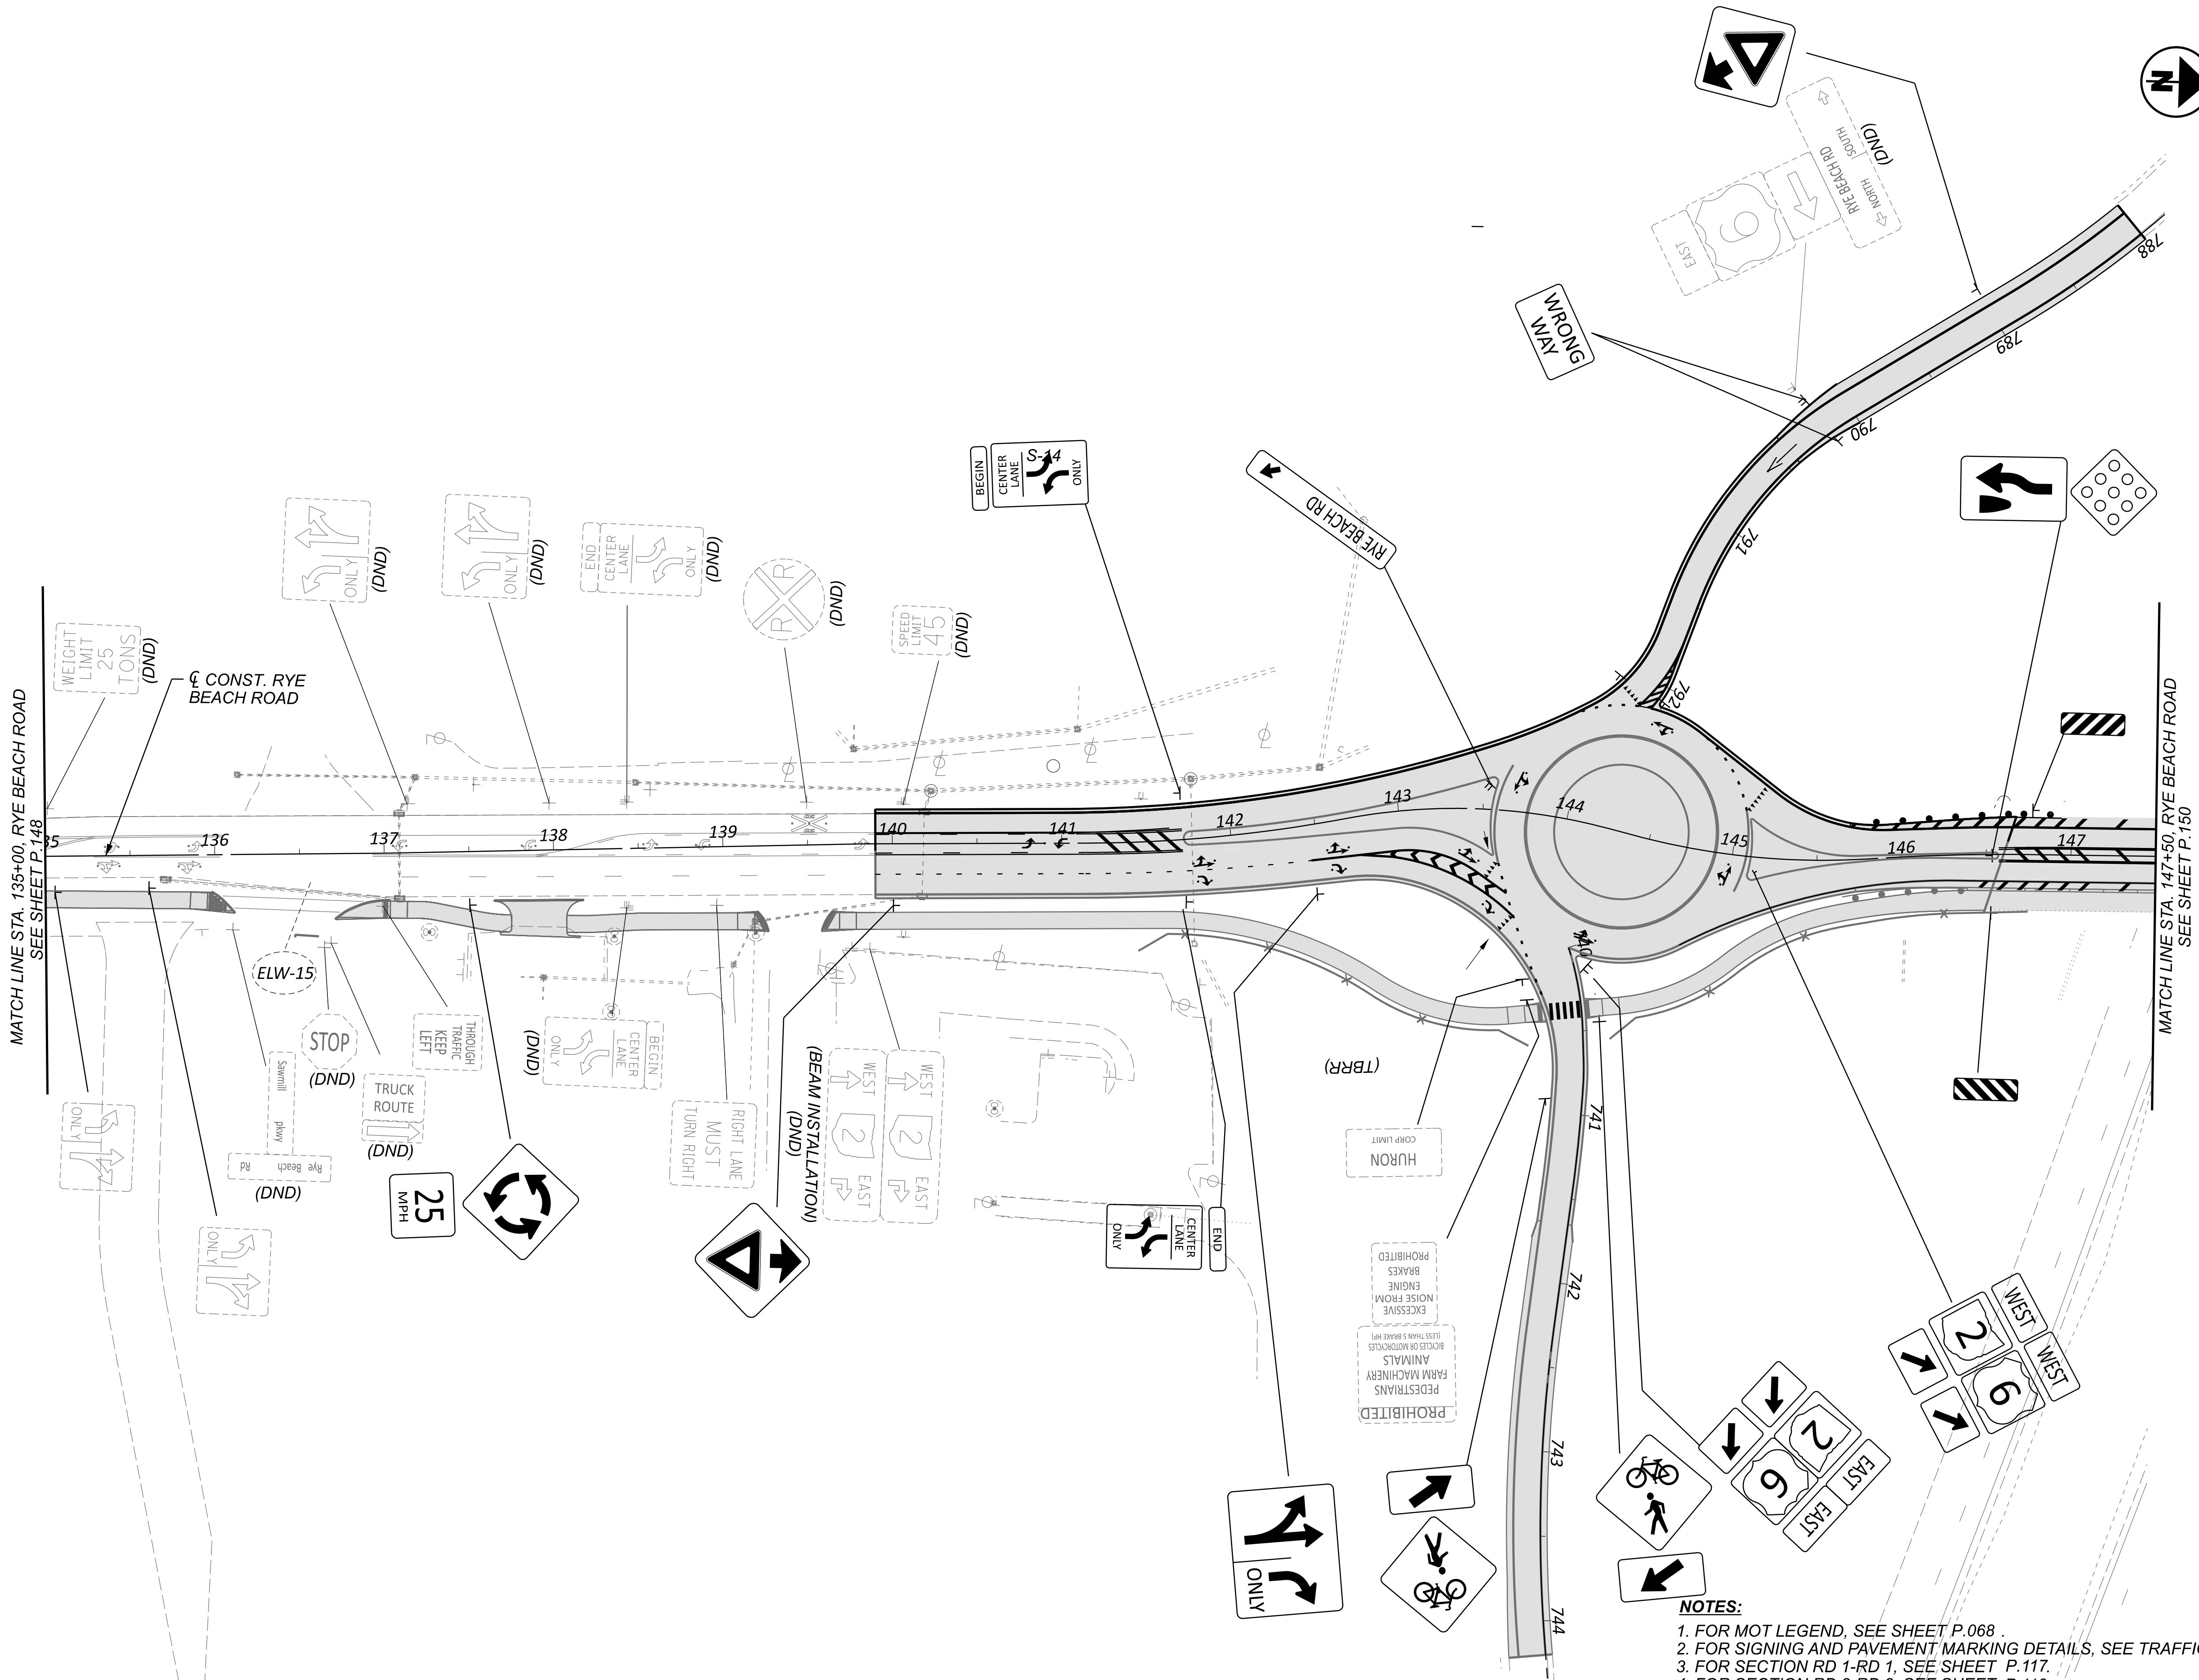


- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068 .
 - 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. FOR SECTION RD 1-RD 1, SEE SHEET P.117.
 - 4. FOR SECTION RD 2-RD 2, SEE SHEET P.118.
 - 5. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
RYE BEACH ROAD - STA. 135+00.00 TO STA. 147+50.00

TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.152	782



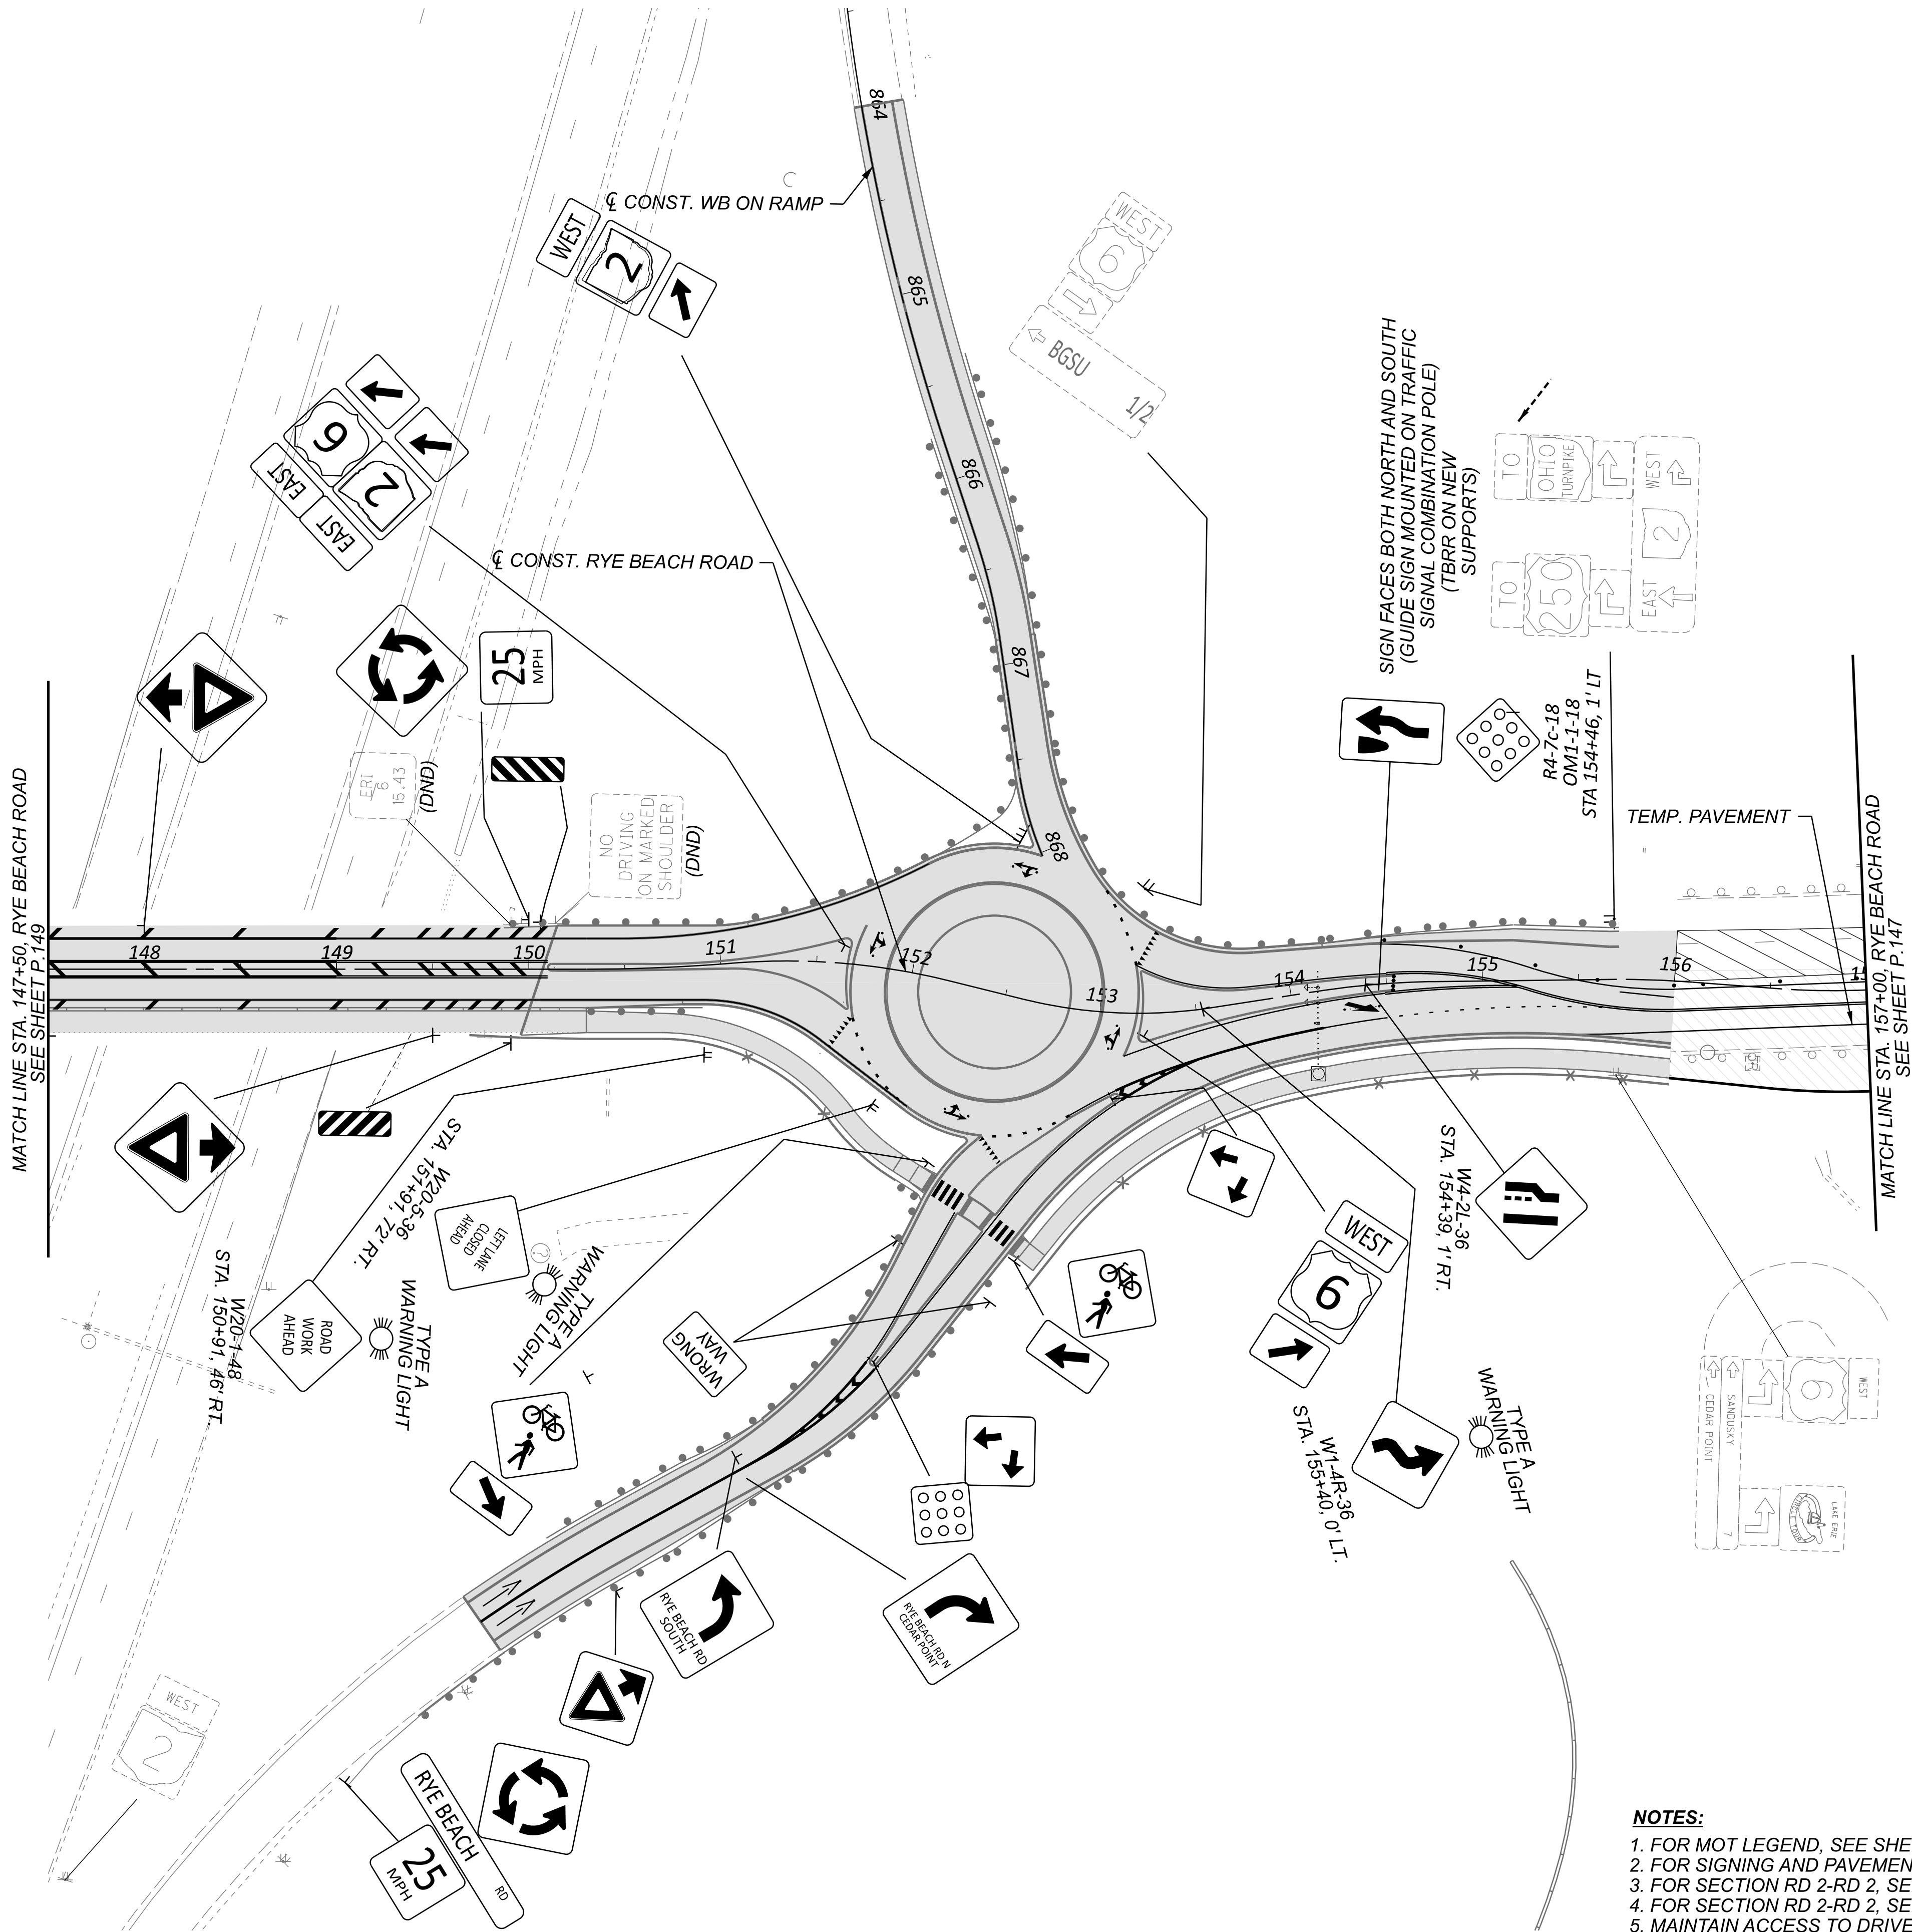

20

TYPE B FLASHING
(YELLOW)
WARNING LIGHT

ROAD
CLOSED

R11-2-48
(PER SCD MT-98.30)

21

R3-1-48
STA. 153+75, LT.
(PER SCD MT-98.30)

22

TYPE A
WARNING LIGHT

RAMP
CLOSED

E5-H2e-48
STA. 155+00, LT.
(PER SCD MT-98.30)

23

TYPE A
WARNING LIGHT

RAMP
CLOSED
AHEAD

E5-H2f-48
STA. 151+40, RT. &
STA. 156+00, LT.
(PER MT-98.30)

24

R3-2-48
STA. 152+50, RT.
(PER SCD MT-98.30)

25

TYPE A
WARNING LIGHT

ROAD
WORK
AHEAD

W20-1-48
(PER SCD MT-98.30)
STA. 157+00, LT.

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. FOR SECTION RD 2-RD 2, SEE SHEET P.119.
4. FOR SECTION RD 2-RD 2, SEE SHEET P.120.
5. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2027/2028 CONSTRUCTION)
RYE BEACH ROAD - STA. 147+50.00 TO STA. 157+00.00

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONVILLE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.153	TOTAL 782

HORIZONTAL
SCALE IN FEET
