

Holloway, Andrew

From: LAUDERMILK II, HOWARD <HL1596@att.com>
Sent: Tuesday, September 12, 2023 12:30 PM
To: Holloway, Andrew; ECKLEY, SCOTT D; Boring, Tammy; Brown, Lawrence; Bryant, Troy
Cc: Opsitnik, Andrew; Amnah, Zachary; STANFIELD, SHAYNE W
Subject: RE: ODOT SR-435 Telecom Conflict

Andrew,

Thanks so much for the phone call, just wanted to follow up so that Scott is on the same page.

Scott, Andrew said most likely the conduit and man hole structures are not going to be in conflict, (not including a future lid adjustment to grade).

The fibers just east and north of Bluegrass will need to be relocated. Andrew should have final plans with cross sections January/February time frame. We should be able to get a project and prints for AT&T construction to start by 4/1.

The east fiber may not be reimbursed, but we will have Shayne Stanfield follow up.

Scott if you want to open a project and get a preliminary plan together, we can get Andrew a print of what we think might work for us.

Andrew, thanks again for all of your coordination efforts on this project, it is much appreciated!

Howard Lauder milk II

The Ohio Bell Telephone Company

Telecommunications Spec (Eng)

Office: (937)296-3588

Cell: (937)286-7218

HL1596@att.com

7201 Far Hills Ave.

Dayton Ohio

45459

From: Andrew.Holloway@dot.ohio.gov <Andrew.Holloway@dot.ohio.gov>
Sent: Tuesday, September 12, 2023 8:37 AM
To: LAUDERMILK II, HOWARD <HL1596@att.com>; ECKLEY, SCOTT D <SE1236@att.com>; Tammy.Boring@dot.ohio.gov; Lawrence.Brown@dot.ohio.gov; Troy.Bryant@dot.ohio.gov
Cc: Andrew.Opsitnik@dot.ohio.gov; Zachary.Amnah@dot.ohio.gov
Subject: RE: ODOT SR-435 Telecom Conflict
Importance: High

Howard,

ODOT is working towards purchasing frontage from that property owner, so AT&T can relocate the box/line running north within the proposed R/W (once acquired) or outside of the R/W if there is some agreement between AT&T and the property owner. I am not sure how reimbursement works for that, but I have included our R/W team on this email to advise. Our R/W team will also advise on how we're going to proceed with reimbursement for the line running east within the easement.

We'll have cross sections by early next year to share, but AT&T should plan to relocate the line running east to along the prop. R/W and outside of the construction limits shown on the attached R/W plan. It would be understandable if AT&T wants to wait until ODOT has final construction plans/cross sections to finalize their relocation design. ODOT sells the design-build contract at the end of September, and the awarded design-build team will develop detailed plans &

continue/finalize relocation coordination with AT&T. ODOT will keep AT&T in the loop as the plans are being developed. We just need AT&T to commit to being ready to begin relocation construction as soon as the R/W has been acquired (4/1/24), so that construction of the roundabout at SR-435/Bluegrass/SR-729 can proceed accordingly. How much time does AT&T need for design/pre-construction activities – if ODOT provided final plans by 2/1/24, would 2 months be enough time (permit would be expedited/reviewed immediately by ODOT) for AT&T to begin work the first week of April?

I found the permits for both facilities, but if AT&T has as-builts – that would be helpful.

Citrix Attachments

117955_RW_20230608_22x34.pdf

21.9 MB

[Download Attachments](#)

Andrew Holloway uses Citrix Files to share documents securely.

Andrew Holloway

Transportation Engineer

ODOT District 6, Planning and Engineering
400 East William Street, Delaware, Ohio 43015
740.833.8107

transportation.ohio.gov



OHIO DEPARTMENT OF
TRANSPORTATION

From: LAUDERMILK II, HOWARD <HL1596@att.com>

Sent: Tuesday, September 12, 2023 7:43 AM

To: Holloway, Andrew <Andrew.Holloway@dot.ohio.gov>; ECKLEY, SCOTT D <SE1236@att.com>

Cc: Opsitnik, Andrew <Andrew.Opsitnik@dot.ohio.gov>; Amnah, Zachary <Zachary.Amnah@dot.ohio.gov>

Subject: RE: ODOT SR-435 Telecom Conflict

Andrew,

Sounds good. We do have a couple questions.

The fiber that runs north out of our box is customer owned conduit, on existing private property. So I'm not sure how reimbursement/relocation works on that.

Also the fiber running east is in an easement, do we start the reimbursement process now for that?

The other important part is knowing where and how to relocate. With out cross sections we have no idea if we are placing back in conflict.

Scott can you please provide anything we have on these fibers? I know the fiber running east was just placed with in the last two months.

Thanks again Andrew we really appreciate you!

Howard Lauder milk II

The Ohio Bell Telephone Company
Telecommunications Spec (Eng)
Office: (937)296-3588
Cell: (937)286-7218
HL1596@att.com
7201 Far Hills Ave.
Dayton Ohio
45459

From: Andrew.Holloway@dot.ohio.gov <Andrew.Holloway@dot.ohio.gov>
Sent: Monday, September 11, 2023 9:19 AM
To: LAUDERMILK II, HOWARD <HL1596@att.com>; ECKLEY, SCOTT D <SE1236@att.com>
Cc: Andrew.Opsitnik@dot.ohio.gov; Zachary.Amnah@dot.ohio.gov
Subject: RE: ODOT SR-435 Telecom Conflict
Importance: High

Thank you for the information Howard; I think we can avoid/minimize relocation of the duct bank along SR-435. But, the box east of Bluegrass will need to be relocated outside of the construction limits along with a segment of the fibers running north & east; see attached plan sheet. The fiber running east will need to be relocated from the box at roughly 111+25 to 114+50 as the foreslope & ditch will be lowered and the line will be uncovered assuming it is a standard 4' depth. The fiber running north will need to be relocated from existing to proposed box.

ODOT will have the r/w acquired by 4/1/24. Please begin re-design efforts so that your relocation crew is prepared to begin work promptly next April.

If you or Scott are able to provide as-builts for the fibers running north & east, that would be helpful.

Andrew Holloway

Transportation Engineer
ODOT District 6, Planning and Engineering
400 East William Street, Delaware, Ohio 43015
740.833.8107
transportation.ohio.gov



From: LAUDERMILK II, HOWARD <HL1596@att.com>
Sent: Thursday, September 7, 2023 10:05 AM
To: Holloway, Andrew <Andrew.Holloway@dot.ohio.gov>; ECKLEY, SCOTT D <SE1236@att.com>
Cc: Opsitnik, Andrew <Andrew.Opsitnik@dot.ohio.gov>; Amnah, Zachary <Zachary.Amnah@dot.ohio.gov>
Subject: RE: ODOT SR-435 Telecom Conflict

Good Morning Andrew,

I wanted to hopefully shed some light on cost and timeline for us. I'm not sure if Scott may have mentioned already that this is a major conduit structure, which contains a vital backbone of our infrastructure. In this we have multiple manholes along with the 12 conduits, a large trunk fiber, large copper feed as well as a large copper distribution line. We are anticipating a 1-2 year timeline at several hundred thousand dollars. That is just in this small portion of the project. I don't want to just throw this out there with out some explanation.

There are several reasons behind the timeline for this. First is the material, to order the new Man holes and copper has been challenging for us, as there has been a shortage industry wide. The other obstacles would be splicing man hours for the copper and scheduling down time for the trunk fiber. We would not be able to take the whole fiber down at once, and given the size this takes longer than normal. Obviously everyone is moving away from copper, however we still are required to have access for folks in rural areas that don't have other options. So we would need to research downsizing availability which also takes time.

I hope this helps give a better understanding of cost/timeline. I really hope that given this information you will be able to work around this structure.

It appears that the main duct structure turns down OH-729 and doesn't continue east on old 35. I believe the box you see east of blue grass feeds north and east direct buried. I think Scott may have some as build information on the new fiber placed east of that box if needed.

Thanks for your time!

Howard Lauder milk II

The Ohio Bell Telephone Company

Telecommunications Spec (Eng)

Office: (937)296-3588

Cell: (937)286-7218

HL1596@att.com

7201 Far Hills Ave.

Dayton Ohio

45459

From: Andrew.Holloway@dot.ohio.gov <Andrew.Holloway@dot.ohio.gov>

Sent: Wednesday, September 6, 2023 3:15 PM

To: ECKLEY, SCOTT D <SE1236@att.com>; LAUDERMILK II, HOWARD <HL1596@att.com>

Cc: Andrew.Opsitnik@dot.ohio.gov; Zachary.Amnah@dot.ohio.gov

Subject: RE: ODOT SR-435 Telecom Conflict

Importance: High

Scott/Howard,

Please see the request below. Additionally, could you provide information on AT&T facilities east of the SR-435/Bluegrass/SR-729 intersection from the intersection to the bridge over "Missouri Ditch". The plan Scott sent shows the duct bank ending at this intersection, but our survey picked up a pedestal/box east of the intersection (see attached image).



Andrew Holloway

Transportation Engineer

ODOT District 6, Planning and Engineering
400 East William Street, Delaware, Ohio 43015
740.833.8107

transportation.ohio.gov



From: Holloway, Andrew


Sent: Wednesday, September 6, 2023 1:20 PM

To: ECKLEY, SCOTT D <SE1236@att.com>

Cc: Opsitnik, Andrew <Andrew.Opsitnik@dot.ohio.gov>; Amnah, Zachary <Zachary.Amnah@dot.ohio.gov>

Subject: RE: ODOT SR-435 Telecom Conflict

Thanks Scott. Do you have a rough estimation on a relocation schedule for this duct bank? ODOT hopes to avoid it, and I know we have discussed in the past that it would be timely. But, once provided notice that relocation is required – how long would re-design and construction take to relocate the duct bank along SR-435 from Davidson Sollars Rd NW to SR-729.

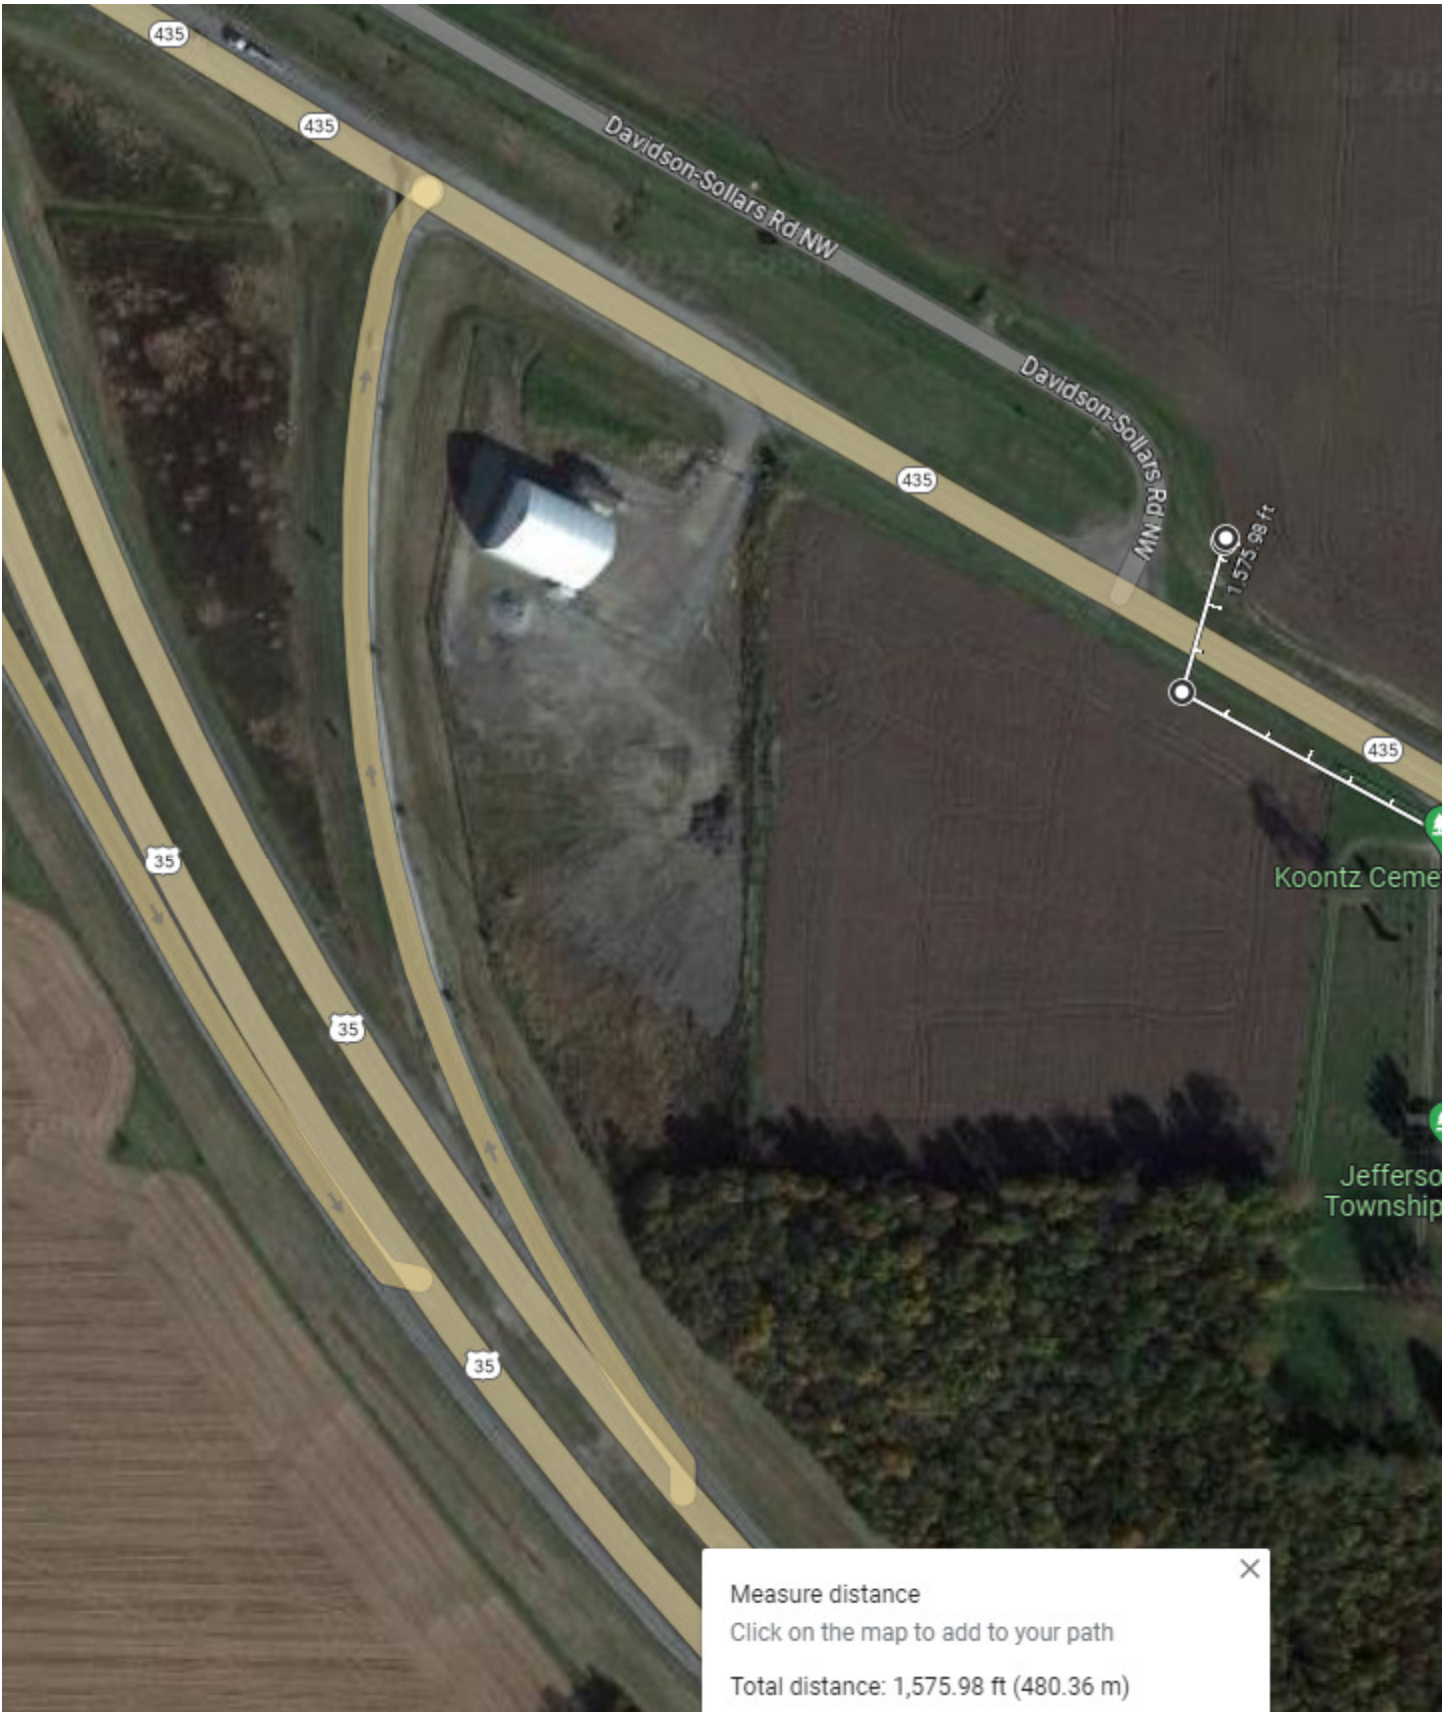

Thanks,
Andrew Holloway
Transportation Engineer
ODOT District 6, Planning and Engineering
400 East William Street, Delaware, Ohio 43015

740.833.8107

transportation.ohio.gov



From: ECKLEY, SCOTT D <SE1236@att.com>
Sent: Tuesday, August 29, 2023 2:49 PM
To: Holloway, Andrew <Andrew.Holloway@dot.ohio.gov>
Subject: ODOT SR-435 Telecom Conflict

Hello Andrew,

Please find attached the remaining conduit plates concerning this area. Thanks

Scott Eckley
Telecommunications Specialist (Engineering)
se1236@us.att.com
Cell Phone +1 (937) 965-9839
7201 FAR HILLS AVE
CENTERVILLE, OH 45459

CAUTION: This is an external email and may not be safe. If the email looks suspicious, please do not click links or open attachments and forward the email to csc@ohio.gov or click the Phish Alert Button if available.
