


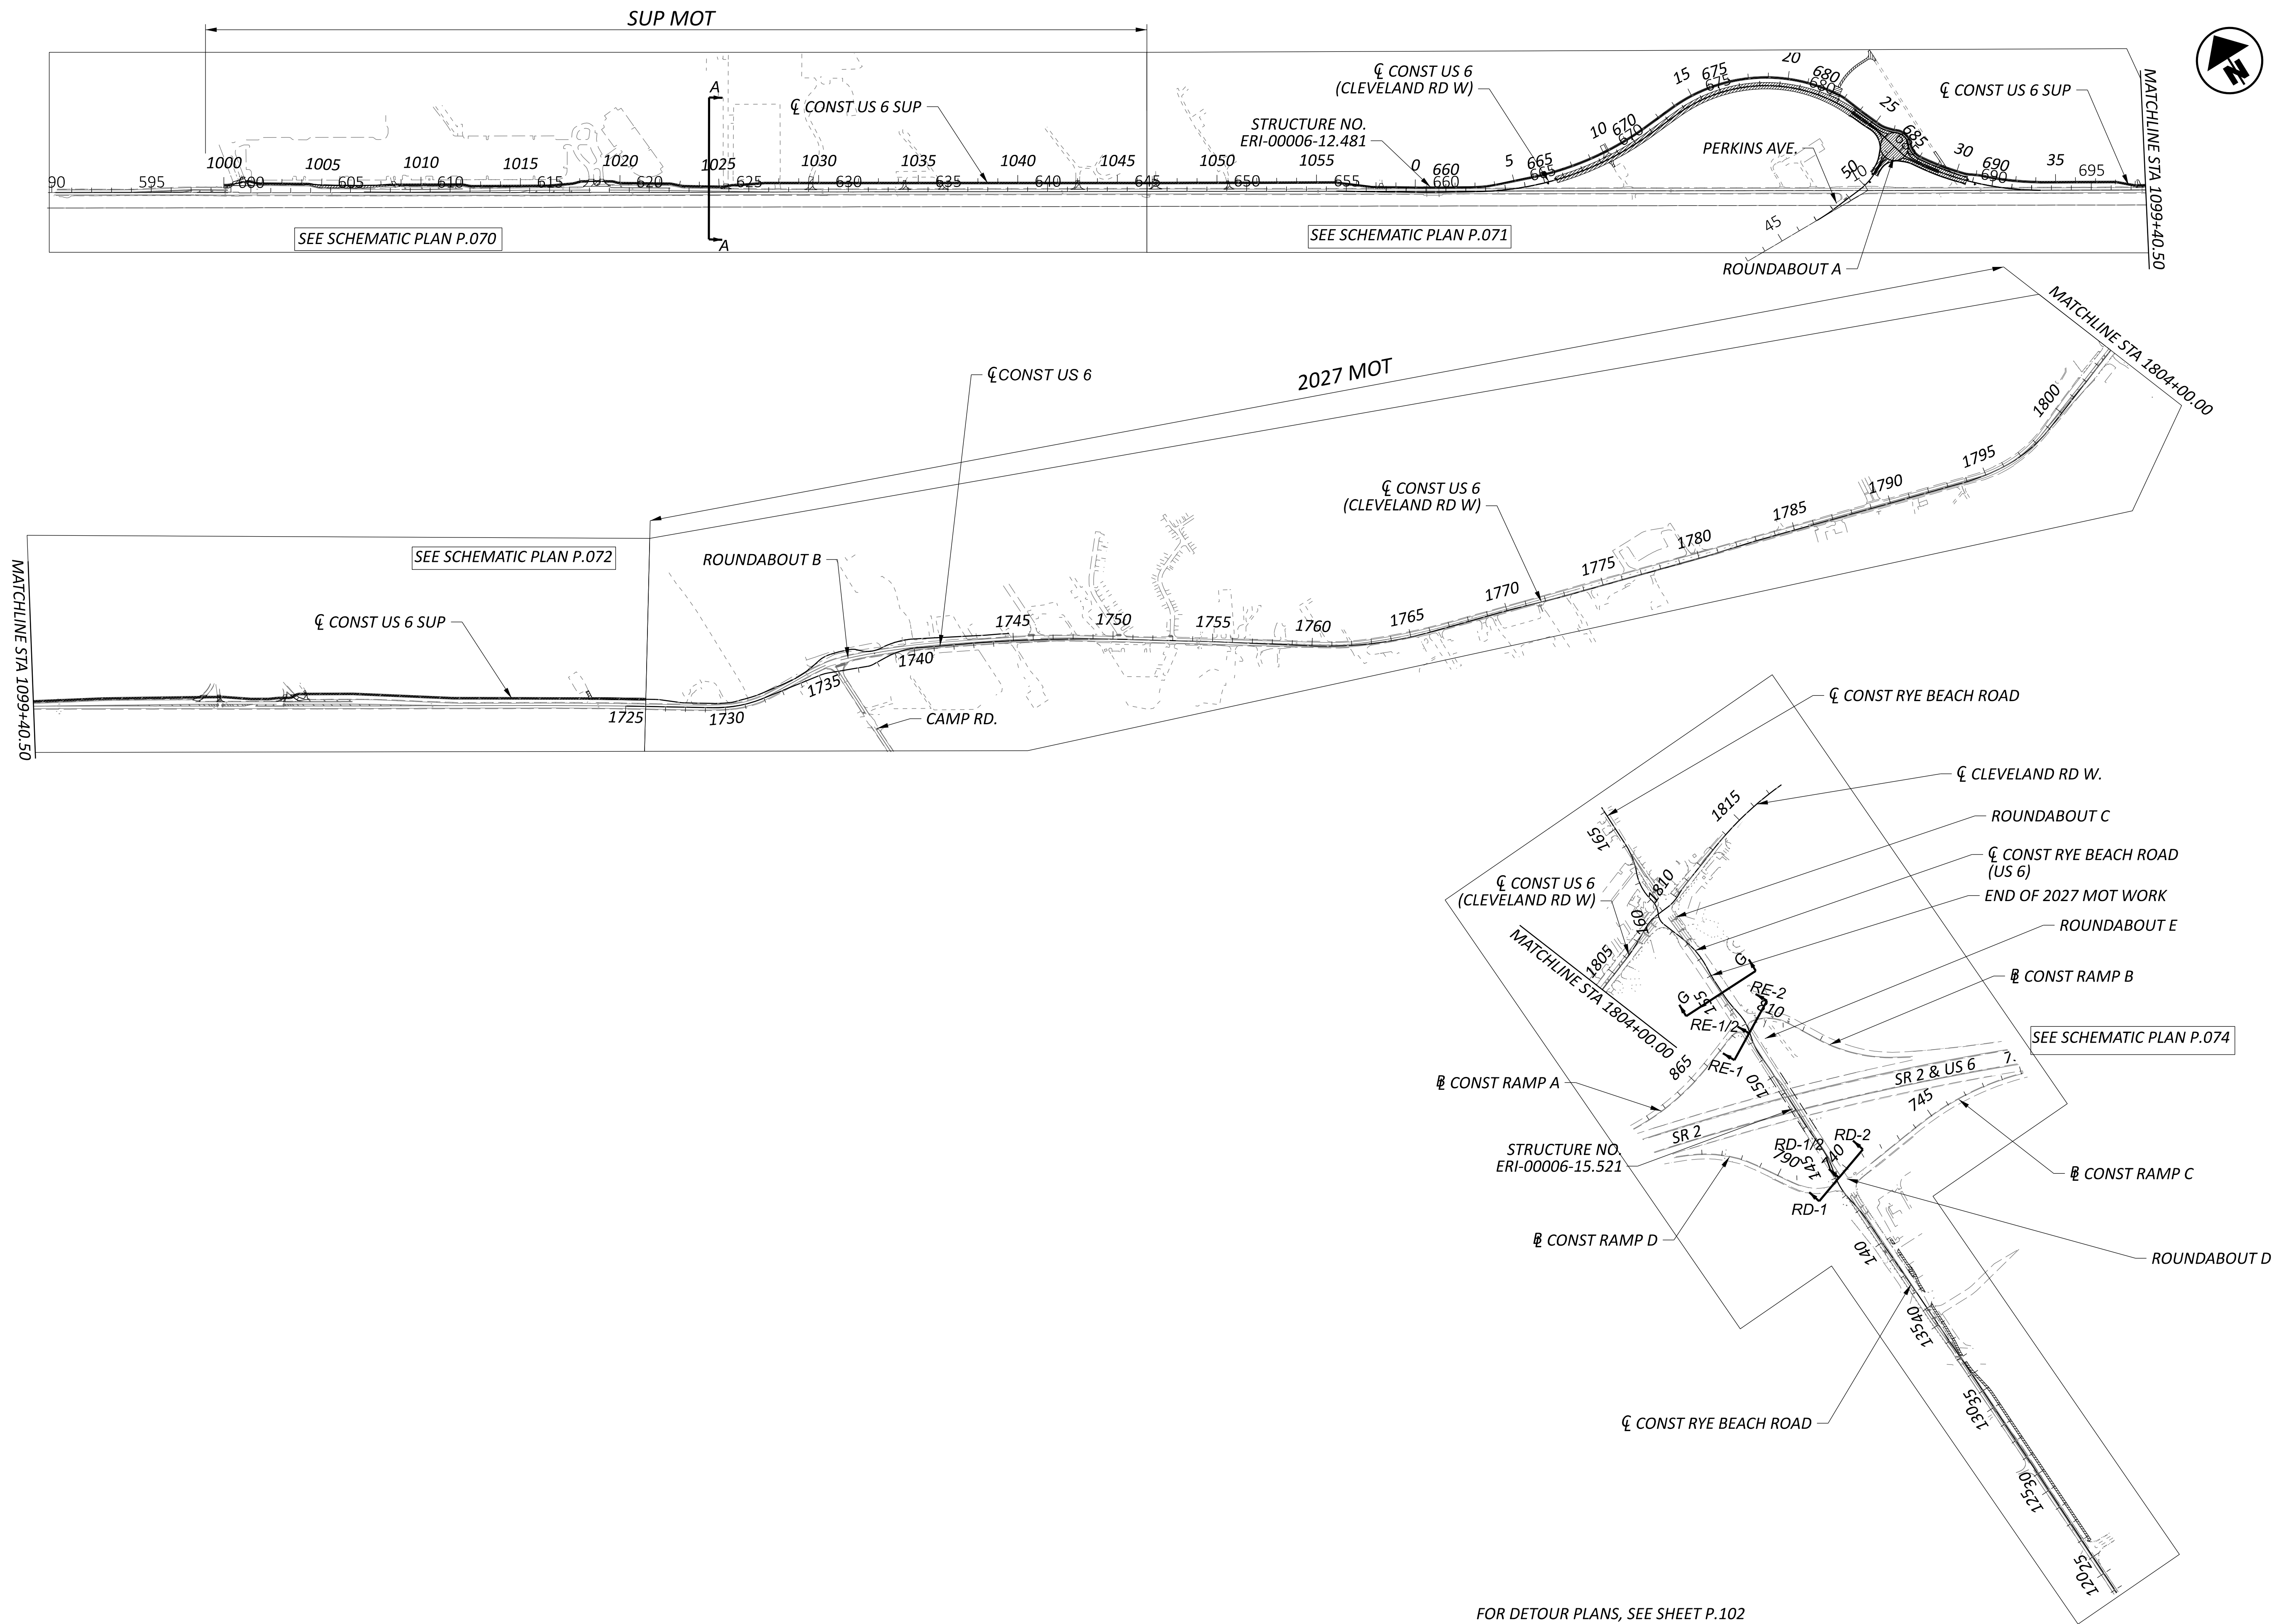

FOR DETOUR PLANS, SEE SHEET P.102

MOT OVERALL SCHEMATIC PLAN - PRE PHASE (2026 CONSTRUCTION)

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA


REVIEWER
SS

DATE
02/28/24

PROJECT ID
116570


SHEET
P.071

TOTAL
782

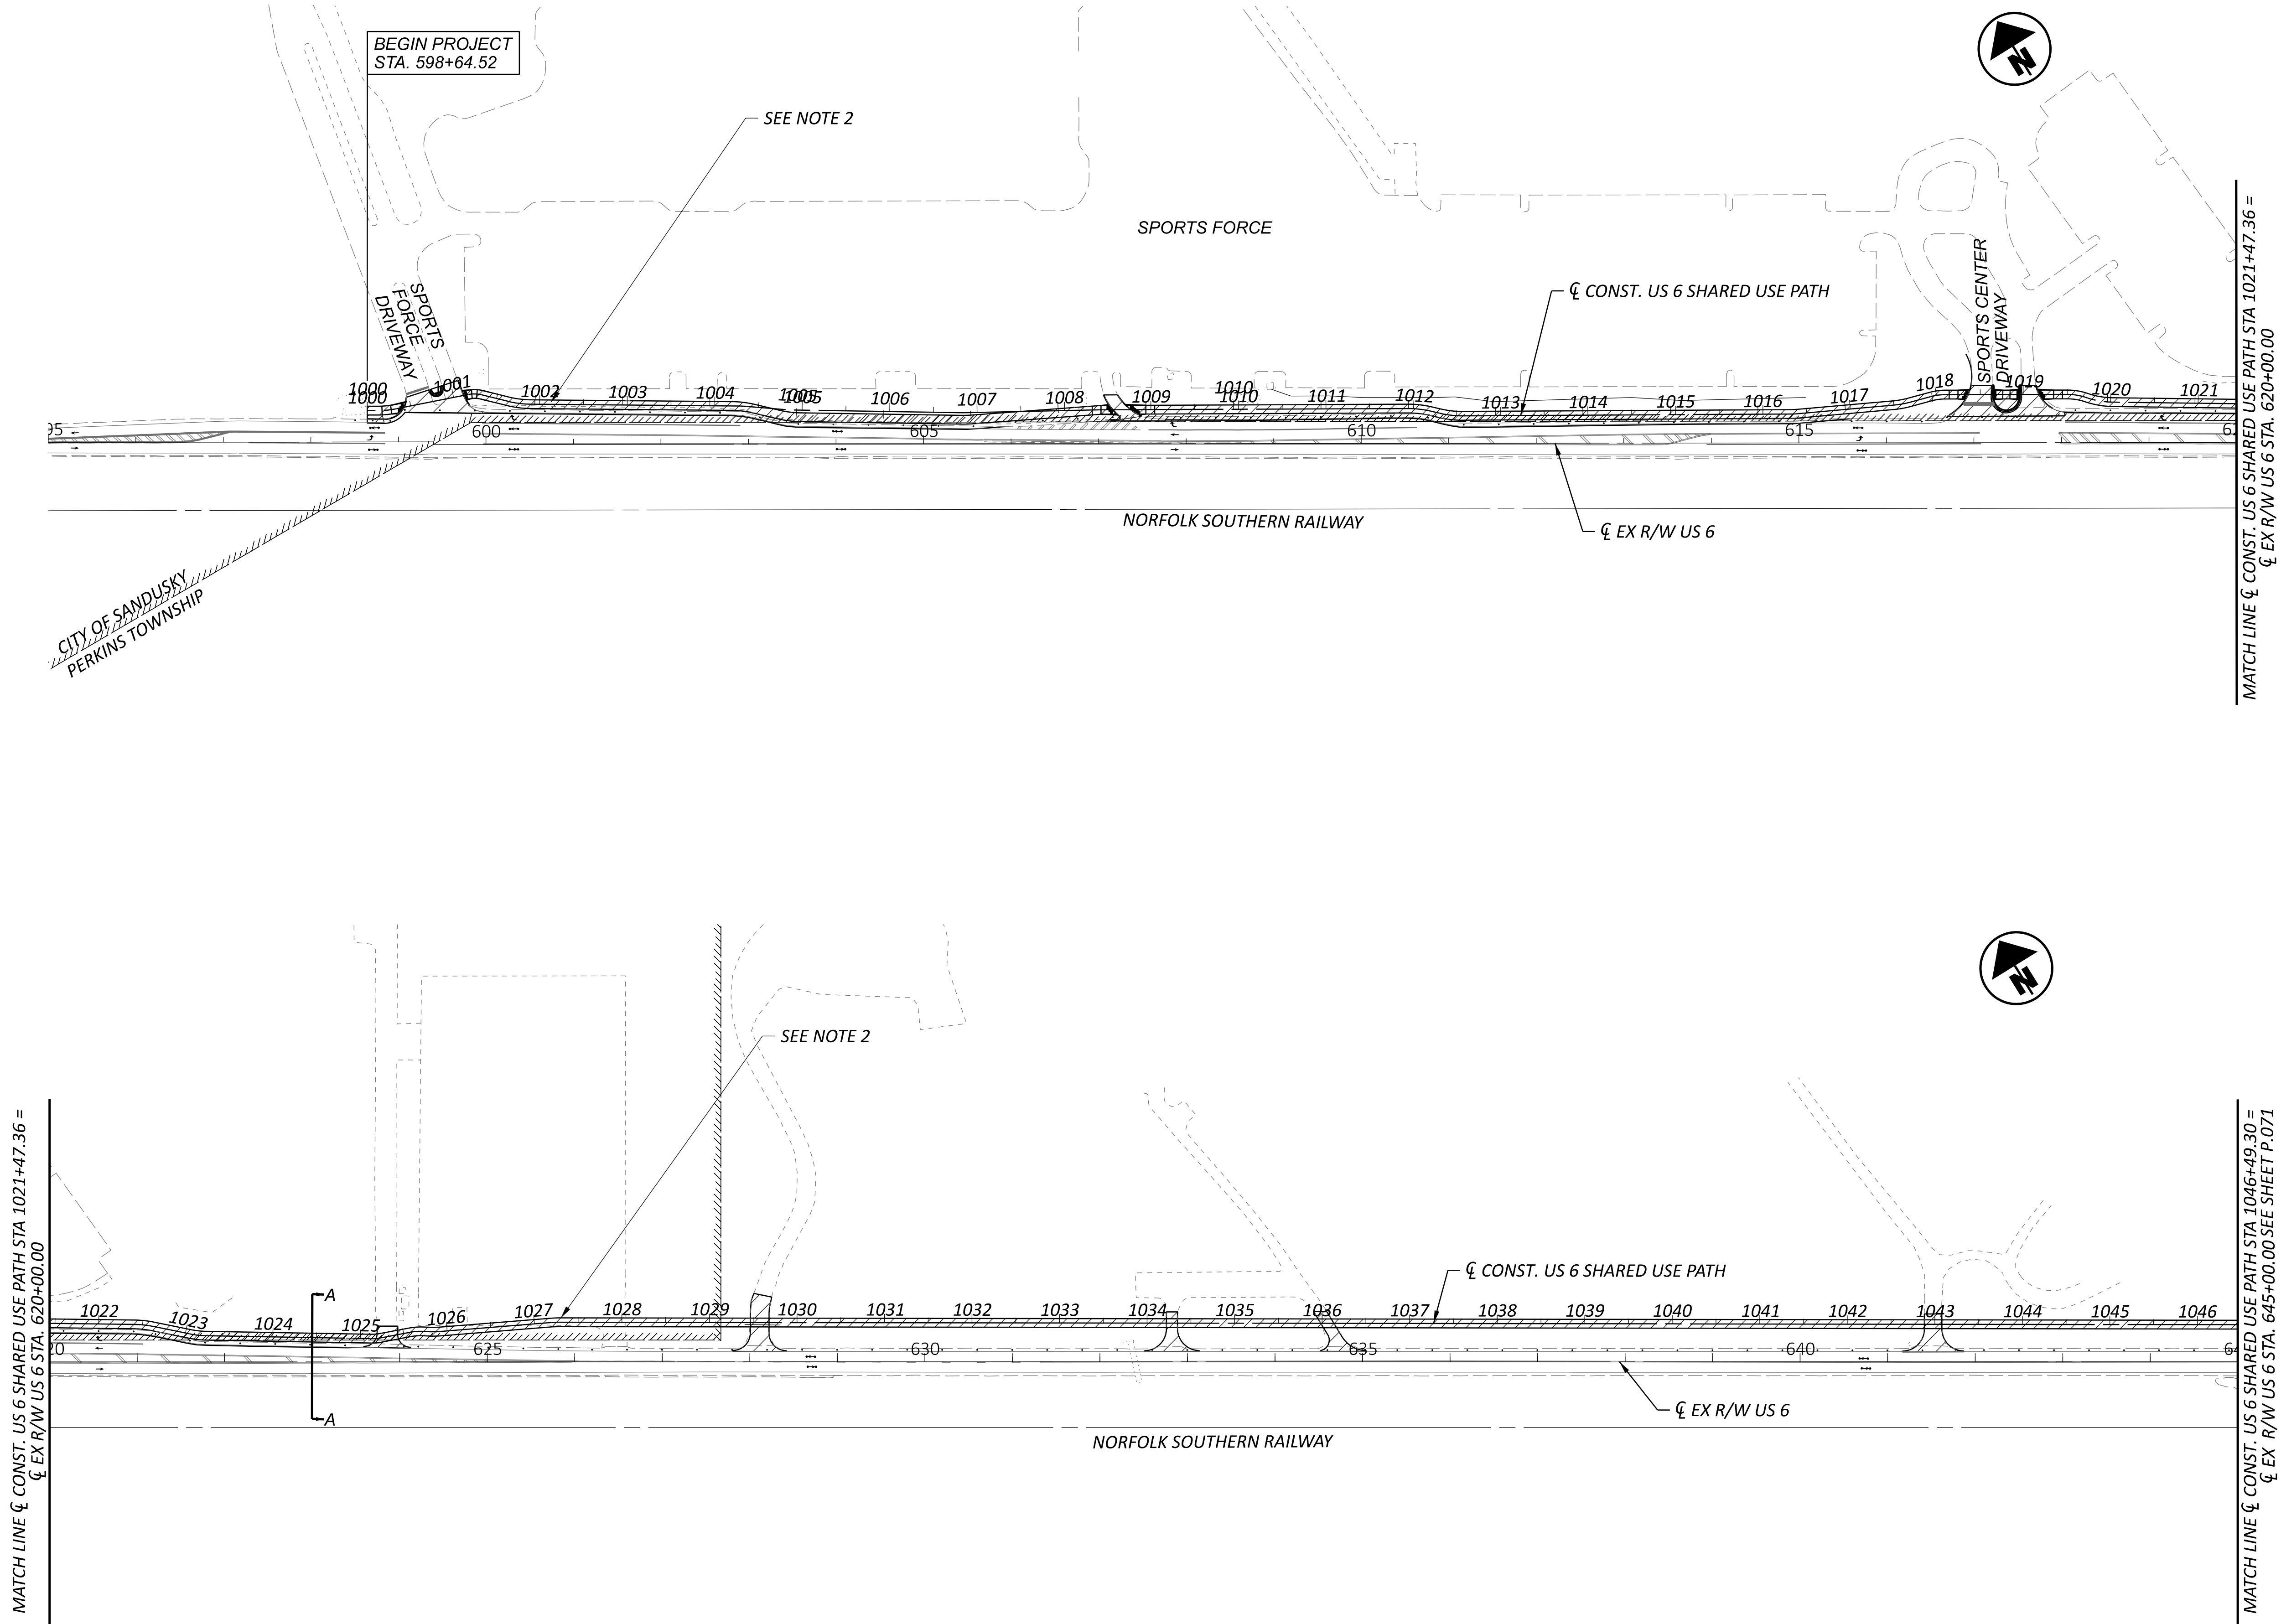


- NOTES:
- FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
 - SUP: USE FLAGGERS TO RESTRICT TRAFFIC TO ONE LANE WHERE NECESSARY TO CONSTRUCT THE RESURFACING AND MULTI-USE PATH OUTSIDE WIDENING AREAS AND PROPOSED ROUNDABOUTS. USE LEOS TO CONTROL TRAFFIC AT SIGNALIZED INTERSECTIONS WHEN NECESSARY. ASSUME SUP CONSTRUCTION DURATION OF 60 DAYS.

HORIZONTAL SCALE IN FEET 0 50 100 200	
MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION) US 6 BEGIN PROJECT TO STA 645+00	
DESIGN AGENCY TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.072	782

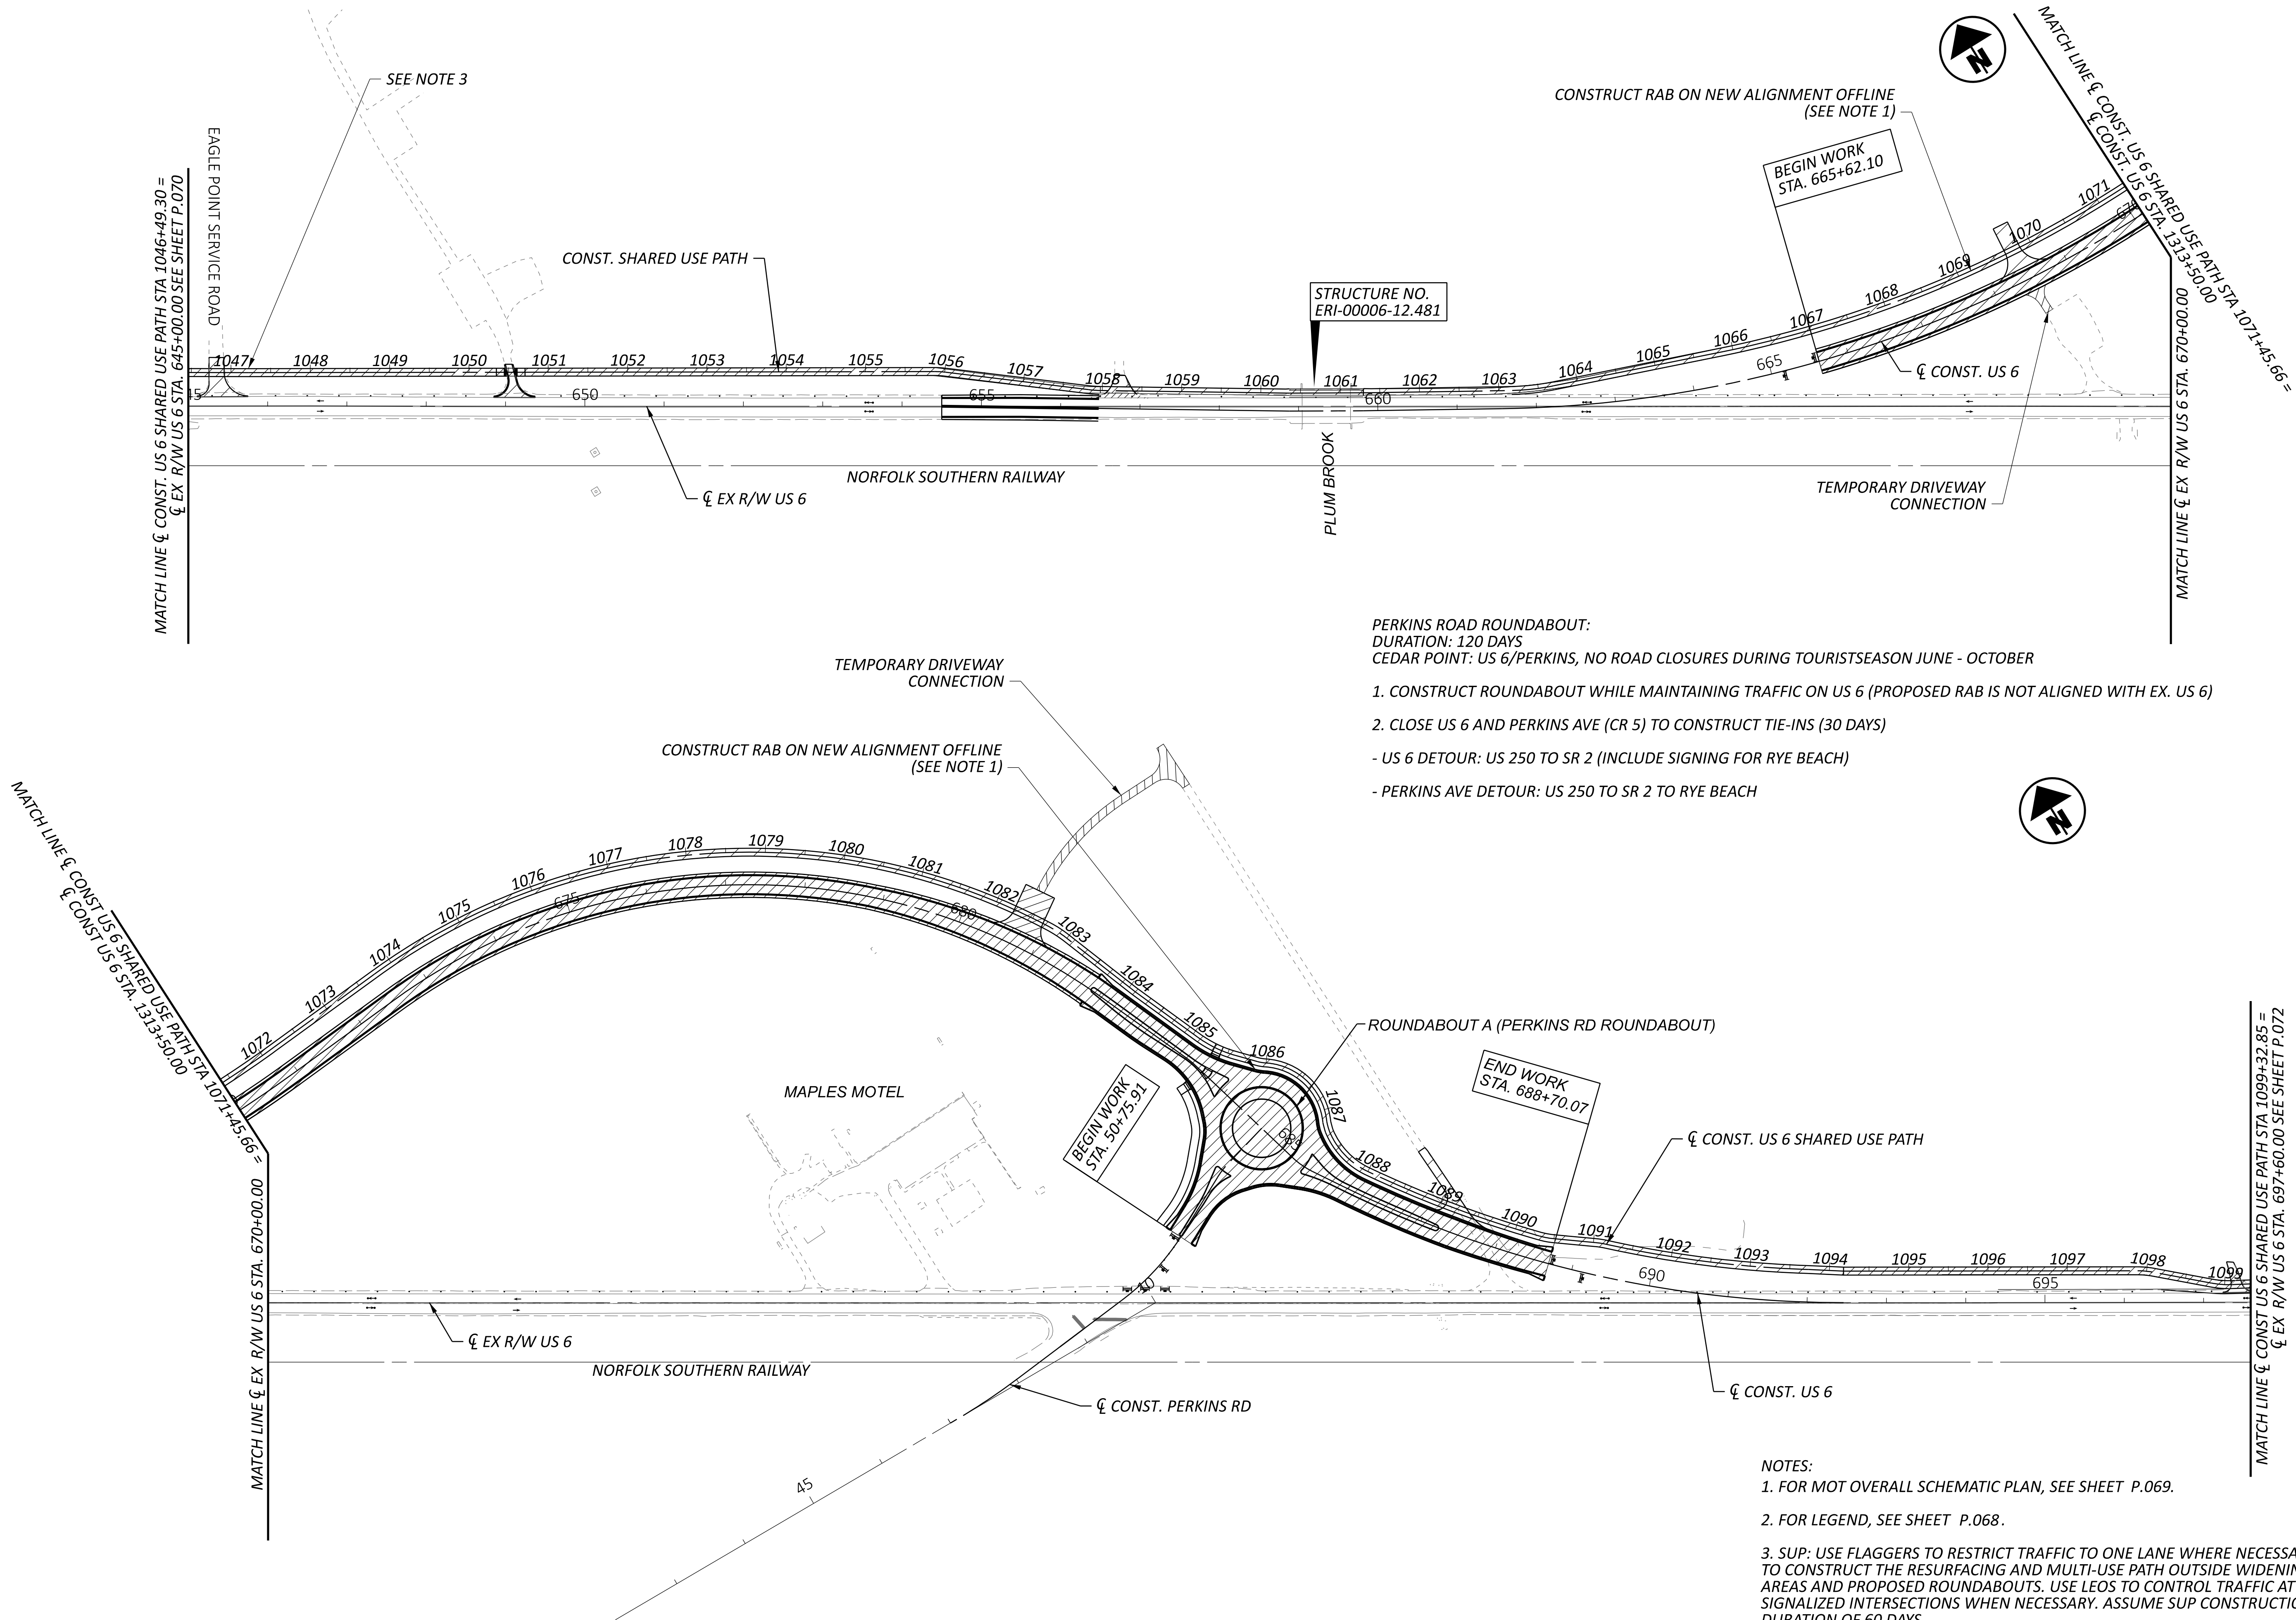

MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION)
US 6 STA 645+00 TO STA 695+00




DESIGN AGENCY
TRANSYSTEMS
400 W. WATSON BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.073 782

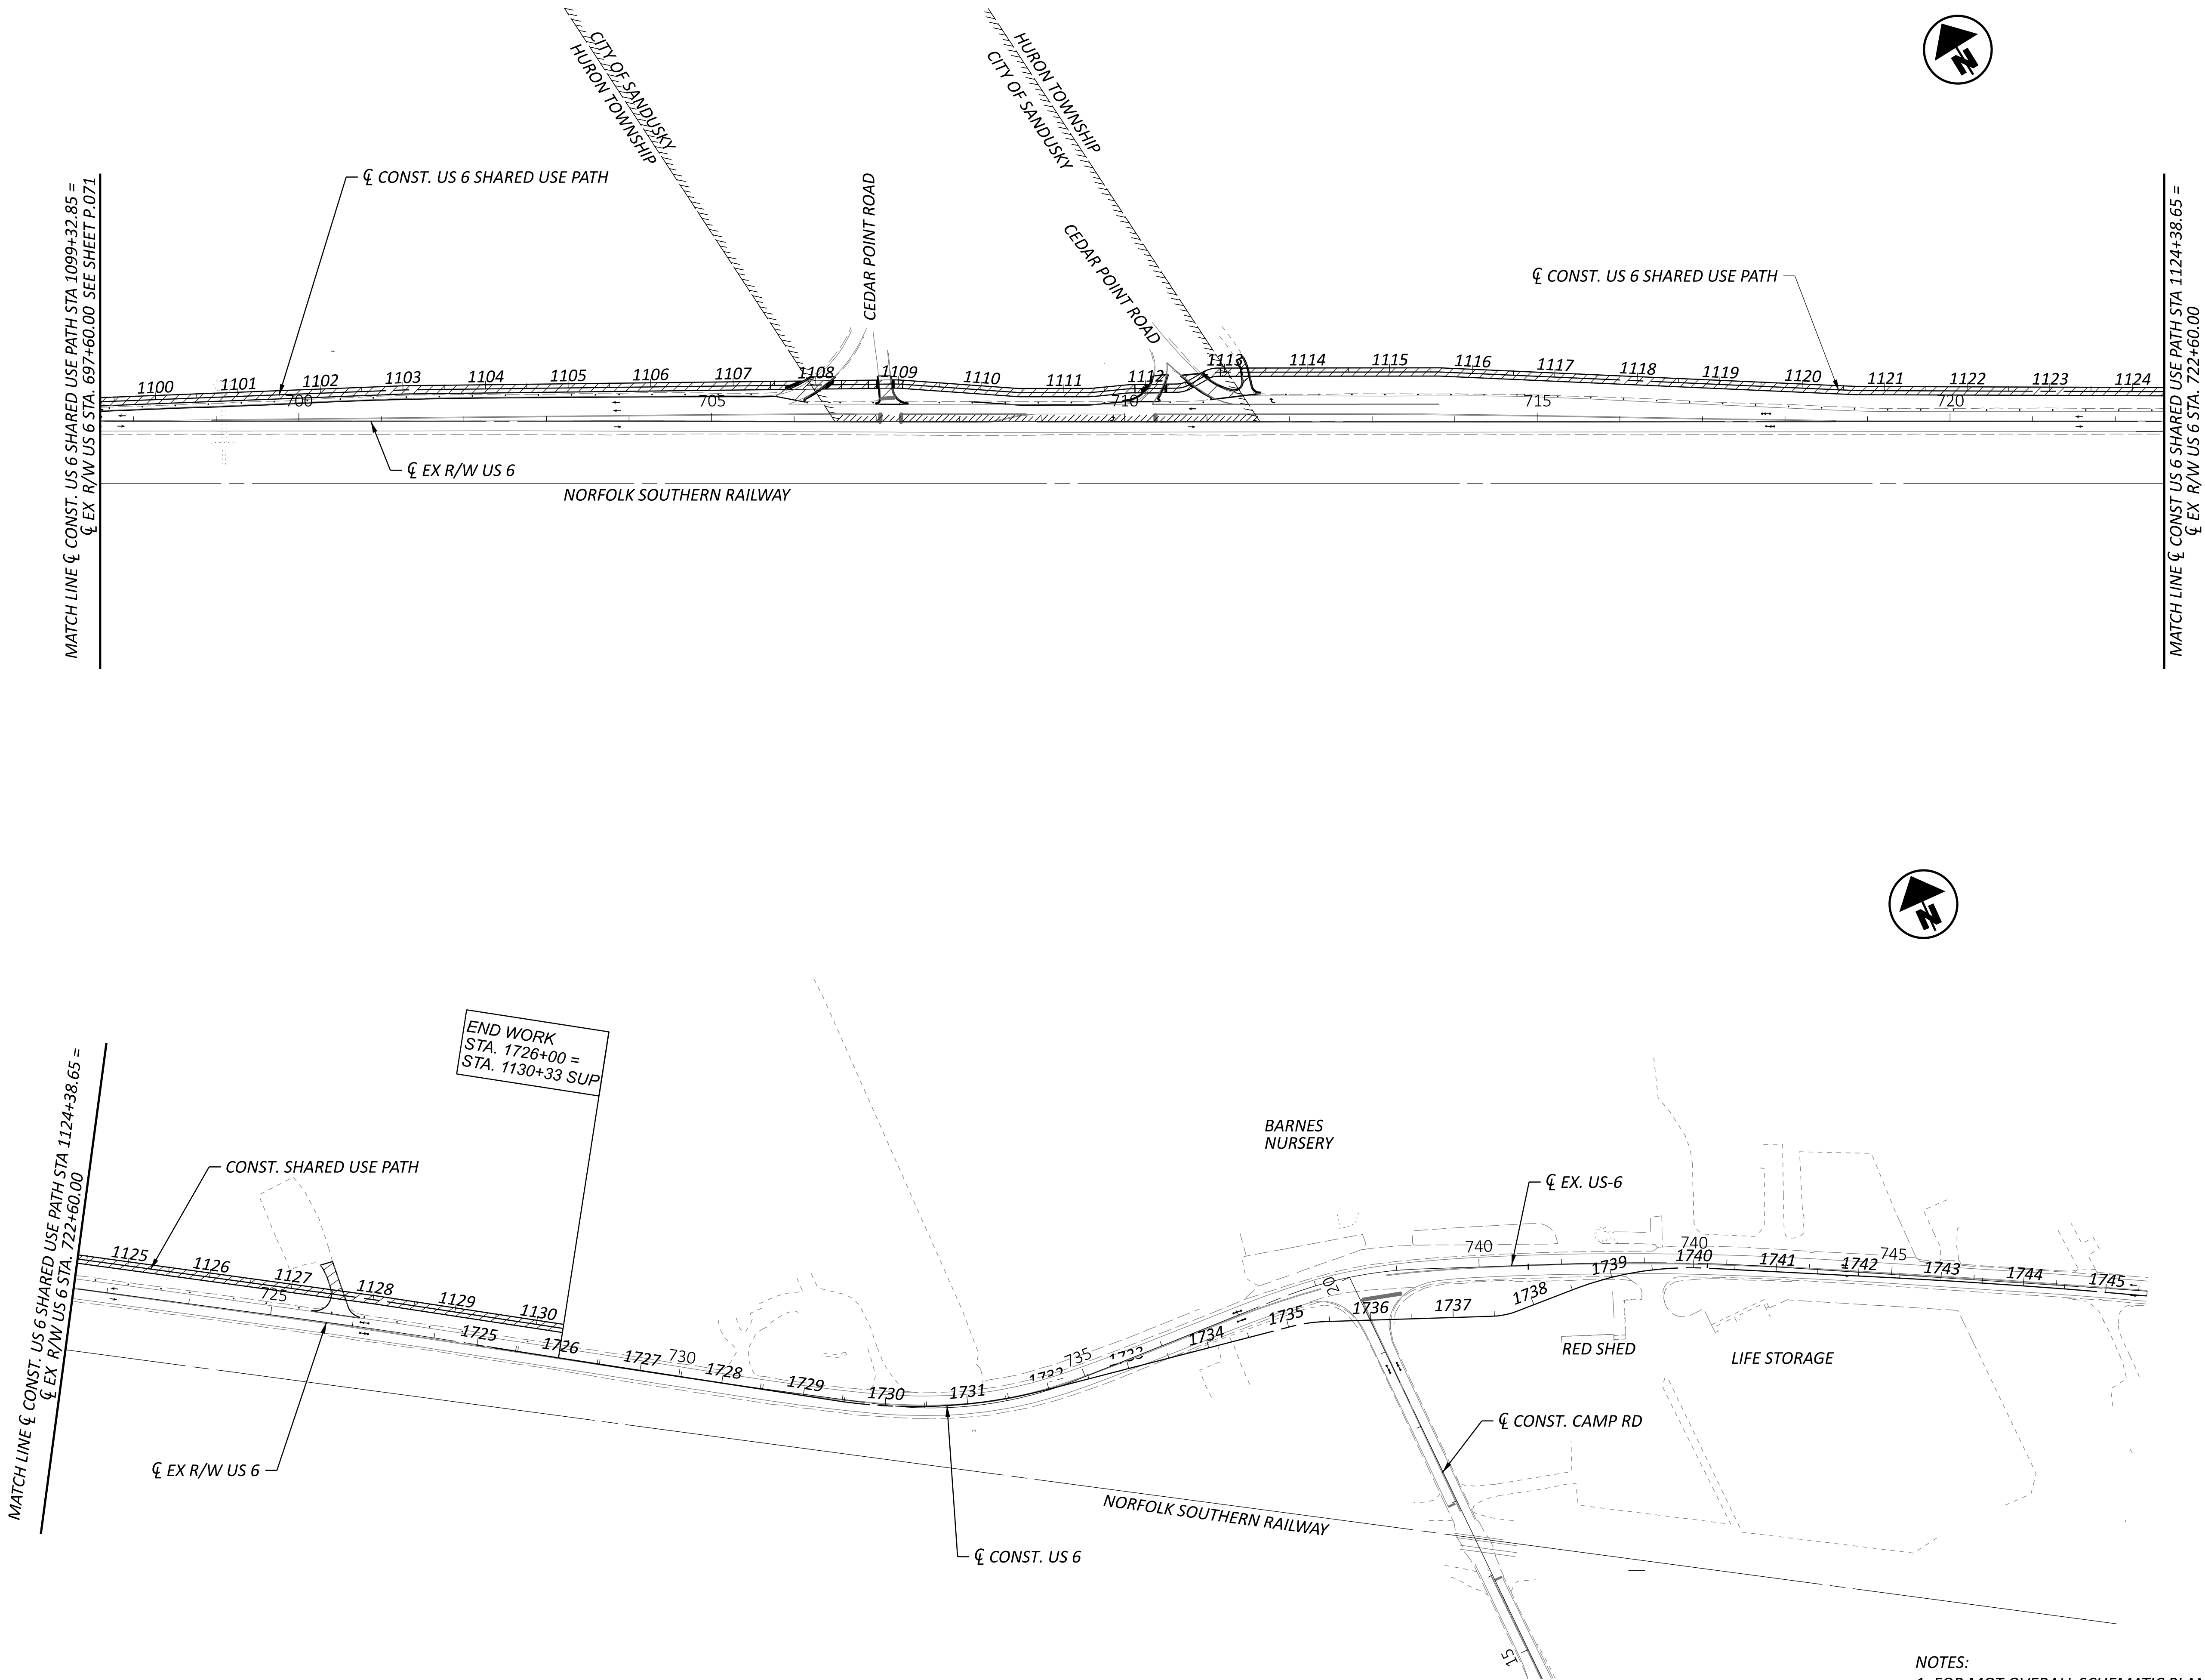

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION)
US 6 STA 695+00 TO STA 1745+50


TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.074 782



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: 100 Scale: 1 PAPER SIZE: 34x22 (in.) DATE: 6/9/2025 TIME: 5:32:50 PM USER: ssadusei
pw:\ohiodot-pw\entley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\Erie\116570\402-Engineering_TransSystems\MOT\Sheets\116570_M18001_2026.dgn



MOT SCHEMATIC PLAN - PRE-PHASE (2026 CONSTRUCTION)
WIDENING SECTION STA 745+50.00 TO STA 804+00.00

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET	TOTAL
P.075	782

- NOTES:**
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
 2. FOR LEGEND, SEE SHEET P.068

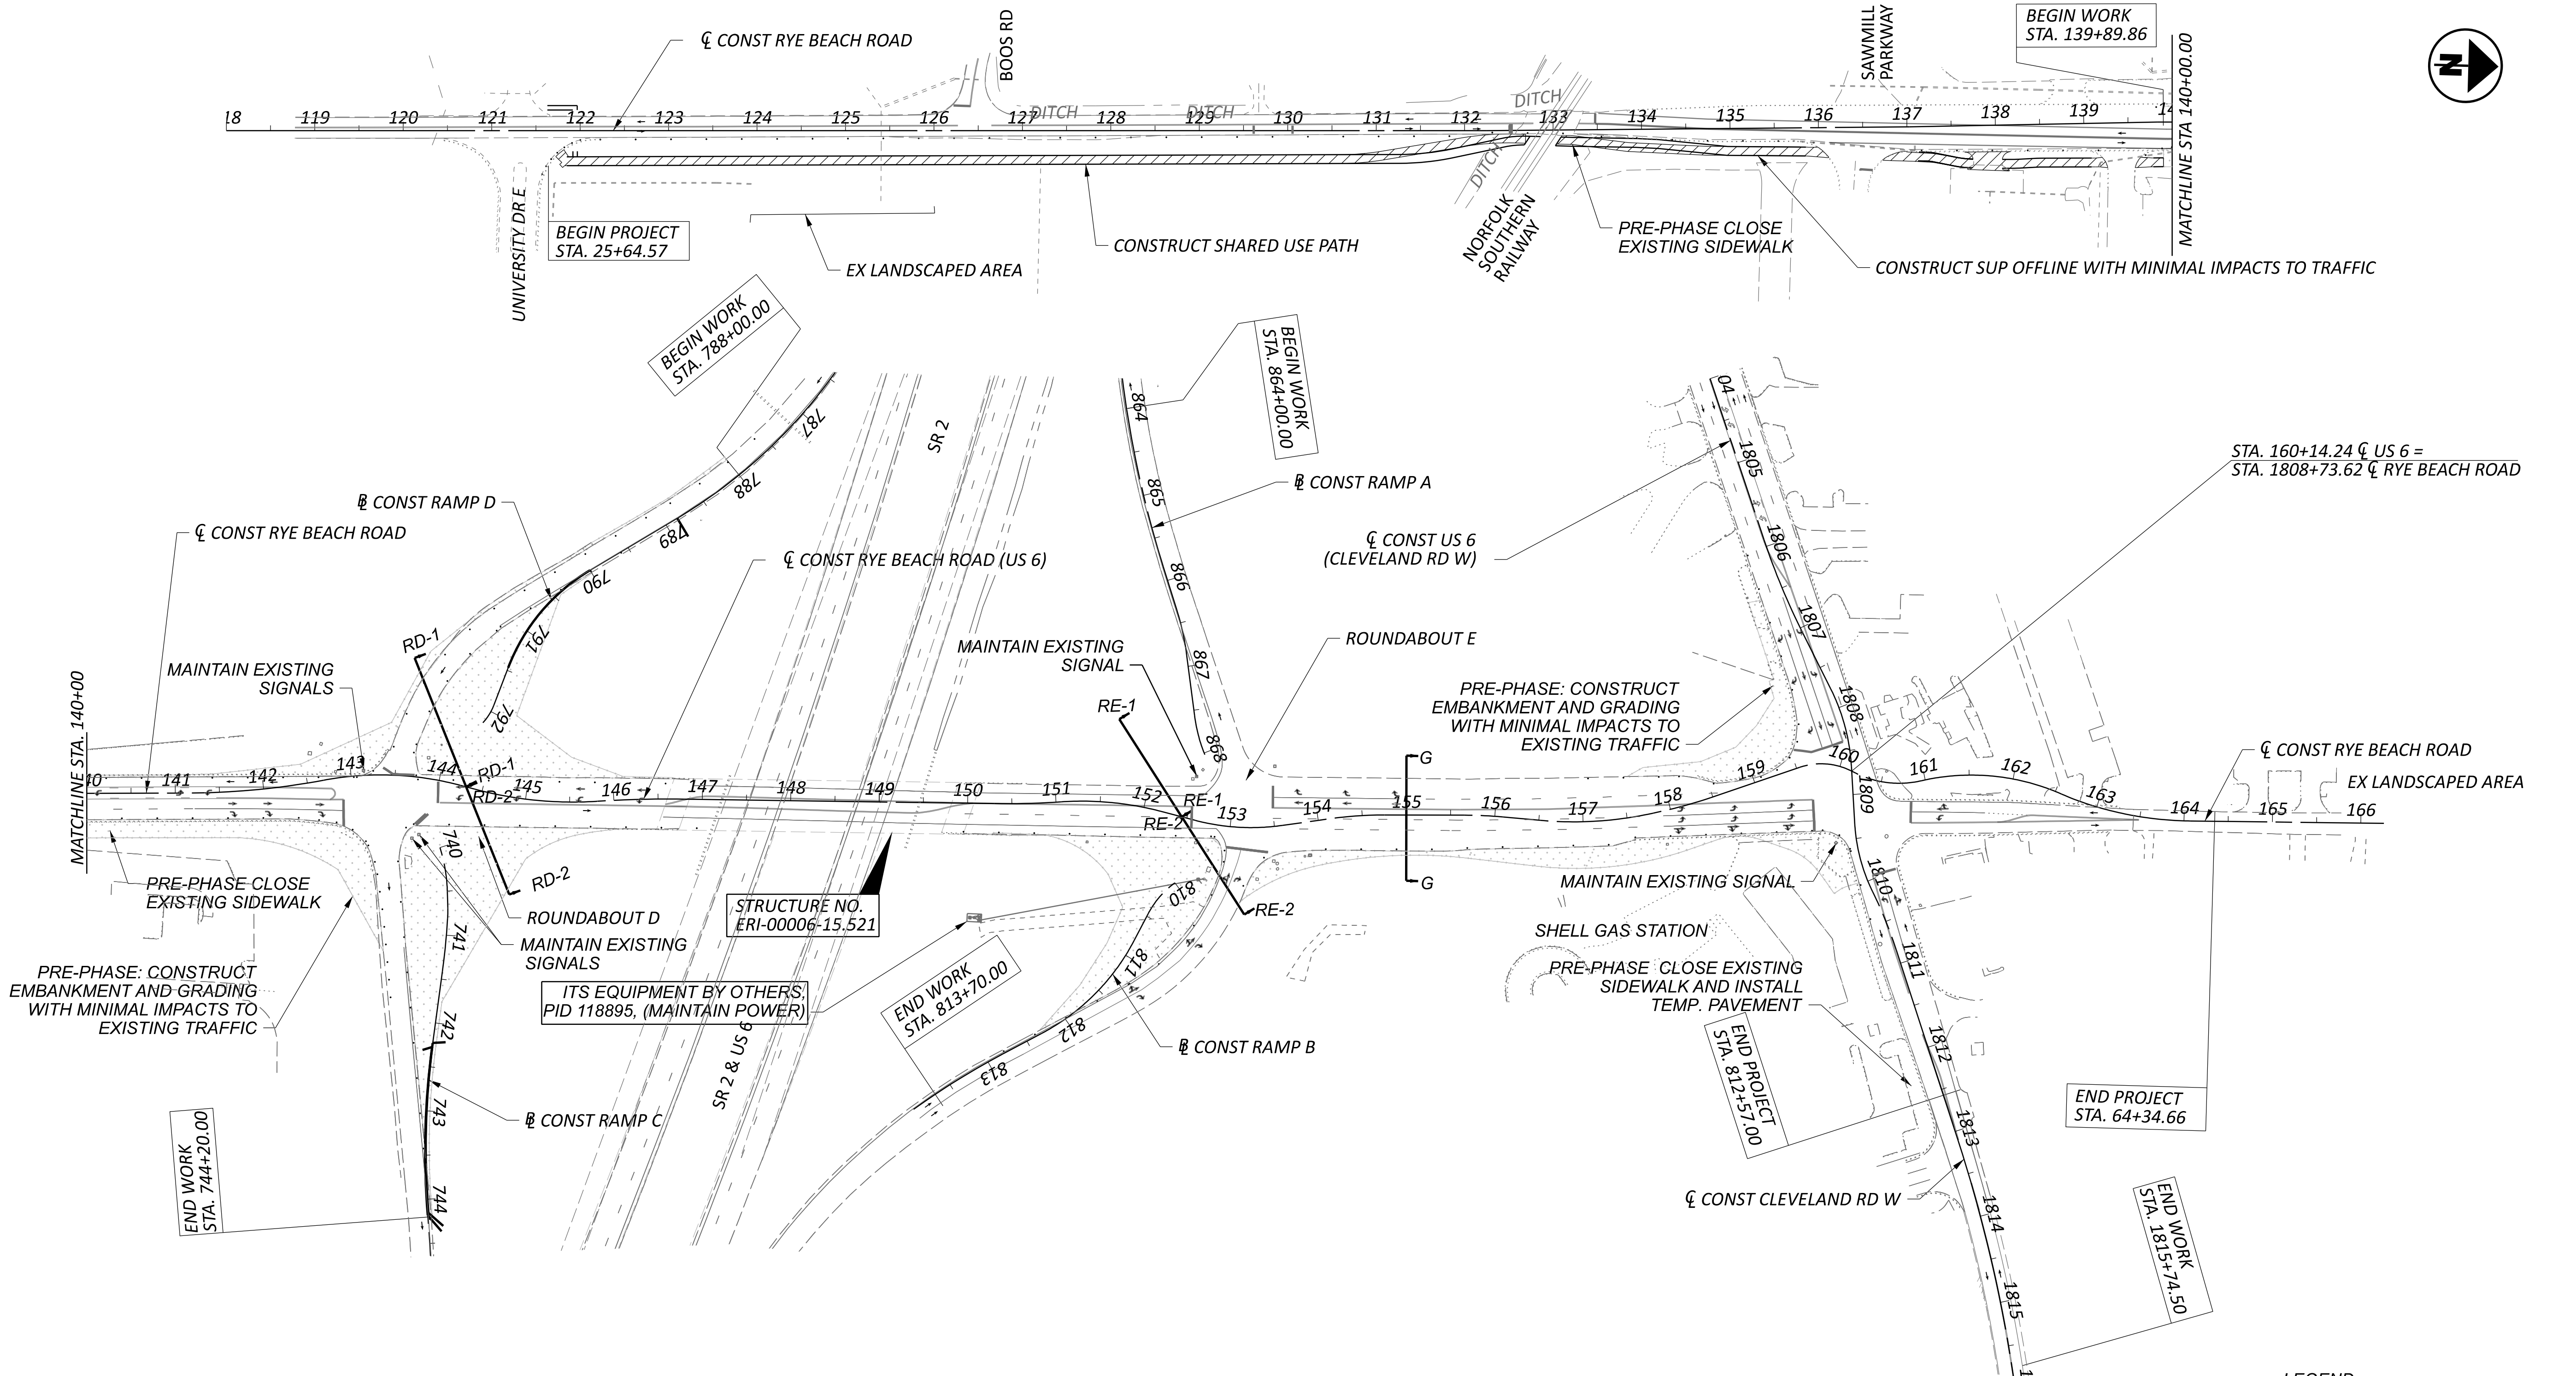

RYE BEACH ROUNDABOUTS:
DURATION: 180 DAYS
CEDAR POINT: NO ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER


PRE-PHASE:
CONSTRUCT EMBANKMENT AND GRADING WITH MINIMAL IMPACTS TO EXISTING TRAFFIC.

LEGEND:

	EMBANKMENT AND GRADING CONSTRUCTED IN PRE-PHASE
	PAVEMENT CONSTRUCTED IN PREVIOUS PHASE
	WORK ZONE
	TEMPORARY PAVEMENT
	DIRECTION OF TRAFFIC DRUMS

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

MOT SCHEMATIC PLAN - PRE PHASE (2026 CONSTRUCTION)
RYE BEACH ROAD STA 118+00.00 TO STA 166+00.00



DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID


116570

SHEET

P.076

TOTAL

782

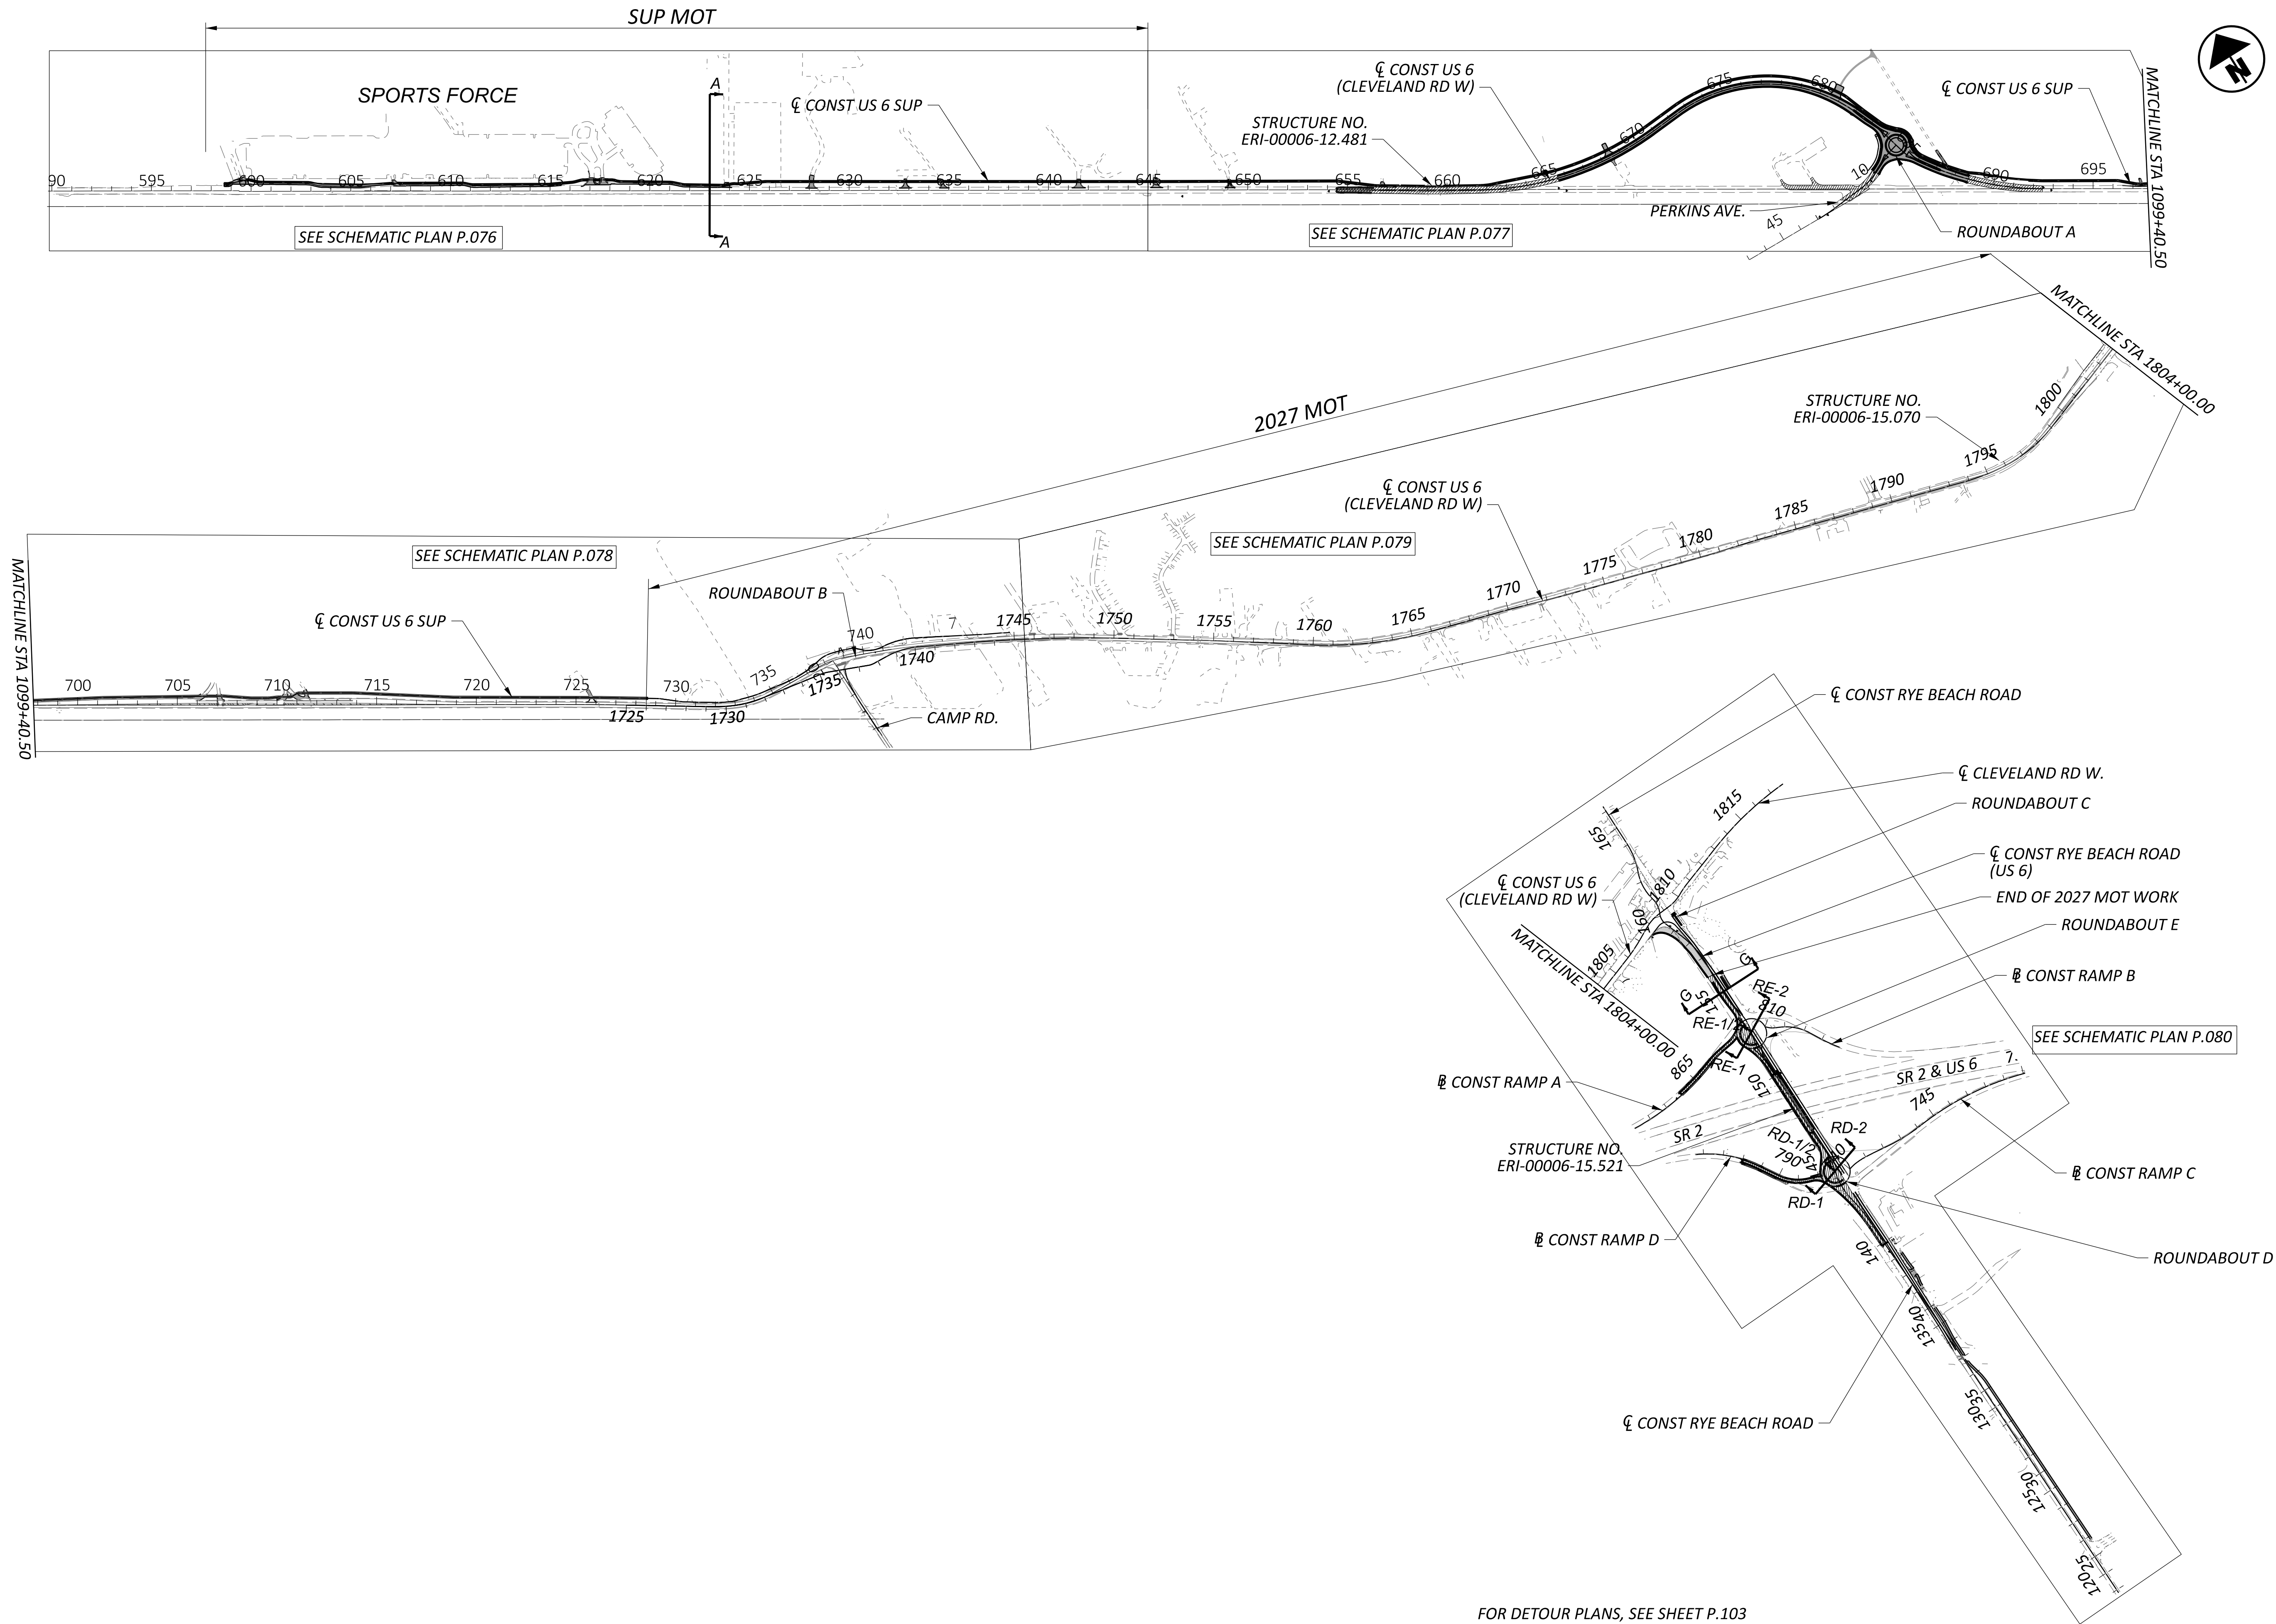

FOR DETOUR PLANS, SEE SHEET P.103

MOT OVERALL SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA


REVIEWER
SS

DATE
02/28/24

PROJECT ID
116570


SHEET
P.077

TOTAL
782

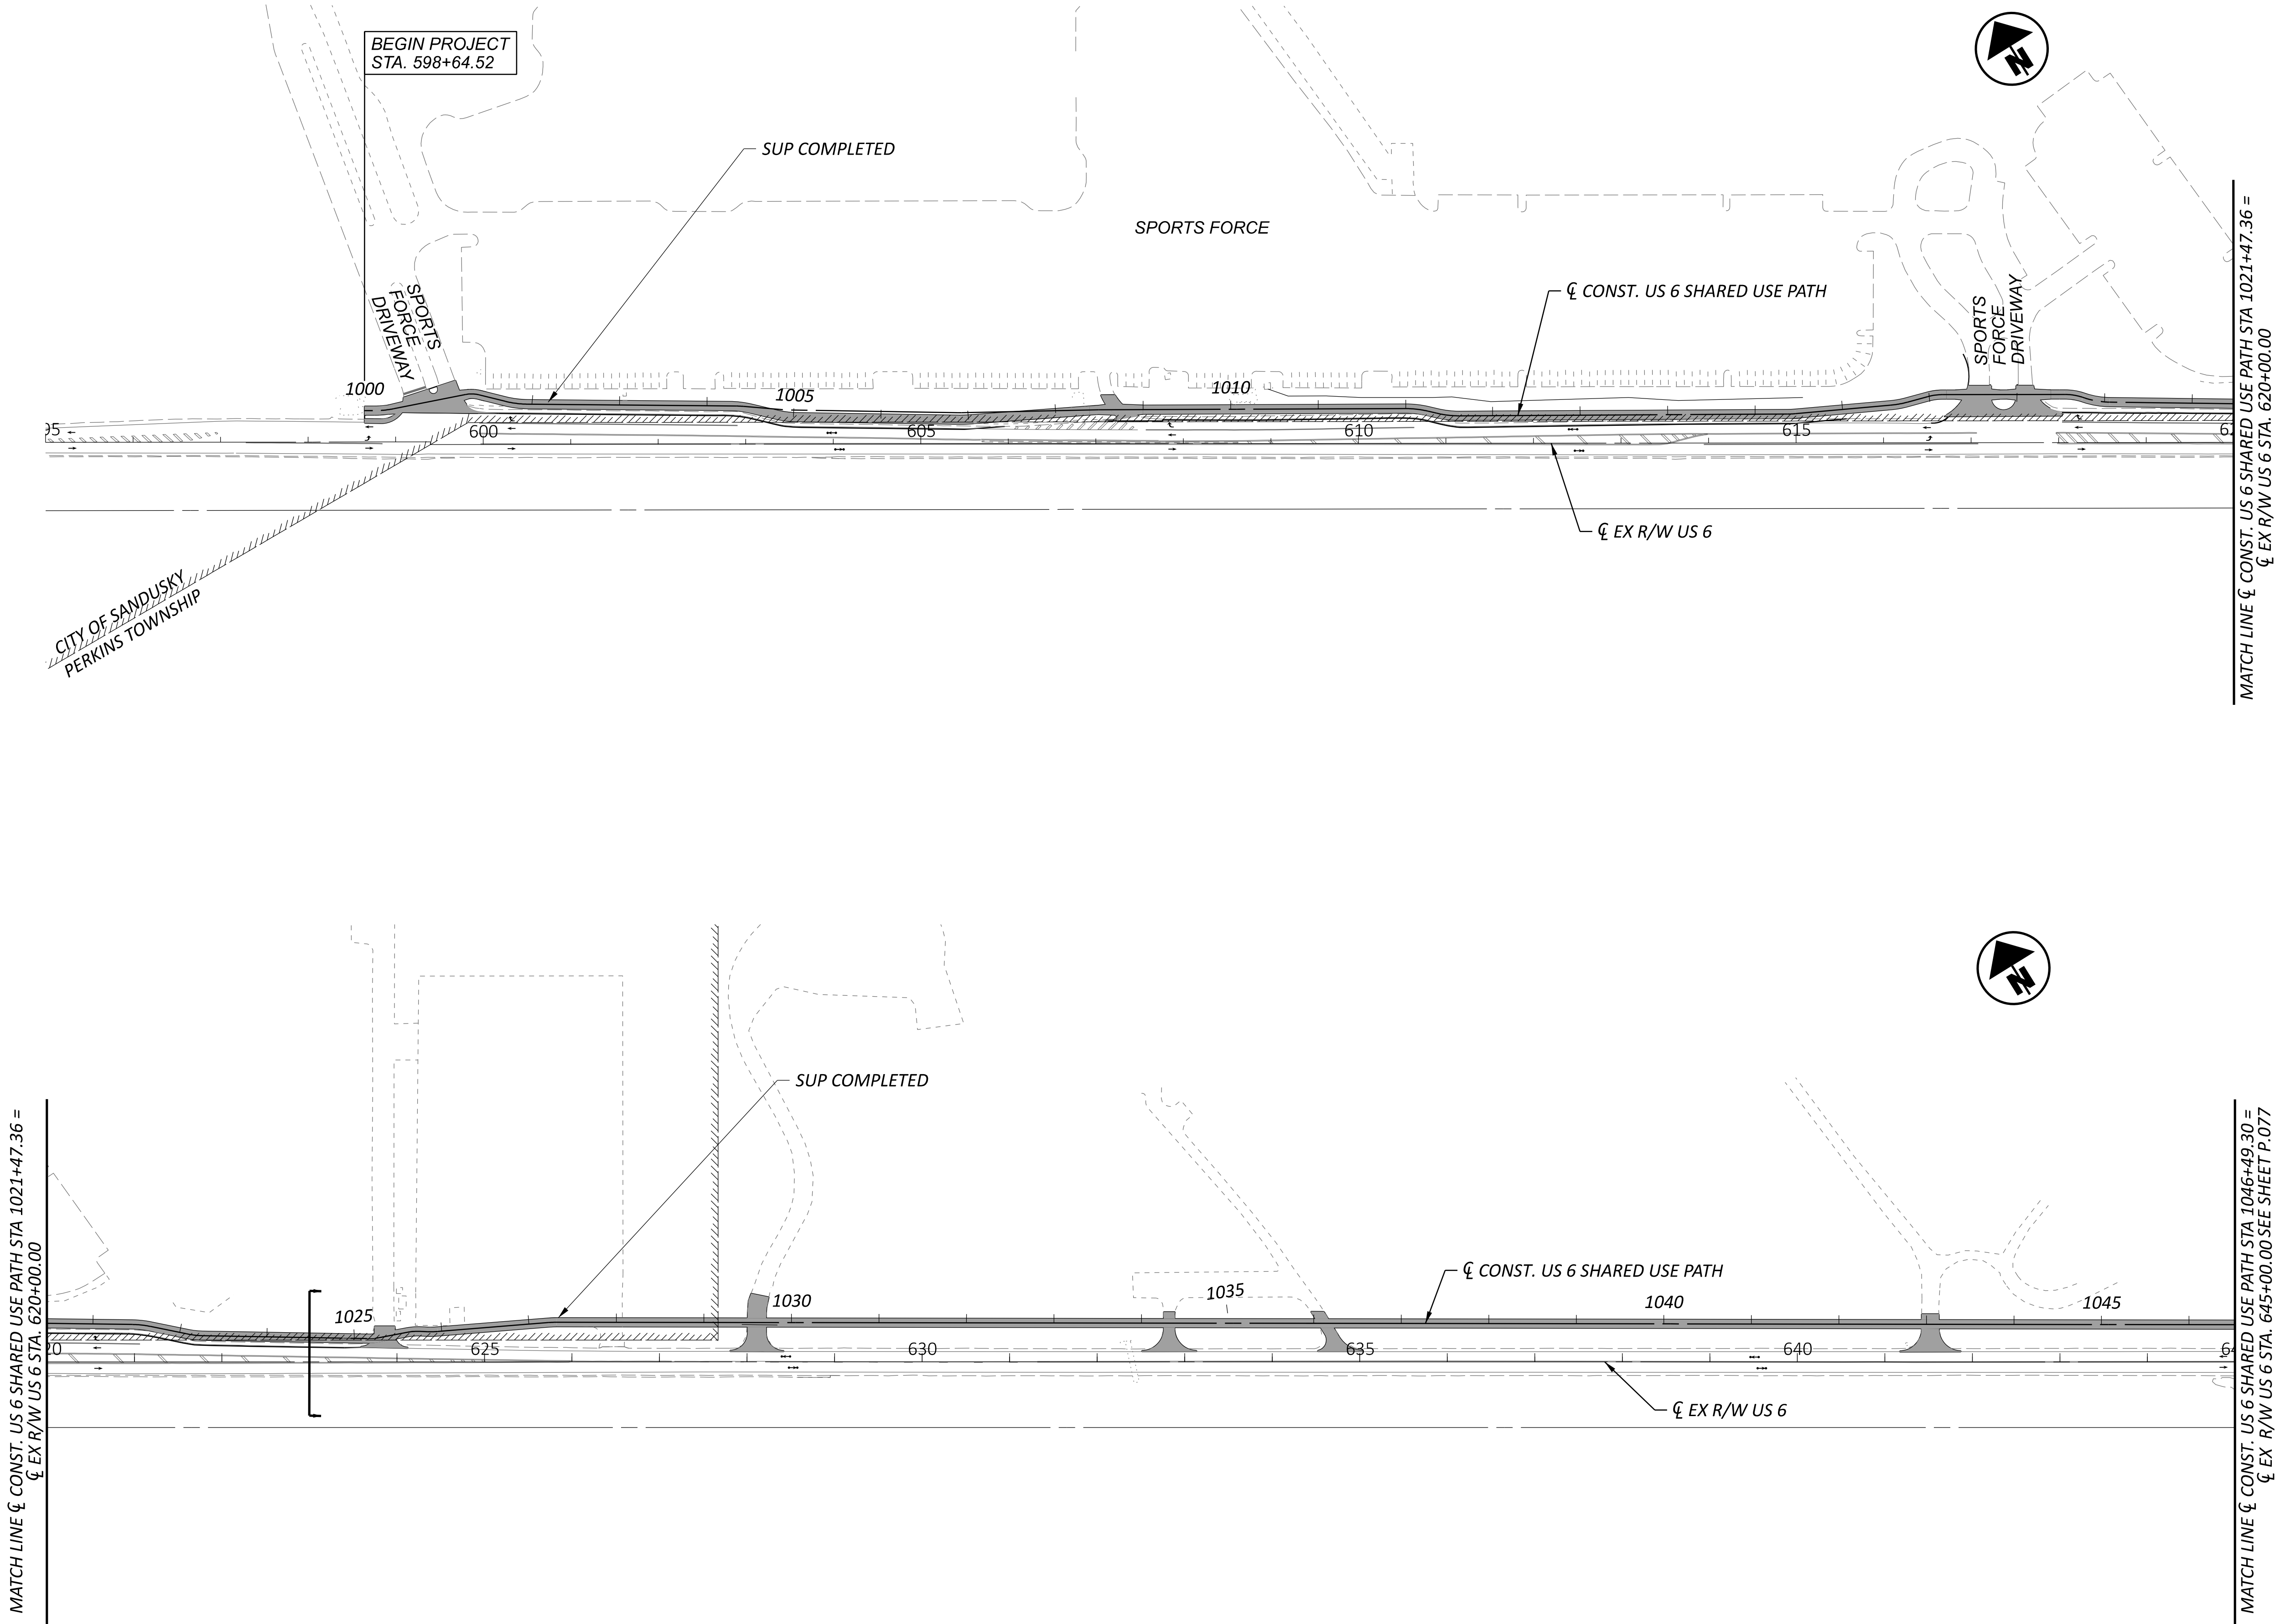

- NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
 2. FOR LEGEND, SEE SHEET P.076

HORIZONTAL SCALE IN FEET 0 50 100 200	
MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION) US 6 BEGIN PROJECT TO STA 645+00	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.078	782

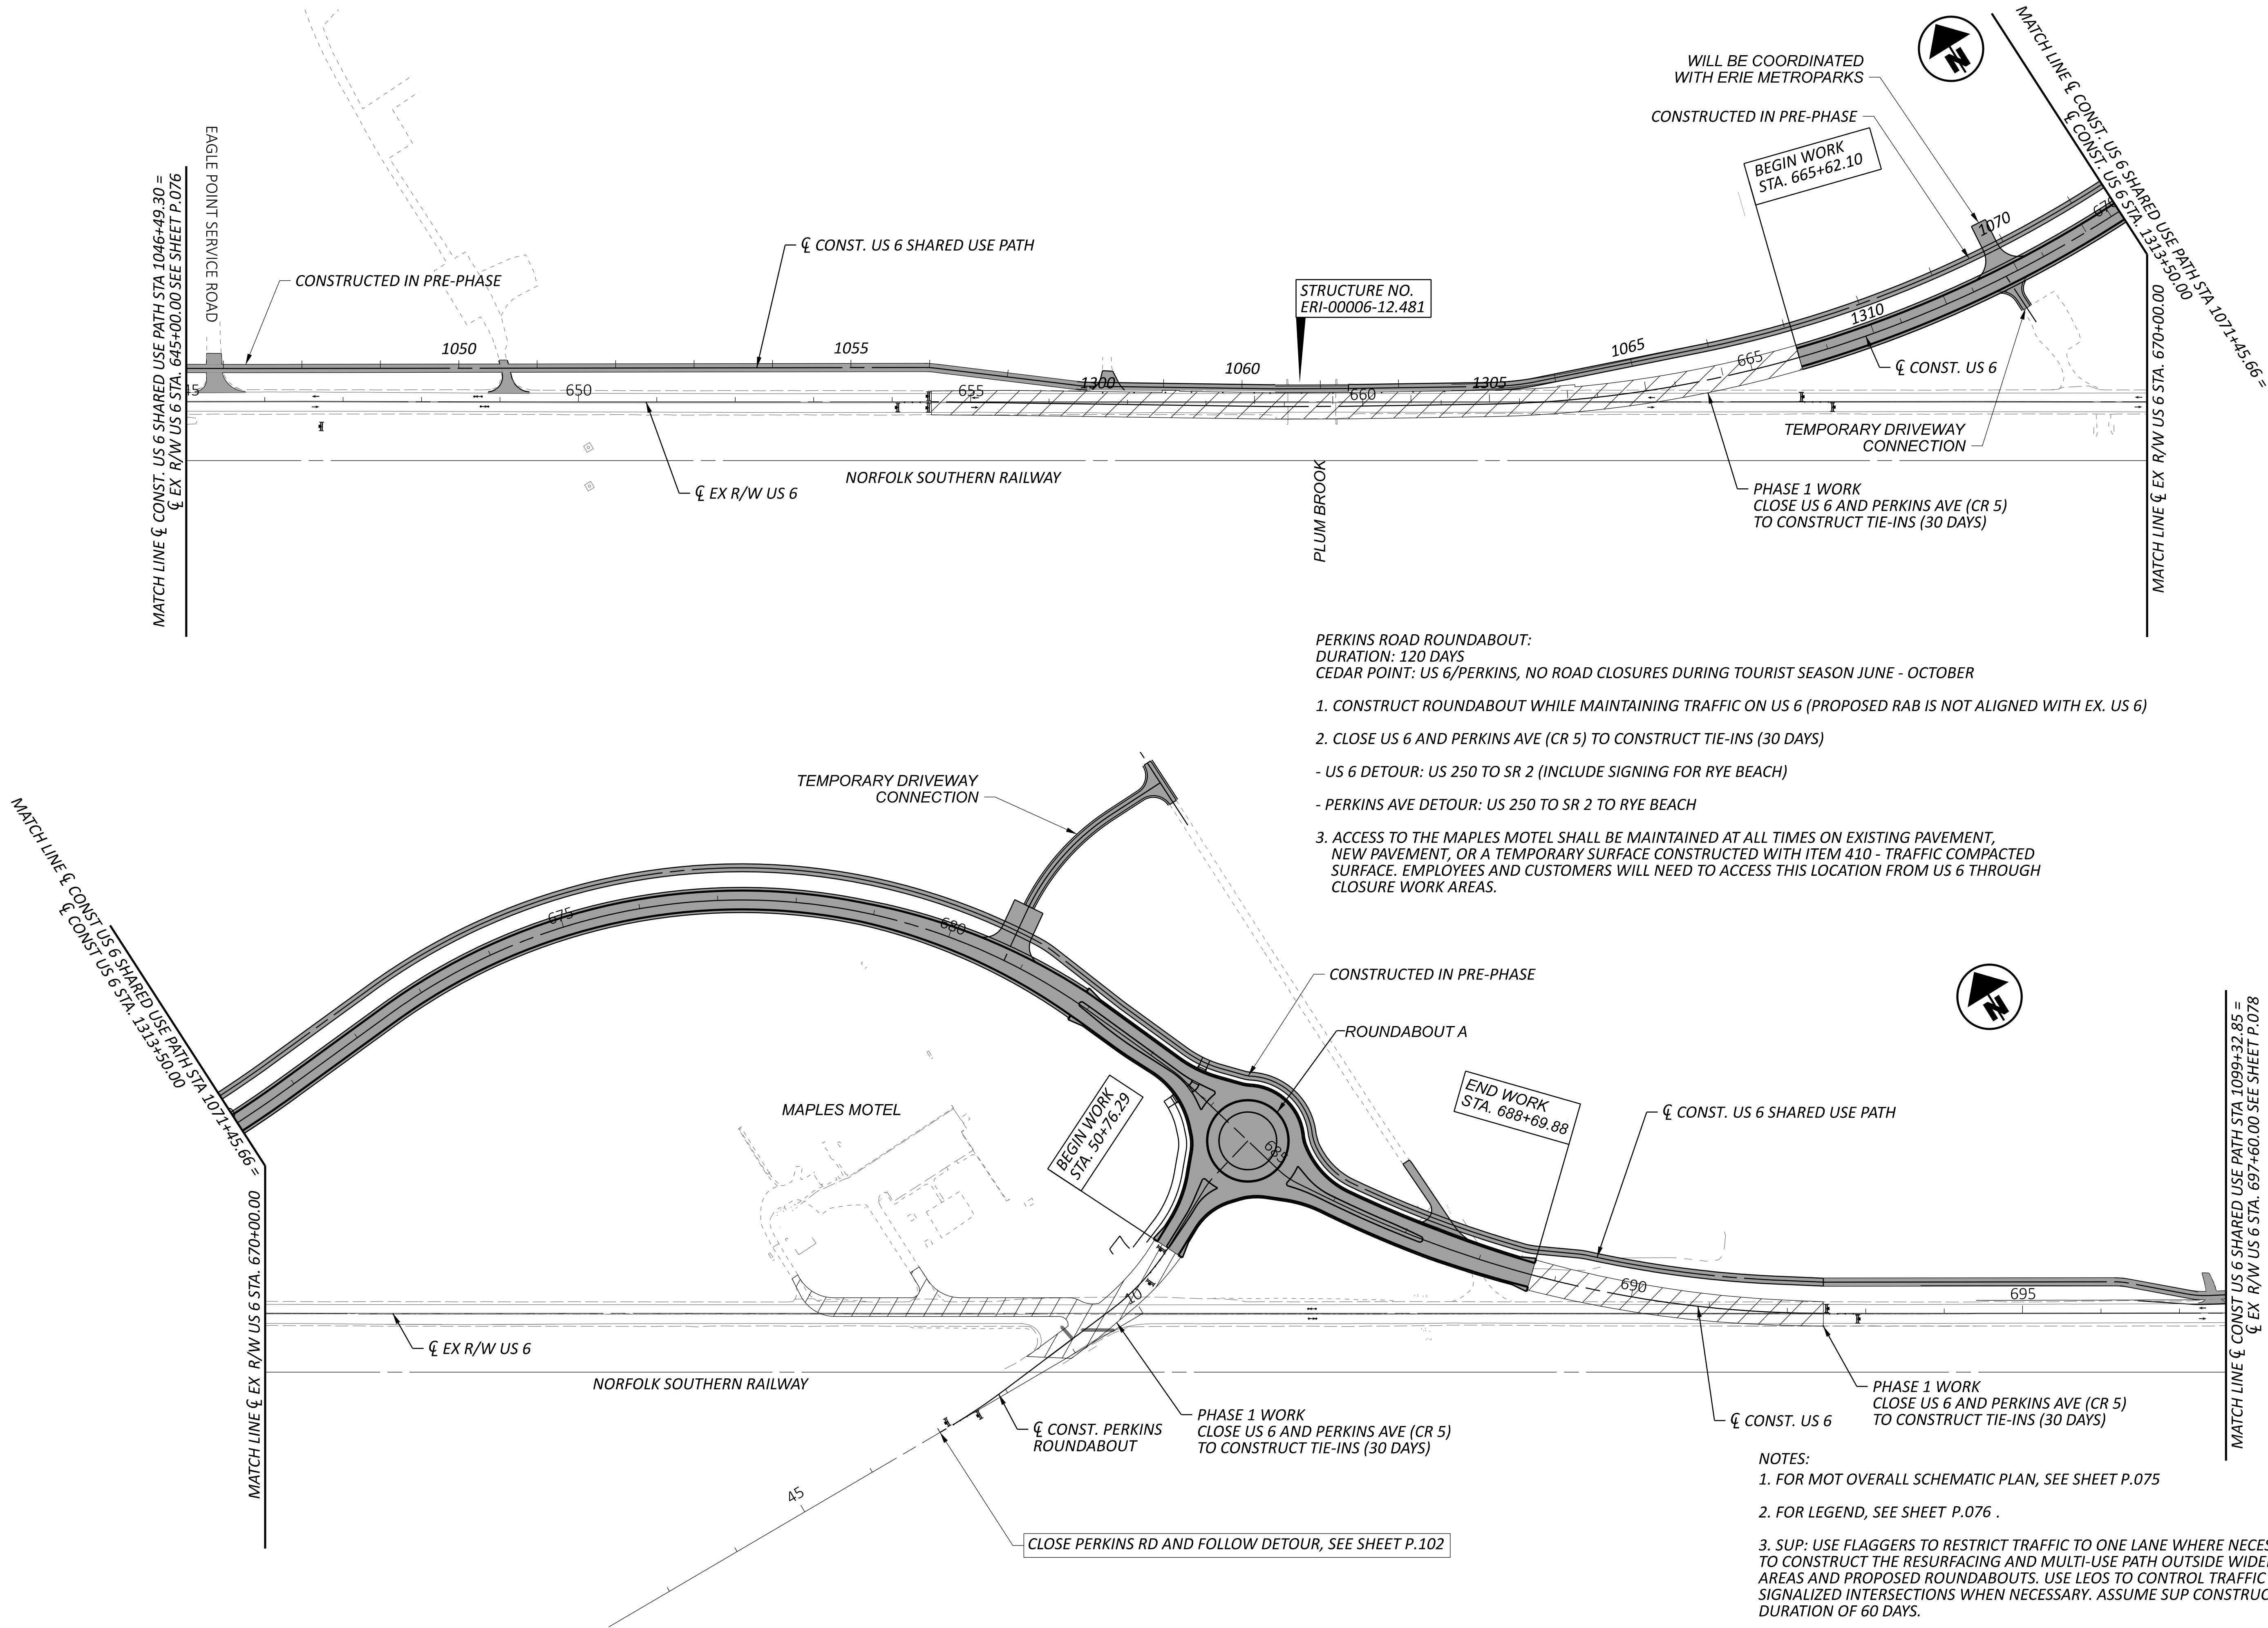


PERKINS ROAD ROUNDABOUT:
DURATION: 120 DAYS
CEDAR POINT: US 6/PERKINS, NO ROAD CLOSURES DURING TOURIST SEASON JUNE - OCTOBER

1. CONSTRUCT ROUNDABOUT WHILE MAINTAINING TRAFFIC ON US 6 (PROPOSED RAB IS NOT ALIGNED WITH EX. US 6)
2. CLOSE US 6 AND PERKINS AVE (CR 5) TO CONSTRUCT TIE-INS (30 DAYS)
 - US 6 DETOUR: US 250 TO SR 2 (INCLUDE SIGNING FOR RYE BEACH)
 - PERKINS AVE DETOUR: US 250 TO SR 2 TO RYE BEACH
3. ACCESS TO THE MAPLES MOTEL SHALL BE MAINTAINED AT ALL TIMES ON EXISTING PAVEMENT, NEW PAVEMENT, OR A TEMPORARY SURFACE CONSTRUCTED WITH ITEM 410 - TRAFFIC COMPACTED SURFACE. EMPLOYEES AND CUSTOMERS WILL NEED TO ACCESS THIS LOCATION FROM US 6 THROUGH CLOSURE WORK AREAS.

- NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
 2. FOR LEGEND, SEE SHEET P.076 .

3. SUP: USE FLAGGERS TO RESTRICT TRAFFIC TO ONE LANE WHERE NECESSARY TO CONSTRUCT THE RESURFACING AND MULTI-USE PATH OUTSIDE WIDENING AREAS AND PROPOSED ROUNDABOUTS. USE LEOS TO CONTROL TRAFFIC AT SIGNALIZED INTERSECTIONS WHEN NECESSARY. ASSUME SUP CONSTRUCTION DURATION OF 60 DAYS.

MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)
US 6 STA 645+00 TO STA 695+00



DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID


116570

SHEET

P.079


TOTAL

782

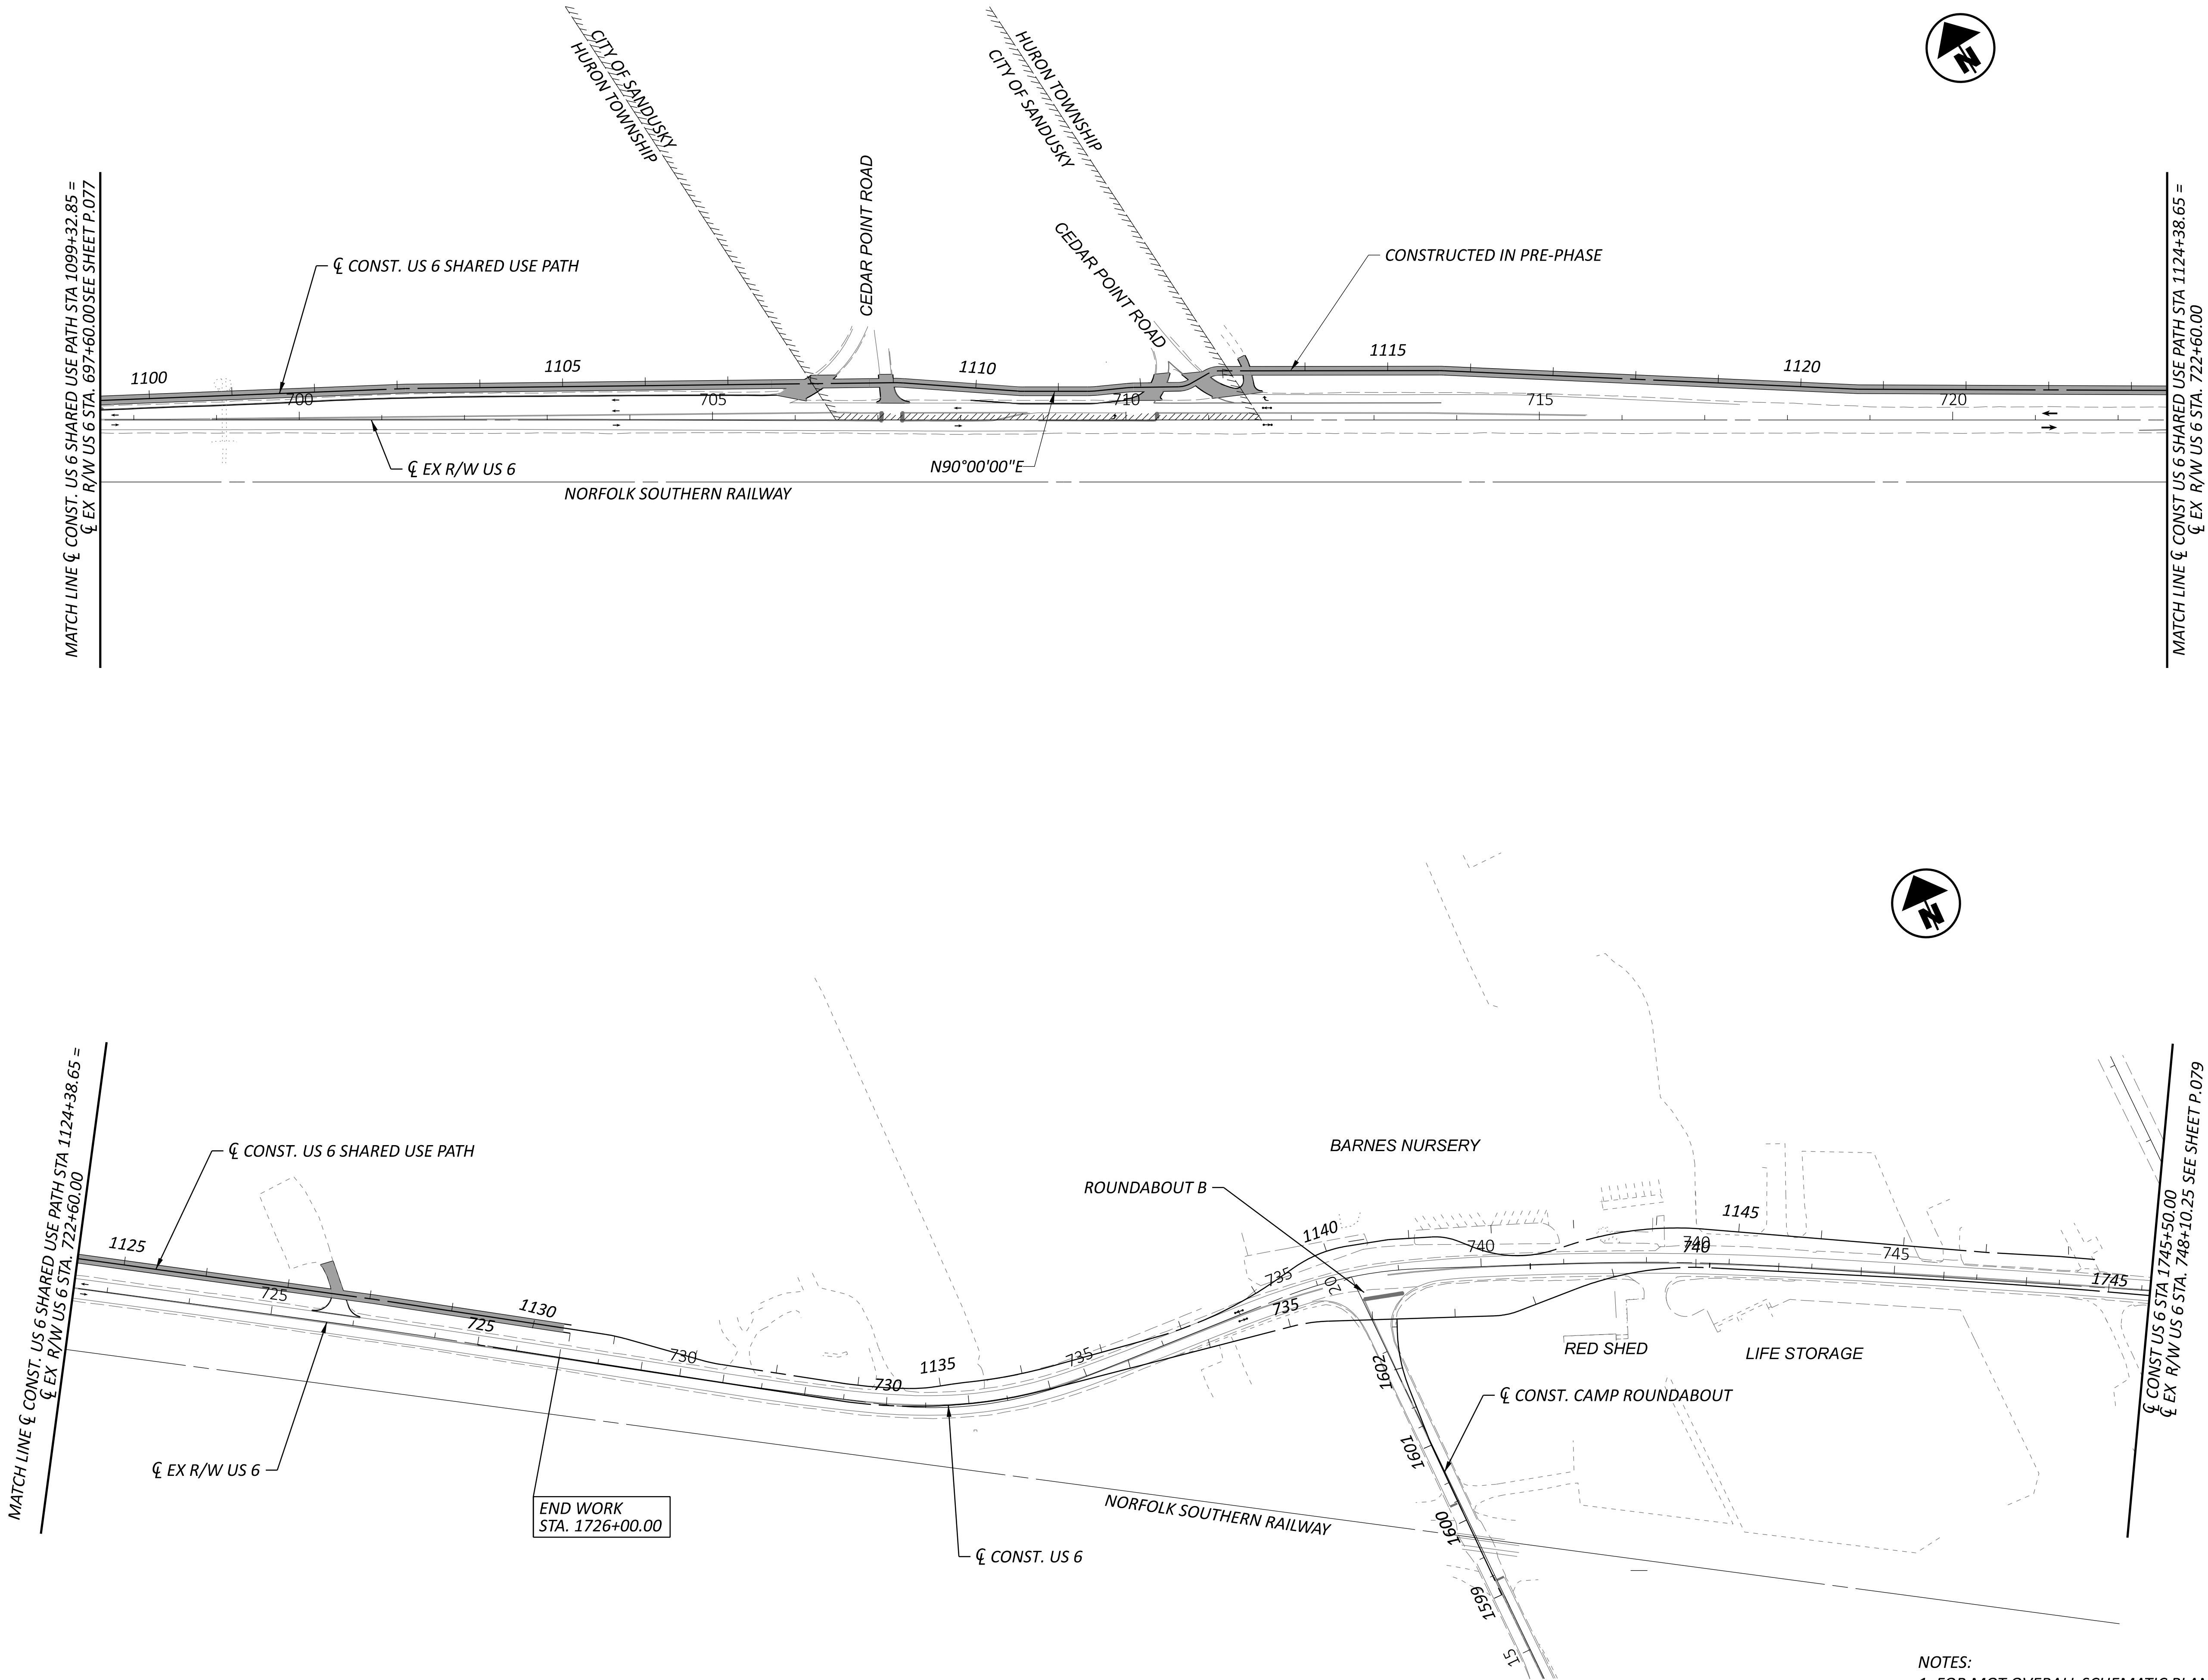

NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.075
2. FOR LEGEND, SEE SHEET P.076

HORIZONTAL SCALE IN FEET 0 50 100 200	
MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION) US 6 STA 695+00 TO STA 745+50	
DESIGN AGENCY TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER SSA	
REVIEWER SS 02/28/24	
PROJECT ID 116570	
SHEET P.080	TOTAL 782

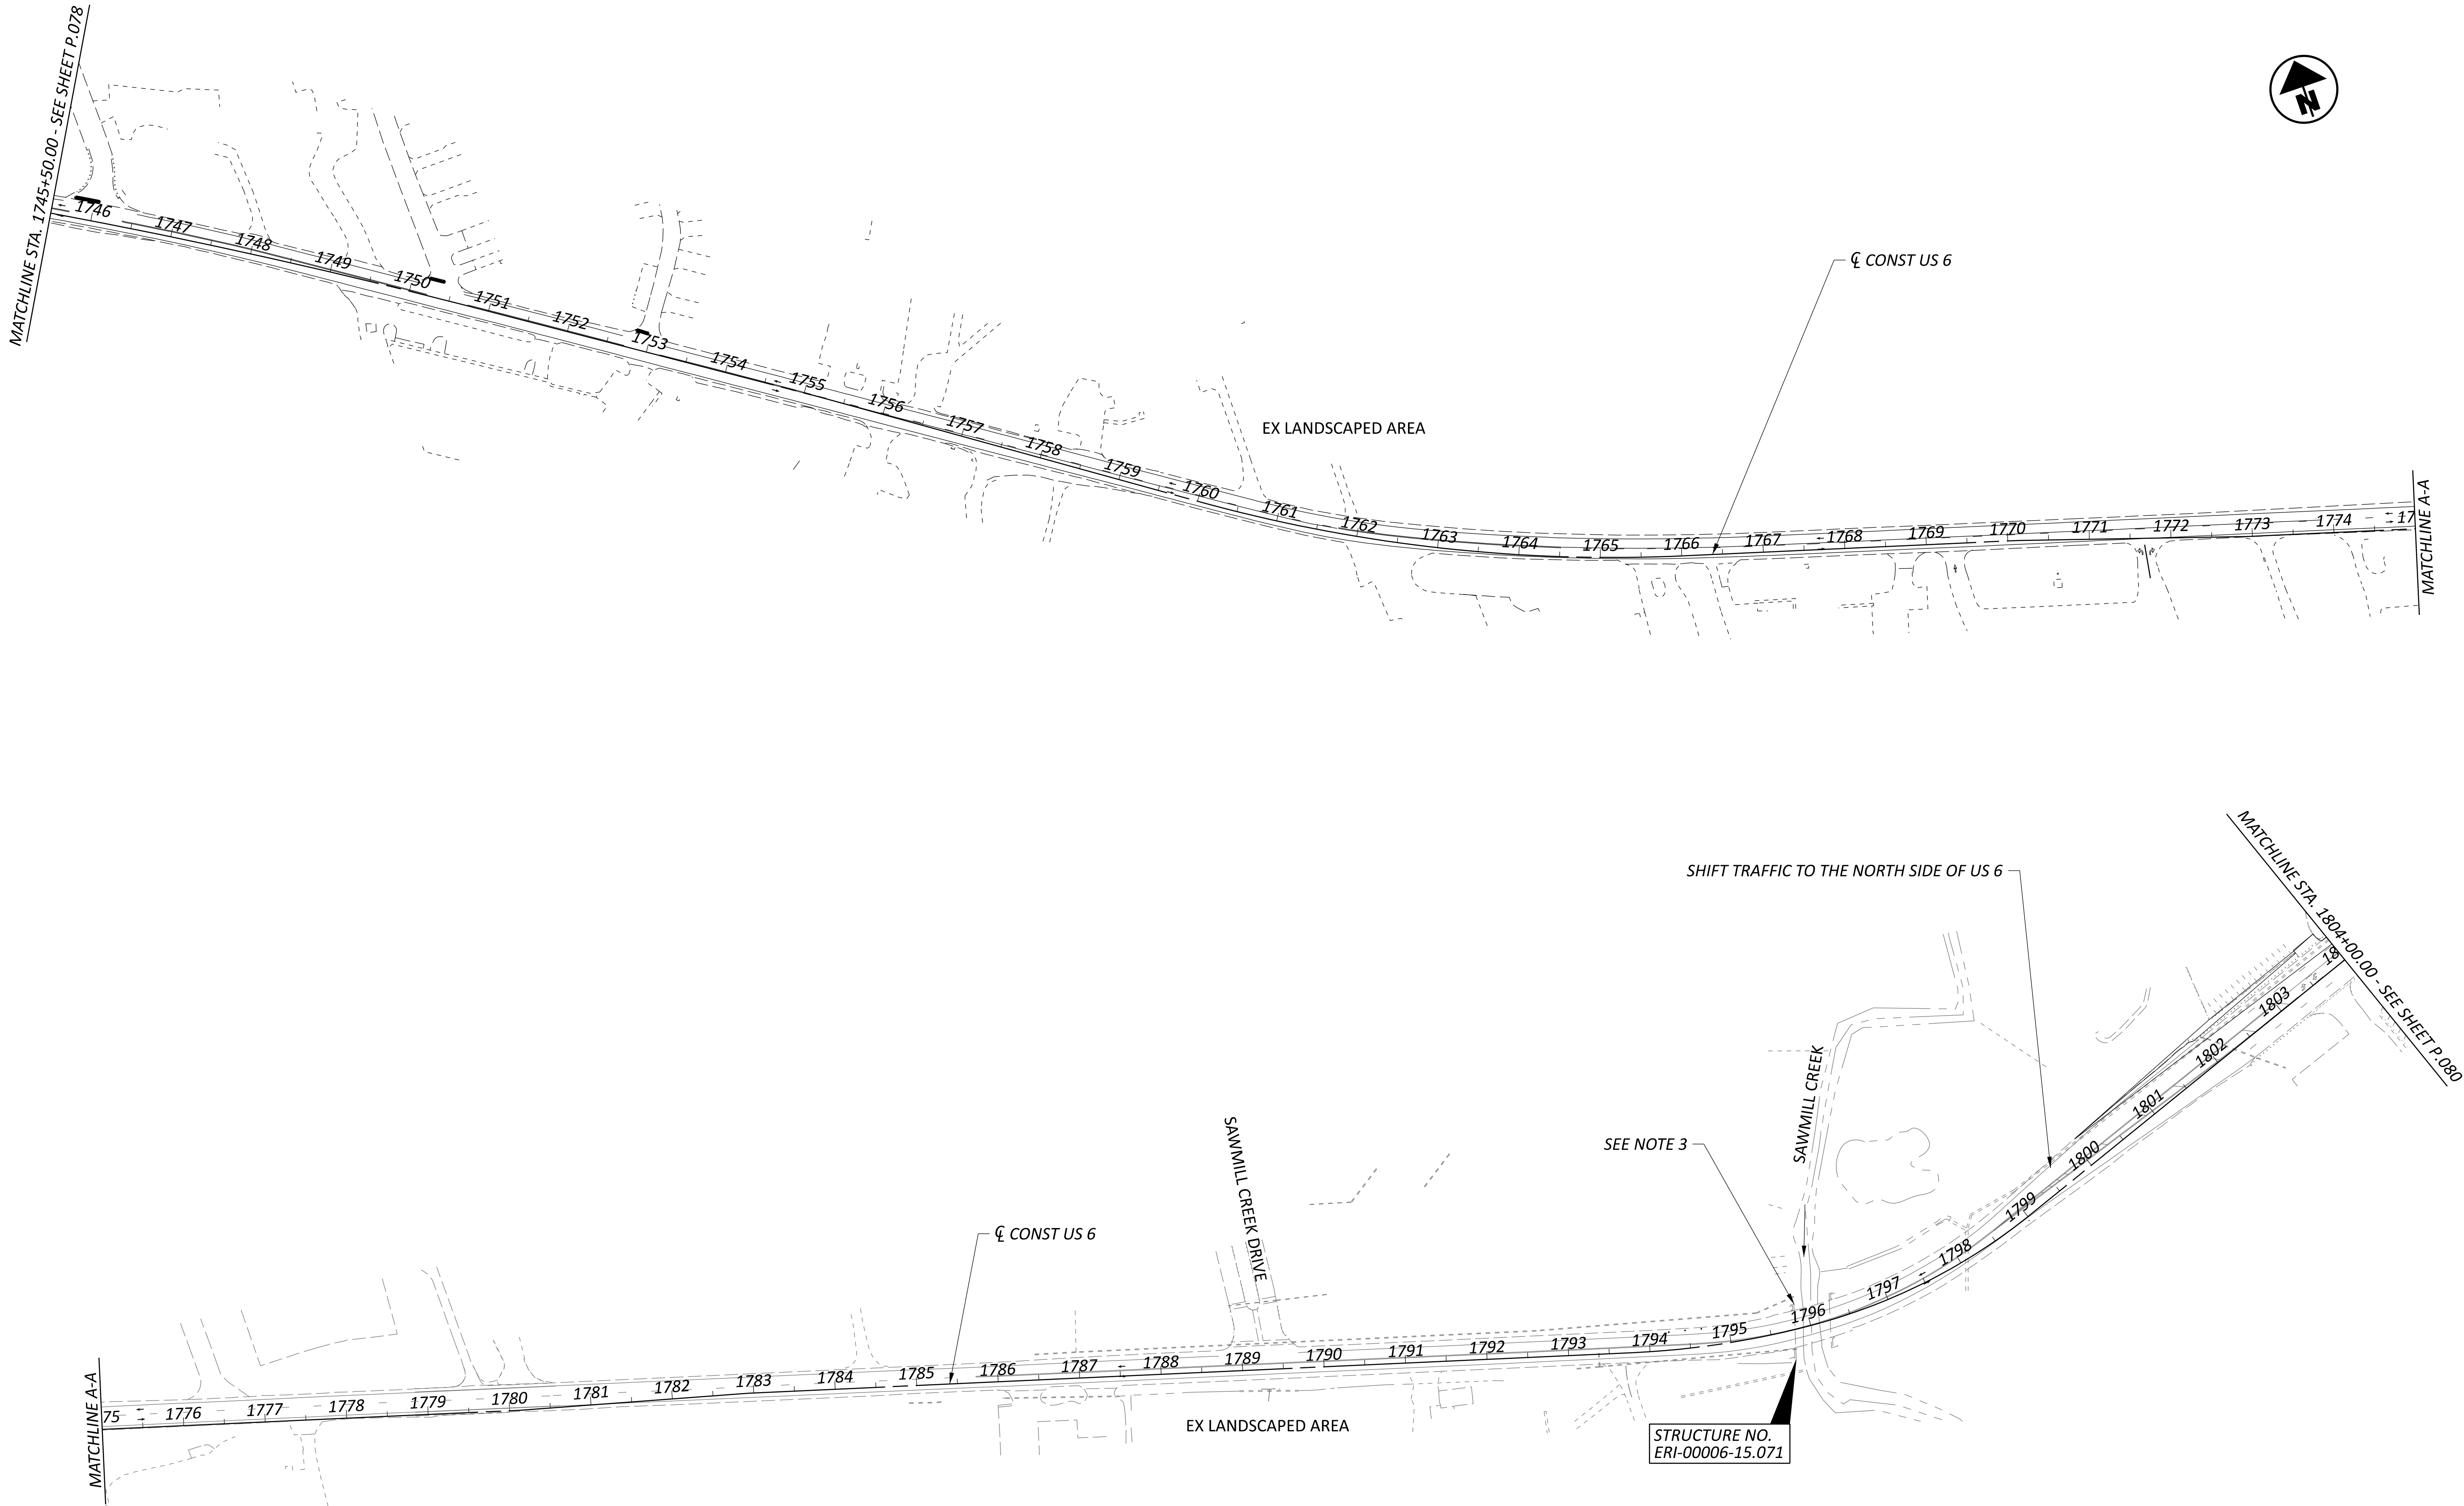

MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)
WIDENING SECTION STA 745+50.00 TO STA 804+00.00

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET	TOTAL
P.081	782

- NOTES:
1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068
3. RELOCATION OF EXISTING UTILITIES IN BETWEEN THE DISTRICT ROW.

RYE BEACH INTERCHANGE:
DURATION: 180 DAYS
CEDAR POINT: NO EAST SIDE ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER

PERFORM THESE PHASES WITH CORRESPONDING PHASES AT THE RYE BEACH/US 6 INTERSECTION:

PHASE 1. SHIFT ONE LANE OF TRAFFIC EACH DIRECTION TO THE EAST SIDE OF RYE BEACH RD AND CONSTRUCT THE WEST SIDE. CLOSE AND DETOUR THE RAMPS ON THE WEST SIDE OF THE INTERCHANGE (THESE CLOSURES CAN BE DONE ANYTIME)

- WB ENTRANCE: SR 2 EB TO SR 13 NB TO SR 2 WB

- EB EXIT: SR 2 EB TO SR 13 NB TO SR 2 WB TO RYE BEACH RD

RYE BEACH ROUNDABOUTS:

DURATION: 180 DAYS

CEDAR POINT: NO ROAD CLOSURES ON US 6 DURING TOURIST SEASON IN JUNE - OCTOBER

PRE-PHASE:

CONSTRUCT EMBANKMENT AND GRADING WITH MINIMAL IMPACTS TO EXISTING TRAFFIC

PHASE 1. CLOSE THE CLEVELAND RD AND RYE BEACH NORTH LEG OF THE INTERSECTION EXCEPT TO LOCAL BUSINESSES/RESIDENCES

- CONSTRUCT TWO RETAINING WALL SECTIONS WITH THE FOLLOWING ALIGNMENT AND ELEVATION CHARACTERISTICS:

WALL SEGMENT A: BEGIN AT STATION 140+50 WITH A WALL HEIGHT OF 0 FEET, INCREASE TO A MAXIMUM HEIGHT OF 4.5 FEET, THEN TAPER BACK DOWN TO 0 FEET AT STATION 145+50.

WALL SEGMENT B: BEGIN AT STATION 150+60 WITH A WALL HEIGHT OF 0 FEET, INCREASE TO A MAXIMUM HEIGHT OF 5.5 FEET, THEN TAPER BACK DOWN TO 0 FEET AT STATION 160+00.


UPON COMPLETION OF EACH WALL SECTION, INSTALL PCB ON TOP, AS SHOWN IN THE PHASE 1 PLANS.
REFER TO THE PLAN AND PROFILE SHEETS FOR ELEVATION VARIATIONS AND ADDITIONAL GEOMETRIC DETAILS.

- CLEVELAND RD: CENTER STREET TO US 6 WB TO RYE BEACH RD NB. FOR DETOUR PLAN, SEE SHEET P.104


- RYE BEACH RD: SAND DR TO ATWOOD PL THEN FOLLOW CLEVELAND RD DETOUR. FOR DETOUR PLAN, SEE SHEET P.104

NOTES:

1. FOR MOT OVERALL SCHEMATIC PLAN, SEE SHEET P.069
2. FOR LEGEND, SEE SHEET P.068

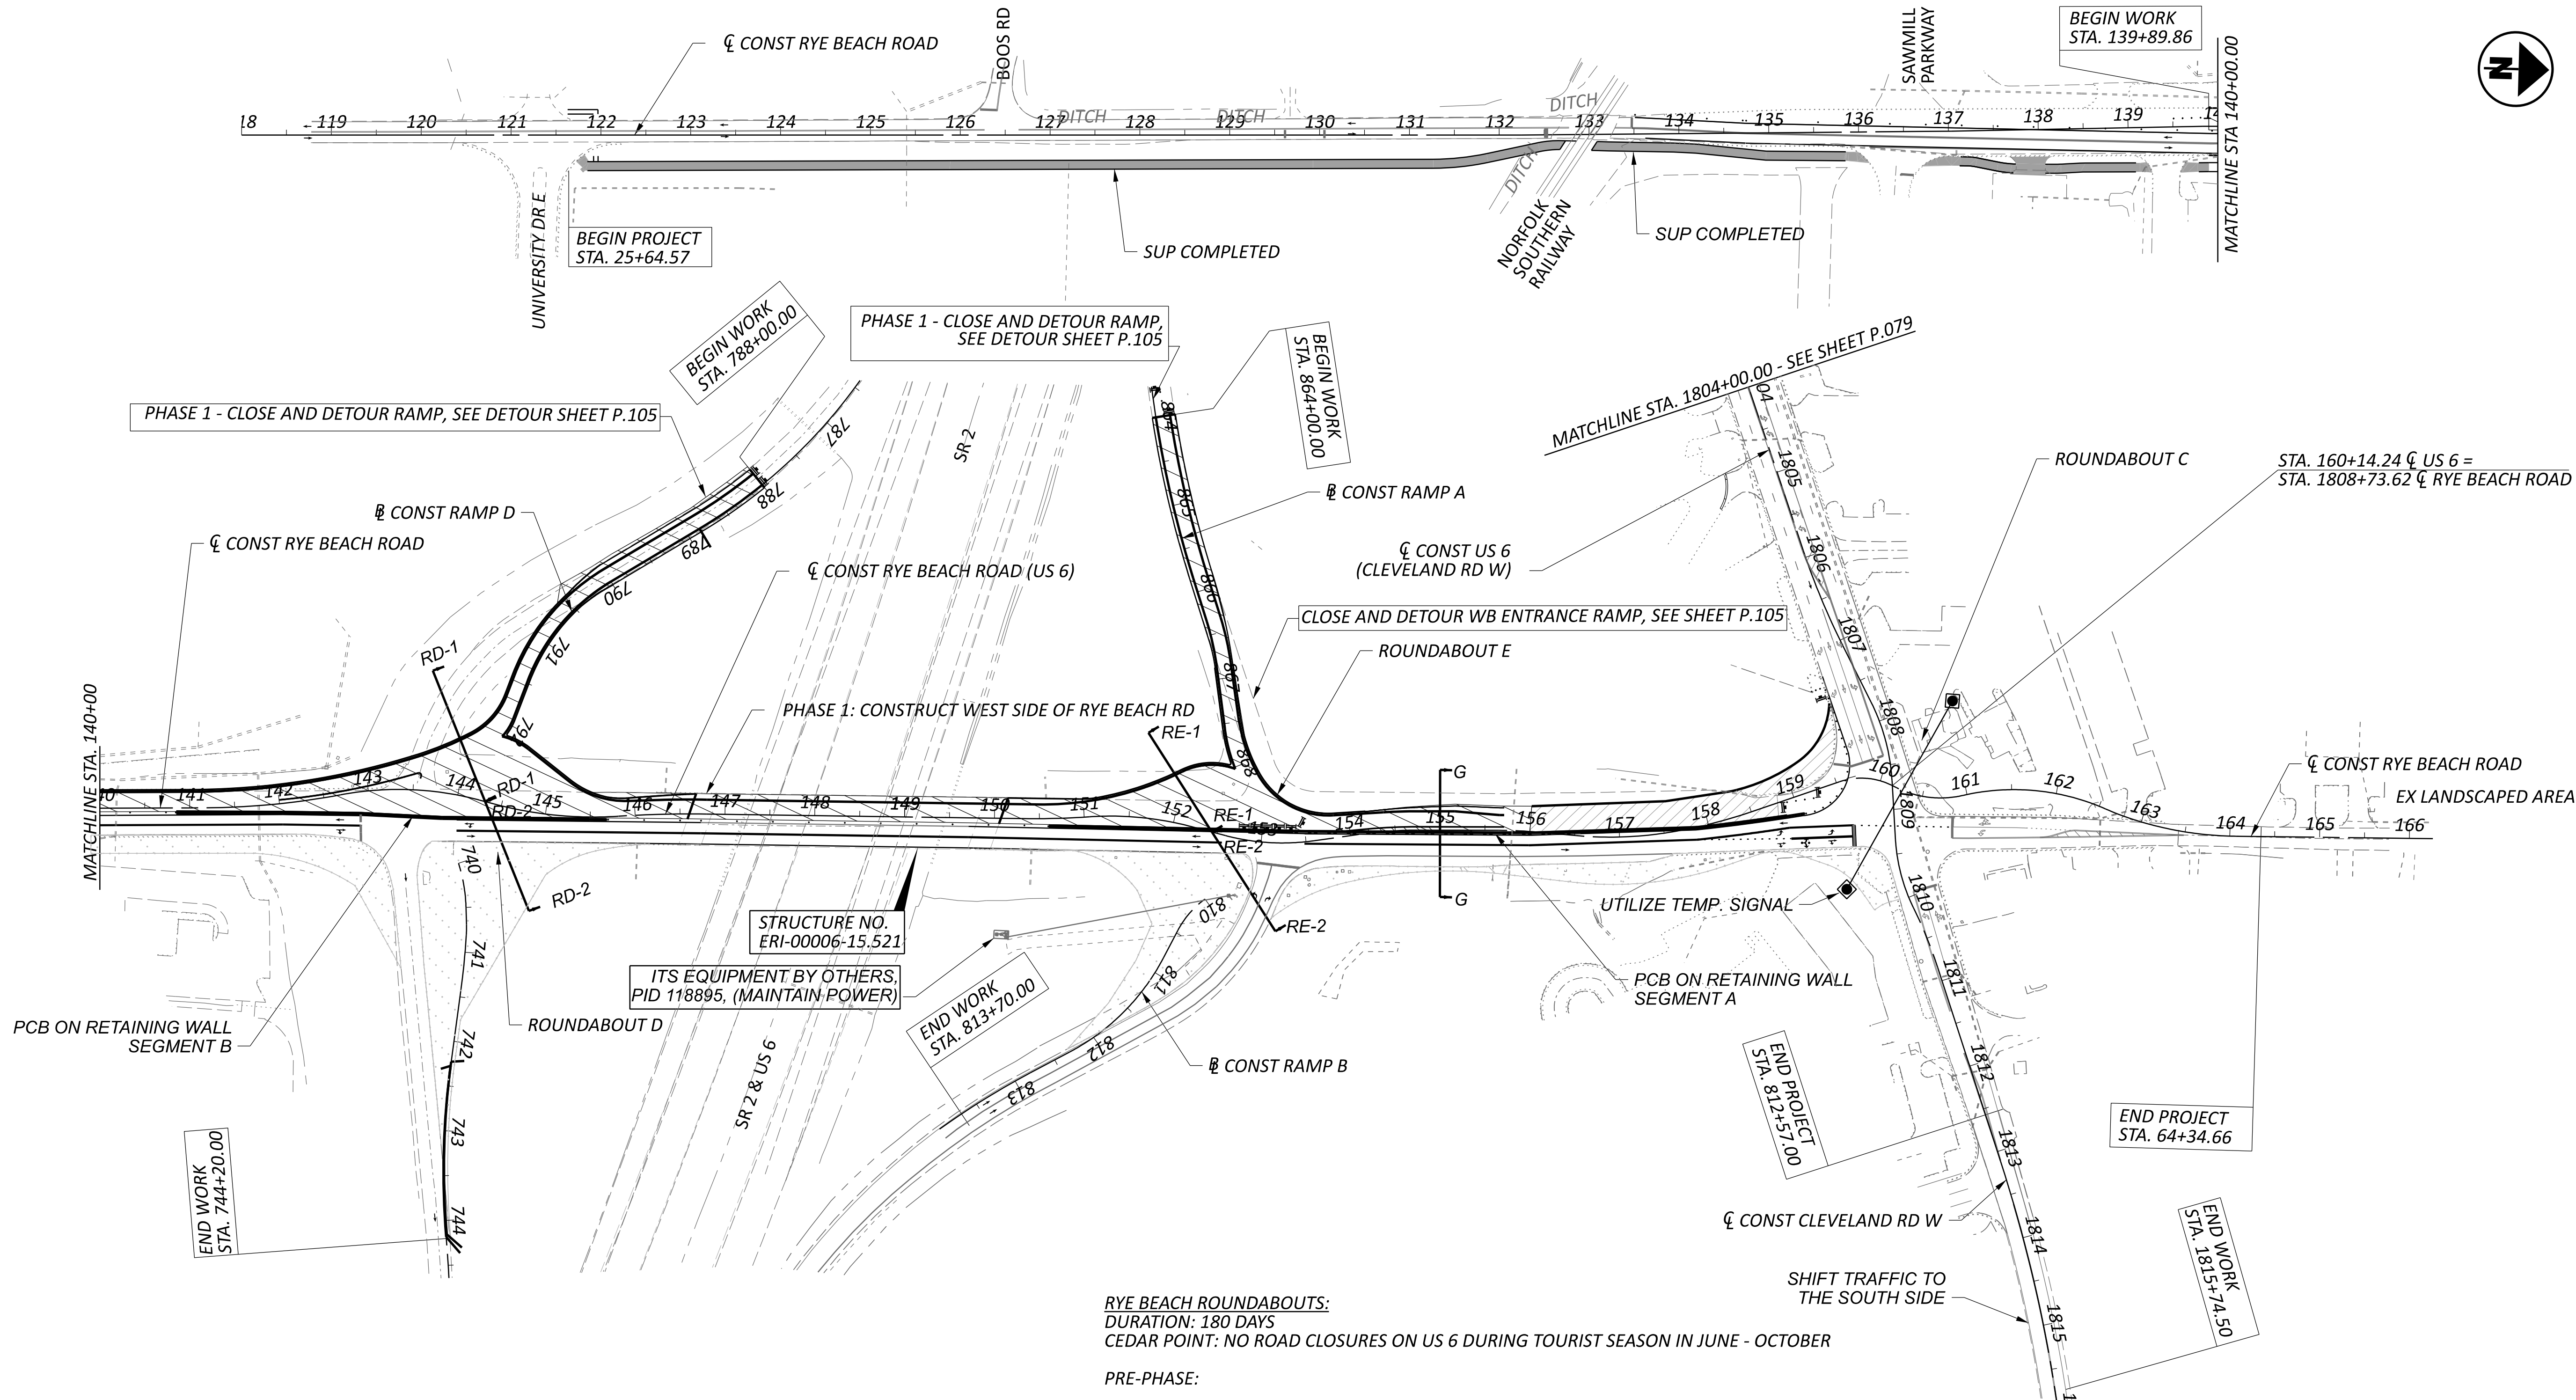

MOT SCHEMATIC PLAN - PHASE 1 (2026 CONSTRUCTION)
RYE BEACH ROAD STA 118+00.00 TO STA 166+00.00



DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID


116570

SHEET

P.082

TOTAL

782

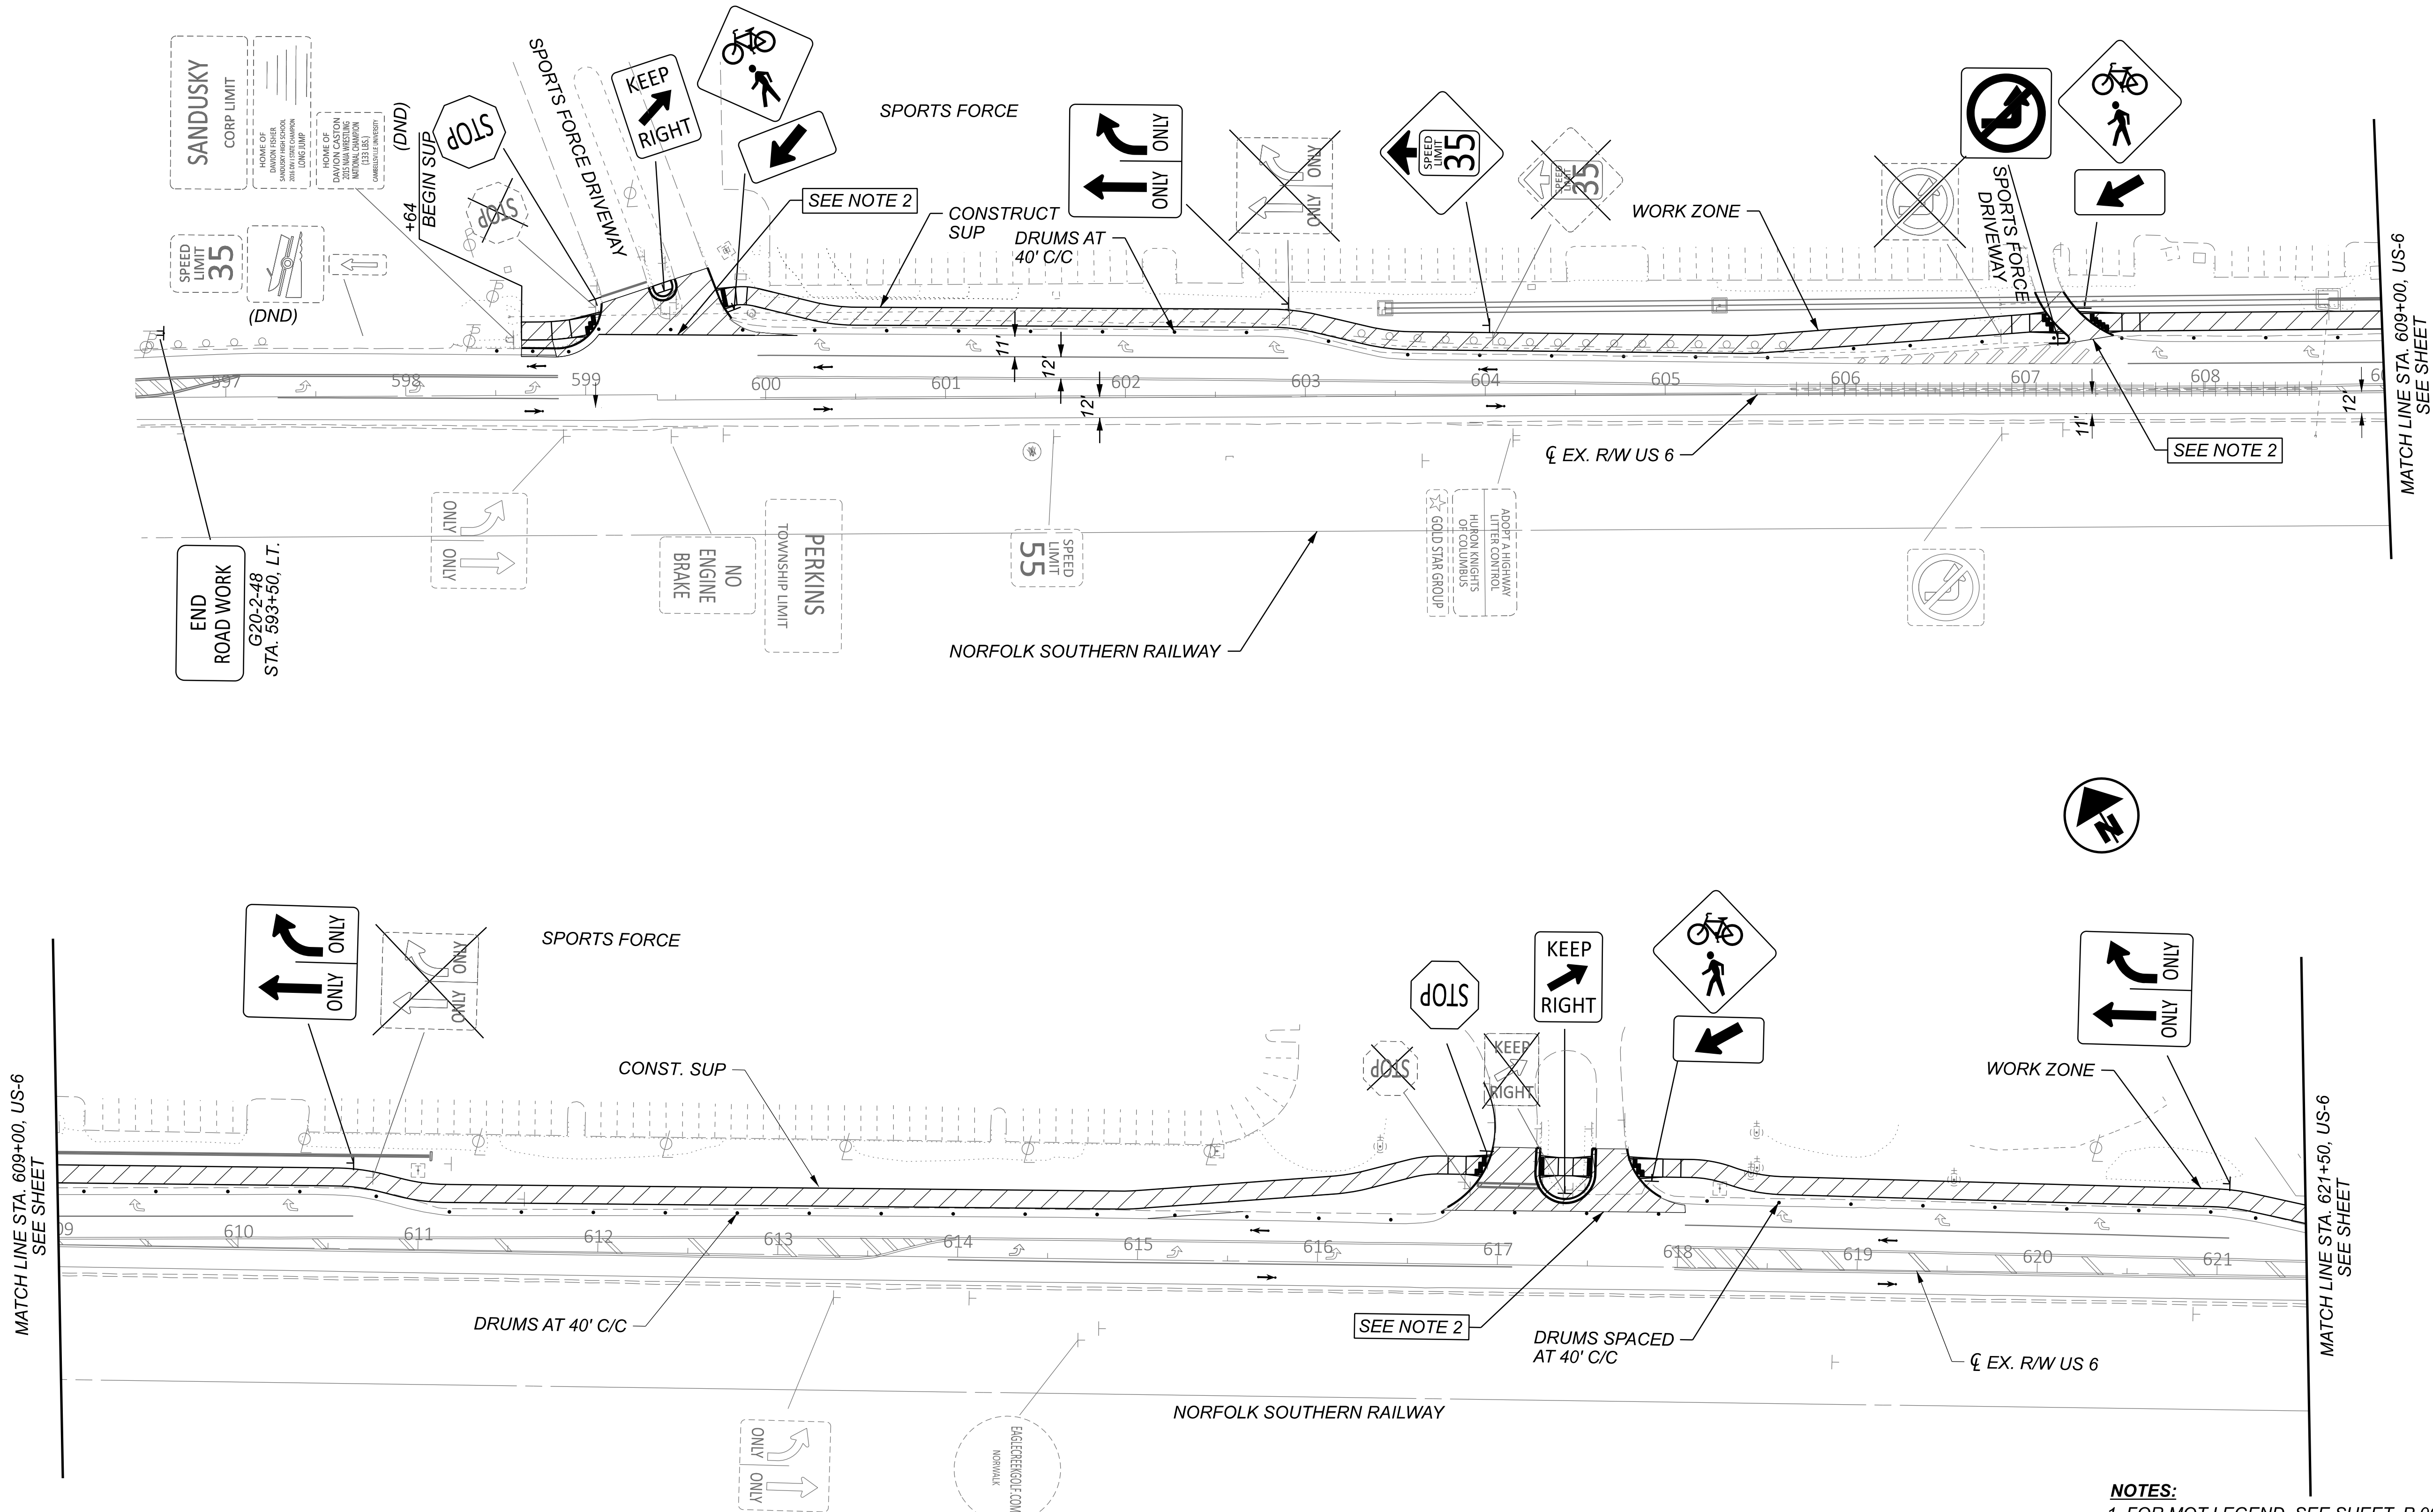

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - BEGIN PROJECT TO STA. 621+50

DESIGN AGENCY

TRANSYSTEMS
400 W. WATSONVILLE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER

SSA

REVIEWER

SS 02/28/24

PROJECT ID

116570


SHEET



P.124

TOTAL

782

HORIZONTAL
SCALE IN FEET




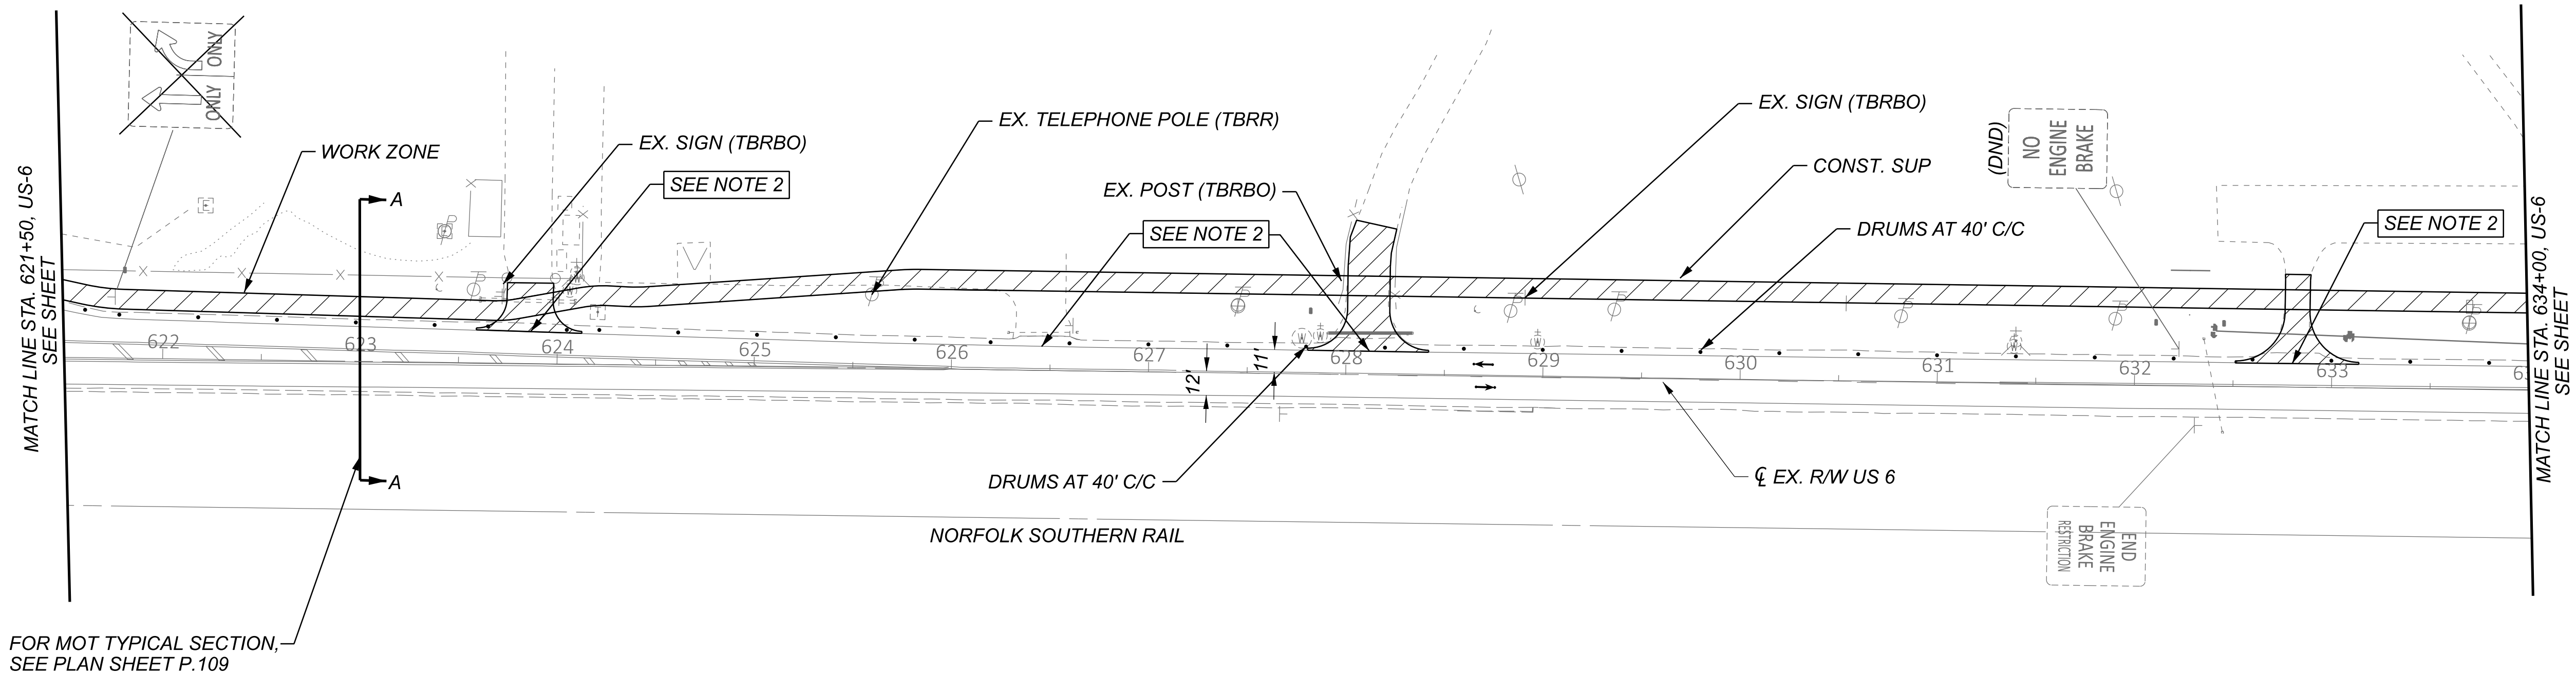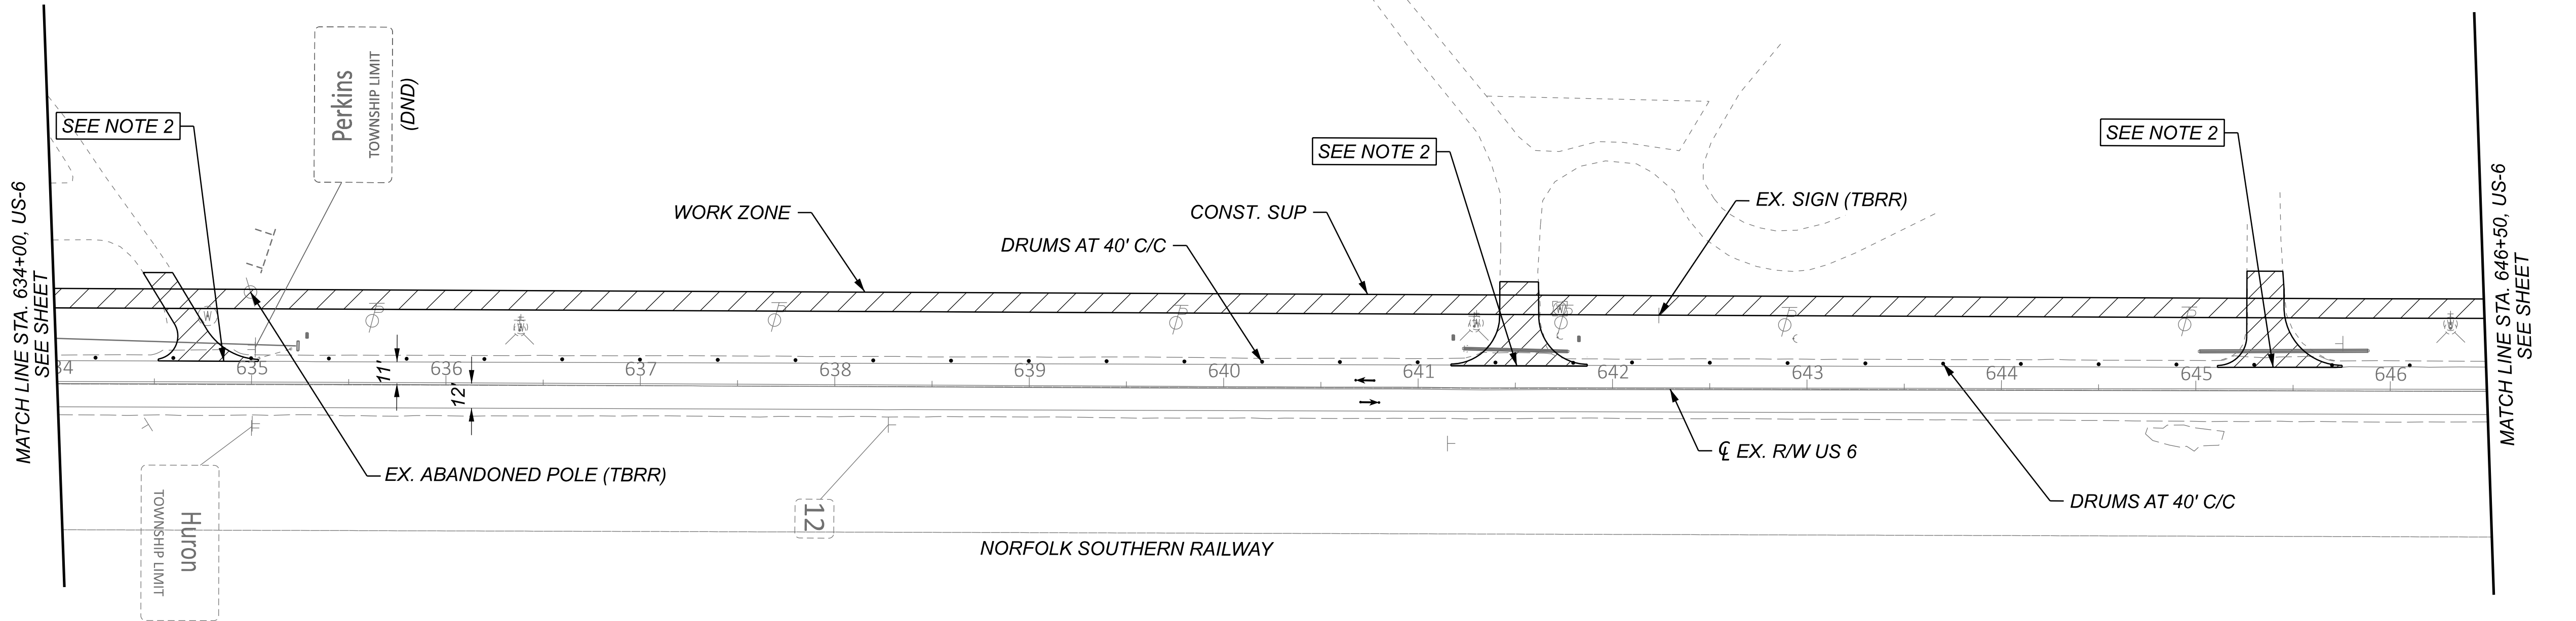


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS
PROJECT ID	02/28/24
SHEET	116570
TOTAL	782


MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 621+50.00 TO STA. 646+50.00



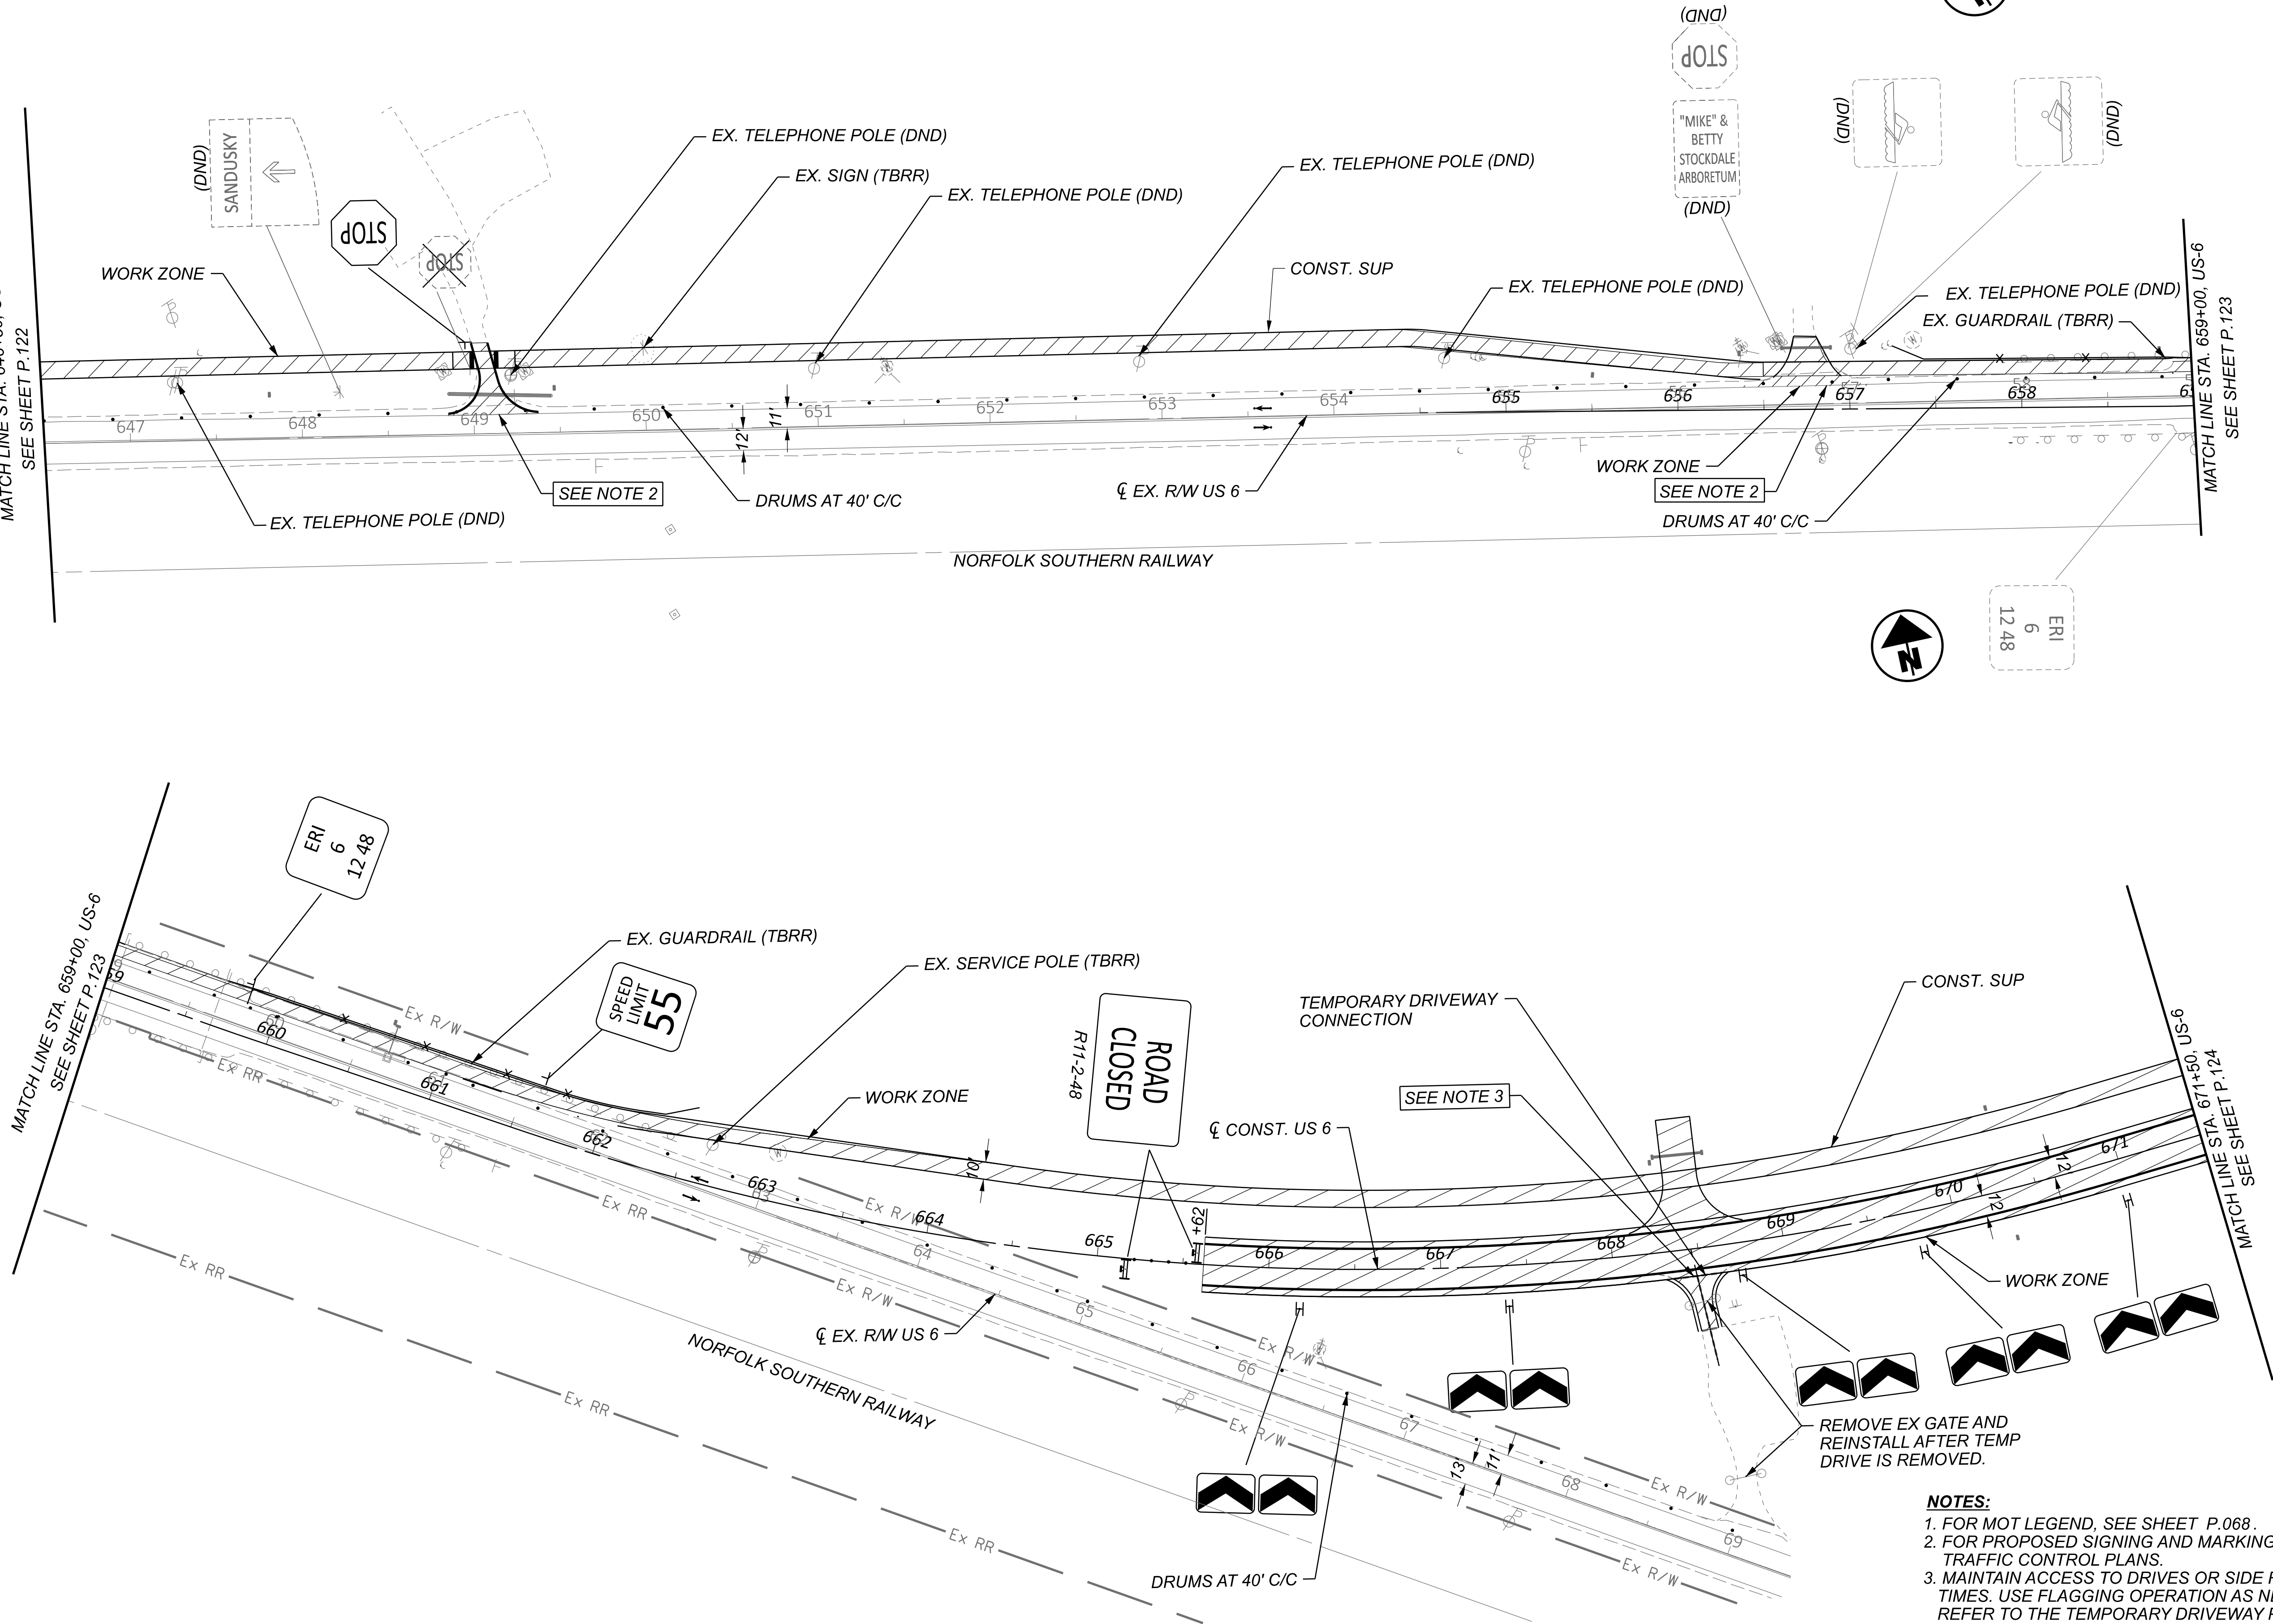

NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.


HORIZONTAL SCALE IN FEET 0 25 50 100	
MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION) US 6 - STA. 646+50.00 TO STA. 671+50.00	
DESIGN AGENCY TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER SSA	
REVIEWER SS 02/28/24	
PROJECT ID 116570	
SHEET P.126	TOTAL 782

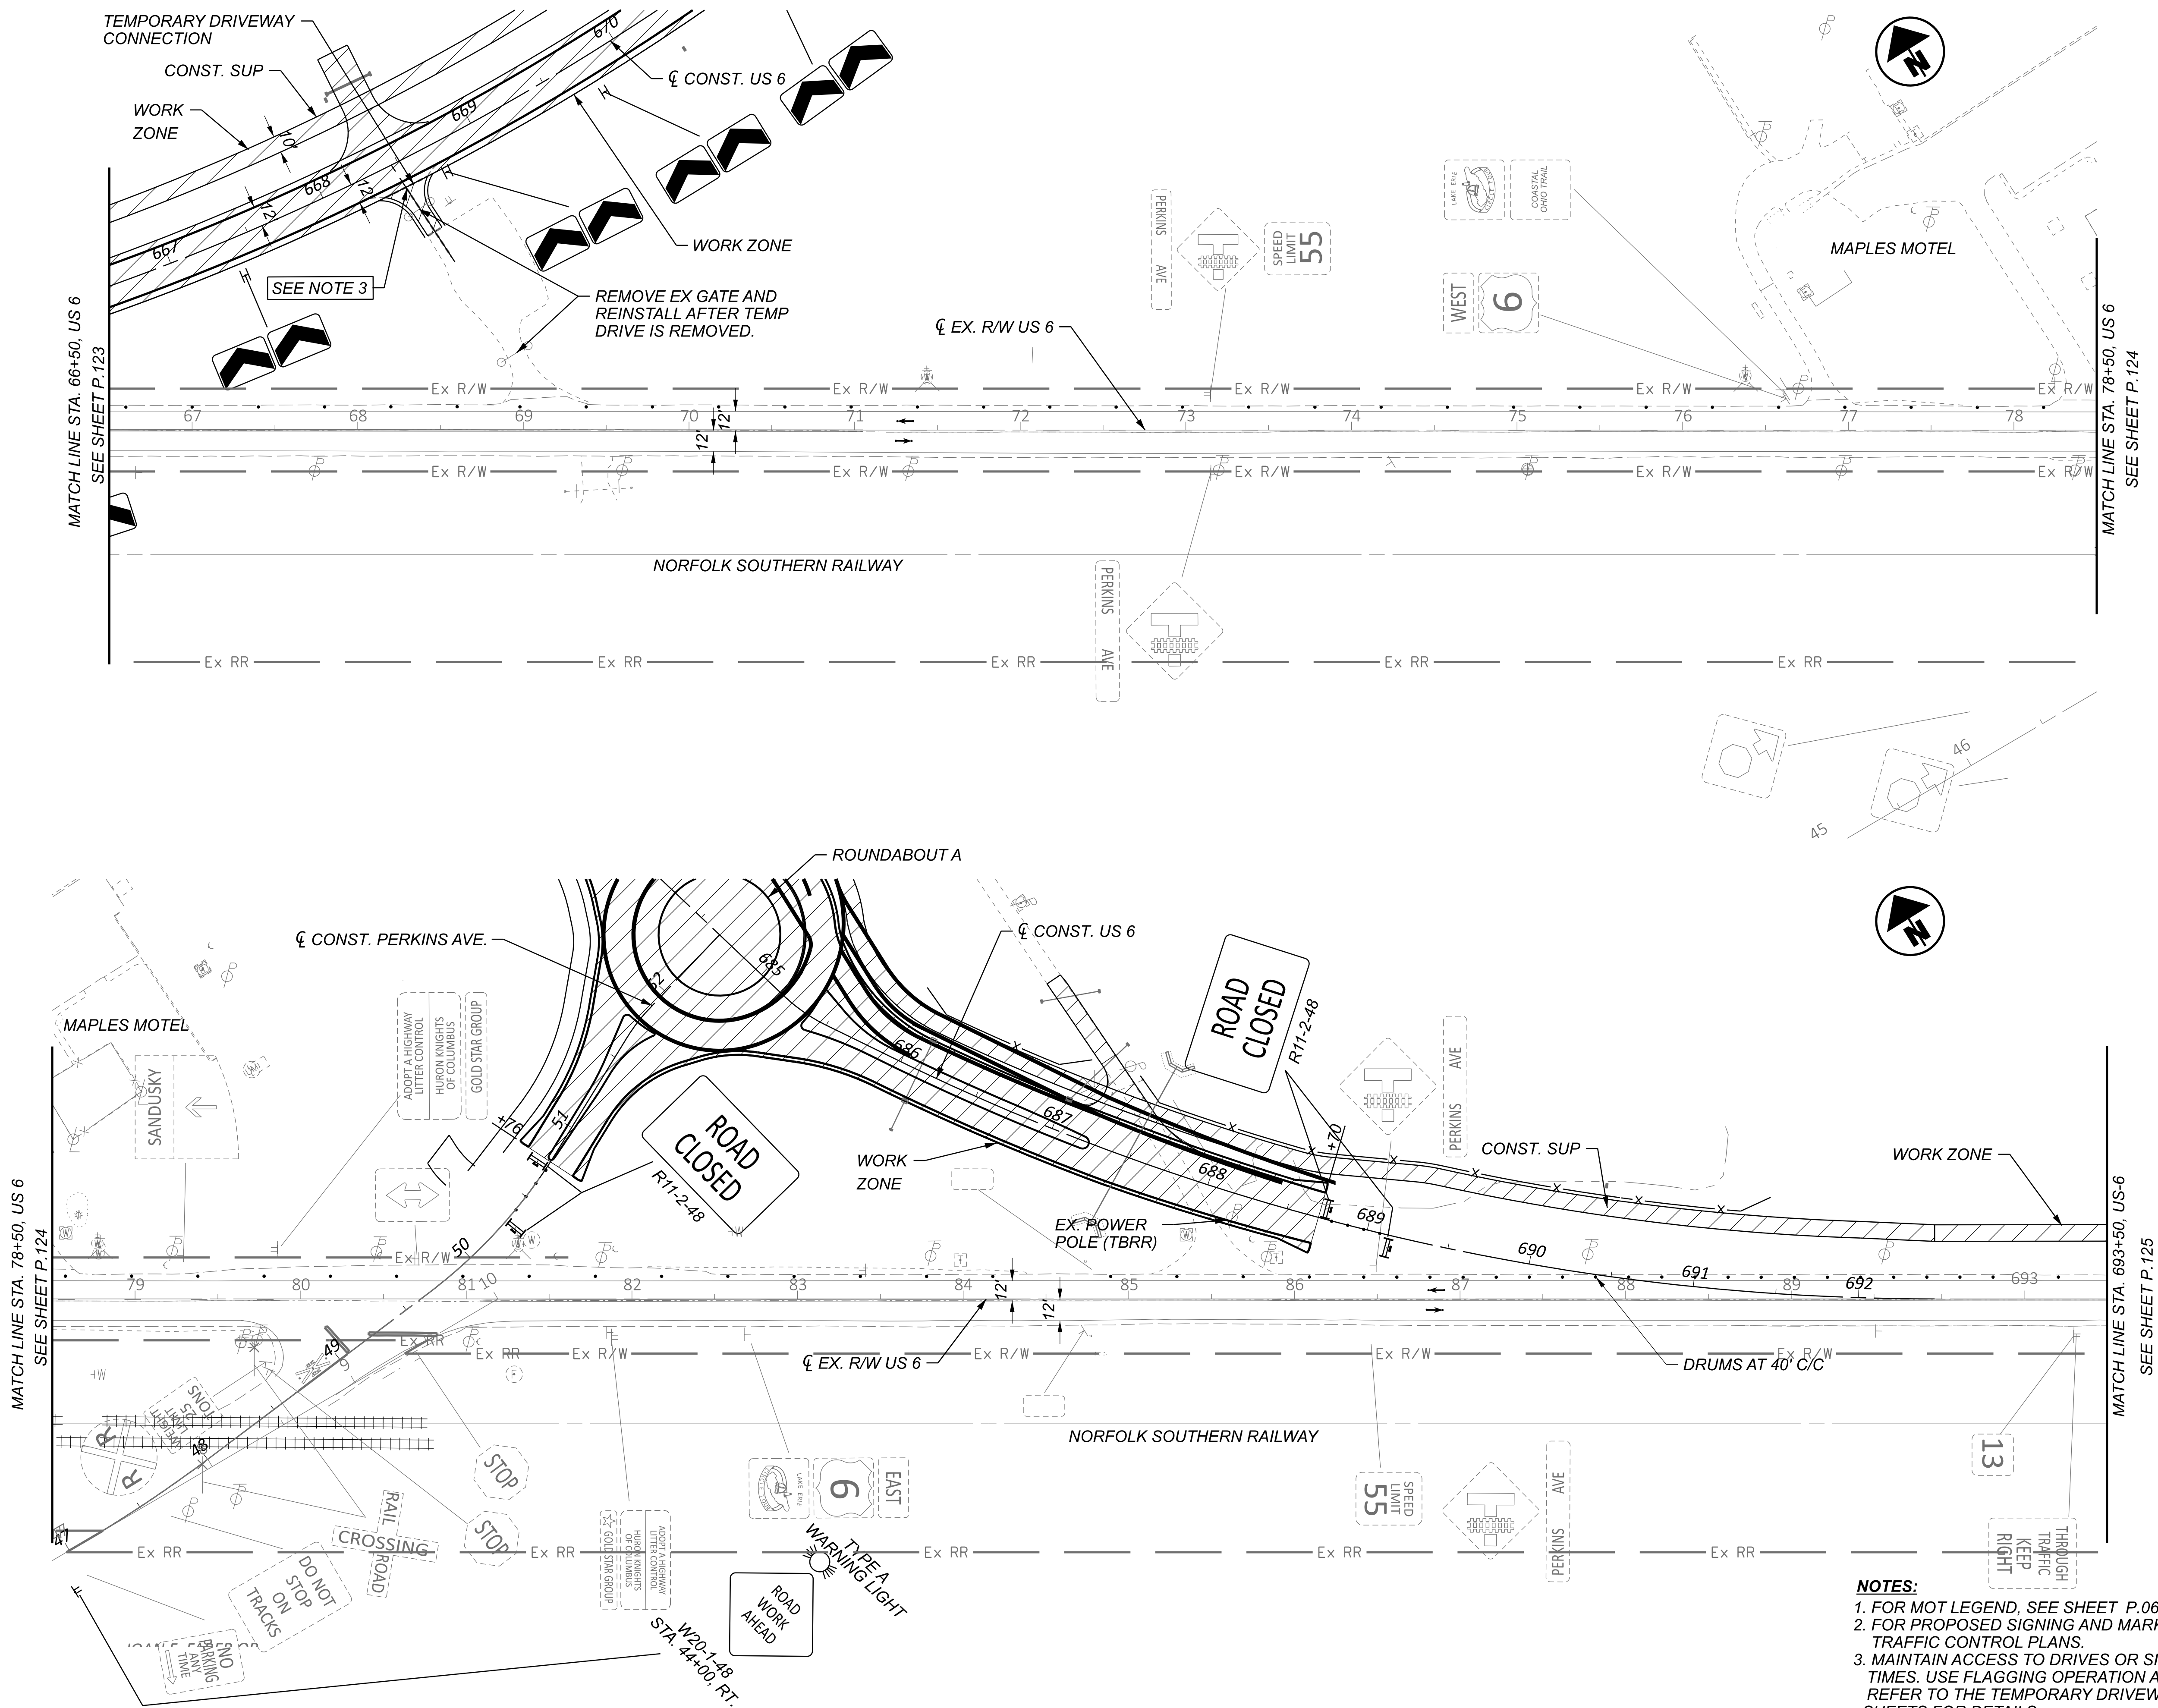


NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 67+00.00 EX. US 6 TO 693+50.00 CONST. US 6 SUP

DESIGN AGENCY	
TRANSYSTEMS	
400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.127	TOTAL 782

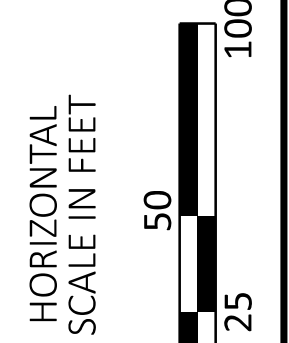

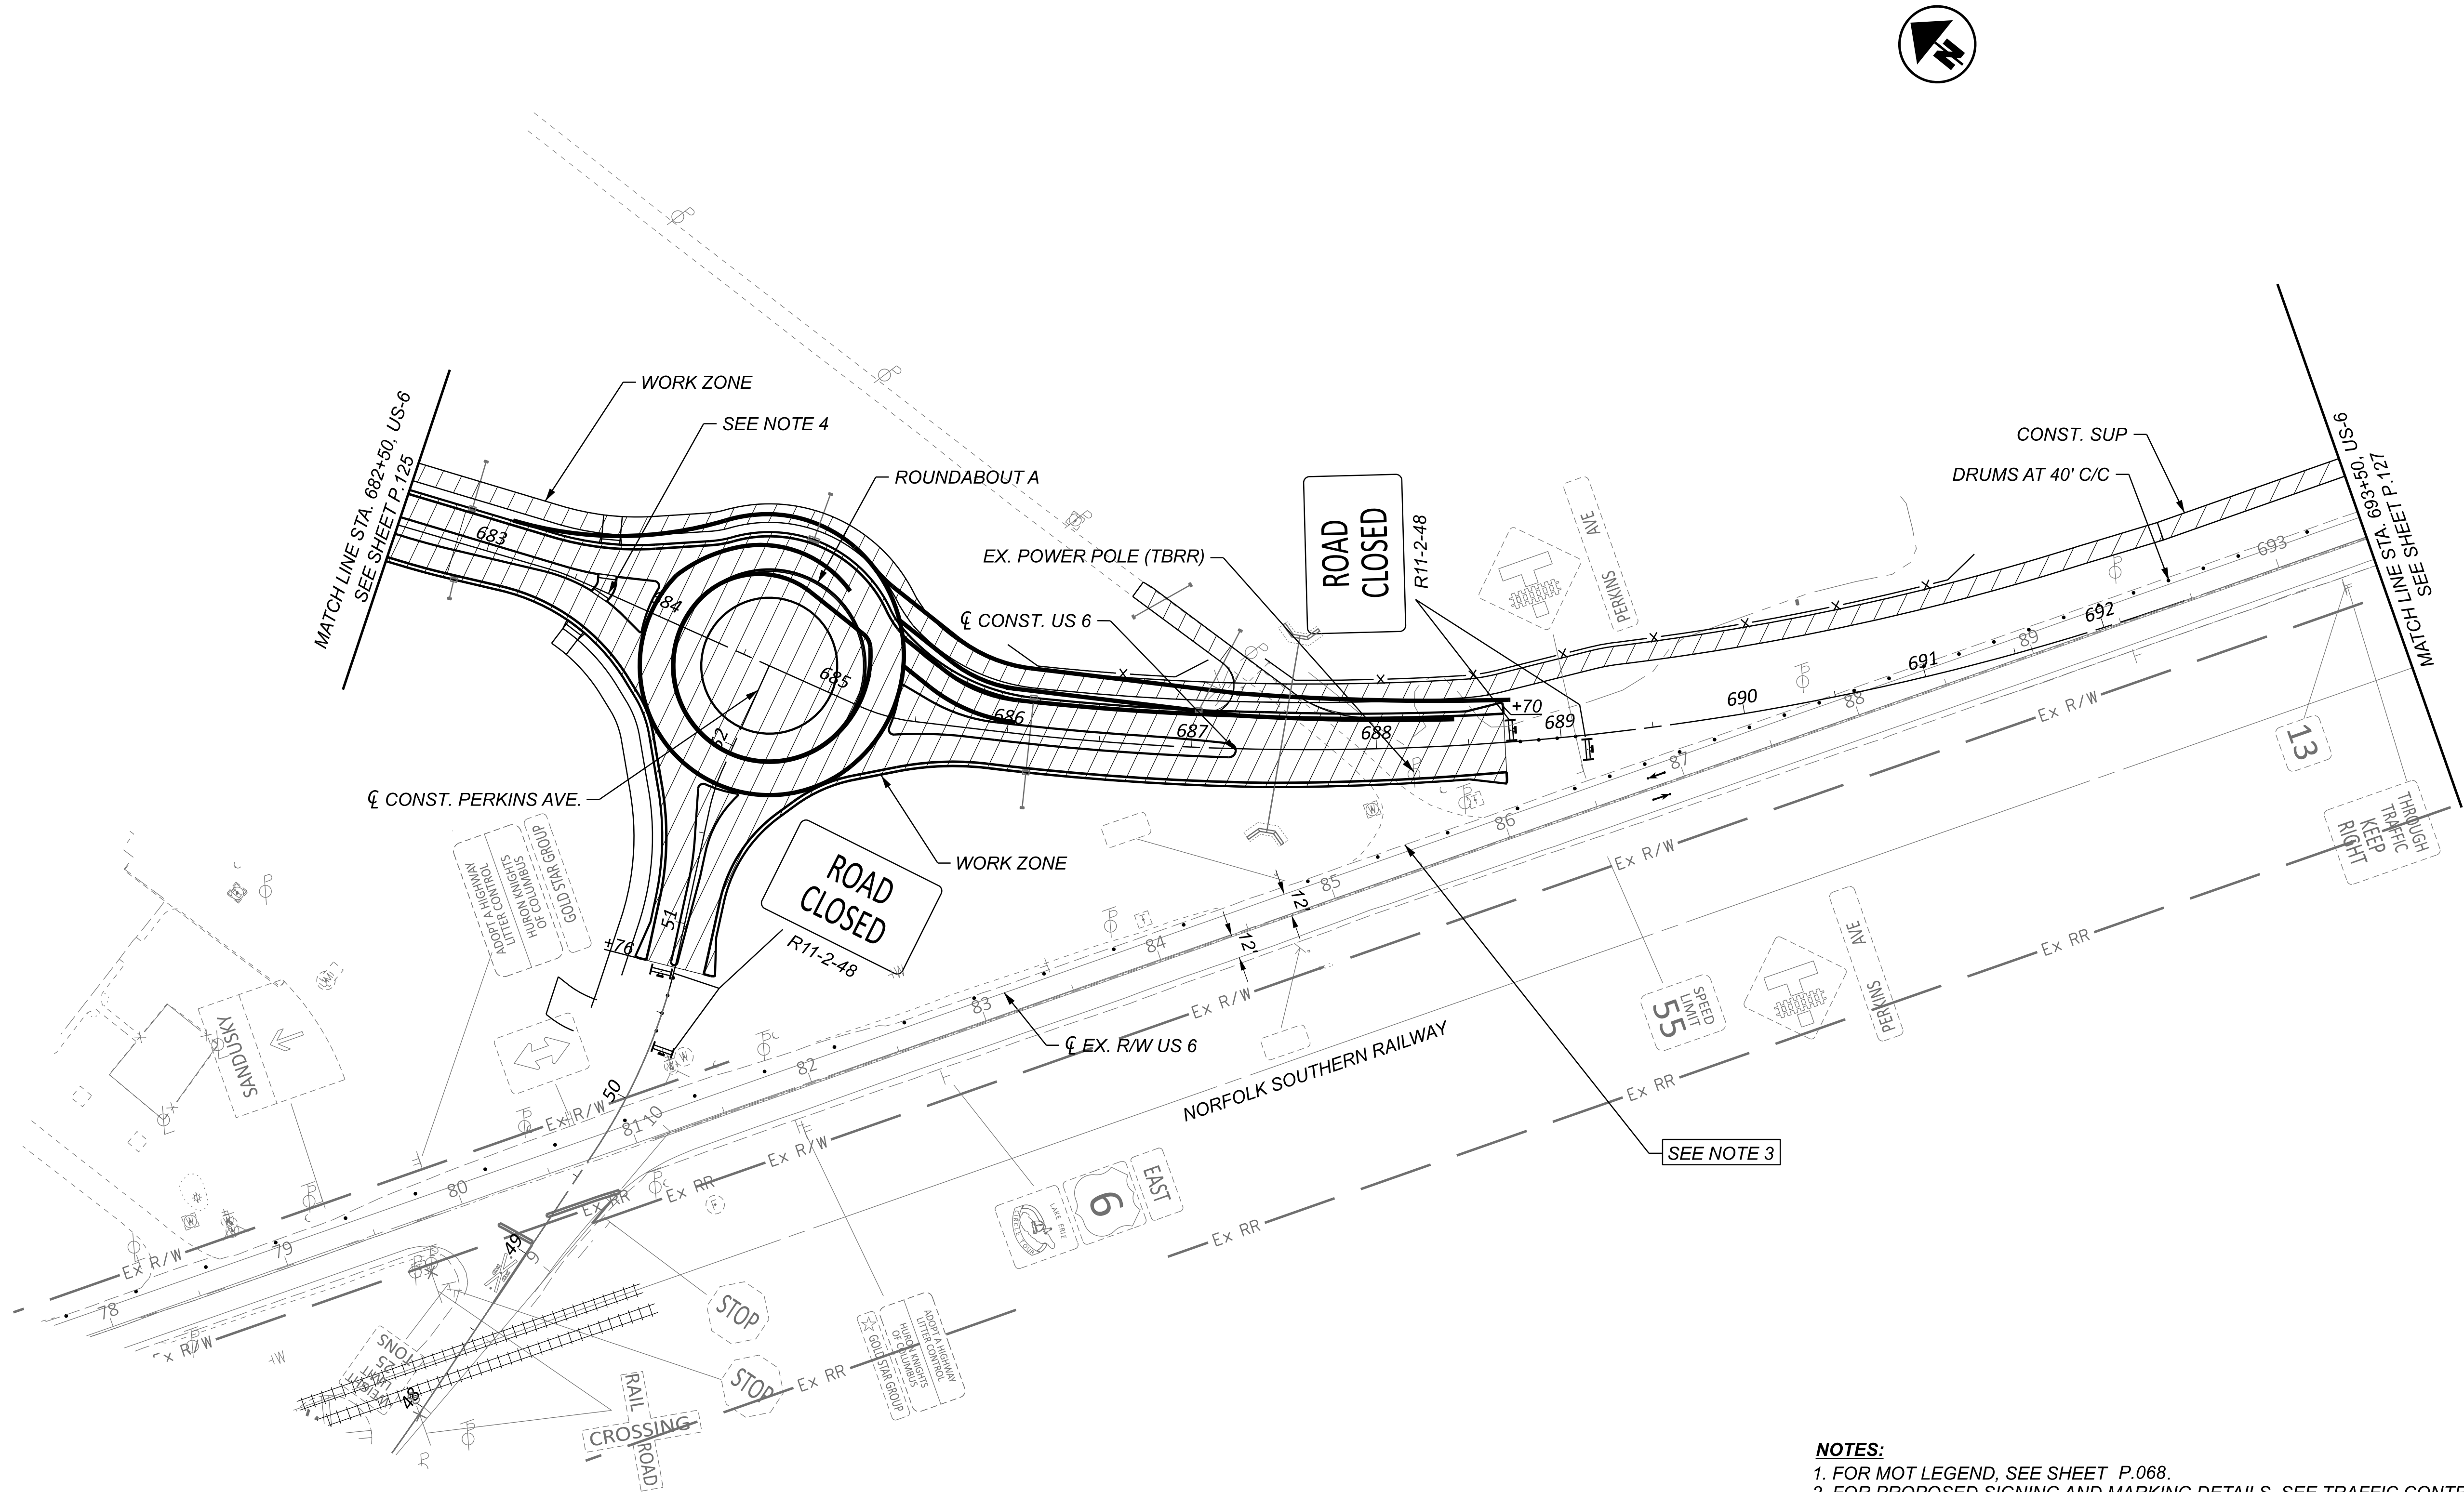


NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.
REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.
4. SOIL STABILIZATION WILL BE REQUIRED ALONG CENTERLINE OF CONSTRUCTION US 6 STA. 681+50 TO 692+50 DUE TO SOFT SOILS ENCOUNTERED IN THE FIELD. THE FILL UNDER THE PROPOSED ROADWAY AND ESPECIALLY THE PROPOSED BOX CULVERT AT STA. 687+50 WILL LIKELY NEED TO BE PRE-LOADED TO ACHIEVE AN ACCEPTABLE BEARING CAPACITY TO PREVENT SETTLEMENT. PRE-LOADING THE FILL REQUIRES MORE TIME DURING CONSTRUCTION, AND IT IS RECOMMENDED THAT THIS AREA BE PRIORITIZED AT THE BEGINNING OF THE CONSTRUCTION SEQUENCING.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 683+00.00 TO STA. 693+50.00


TRANSYSTEMS
400 W. WATSON BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	P.129
TOTAL	782




NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.
4. SOIL STABILIZATION WILL BE REQUIRED ALONG CENTERLINE OF CONSTRUCTION US 6 STA. 681+50 TO 692+50 DUE TO SOFT SOILS ENCOUNTERED IN THE FIELD. THE FILL UNDER THE PROPOSED ROADWAY AND ESPECIALLY THE PROPOSED BOX CULVERT AT STA. 687+50 WILL LIKELY NEED TO BE PRE-LOADED TO ACHIEVE AN ACCEPTABLE BEARING CAPACITY TO PREVENT SETTLEMENT. PRE-LOADING THE FILL REQUIRES MORE TIME DURING CONSTRUCTION, AND IT IS RECOMMENDED THAT THIS AREA BE PRIORITIZED AT THE BEGINNING OF THE CONSTRUCTION SEQUENCING.

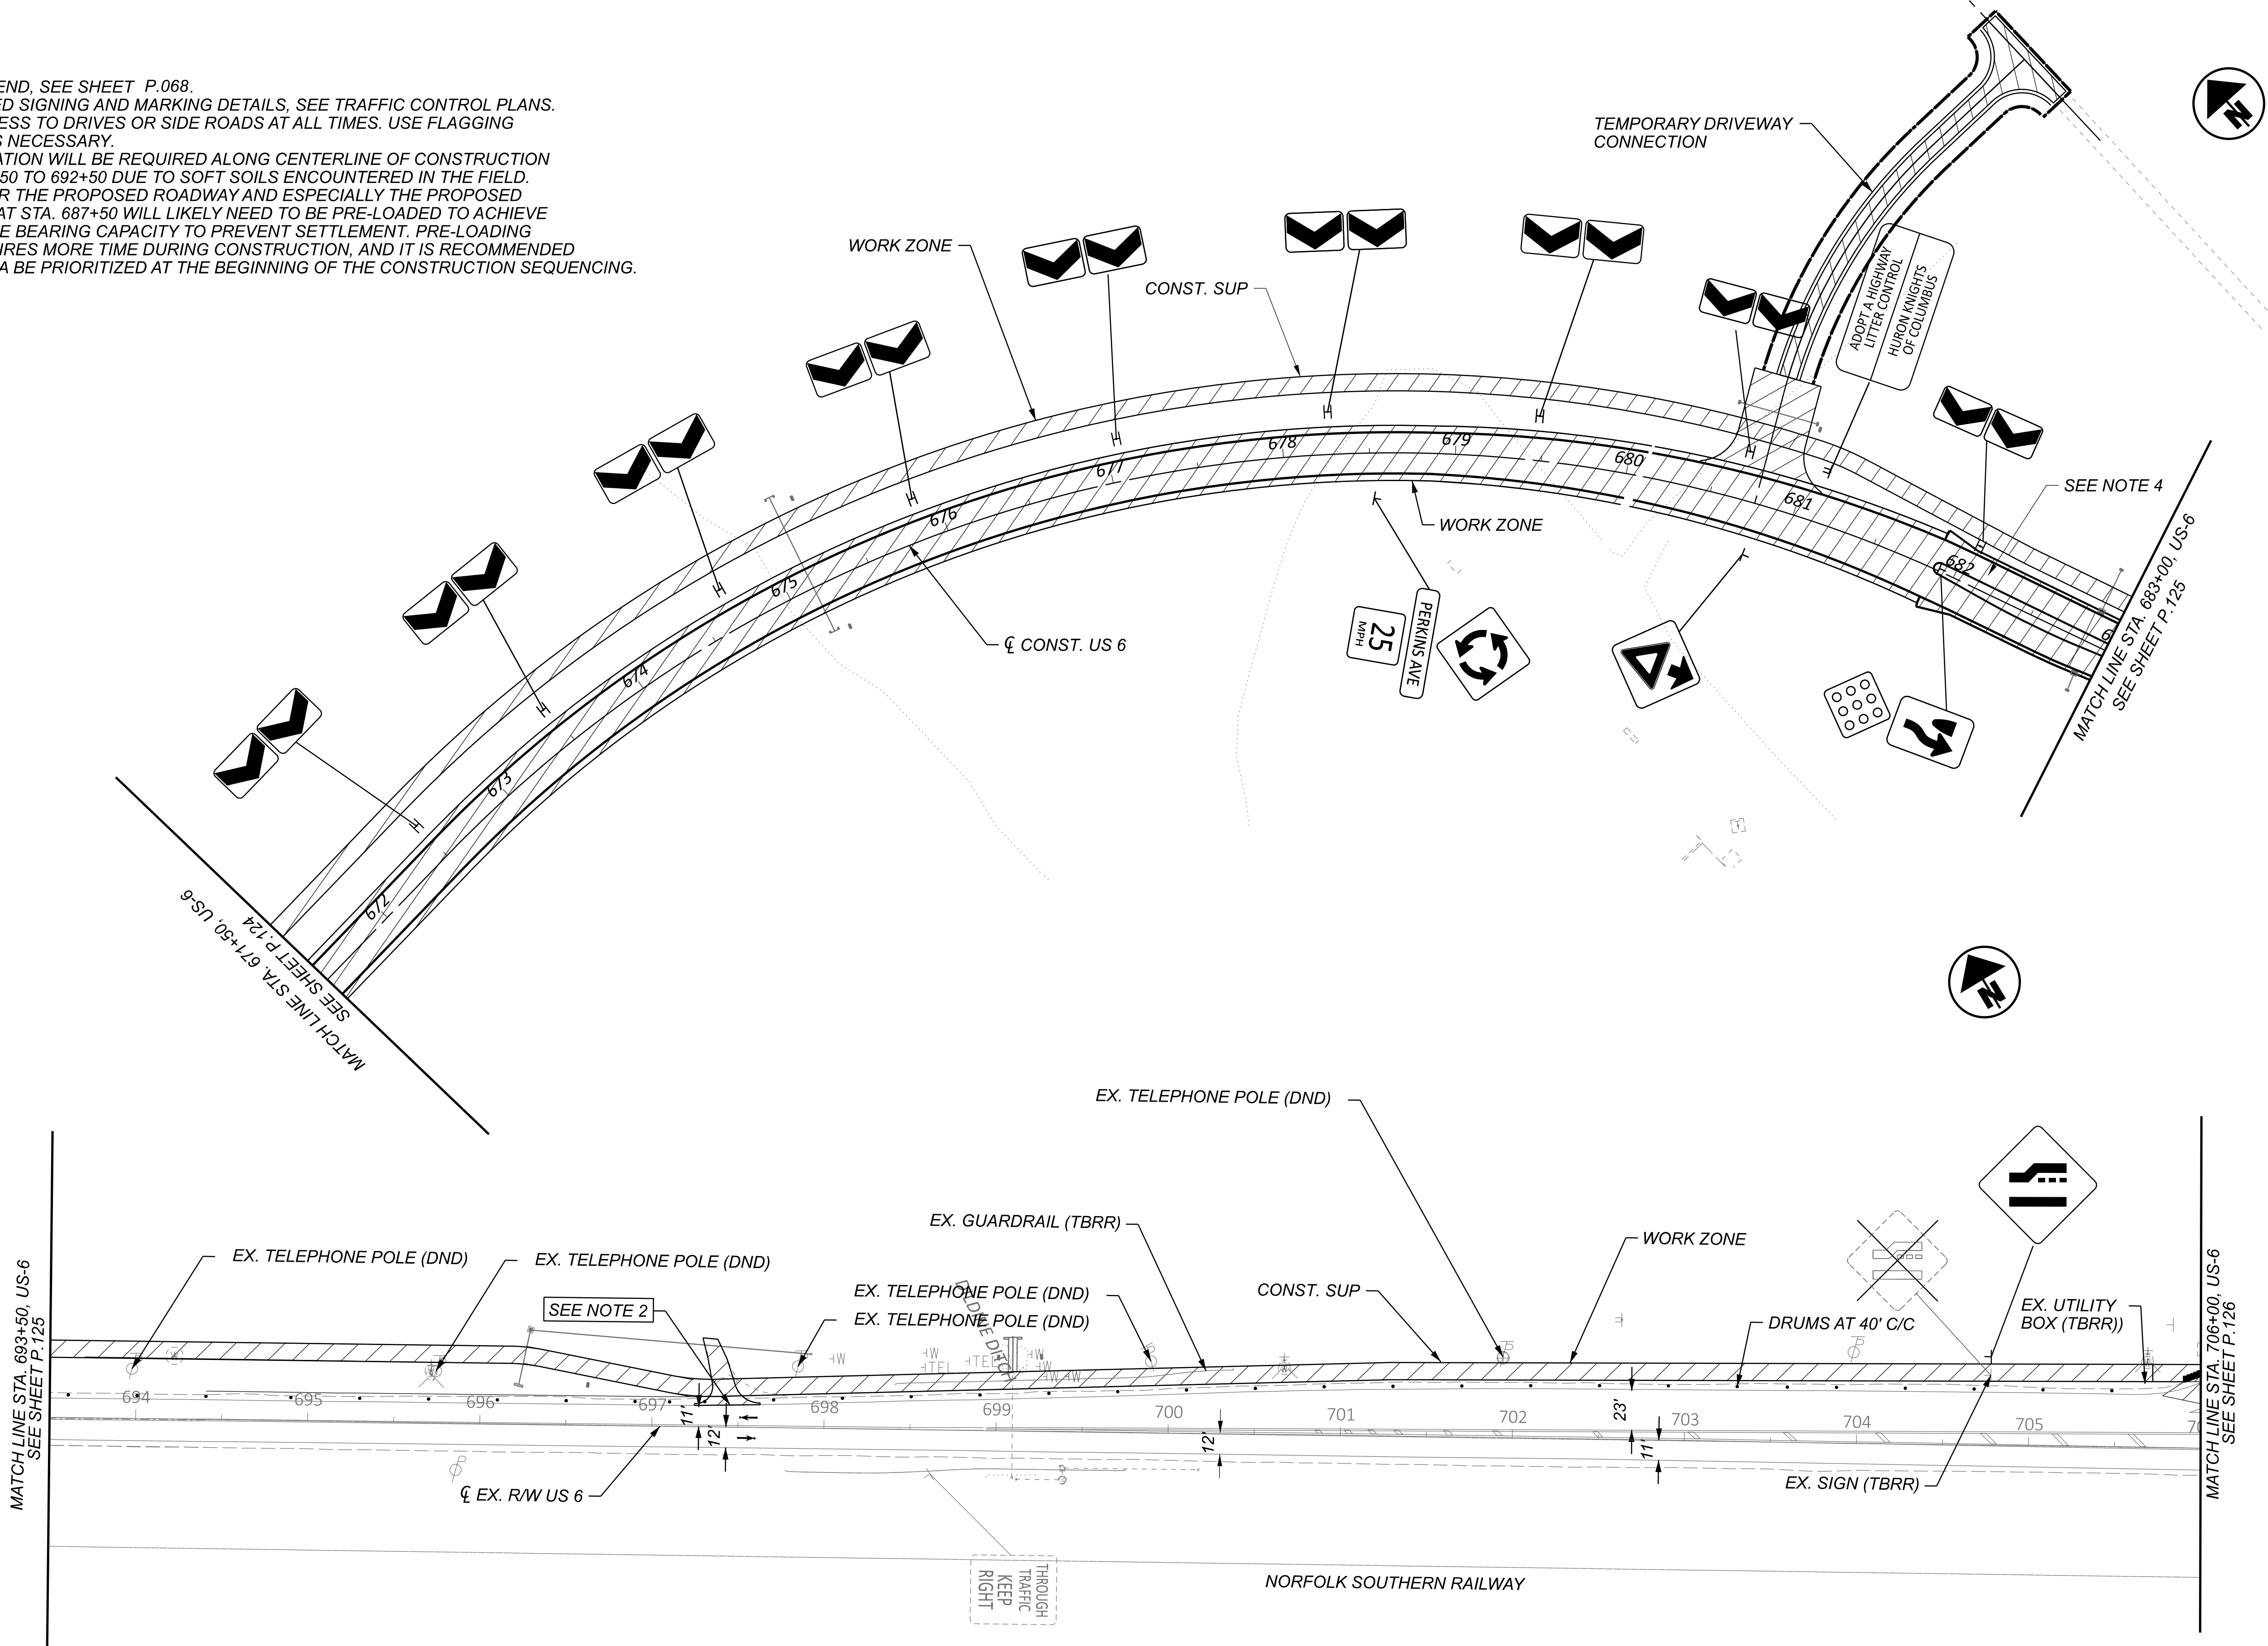

MODEL: CLP_SUP 1 - Plan 12-13 [Sheet] PAPER SIZE: 34x22 (in) DATE: 6/9/2025 TIME: 5:34:01 PM USER: ssadusei
 pw:\volhiodot-pw.bentley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\Erle\116570402-Engineering_TransSystems\WOT\Sheets\116570_MP000_2026.dgn




DESIGN AGENCY
TRANSYSTEMS
 400 W. NATIONWIDE BLVD., STE. 225
 COLUMBUS, OHIO 43215


DESIGNER
 SSA

REVIEWER
 SS 02/28/

PROJECT ID
 116570

SHEET TOTAL
 P.130 | 78

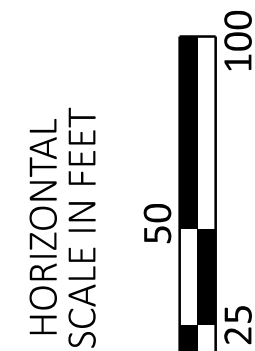


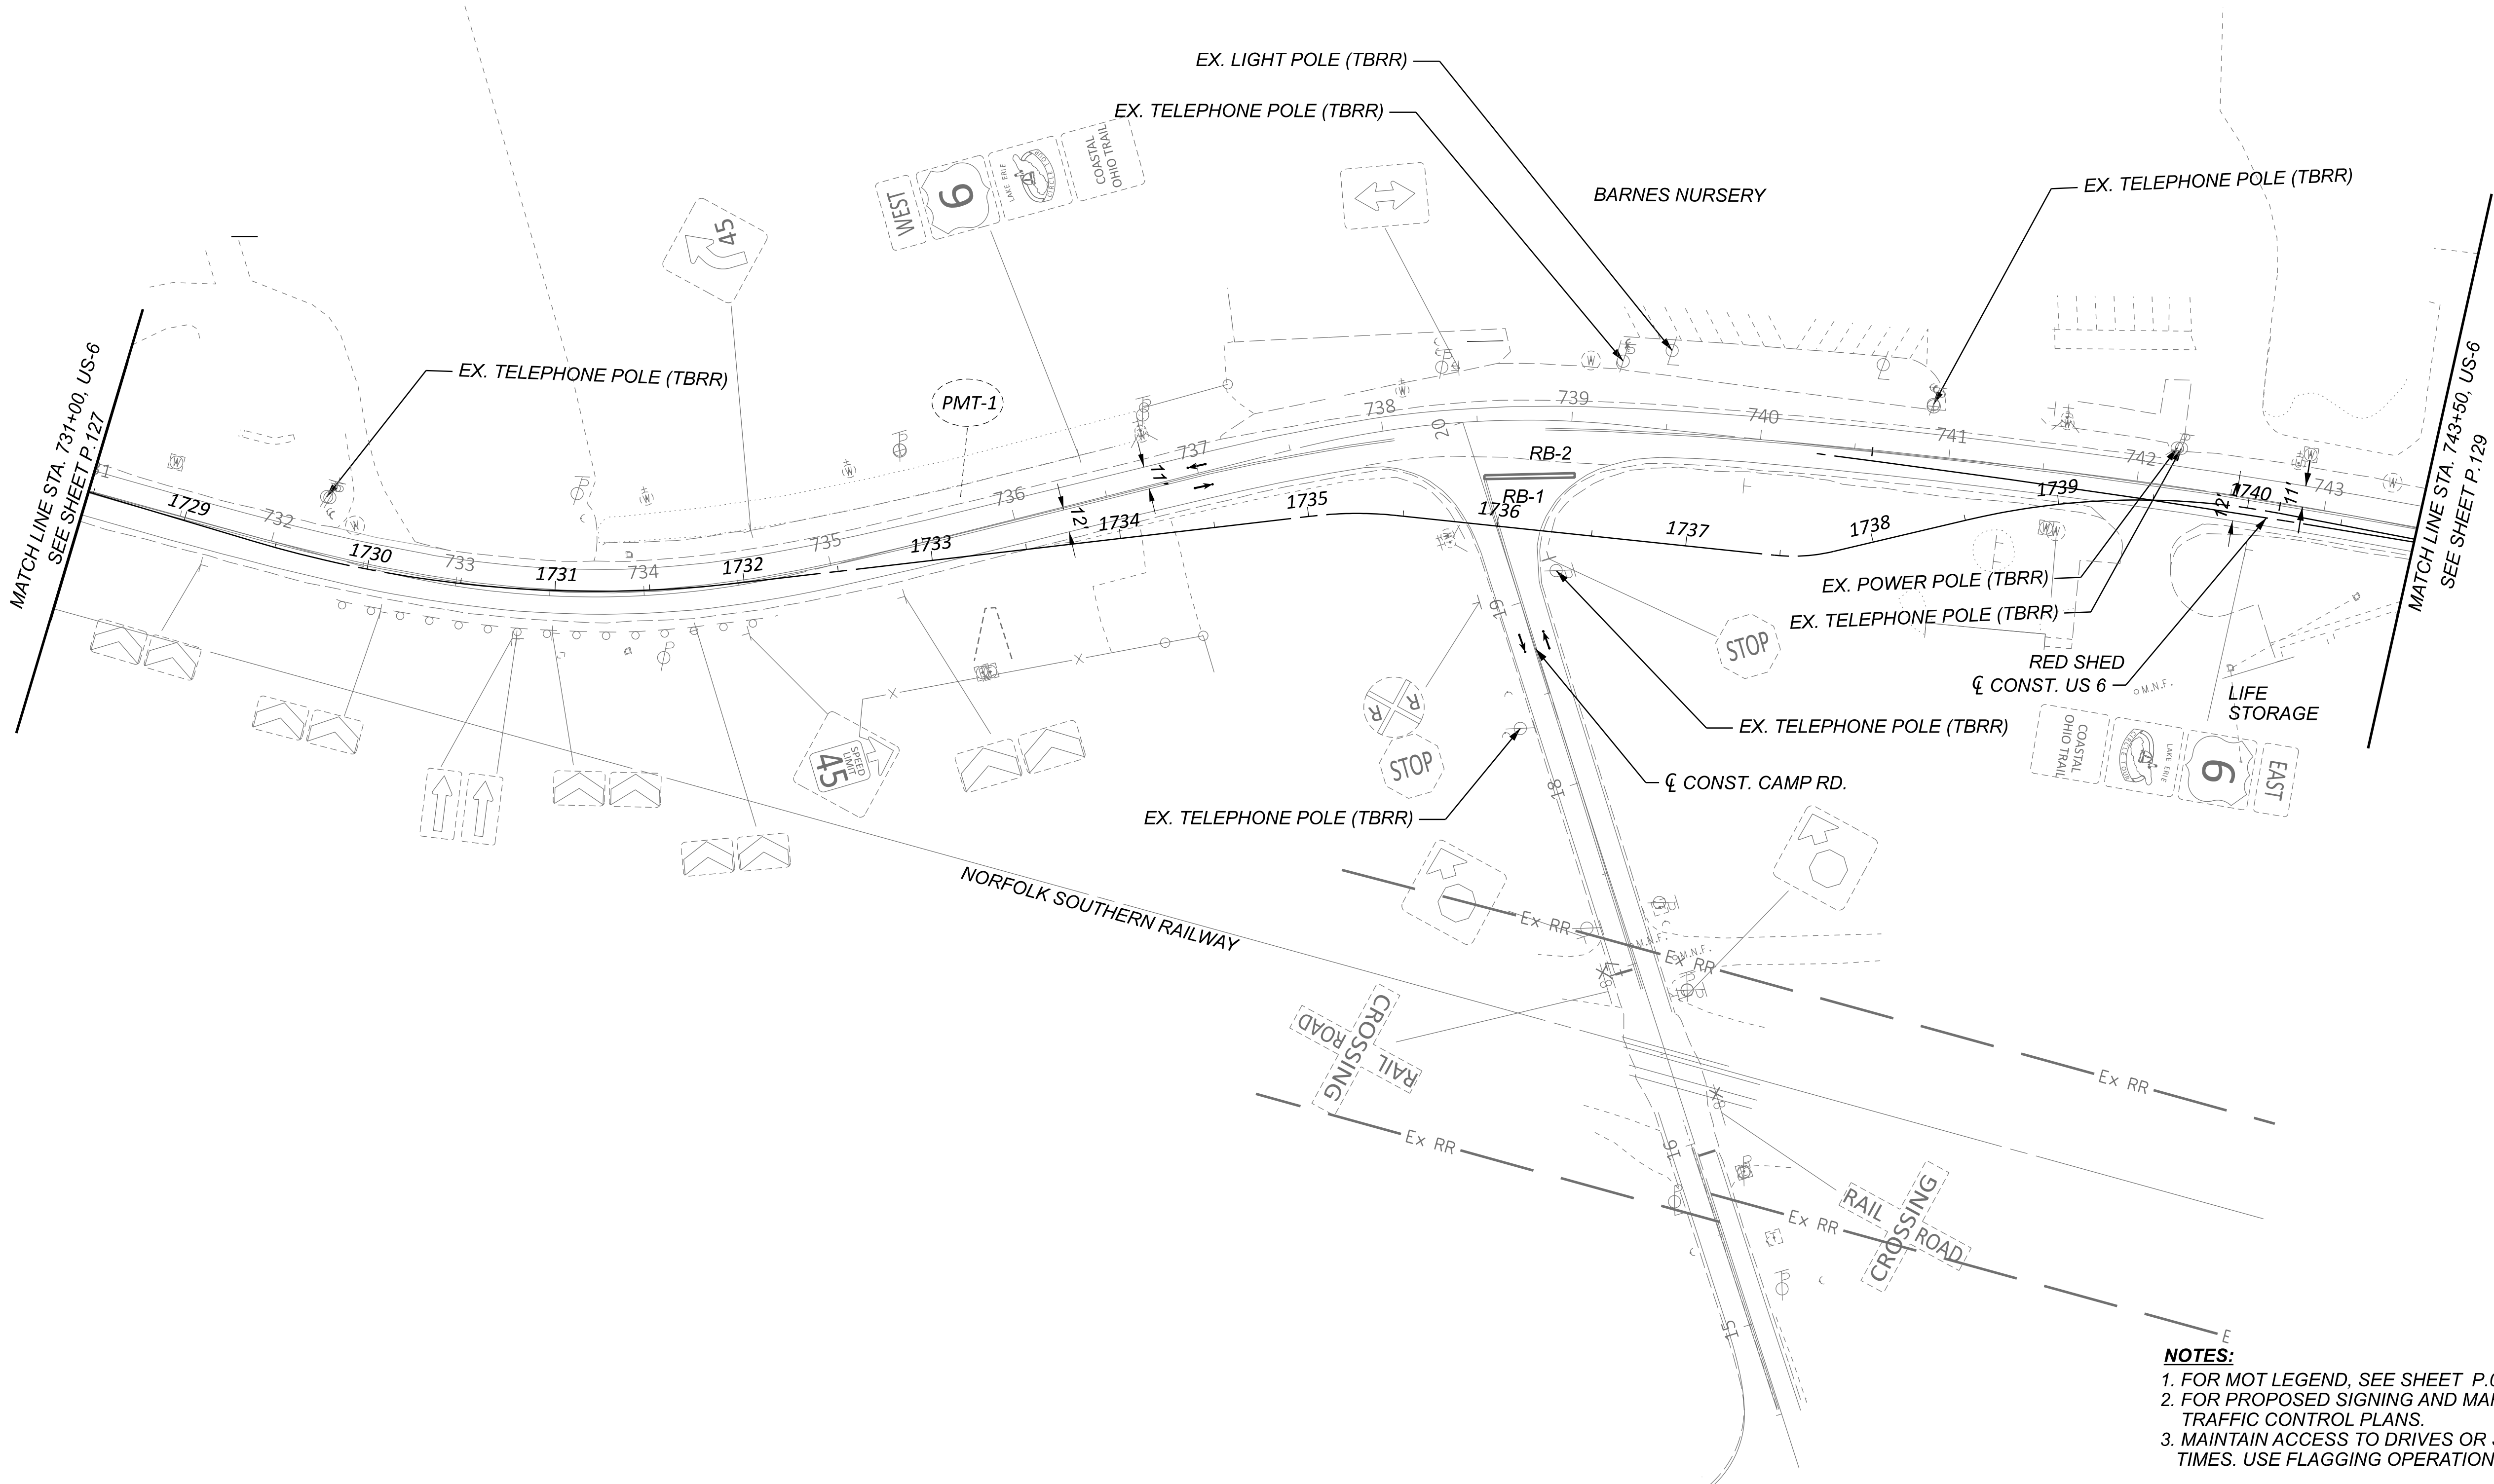

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 731+00.00 TO STA. 743+50.00

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	TOTAL
P.131	782



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 1 - Plan 15-16 [Sheet] PAPER SIZE: 34x22 (in) DATE: 6/9/2025 TIME: 5:34:05 PM USER: ssadusei
 \\pw\ohiodor-pw.bentley.com:ohiodor-pw-02\Documents\01 Active Projects\District 03\Erie\116570\402-Engineering_TransSystems\TransSystems\MOT\Sheets\116570_MP000_2026.dgn

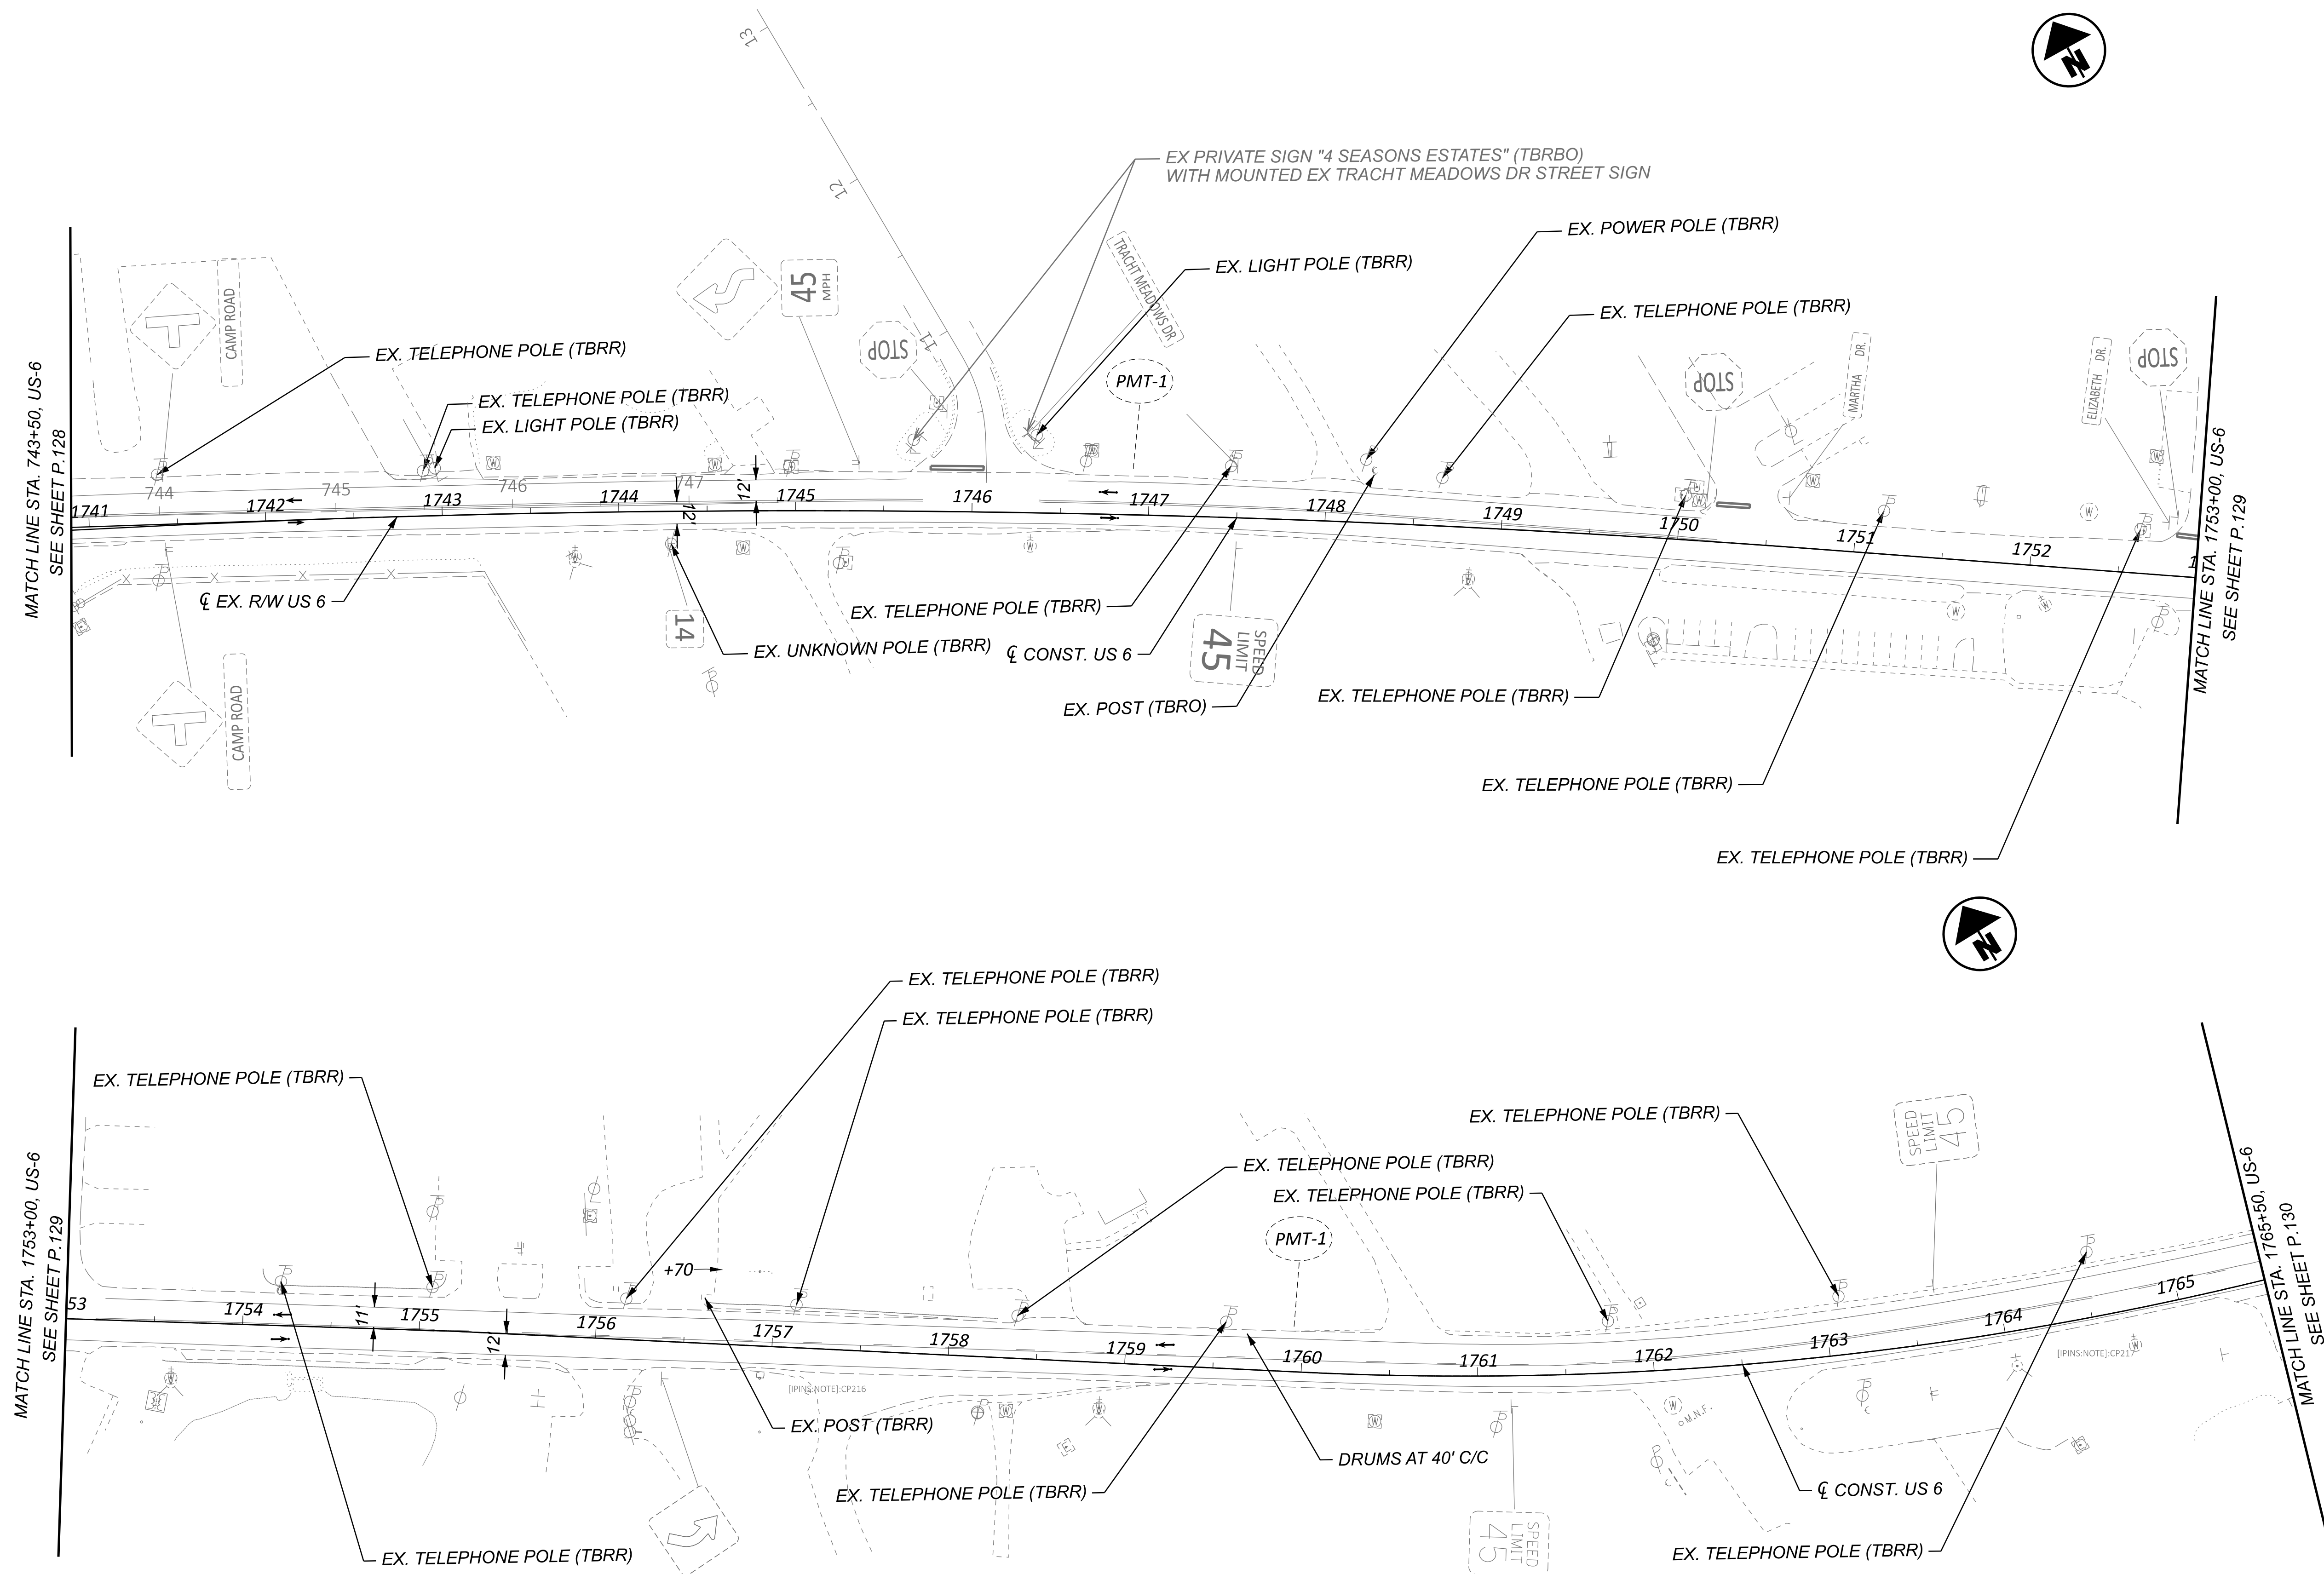

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.



MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - EX. US 6 STA. 743+50.00 TO CONST. US 6 STA. 1765+50.00

DESIGN AGENCY

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.132	782




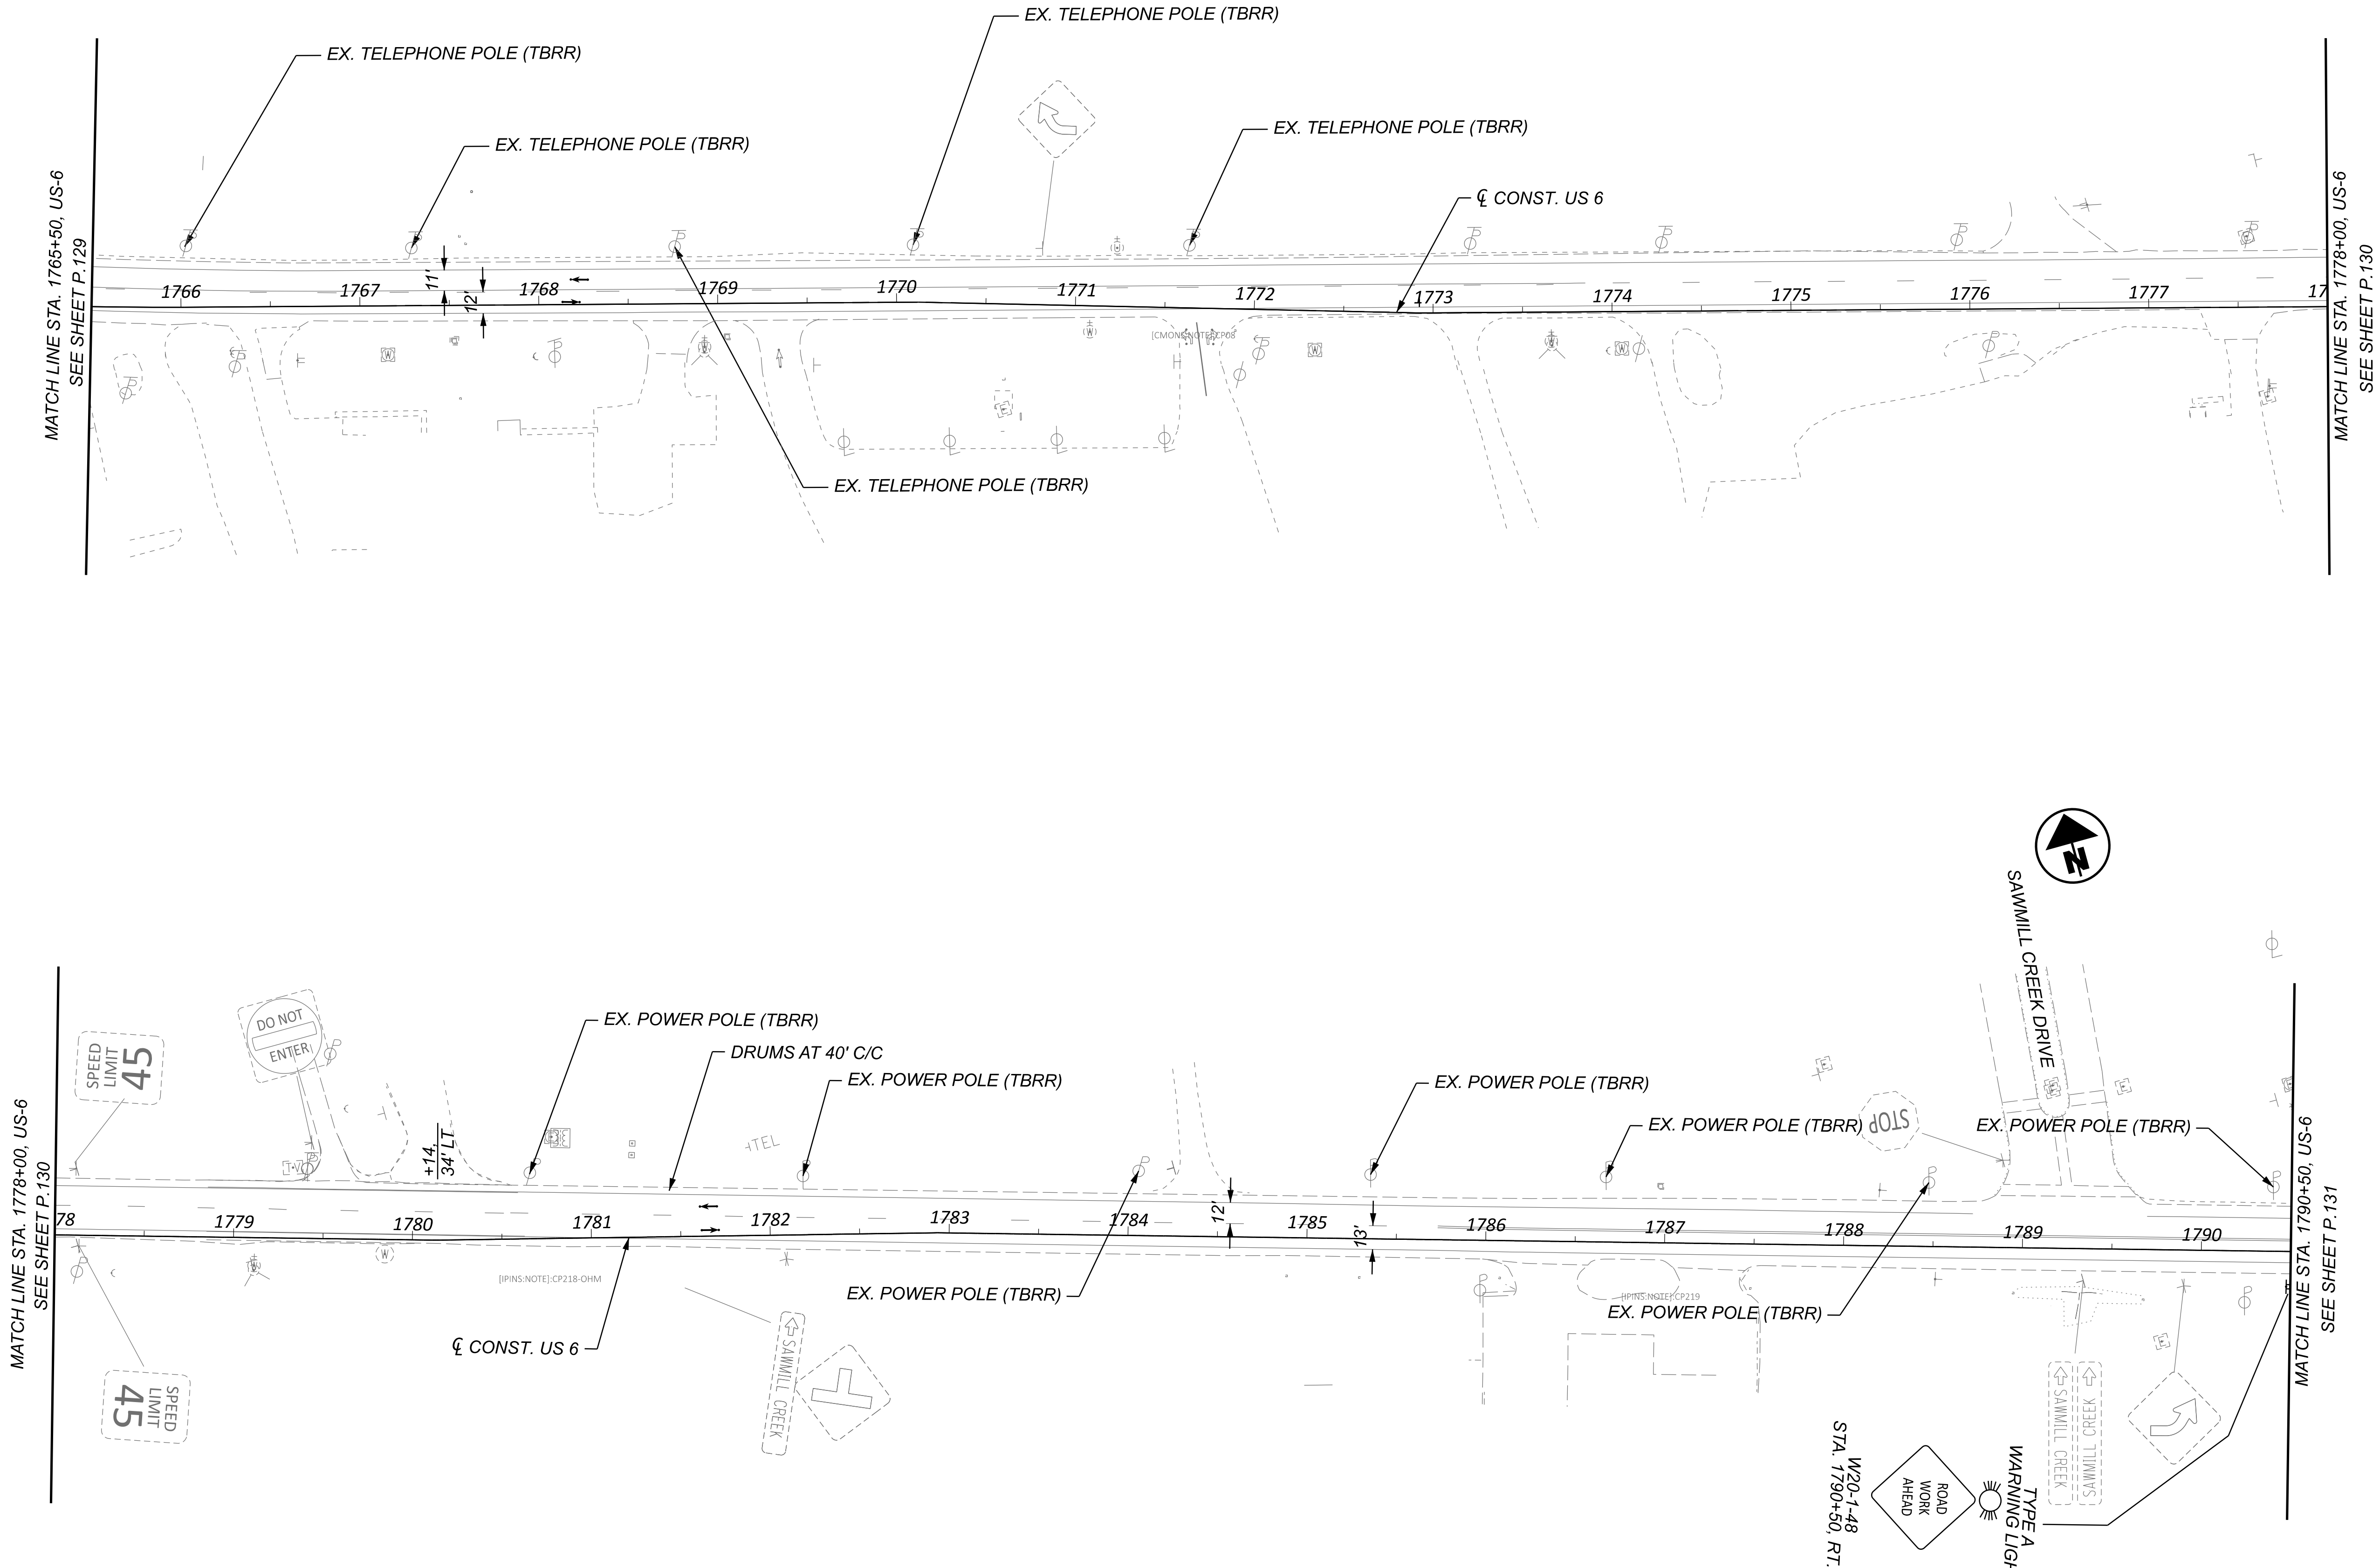


NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 1765+50.00 TO STA. 1790+50.00

DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	TOTAL
P.133	782

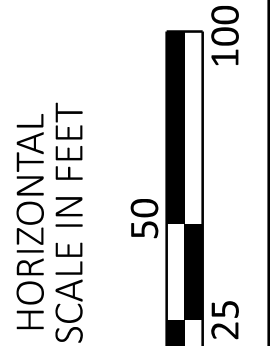


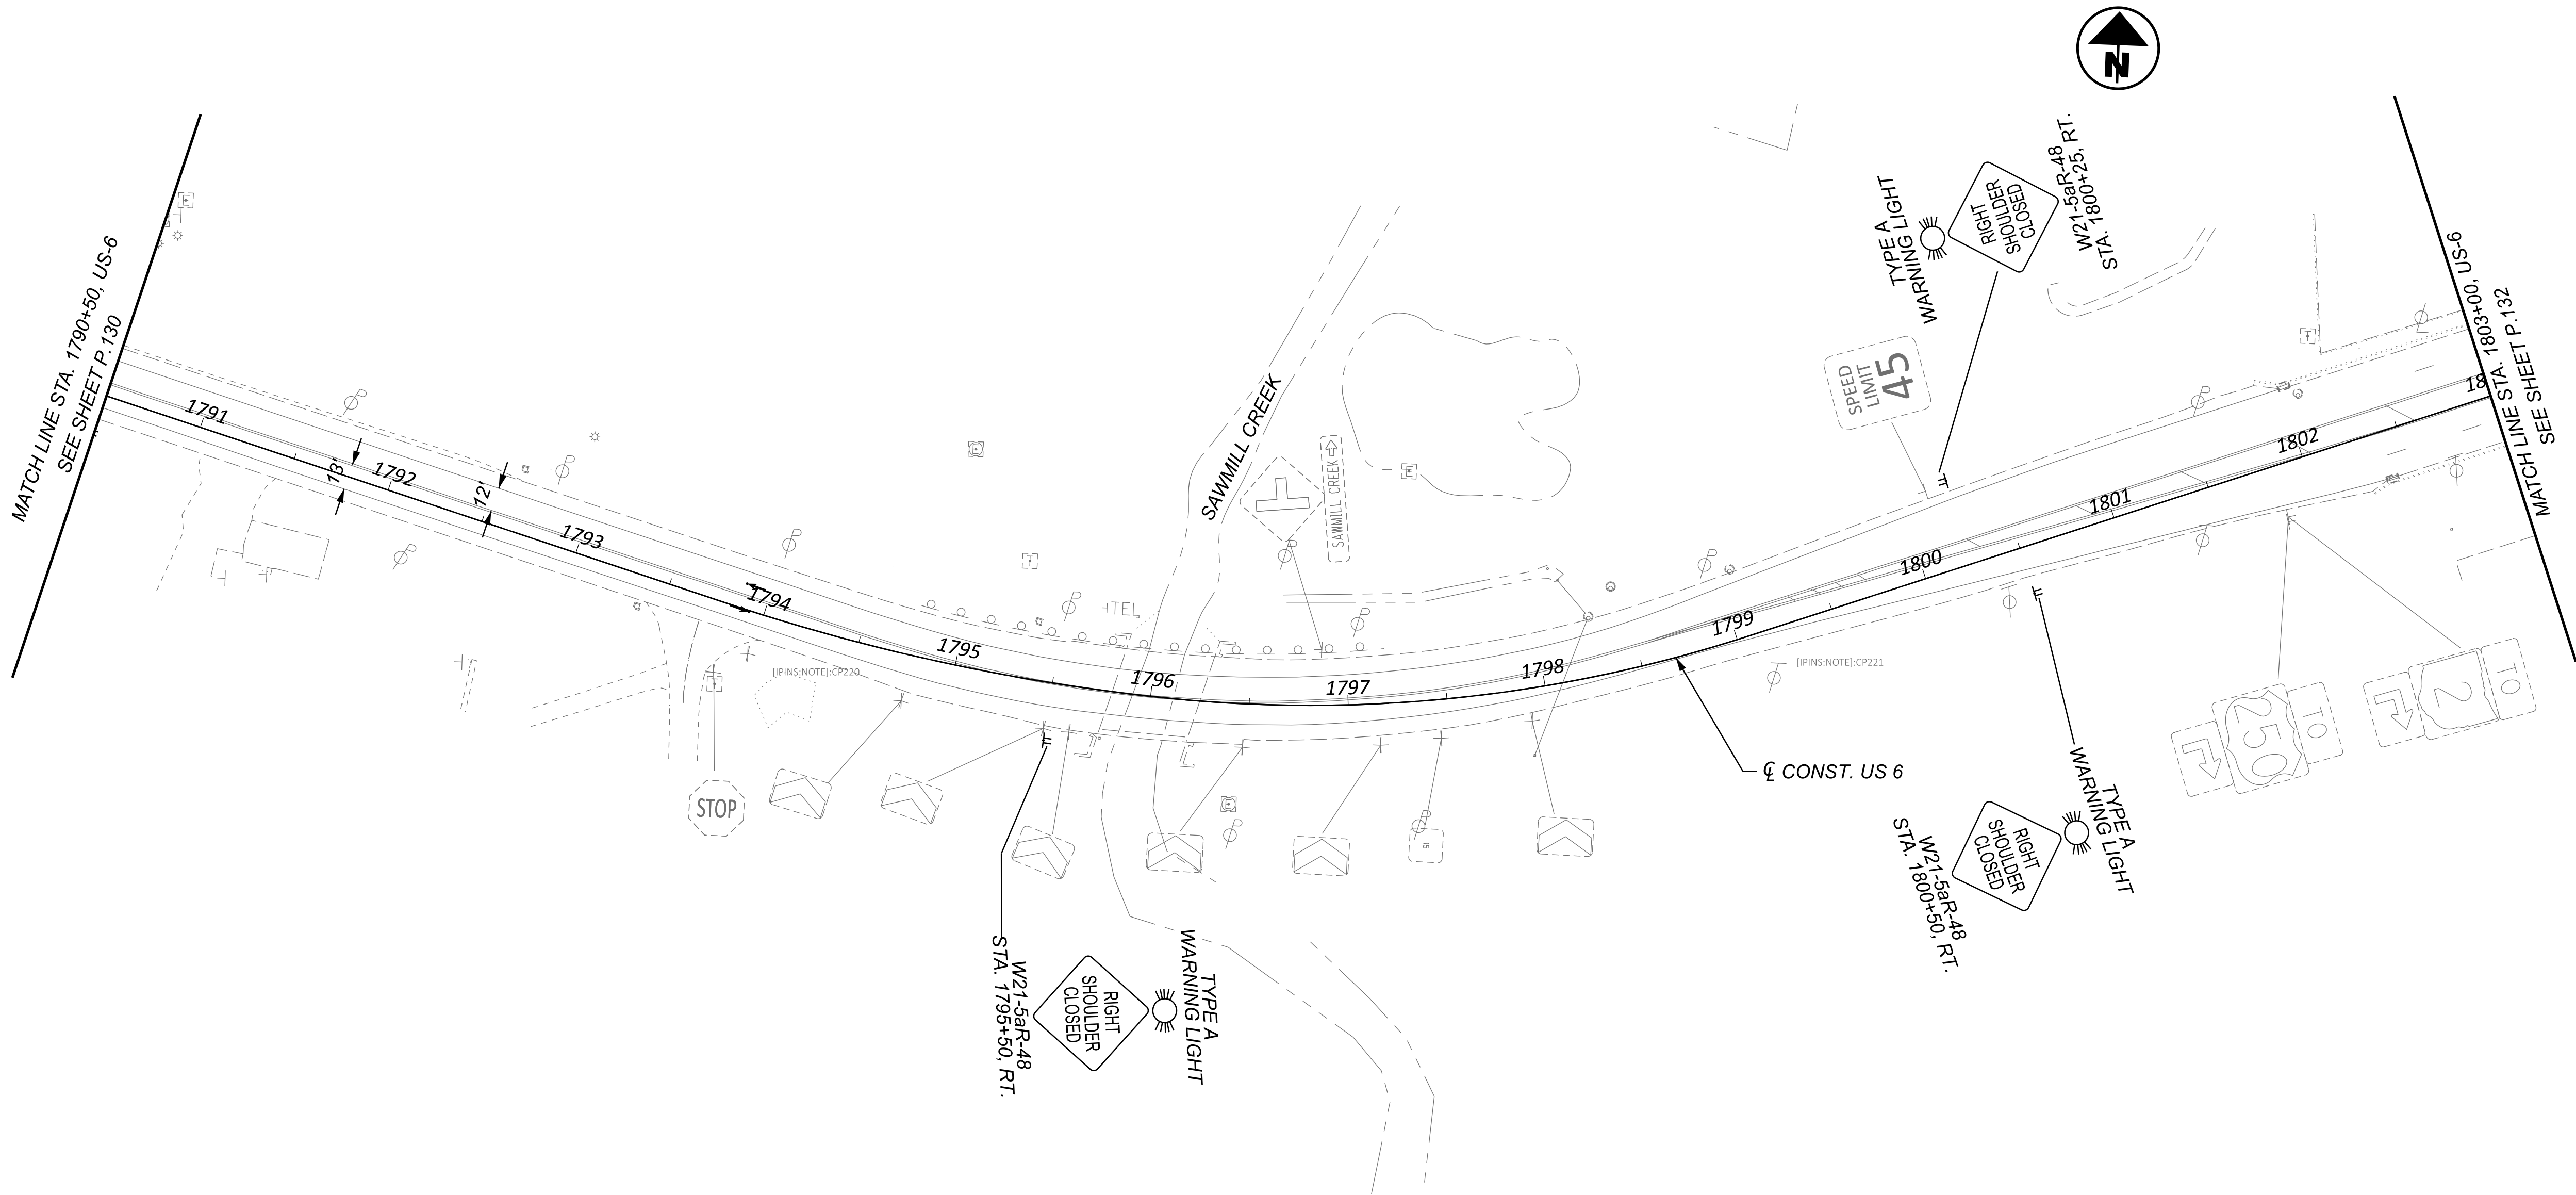



- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
US 6 - STA. 1790+50.00 TO STA. 1803+00.00

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.134	782



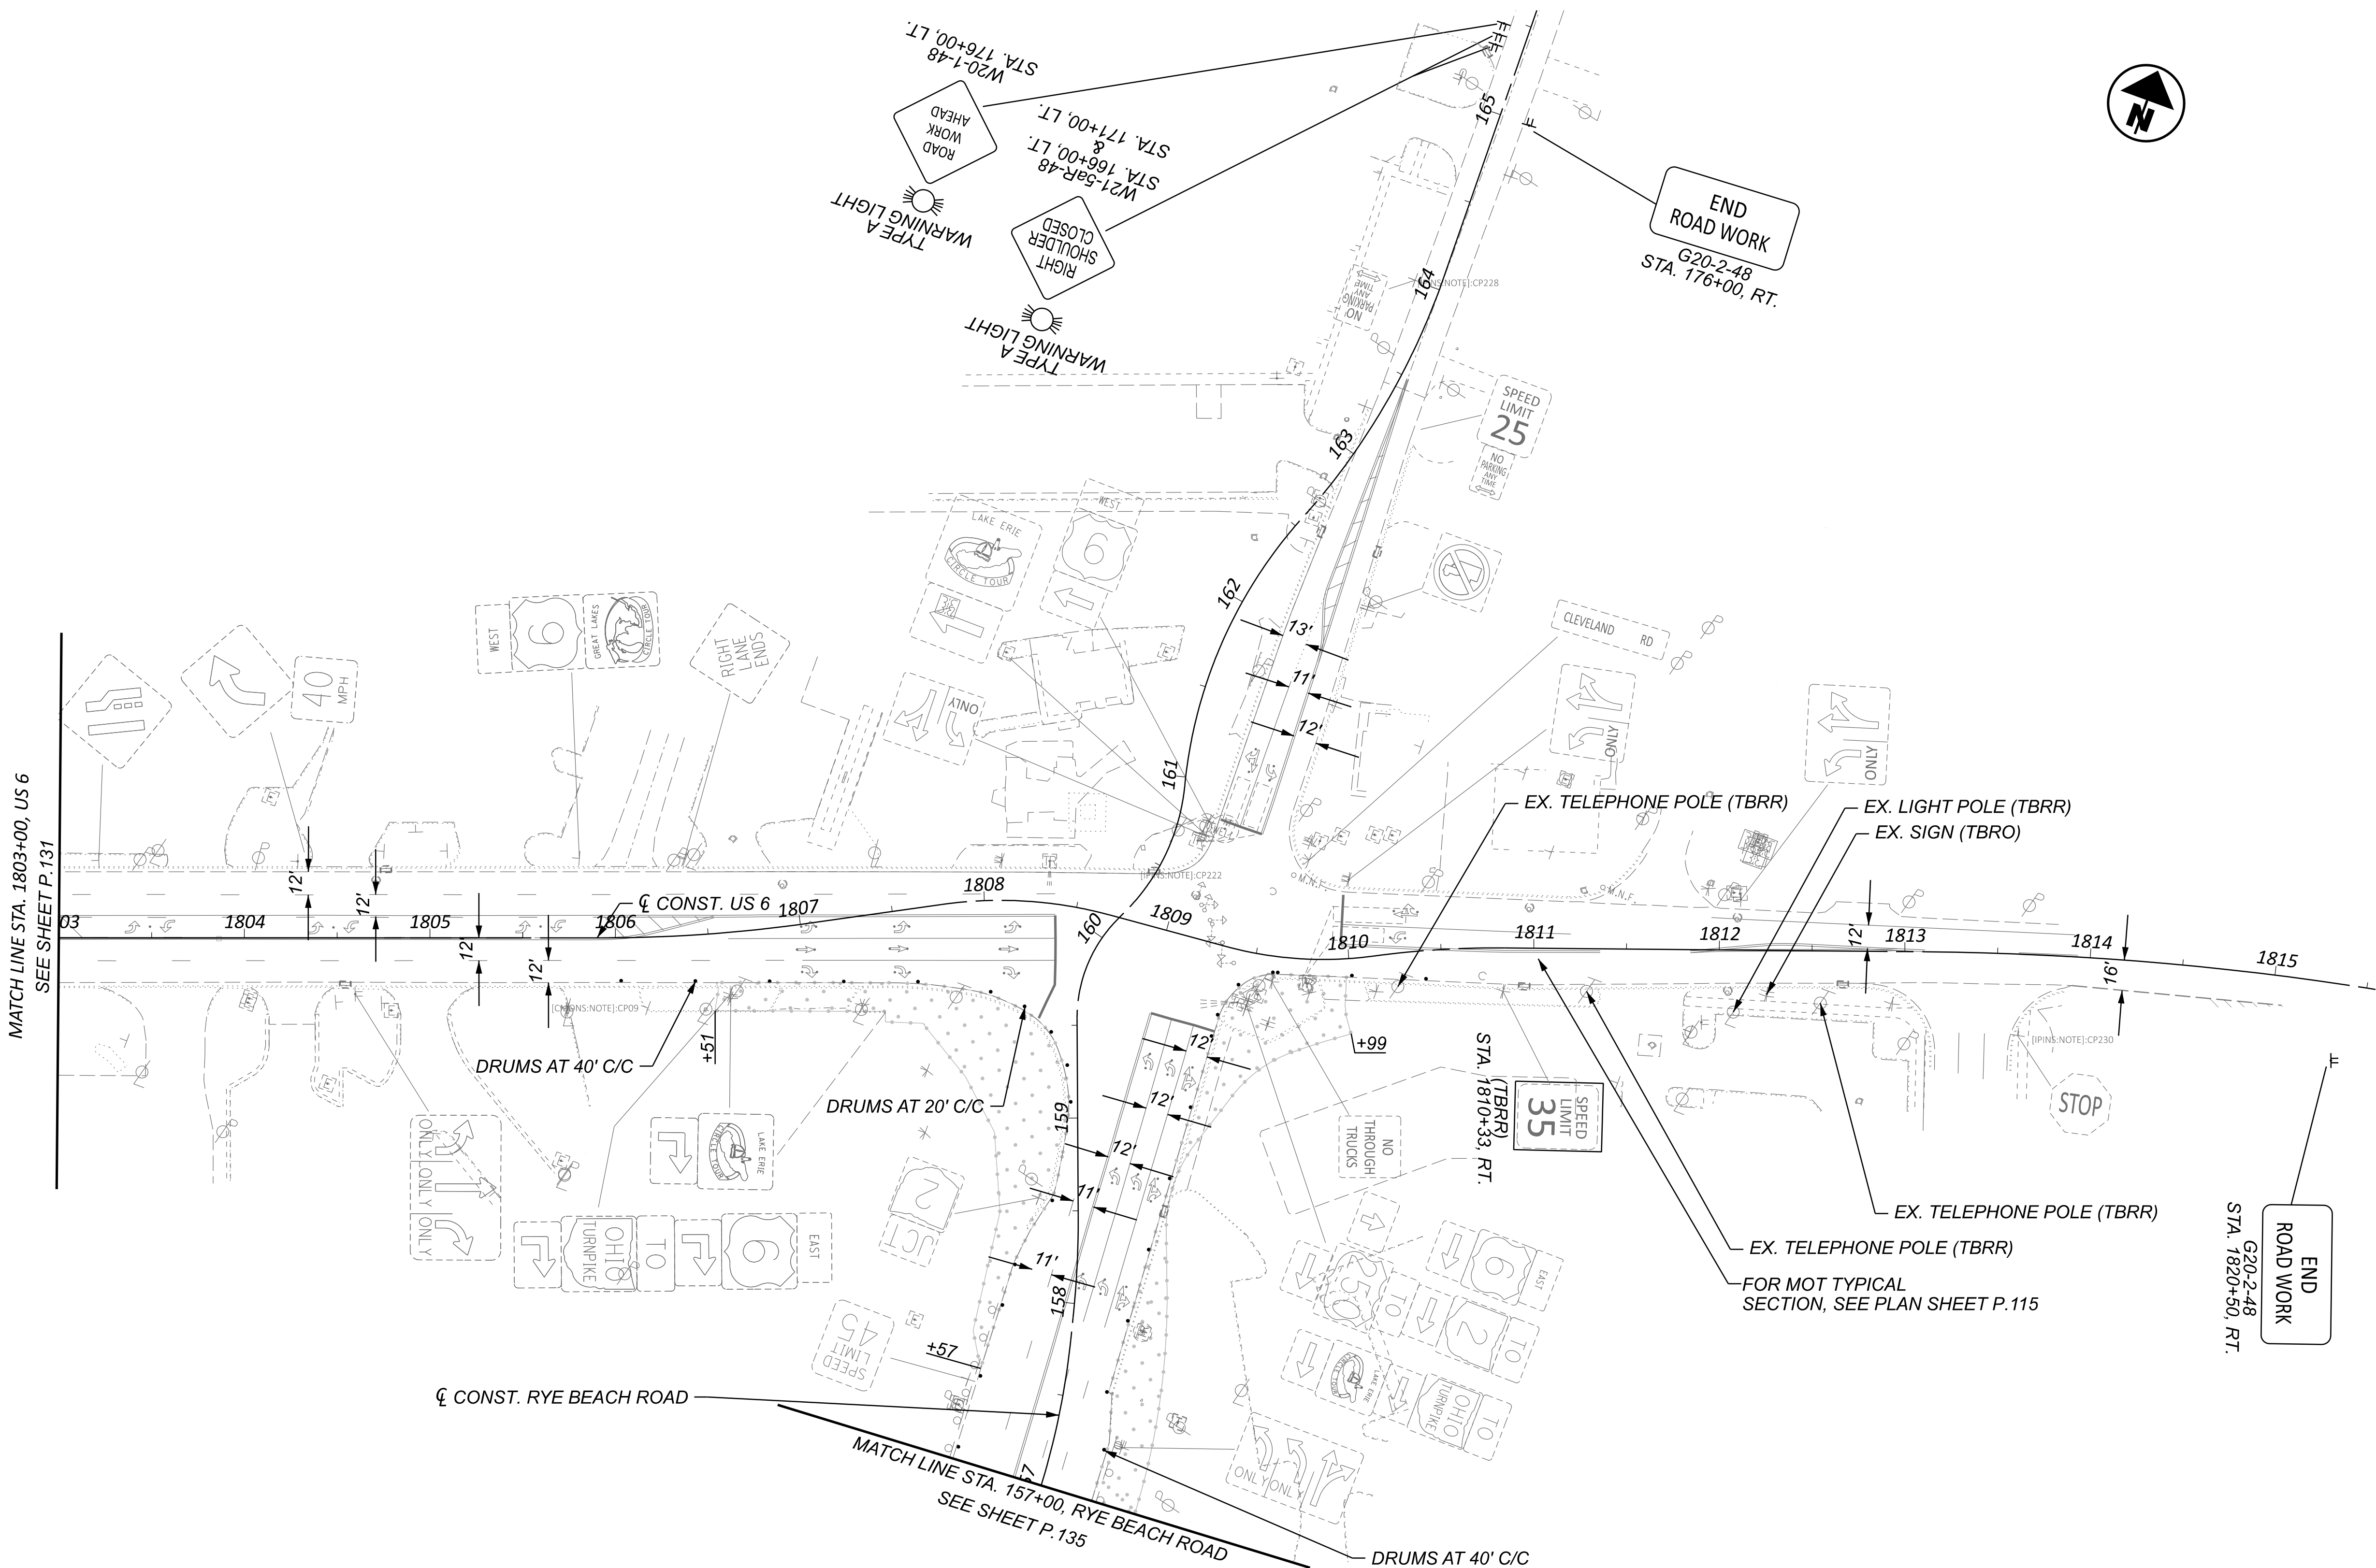

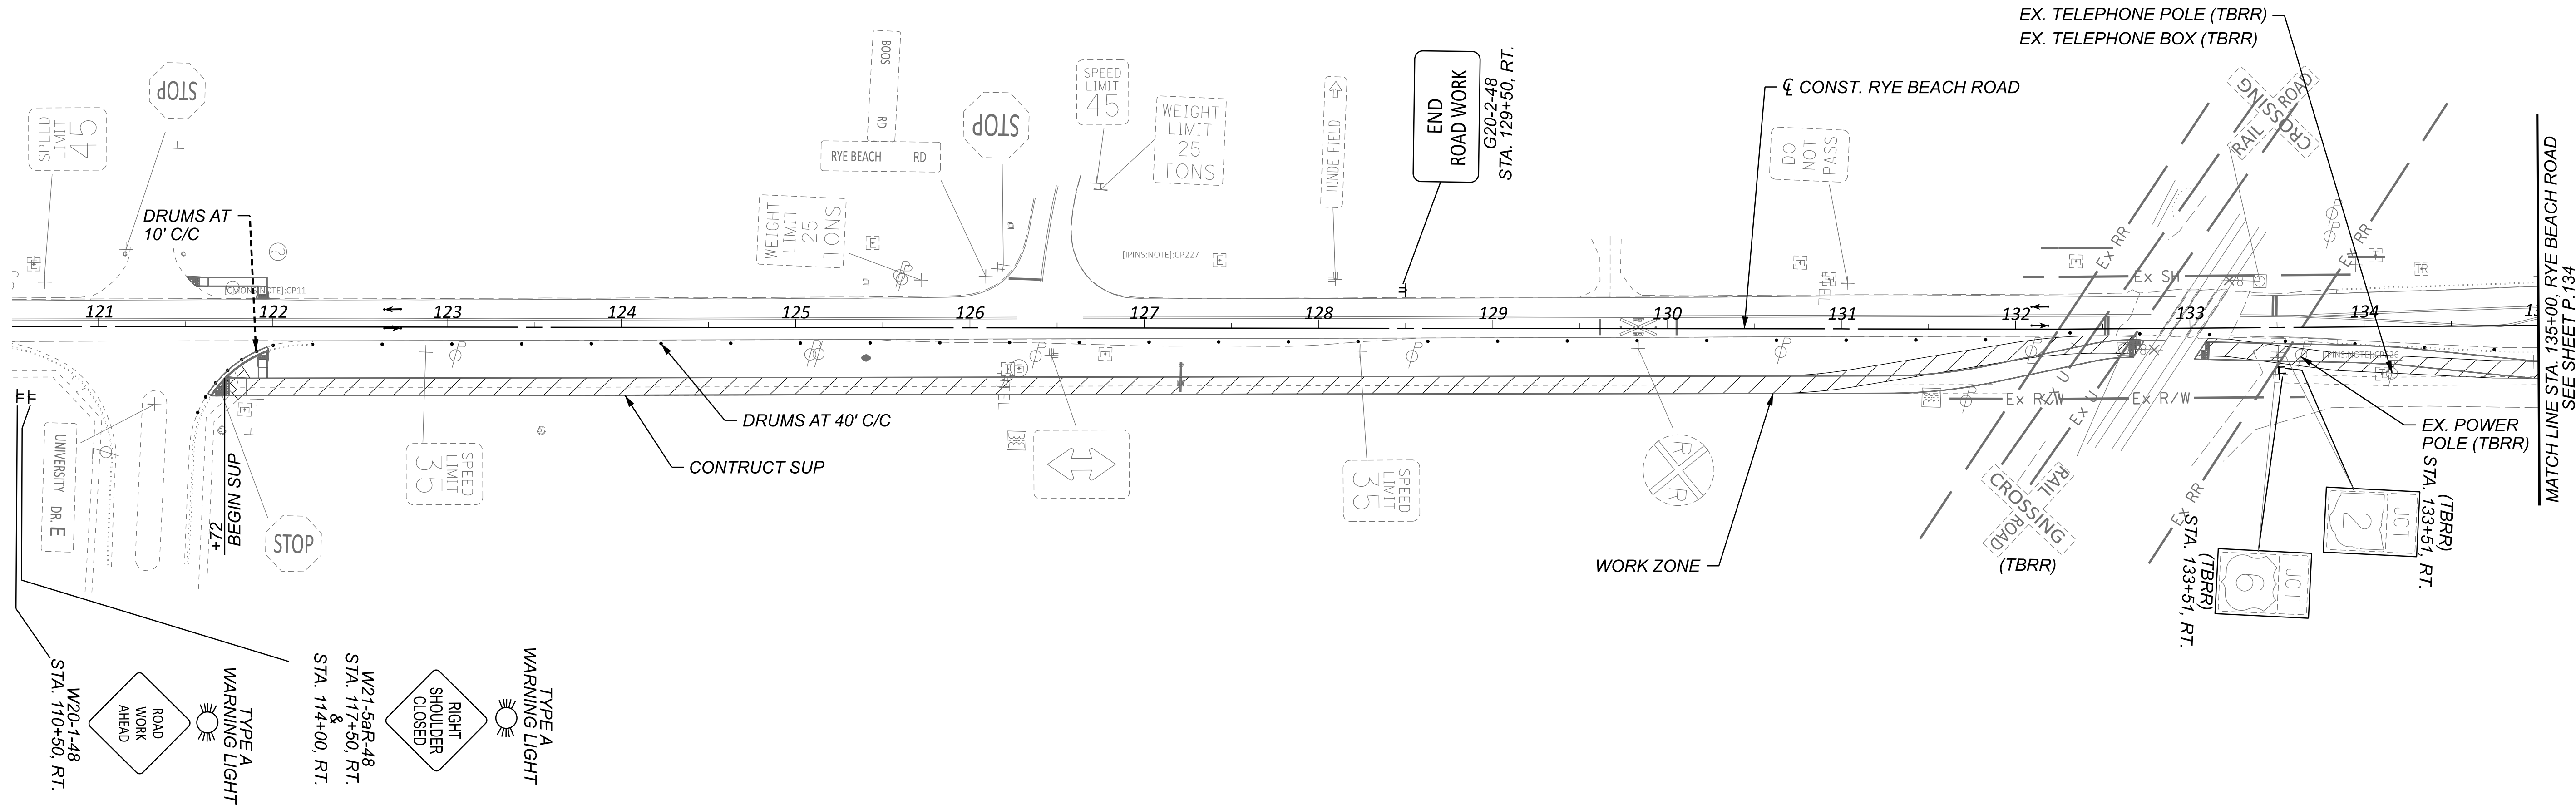

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
RYE BEACH ROAD - BEGIN PROJECT TO STA. 135+00.00


TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215


DESIGNER
SSA

REVIEWER
SS 02/28/24

PROJECT ID
116570

SHEET TOTAL
P.136 782

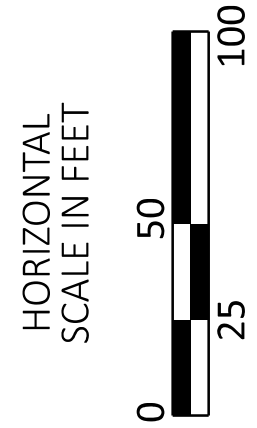

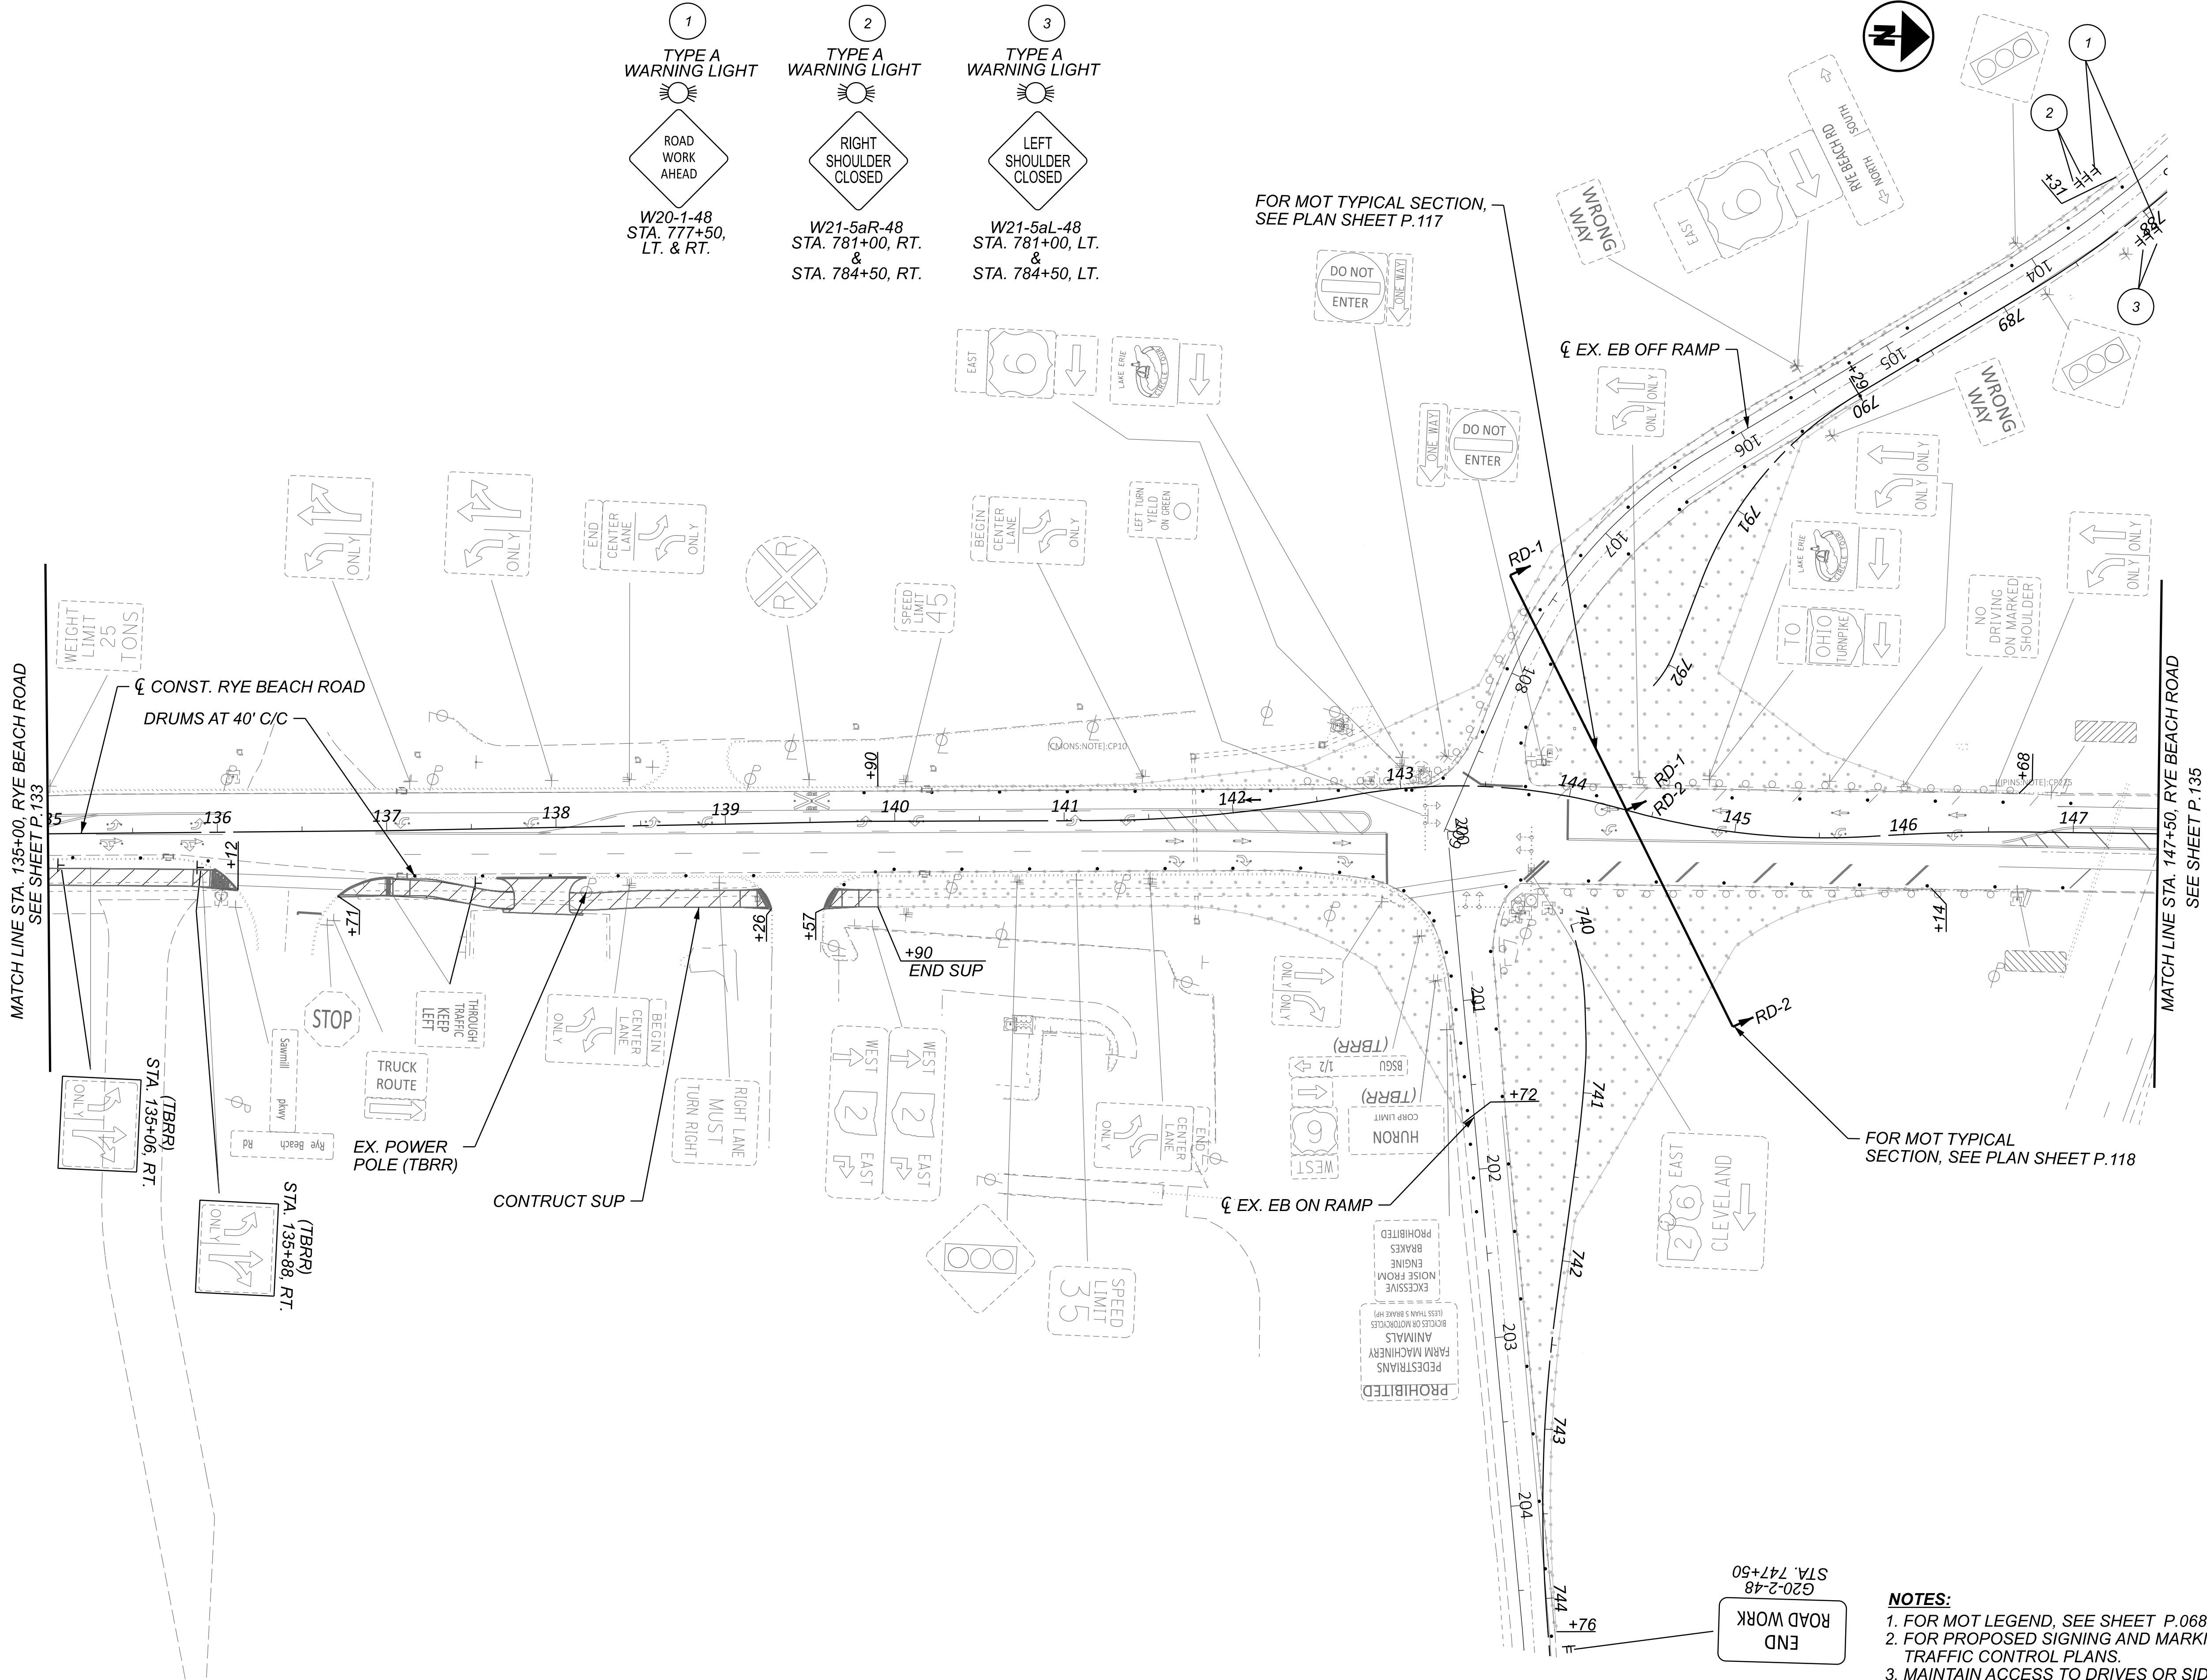






END
ROAD WORK
STA. 747+50
G20-2-48

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PRE-PHASE (2026 CONSTRUCTION)
RYE BEACH ROAD - STA. 135+00.00 TO STA. 147+50.00

DESIGN AGENCY	
TRANSYSTEMS	
400 W. WATKINSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.137	TOTAL 782



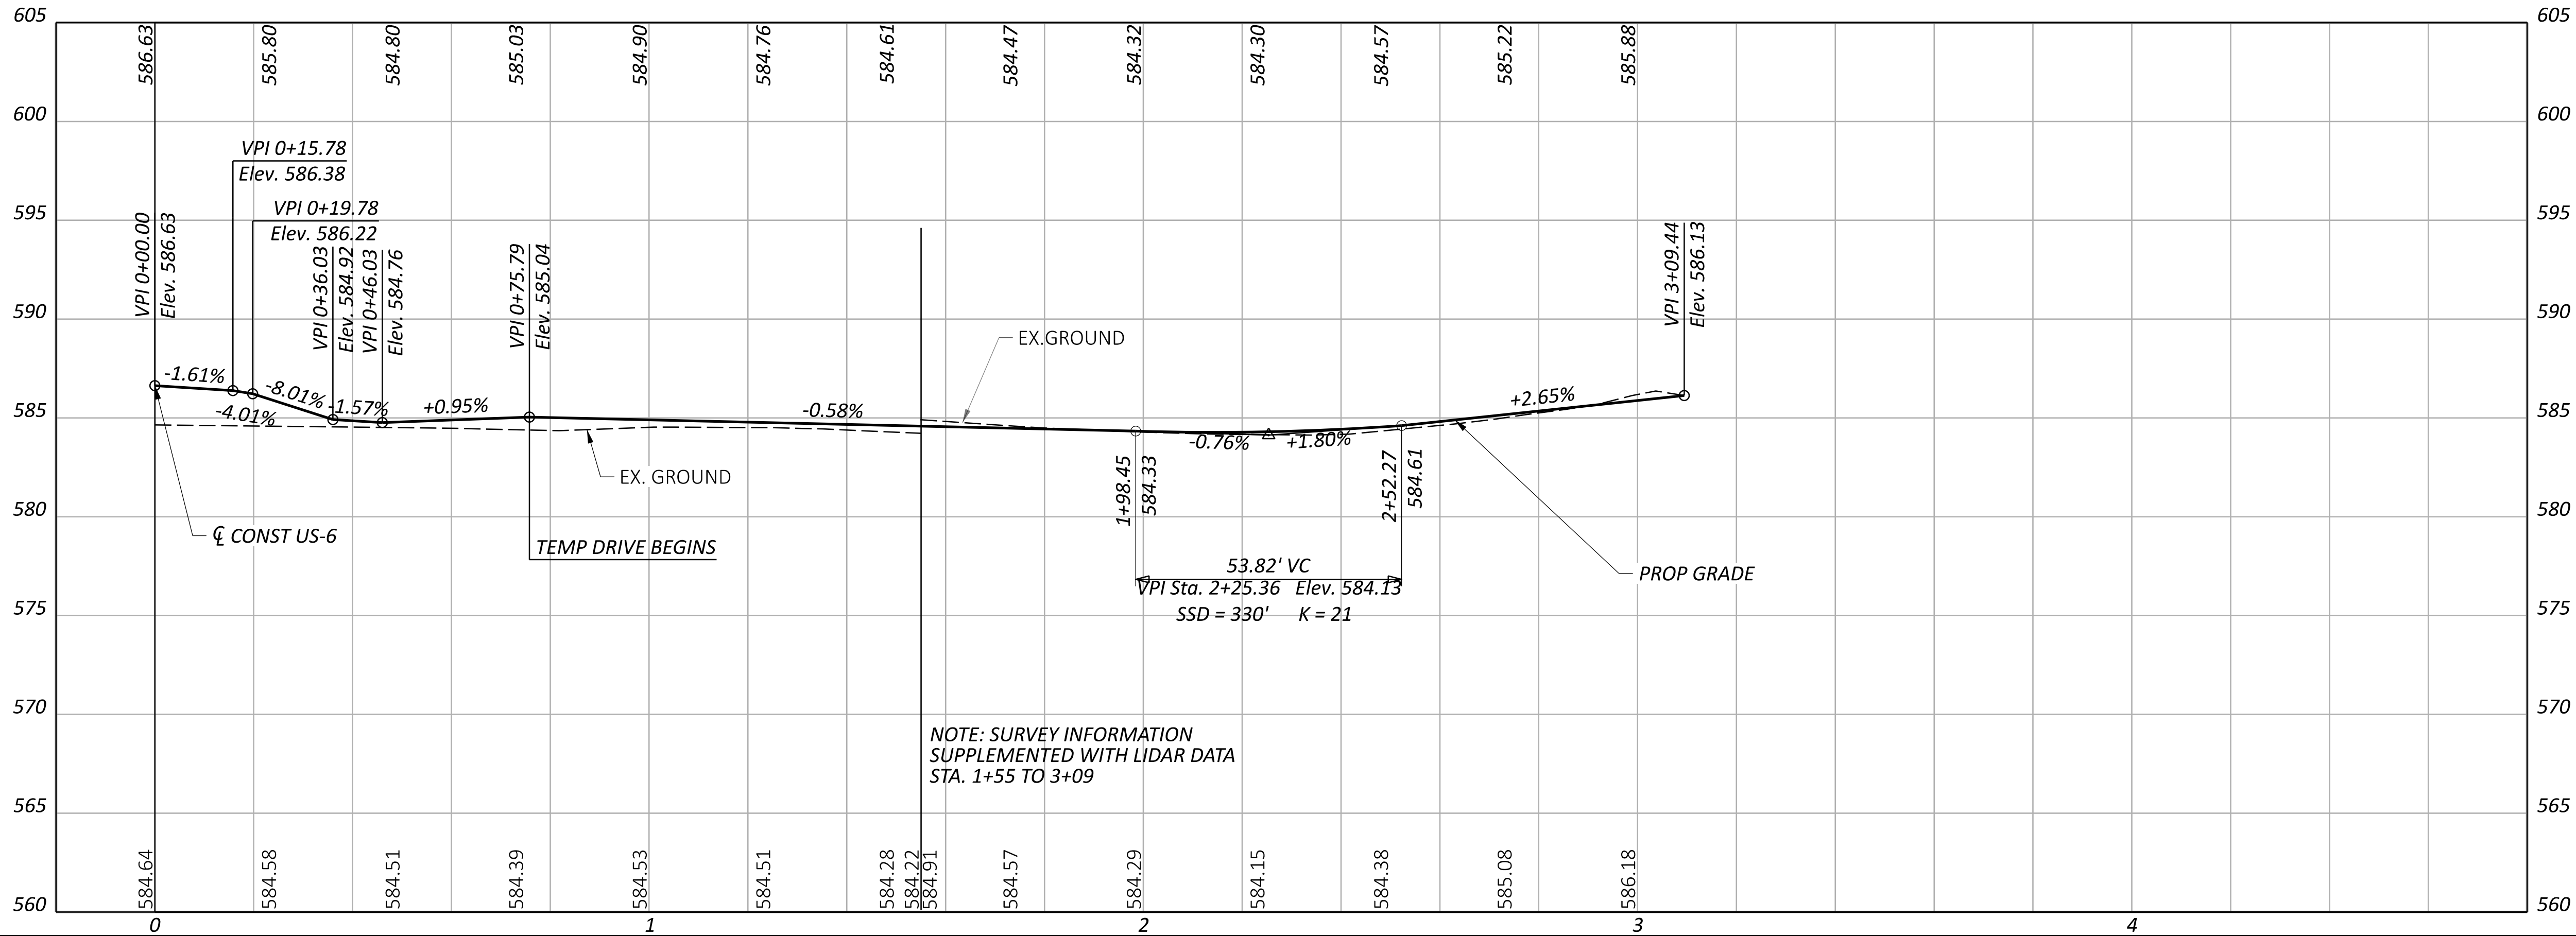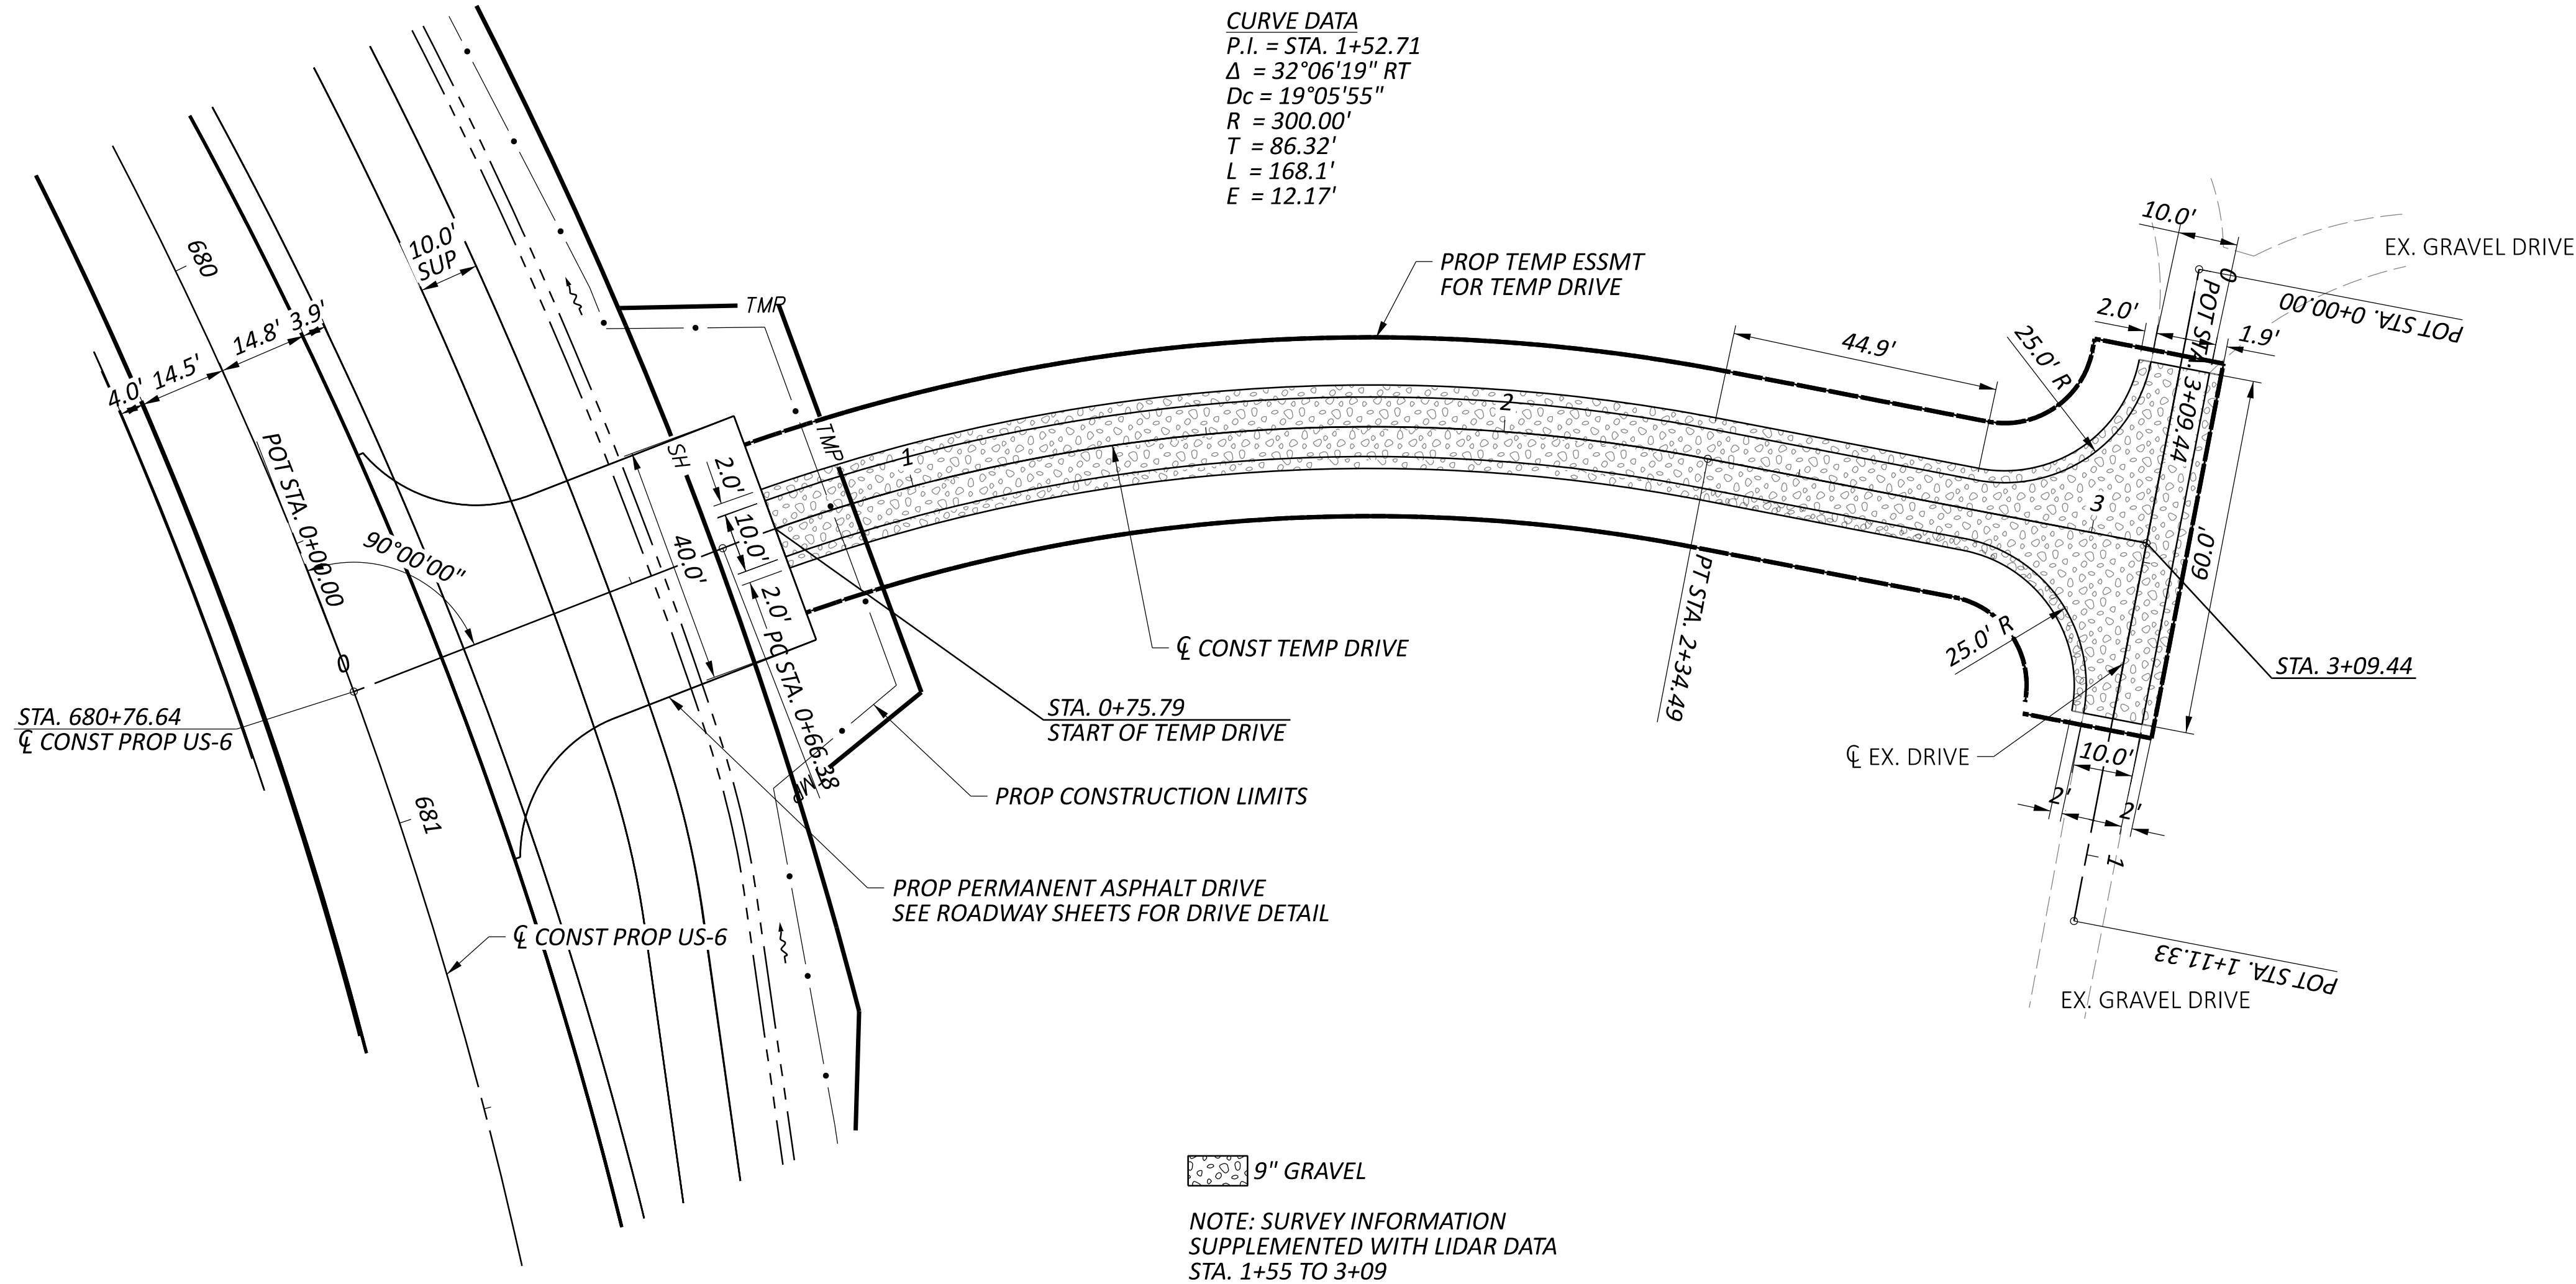

MOT PRE-PHASE - TEMPORARY DRIVEWAY PLAN AND PROFILE
US 6 - STA 680+76.64




DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER
XXX

REVIEWER
XXX MM-DD-YY

PROJECT ID
116570

SHEET TOTAL
P.0 0

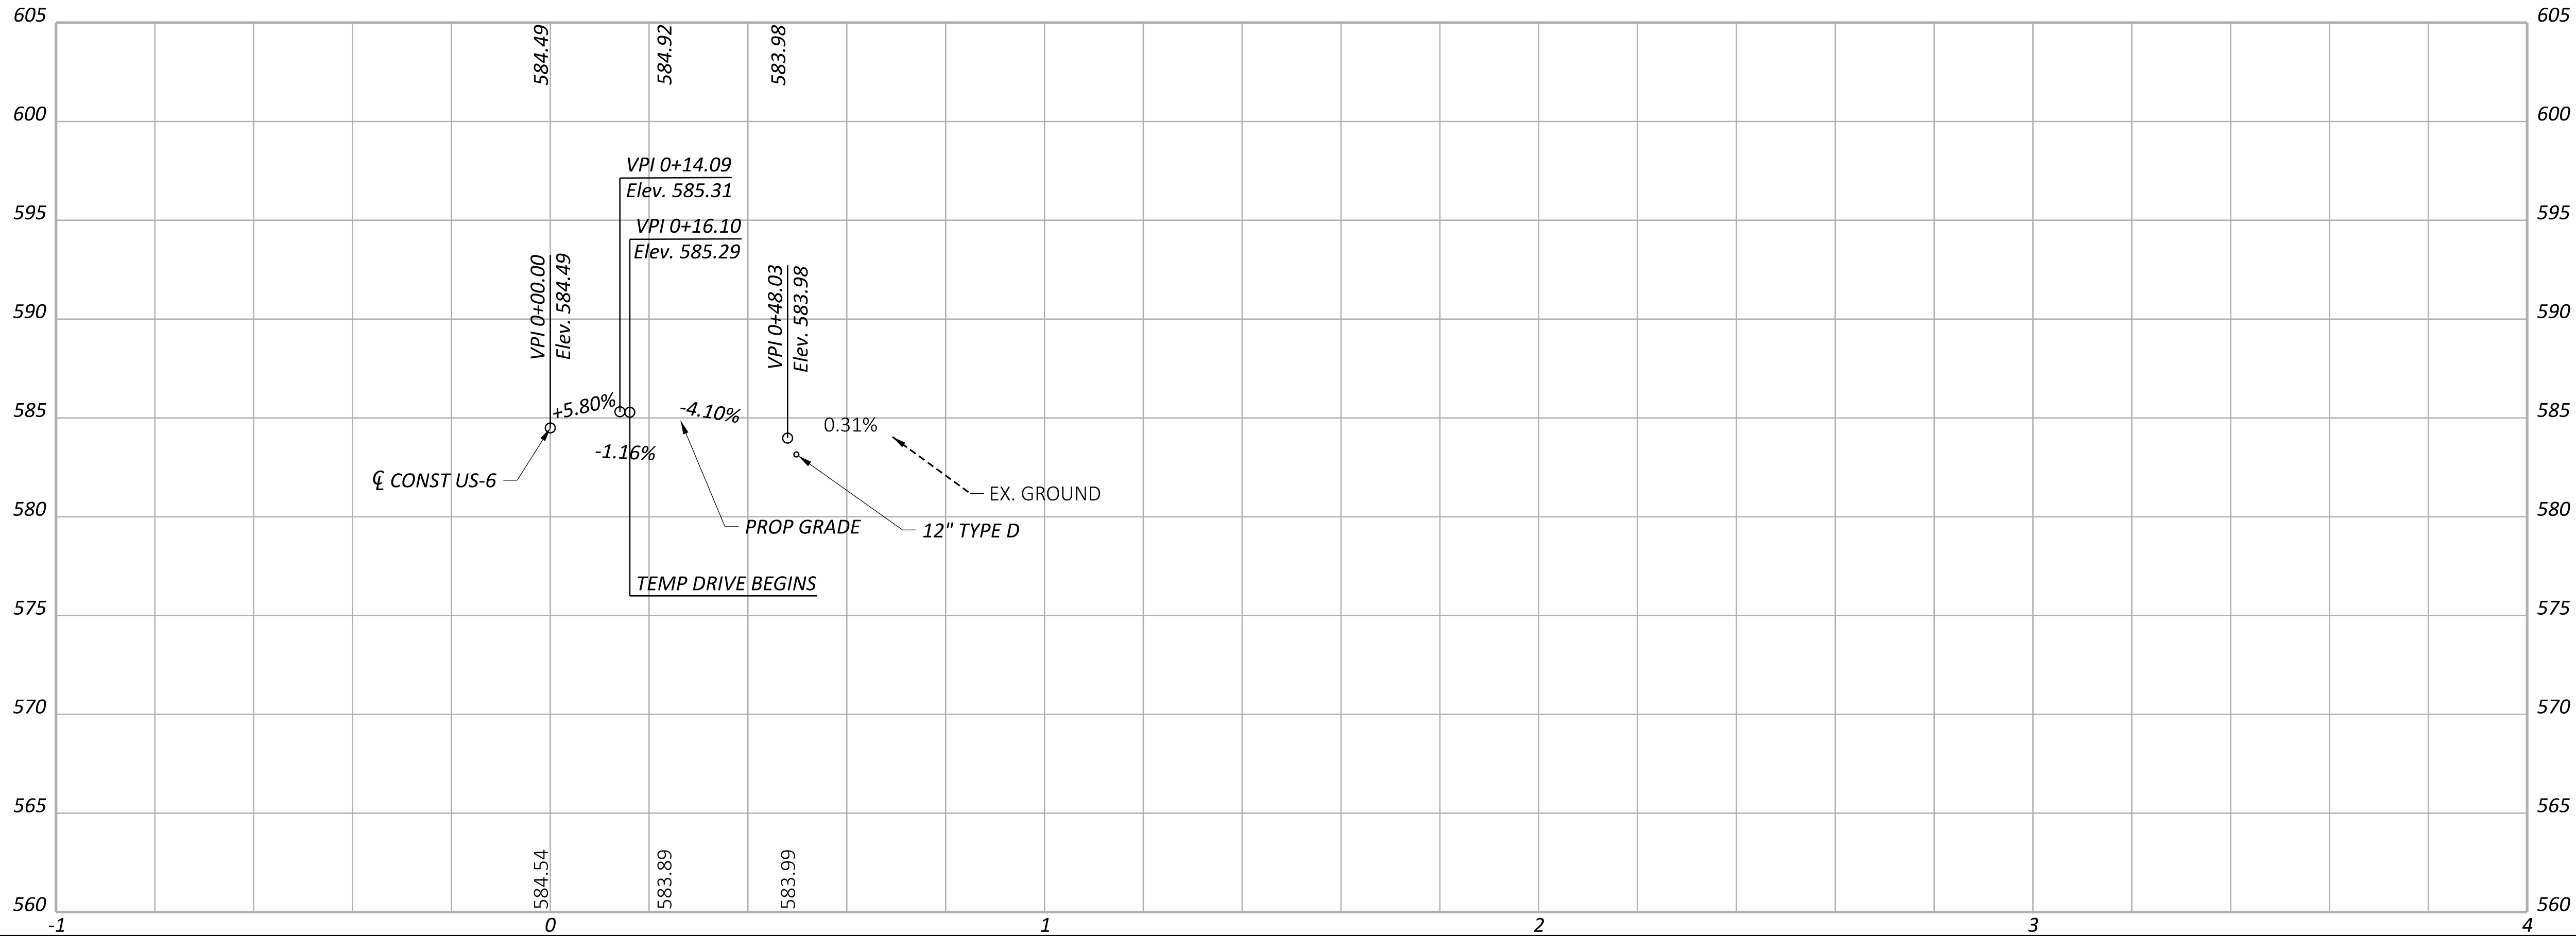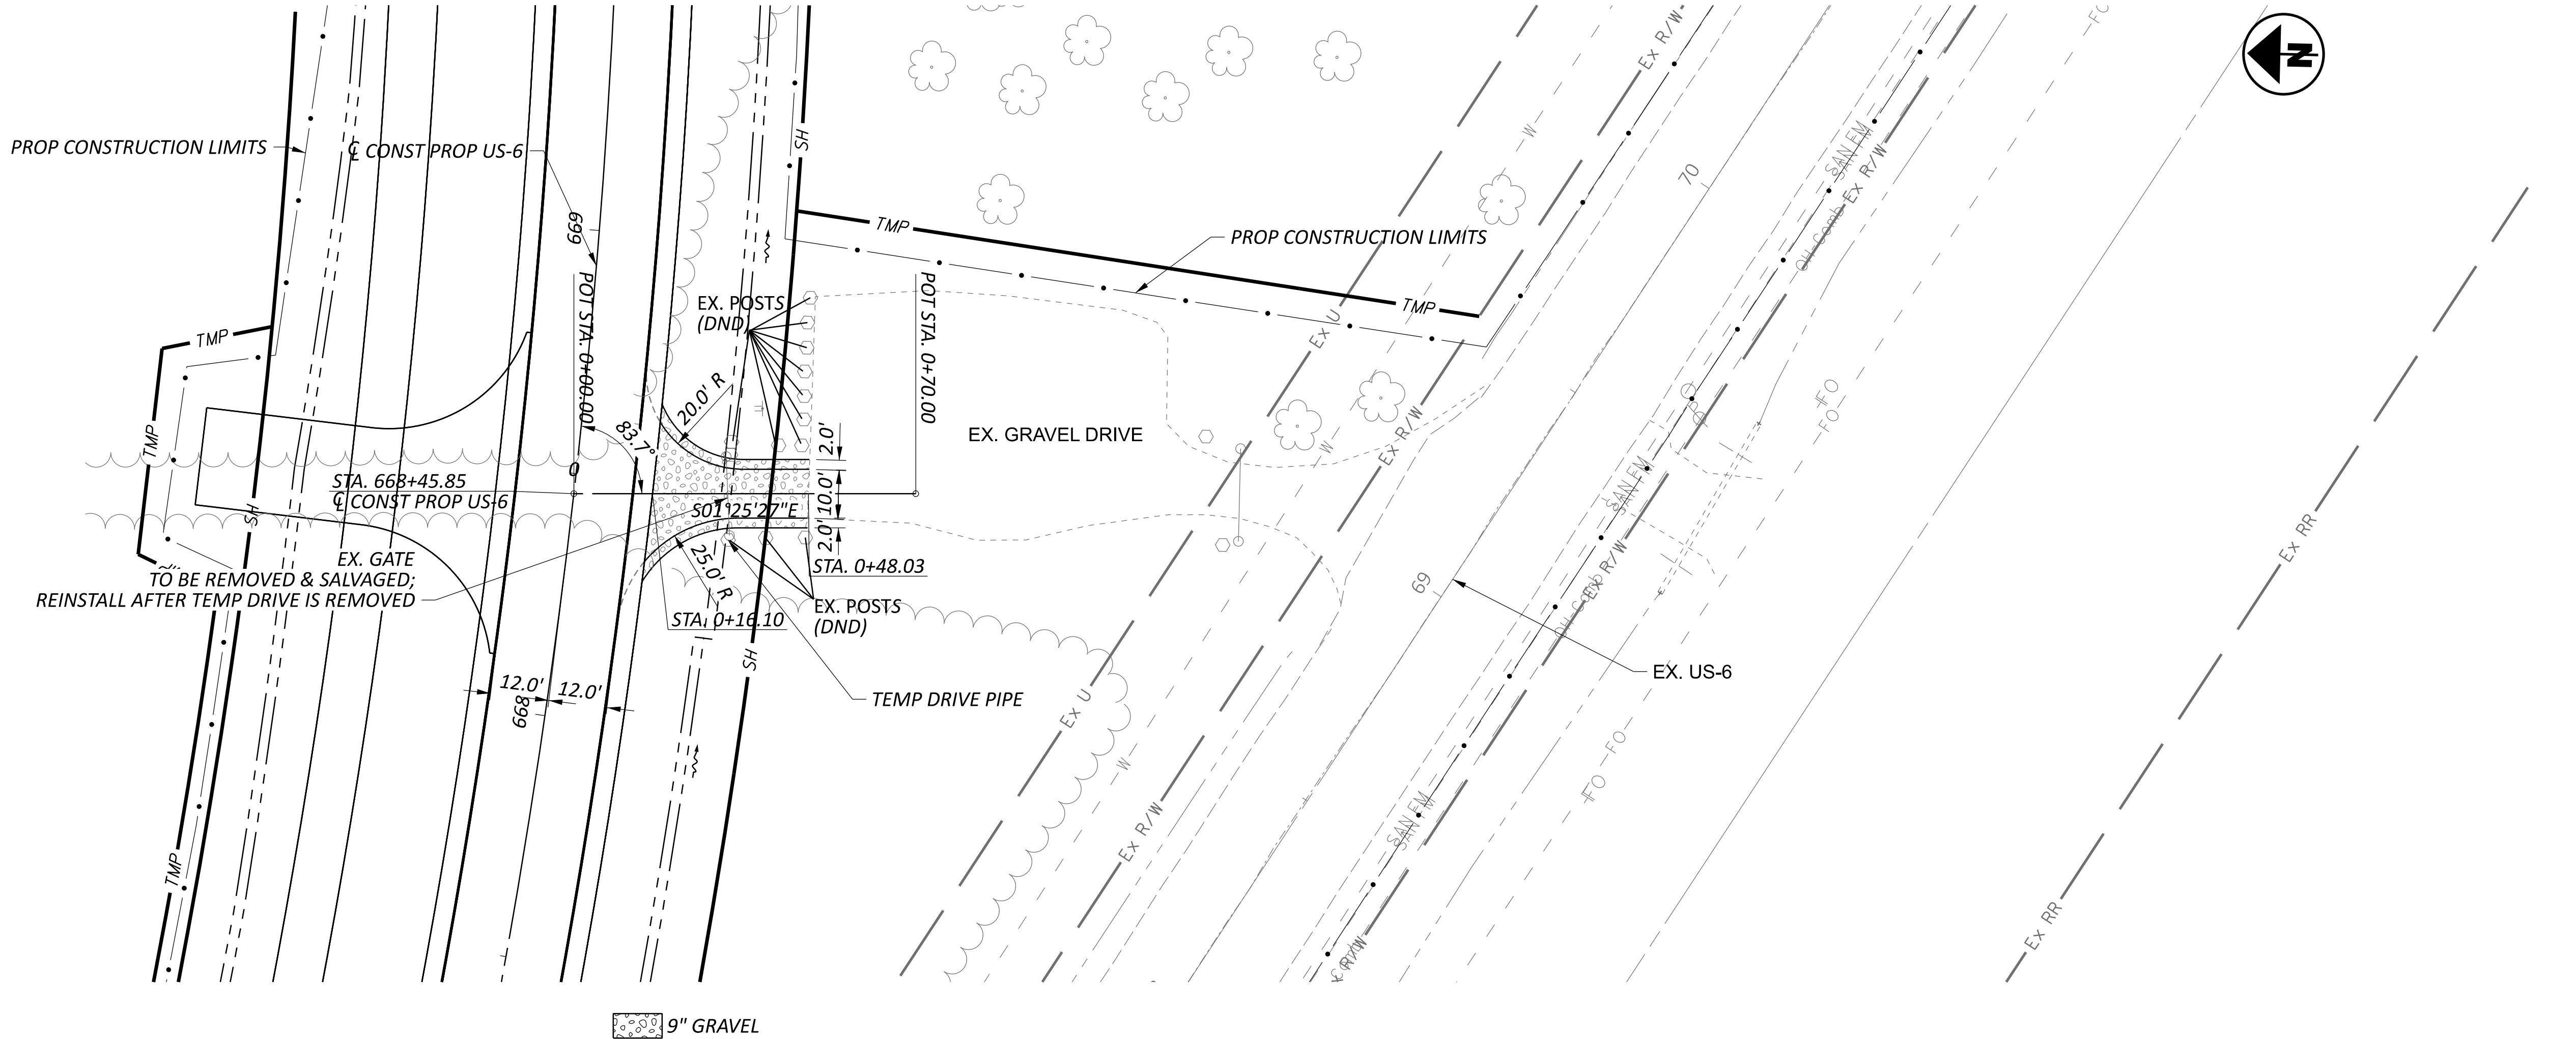

MOT PRE-PHASE TEMPORARY DRIVEWAY PLAN AND PROFILE
US 6 - STA. 668+45.85

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 205
COLUMBUS, OHIO 43215

DESIGNER
XXX


REVIEWER
XXX MM-DD-YY

PROJECT ID
116570

SHEET
P.0

TOTAL
0





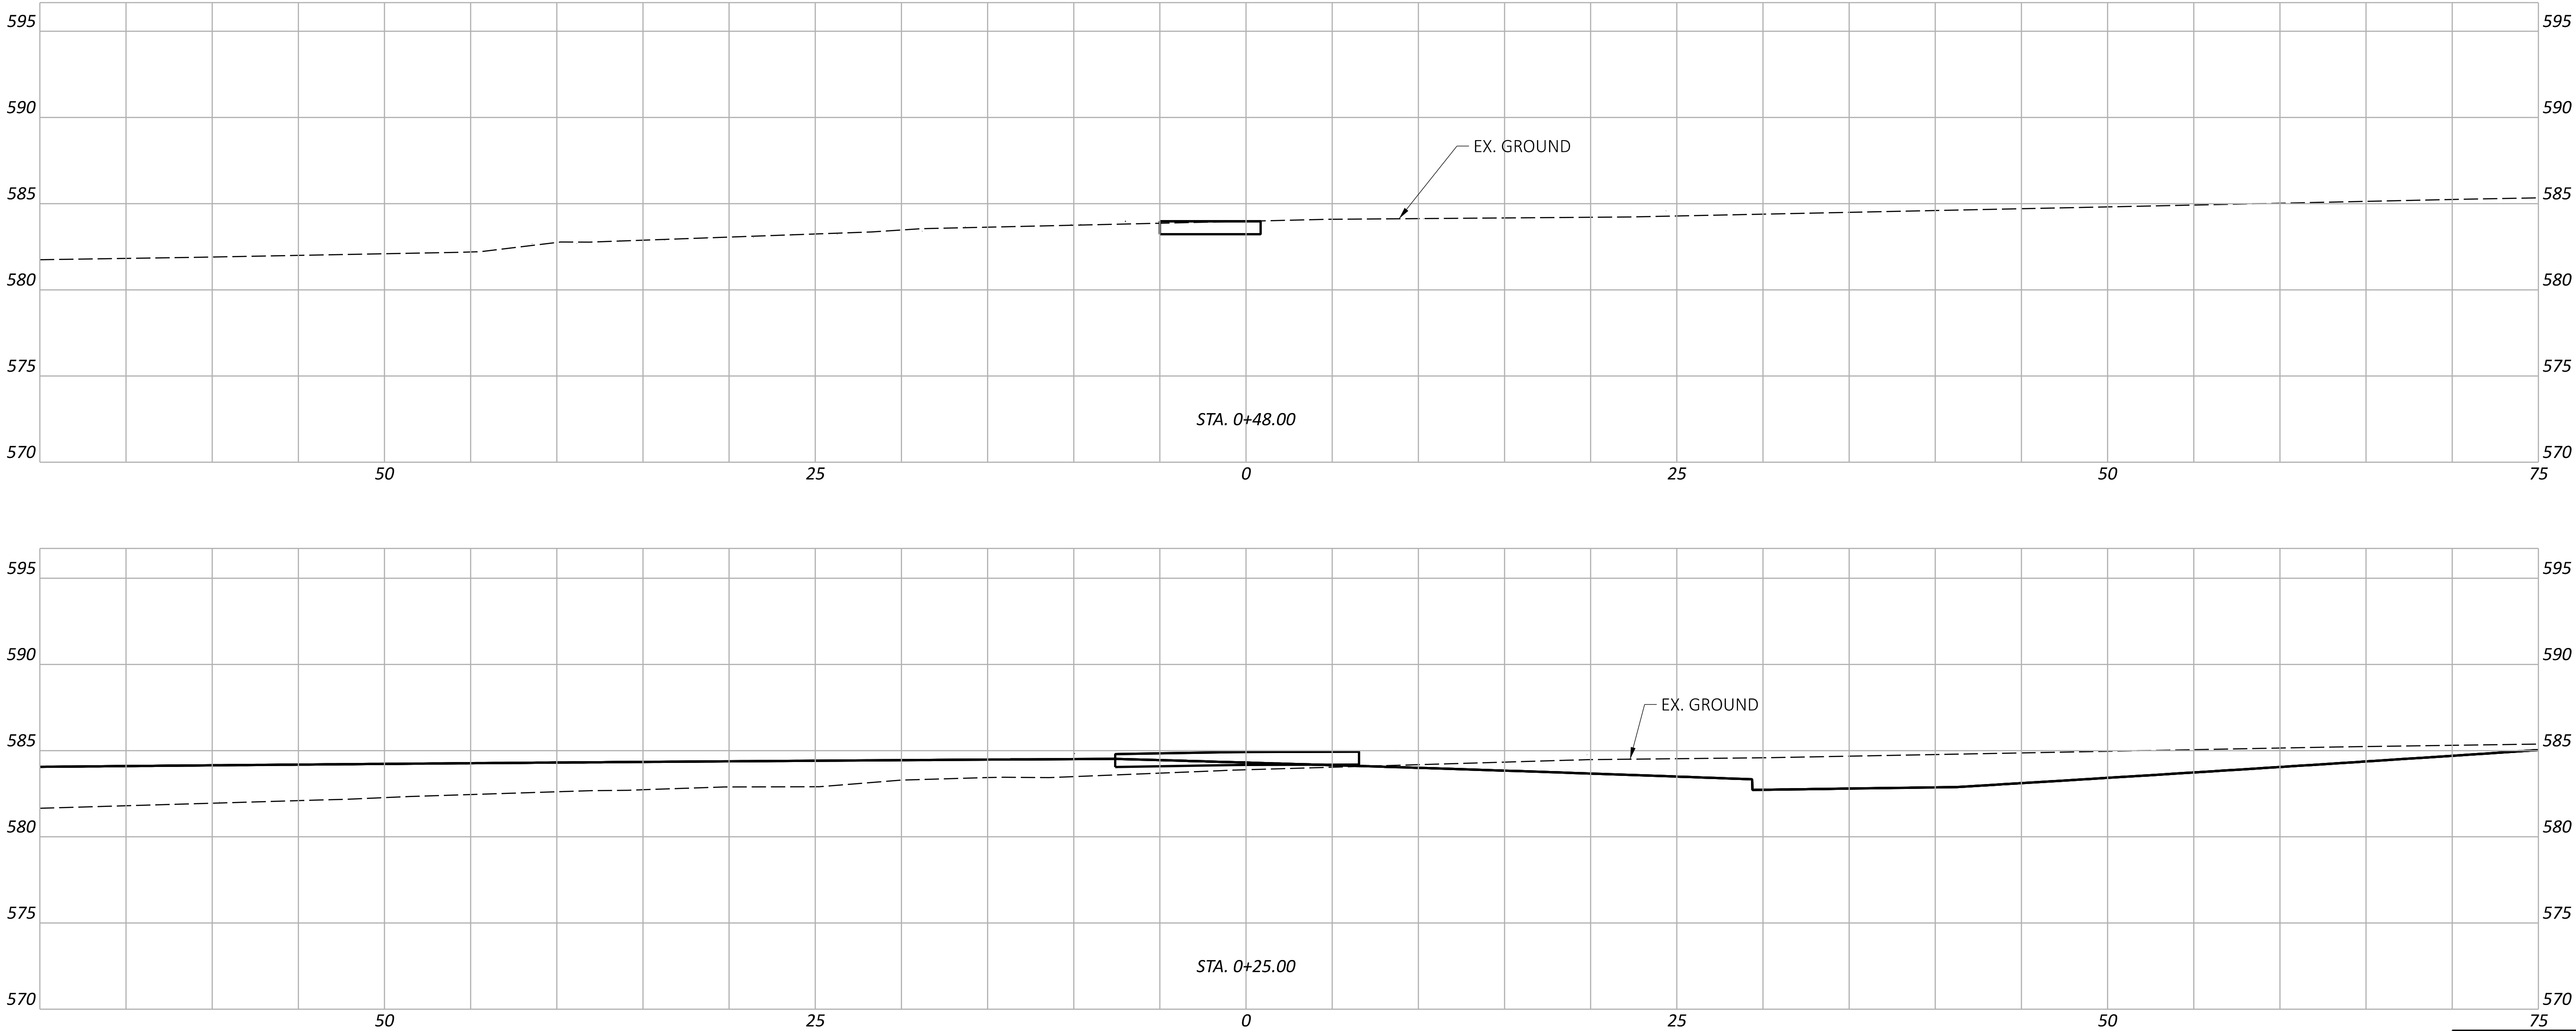



Sheet Totals		
Seeding	Cut	Fill

SHEET	TOTAL
P.0	0

DESIGN AGENCY
TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225 COLUMBUS, OHIO 43215
DESIGNER
XXX
REVIEWER
XXX MM/DD/YY
PROJECT ID
116570

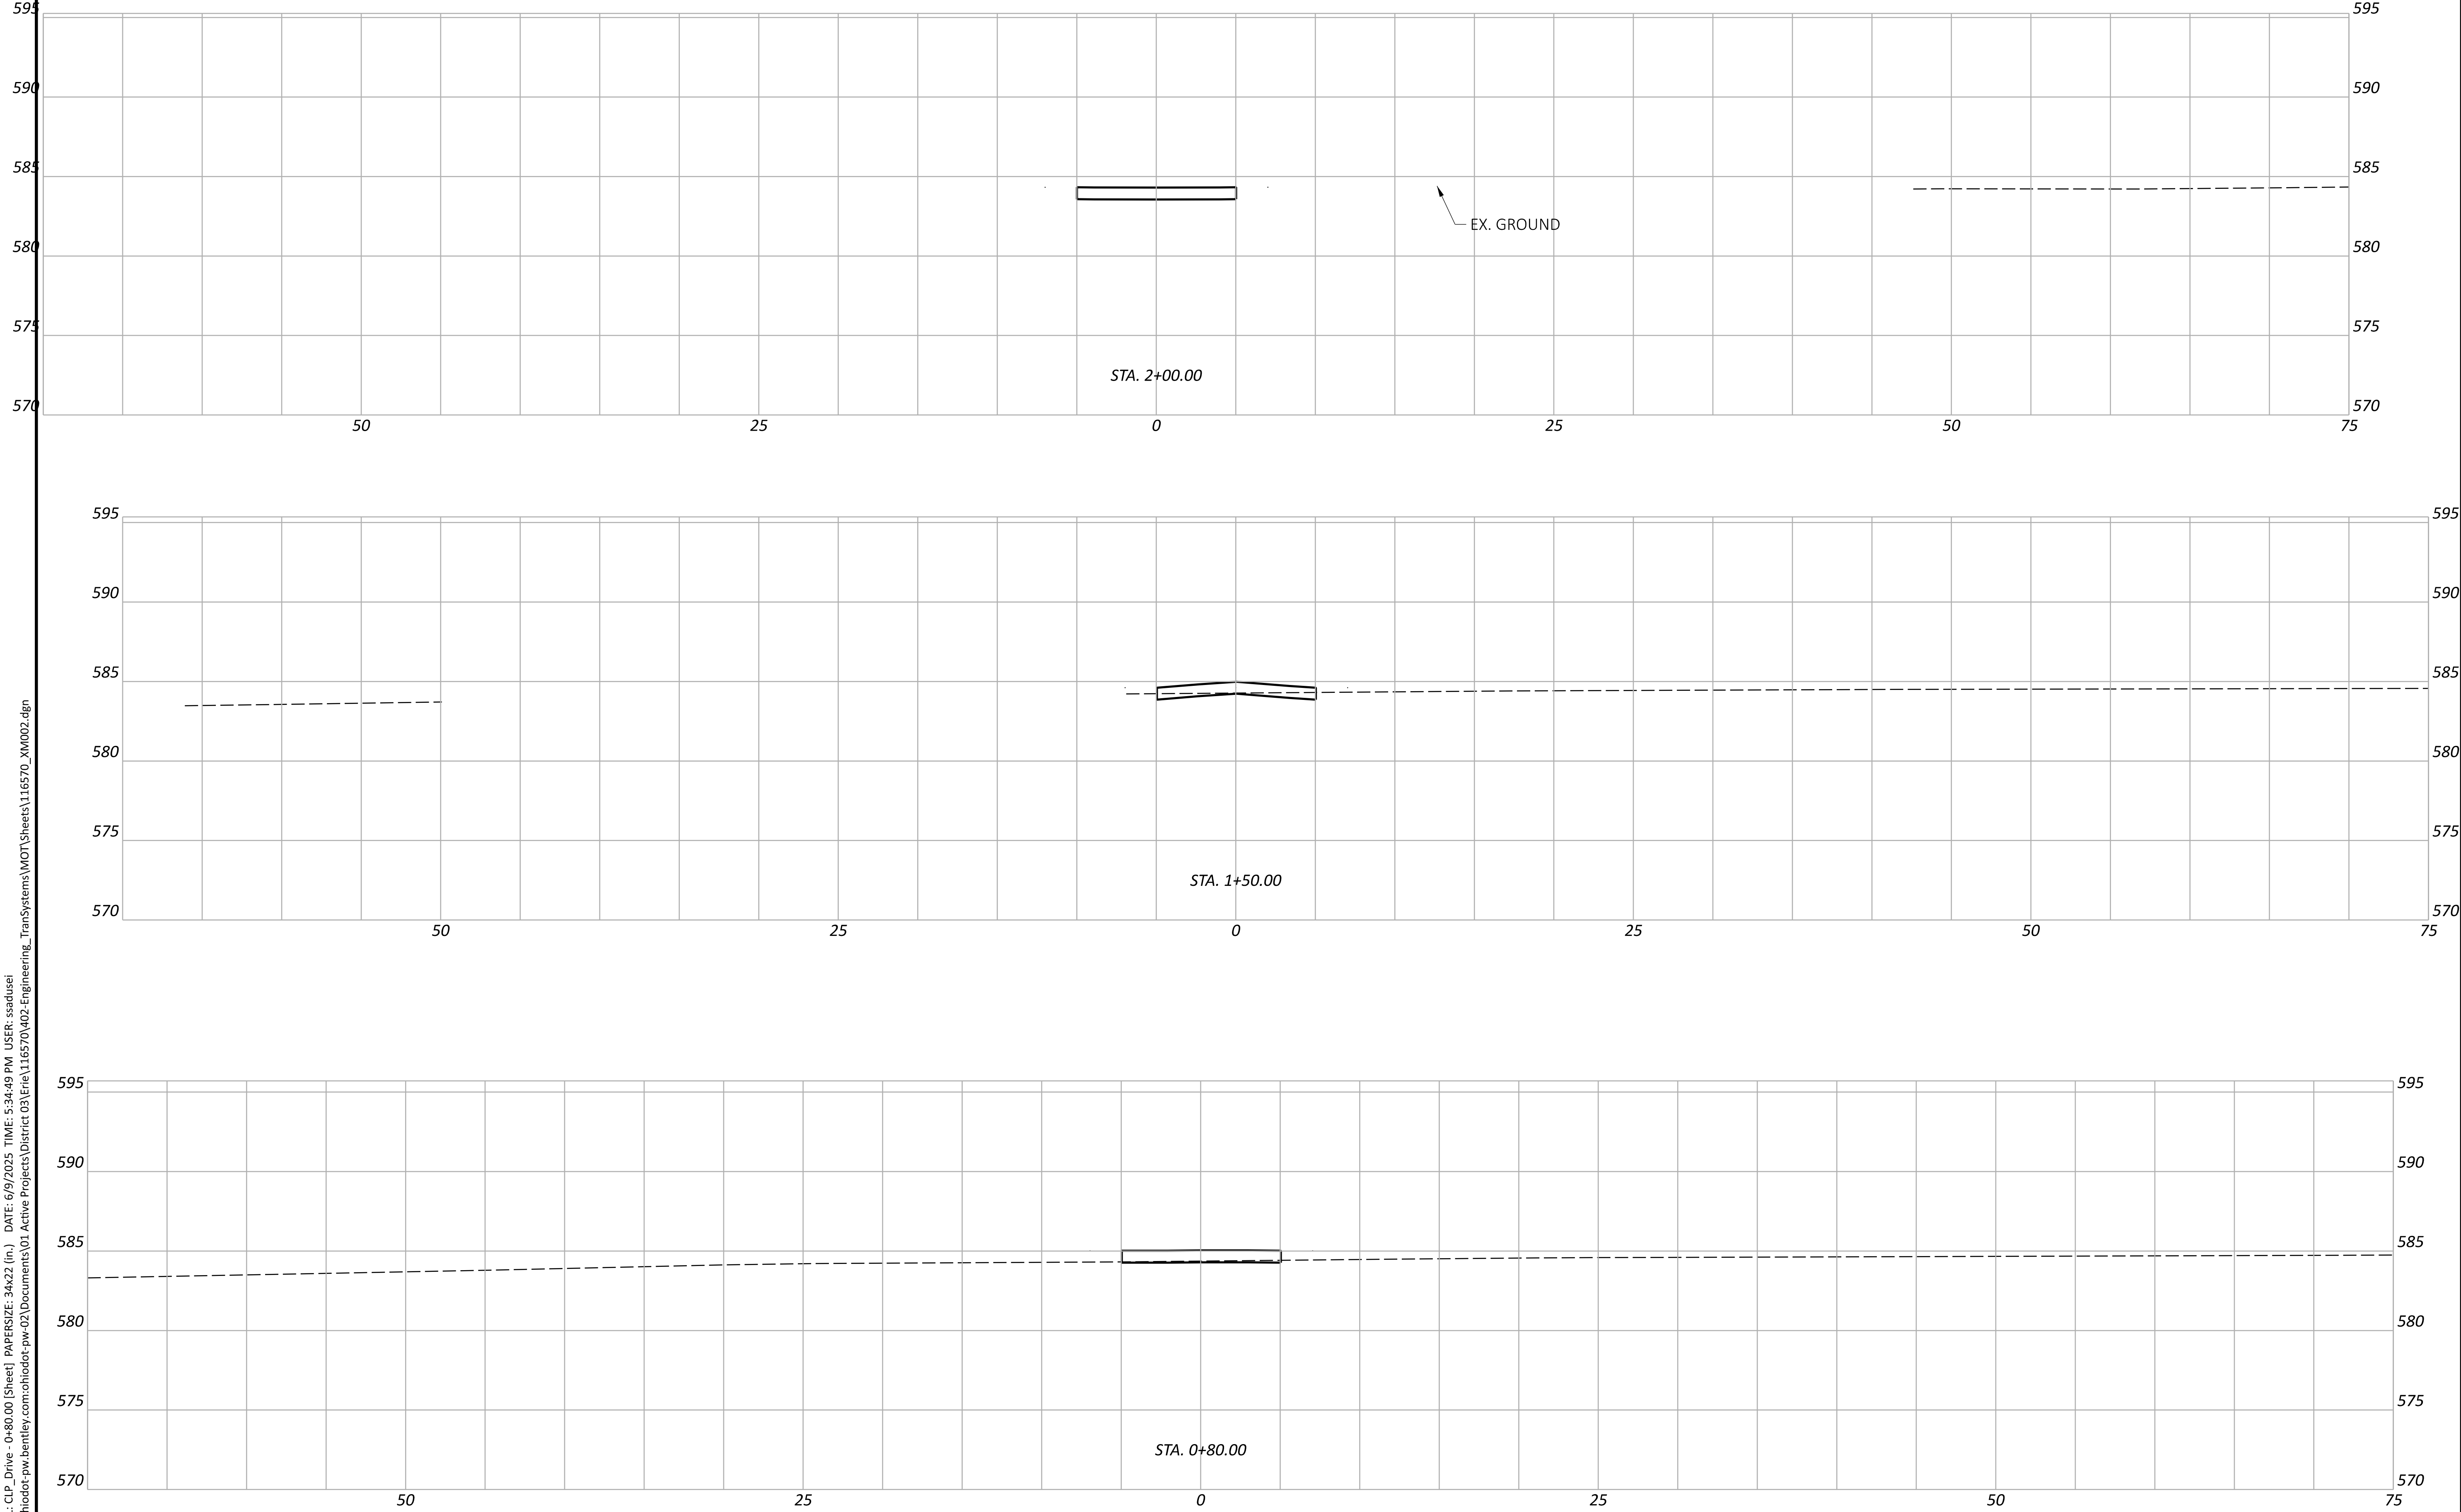

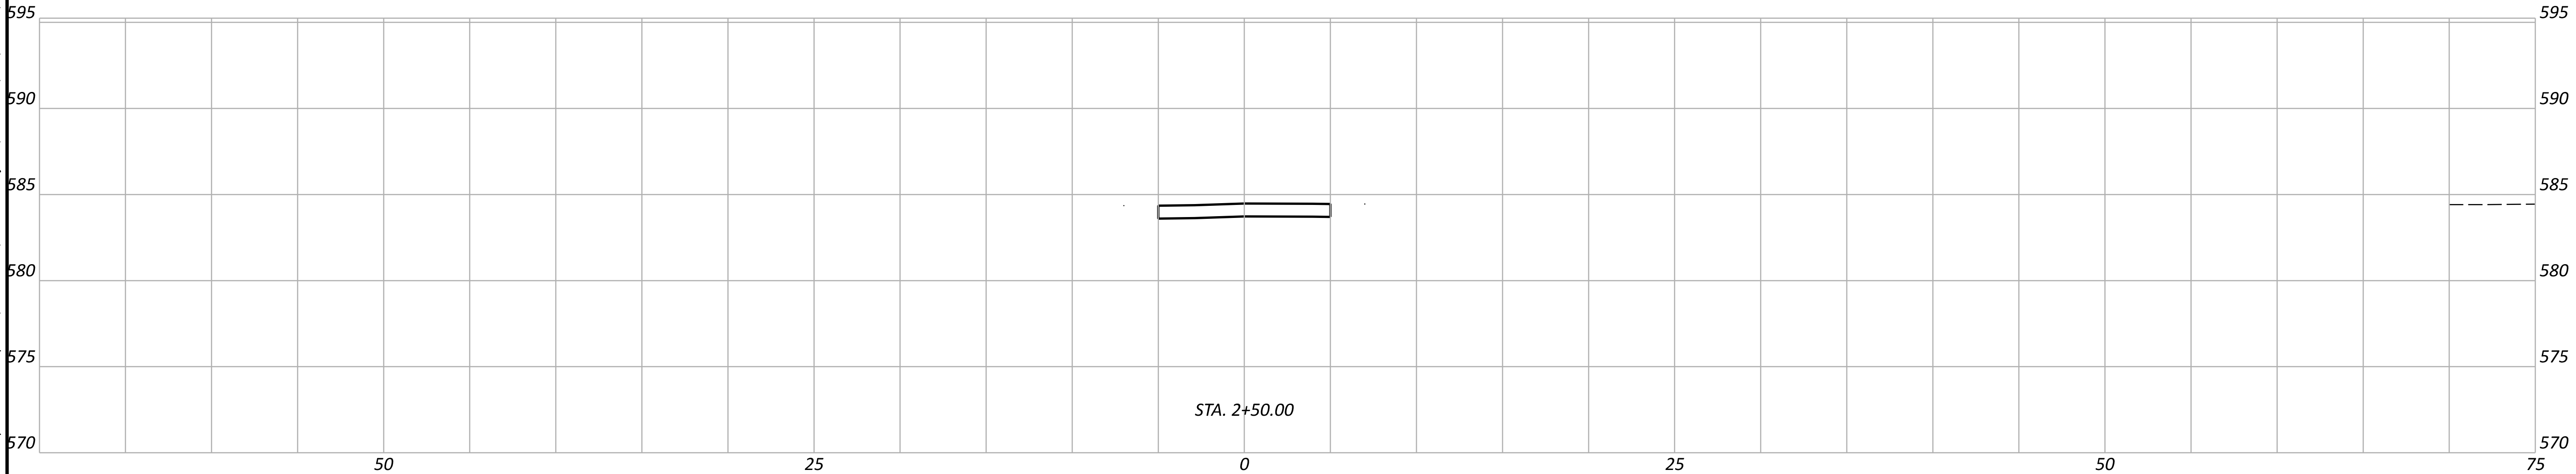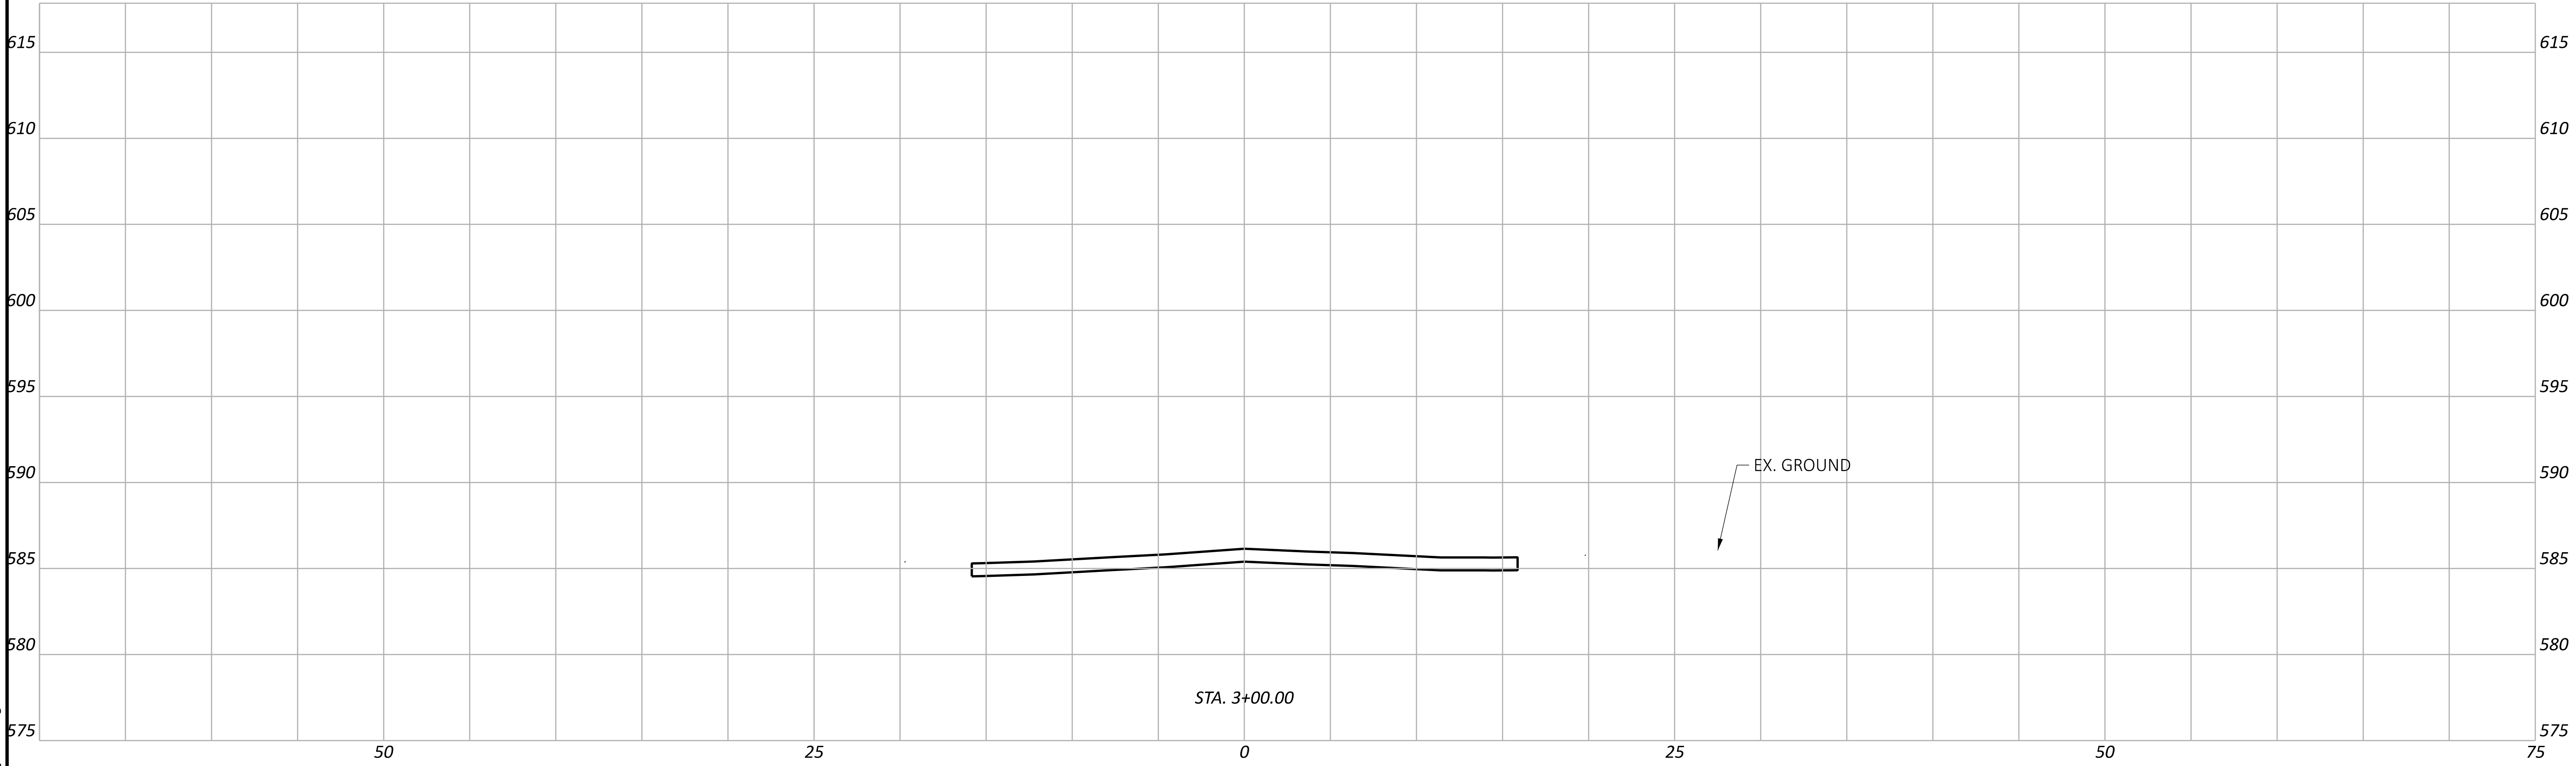

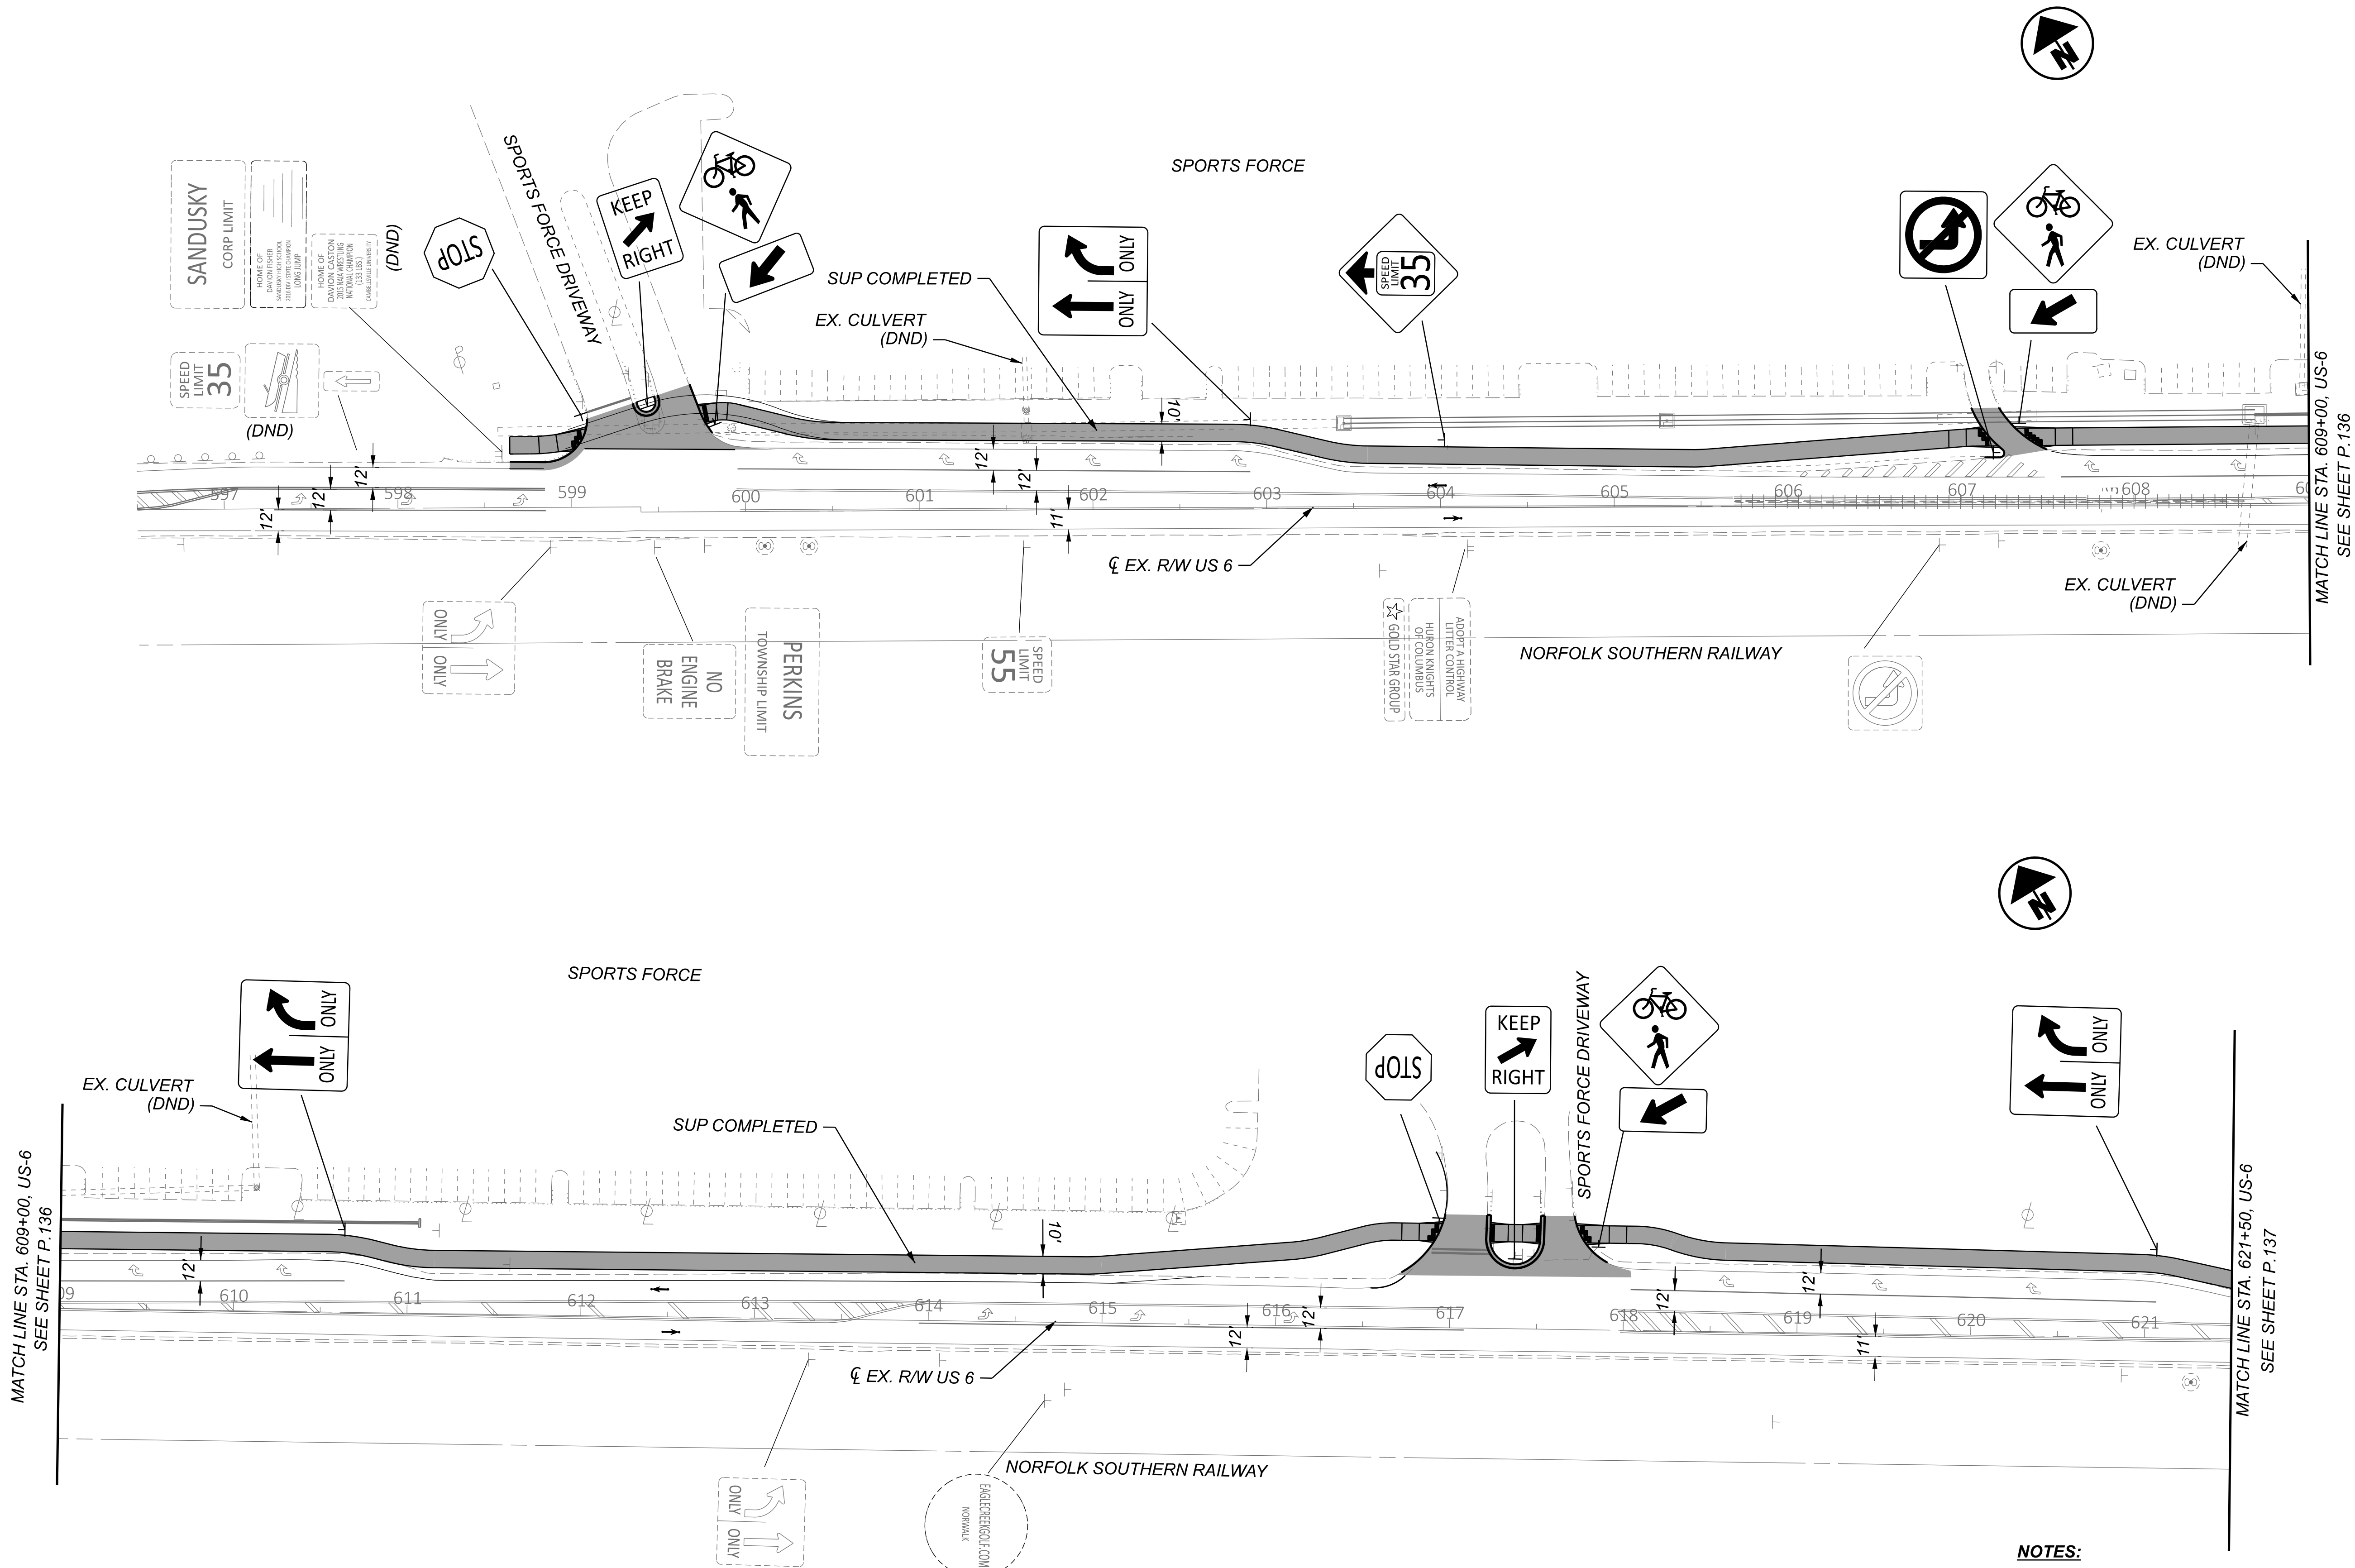



- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - BEGIN PROJECT TO STA. 621+50


TRANSYSTEMS
400 W. WATSONWIDE BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.139	782



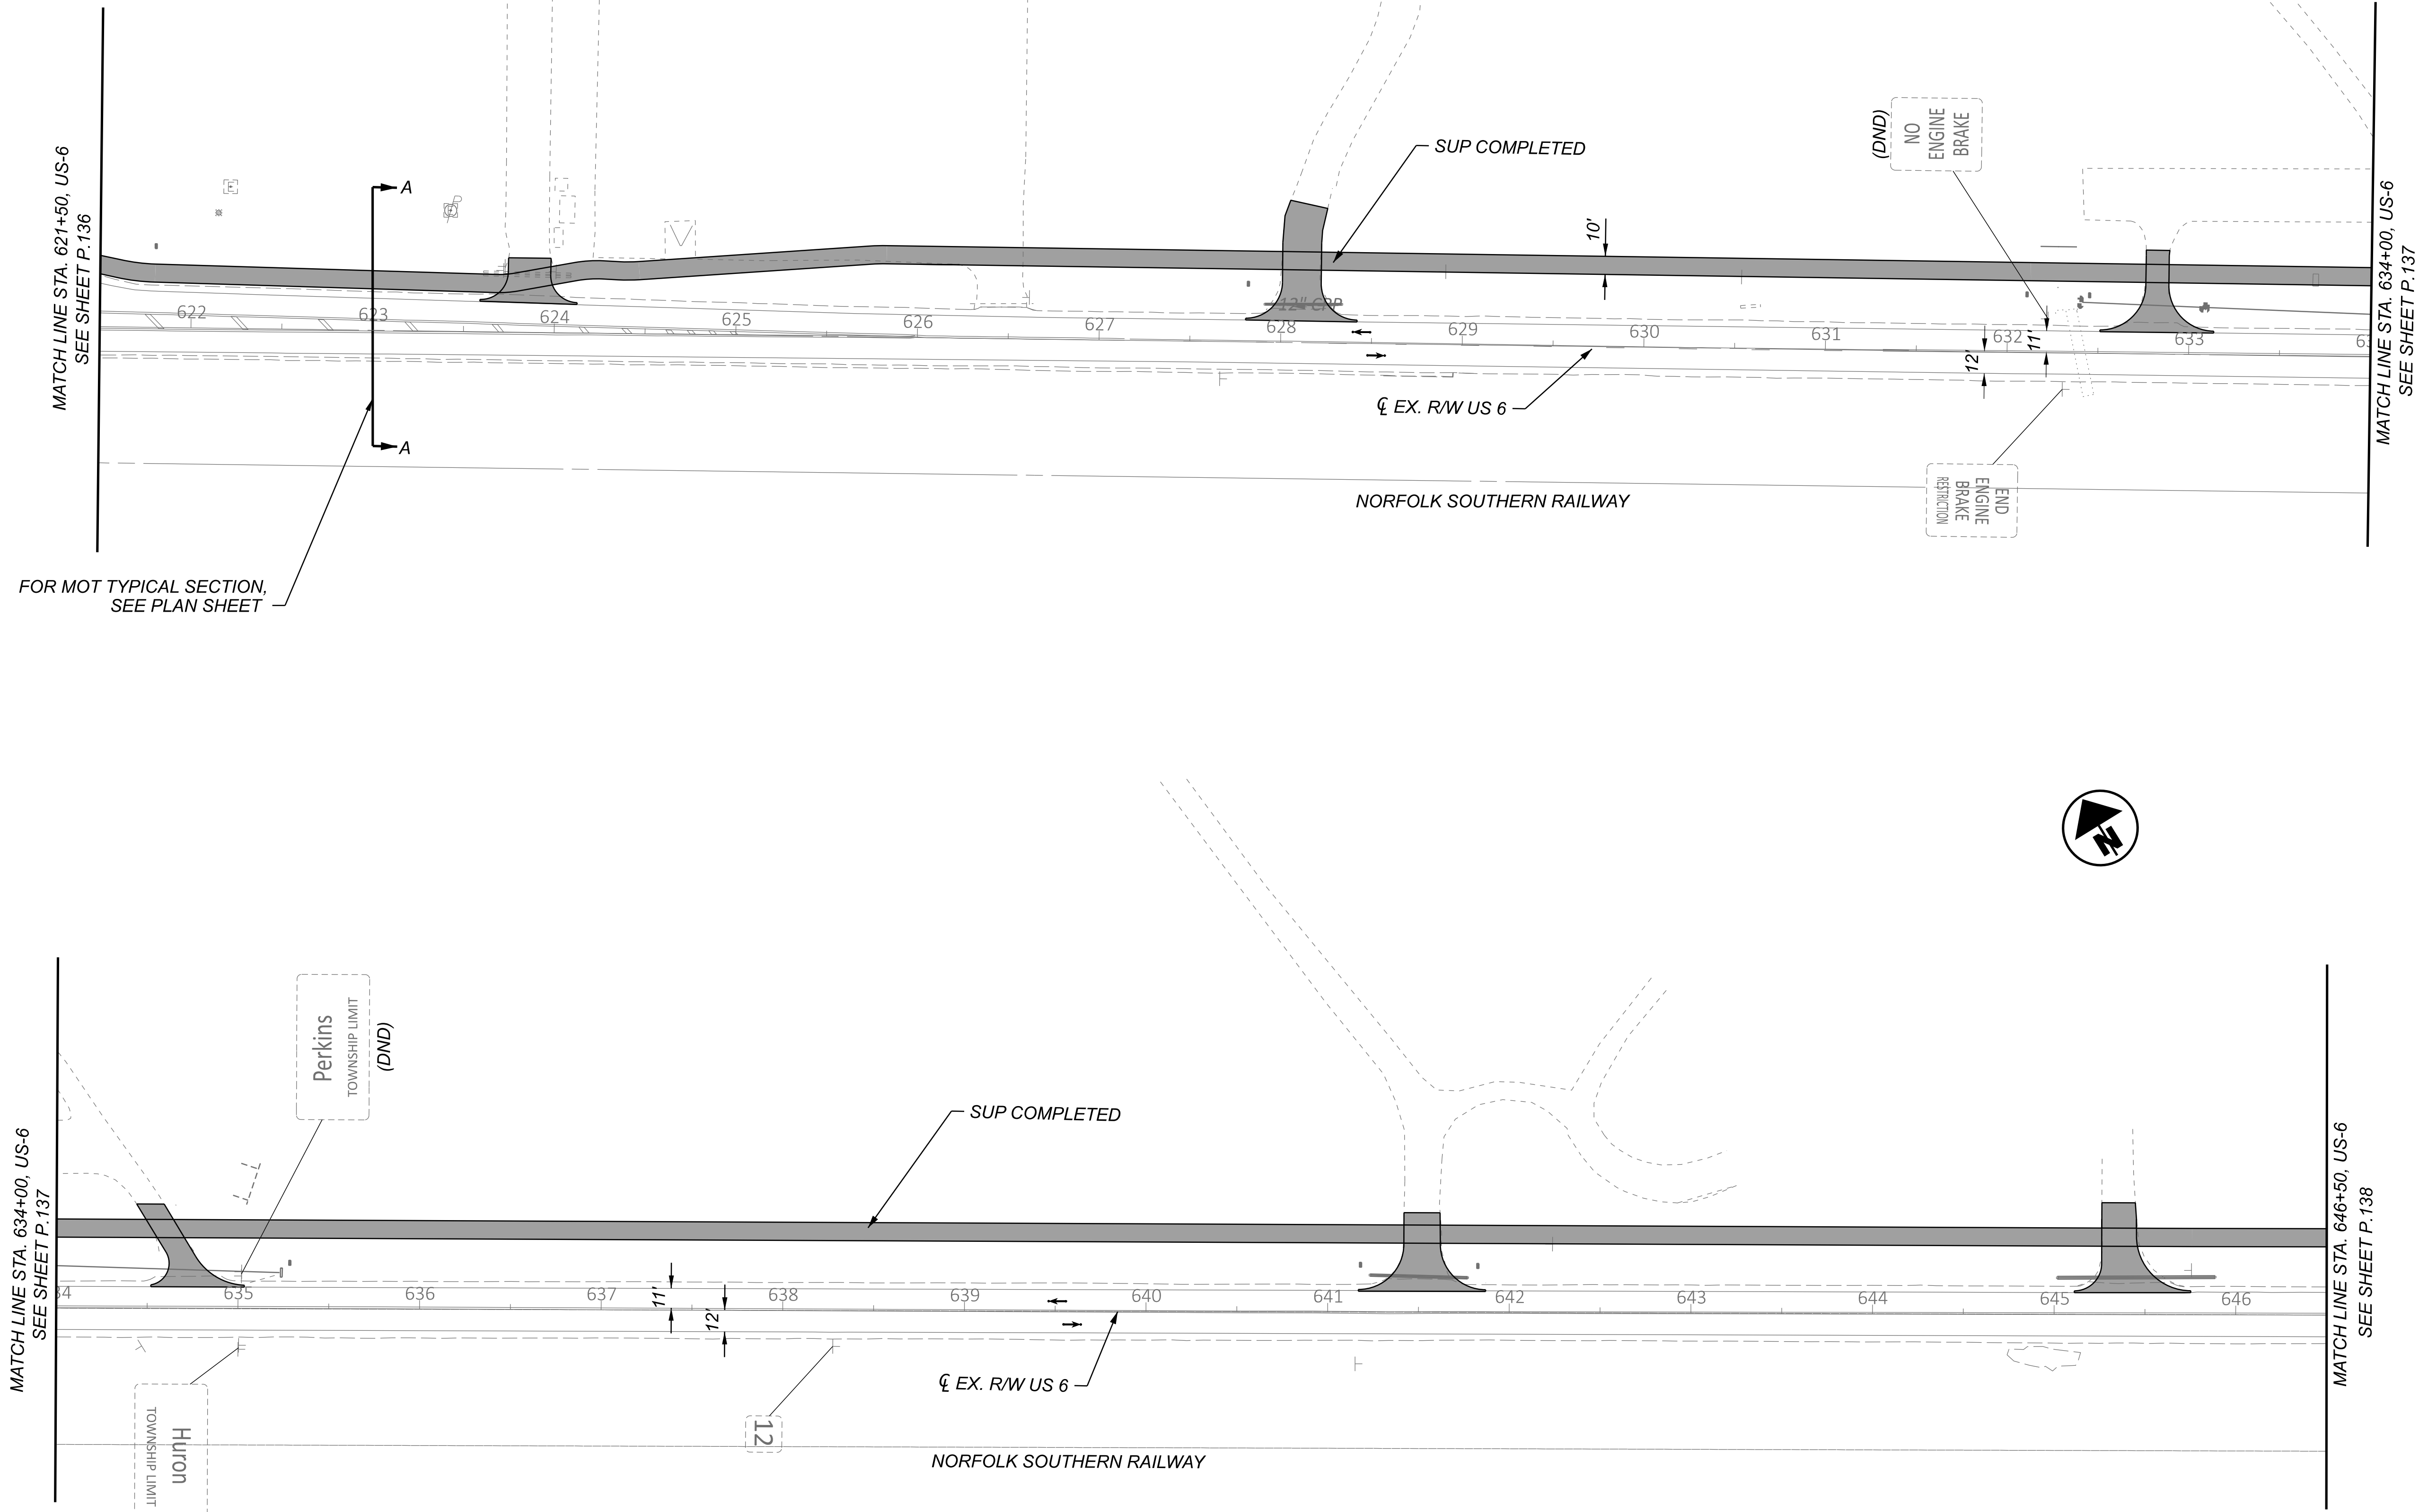


NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. FOR SECTION A-A, SEE SHEET P.109.
4. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALLTIMES. USE FLAGGING OPERATION AS NECESSARY.

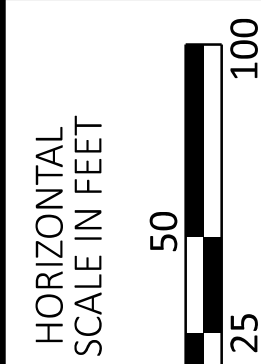

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 621+50.00 TO STA. 646+50.00


DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	TOTAL
P.140	782

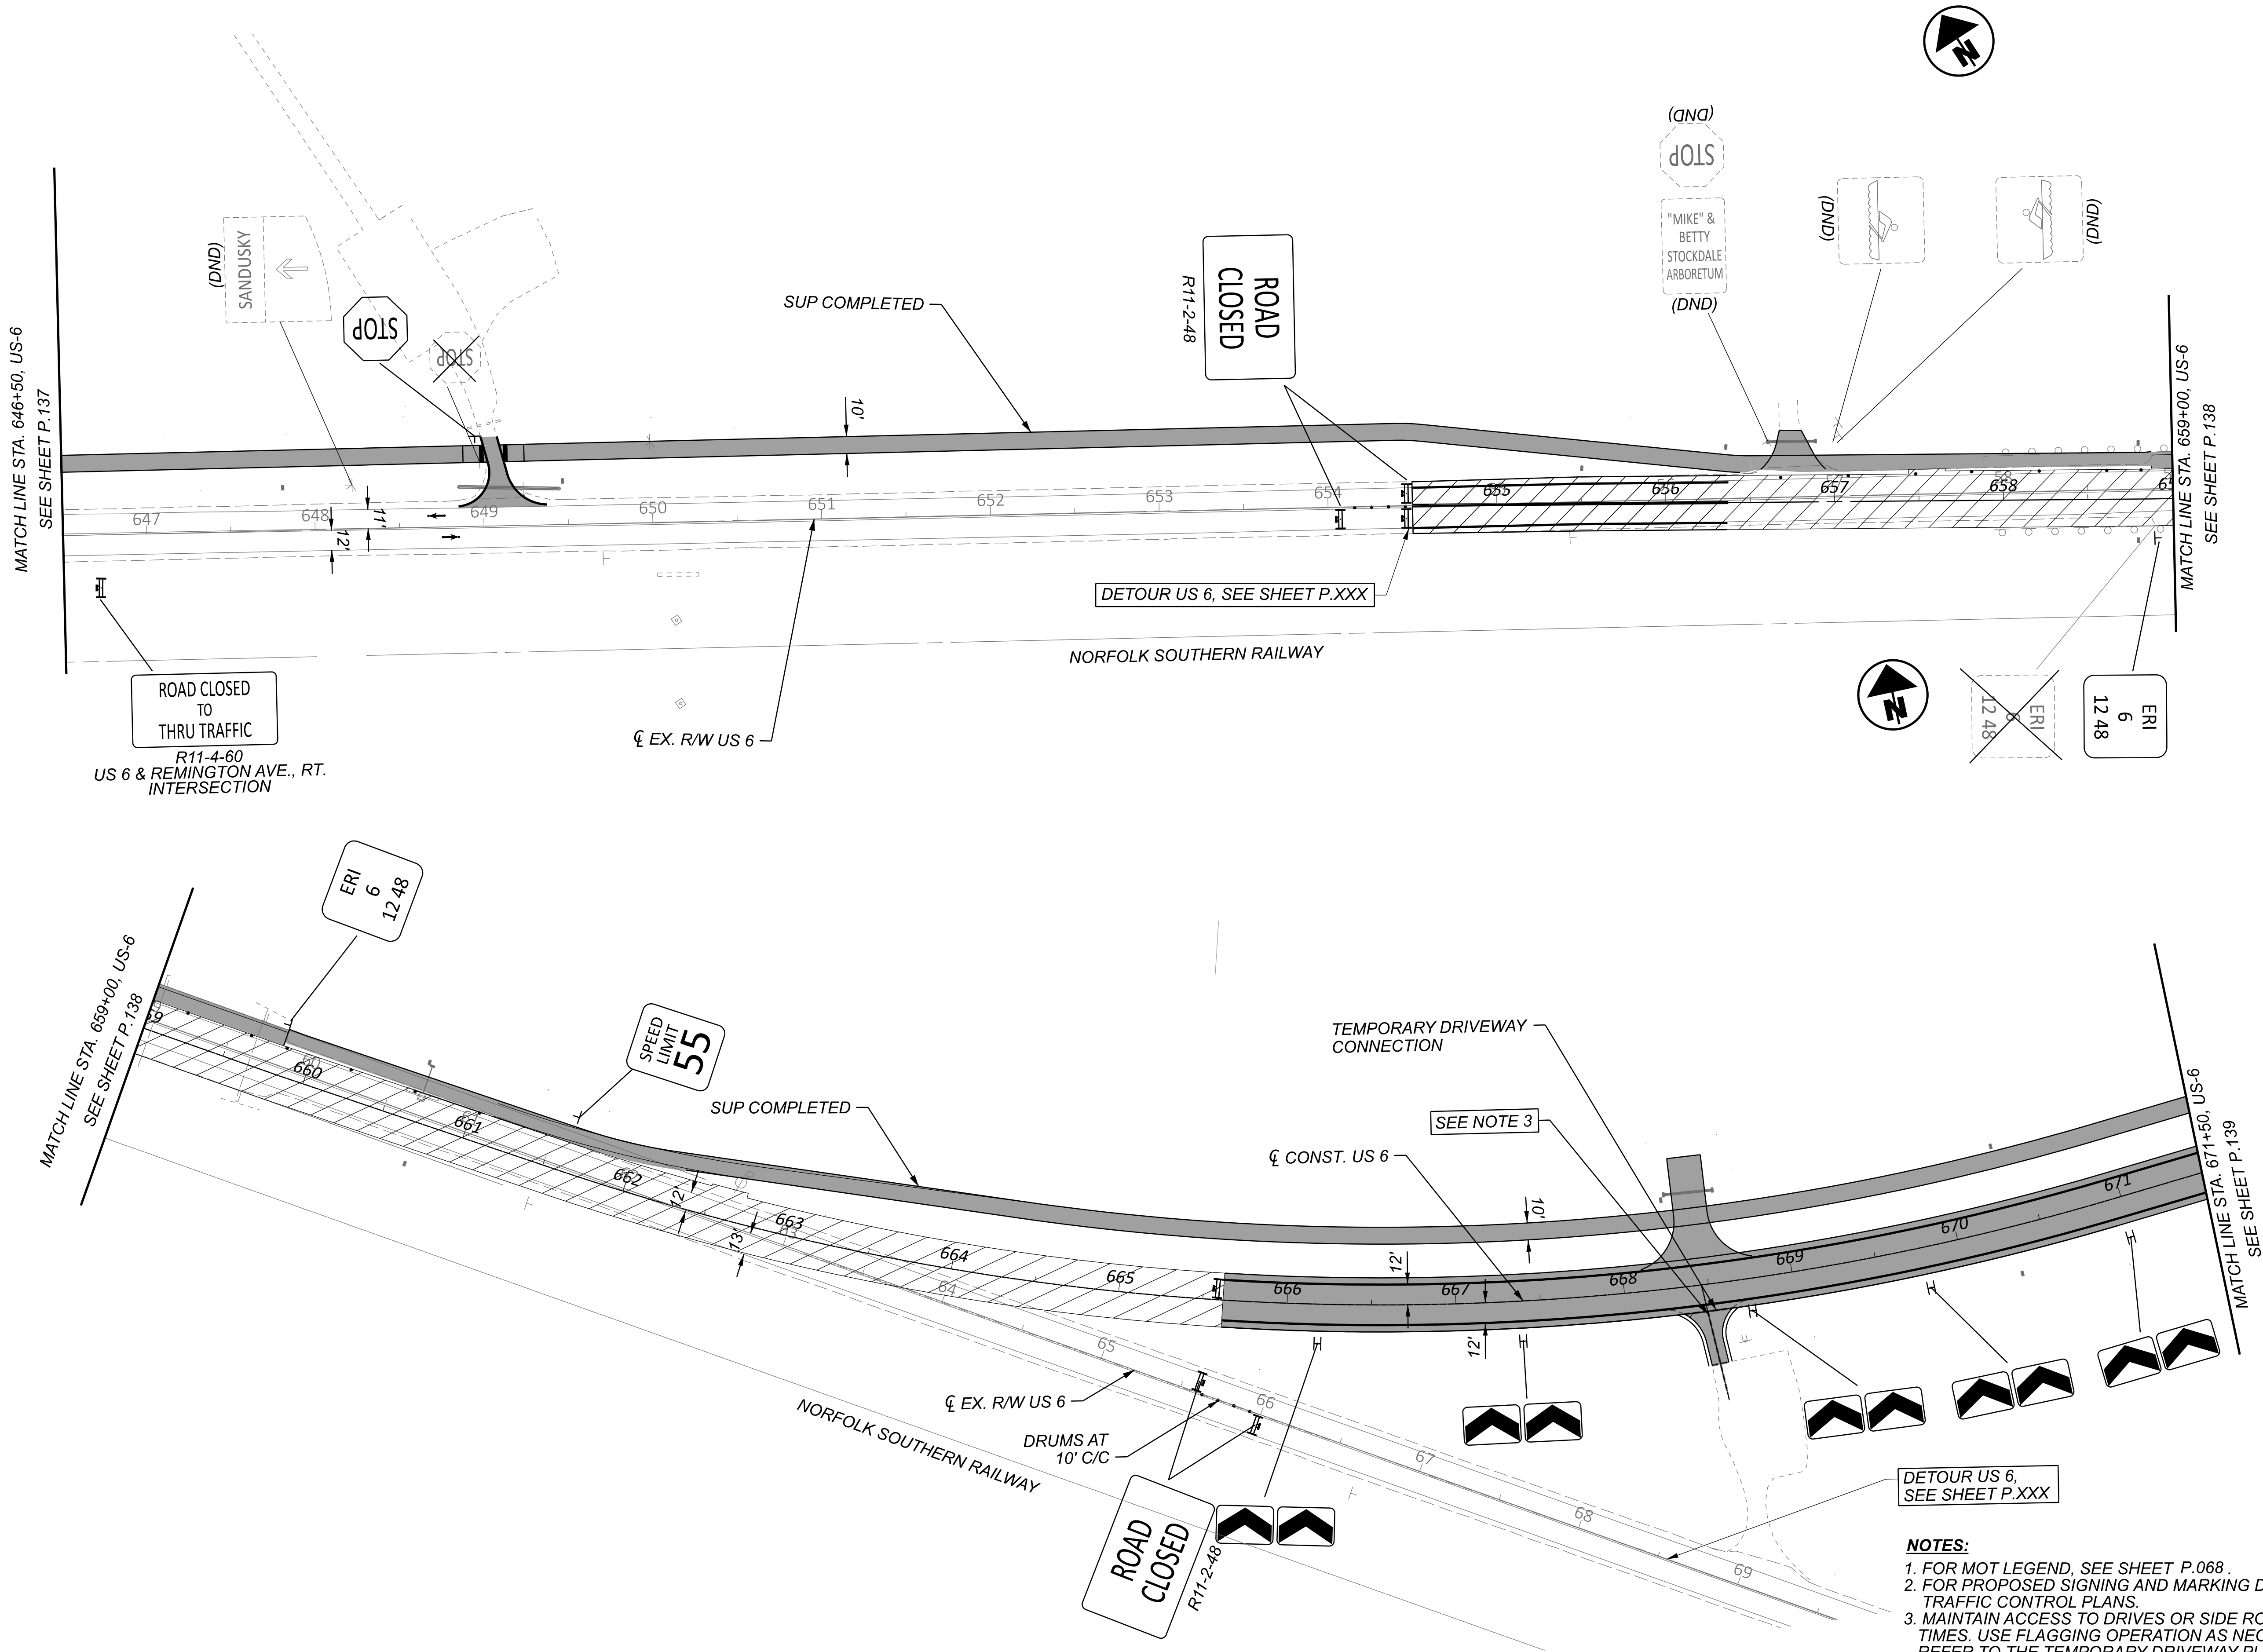


NOTES:
1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 646+50.00 TO STA. 671+50.00


DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.141	782

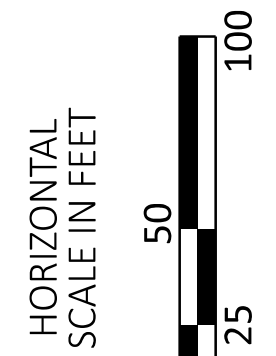

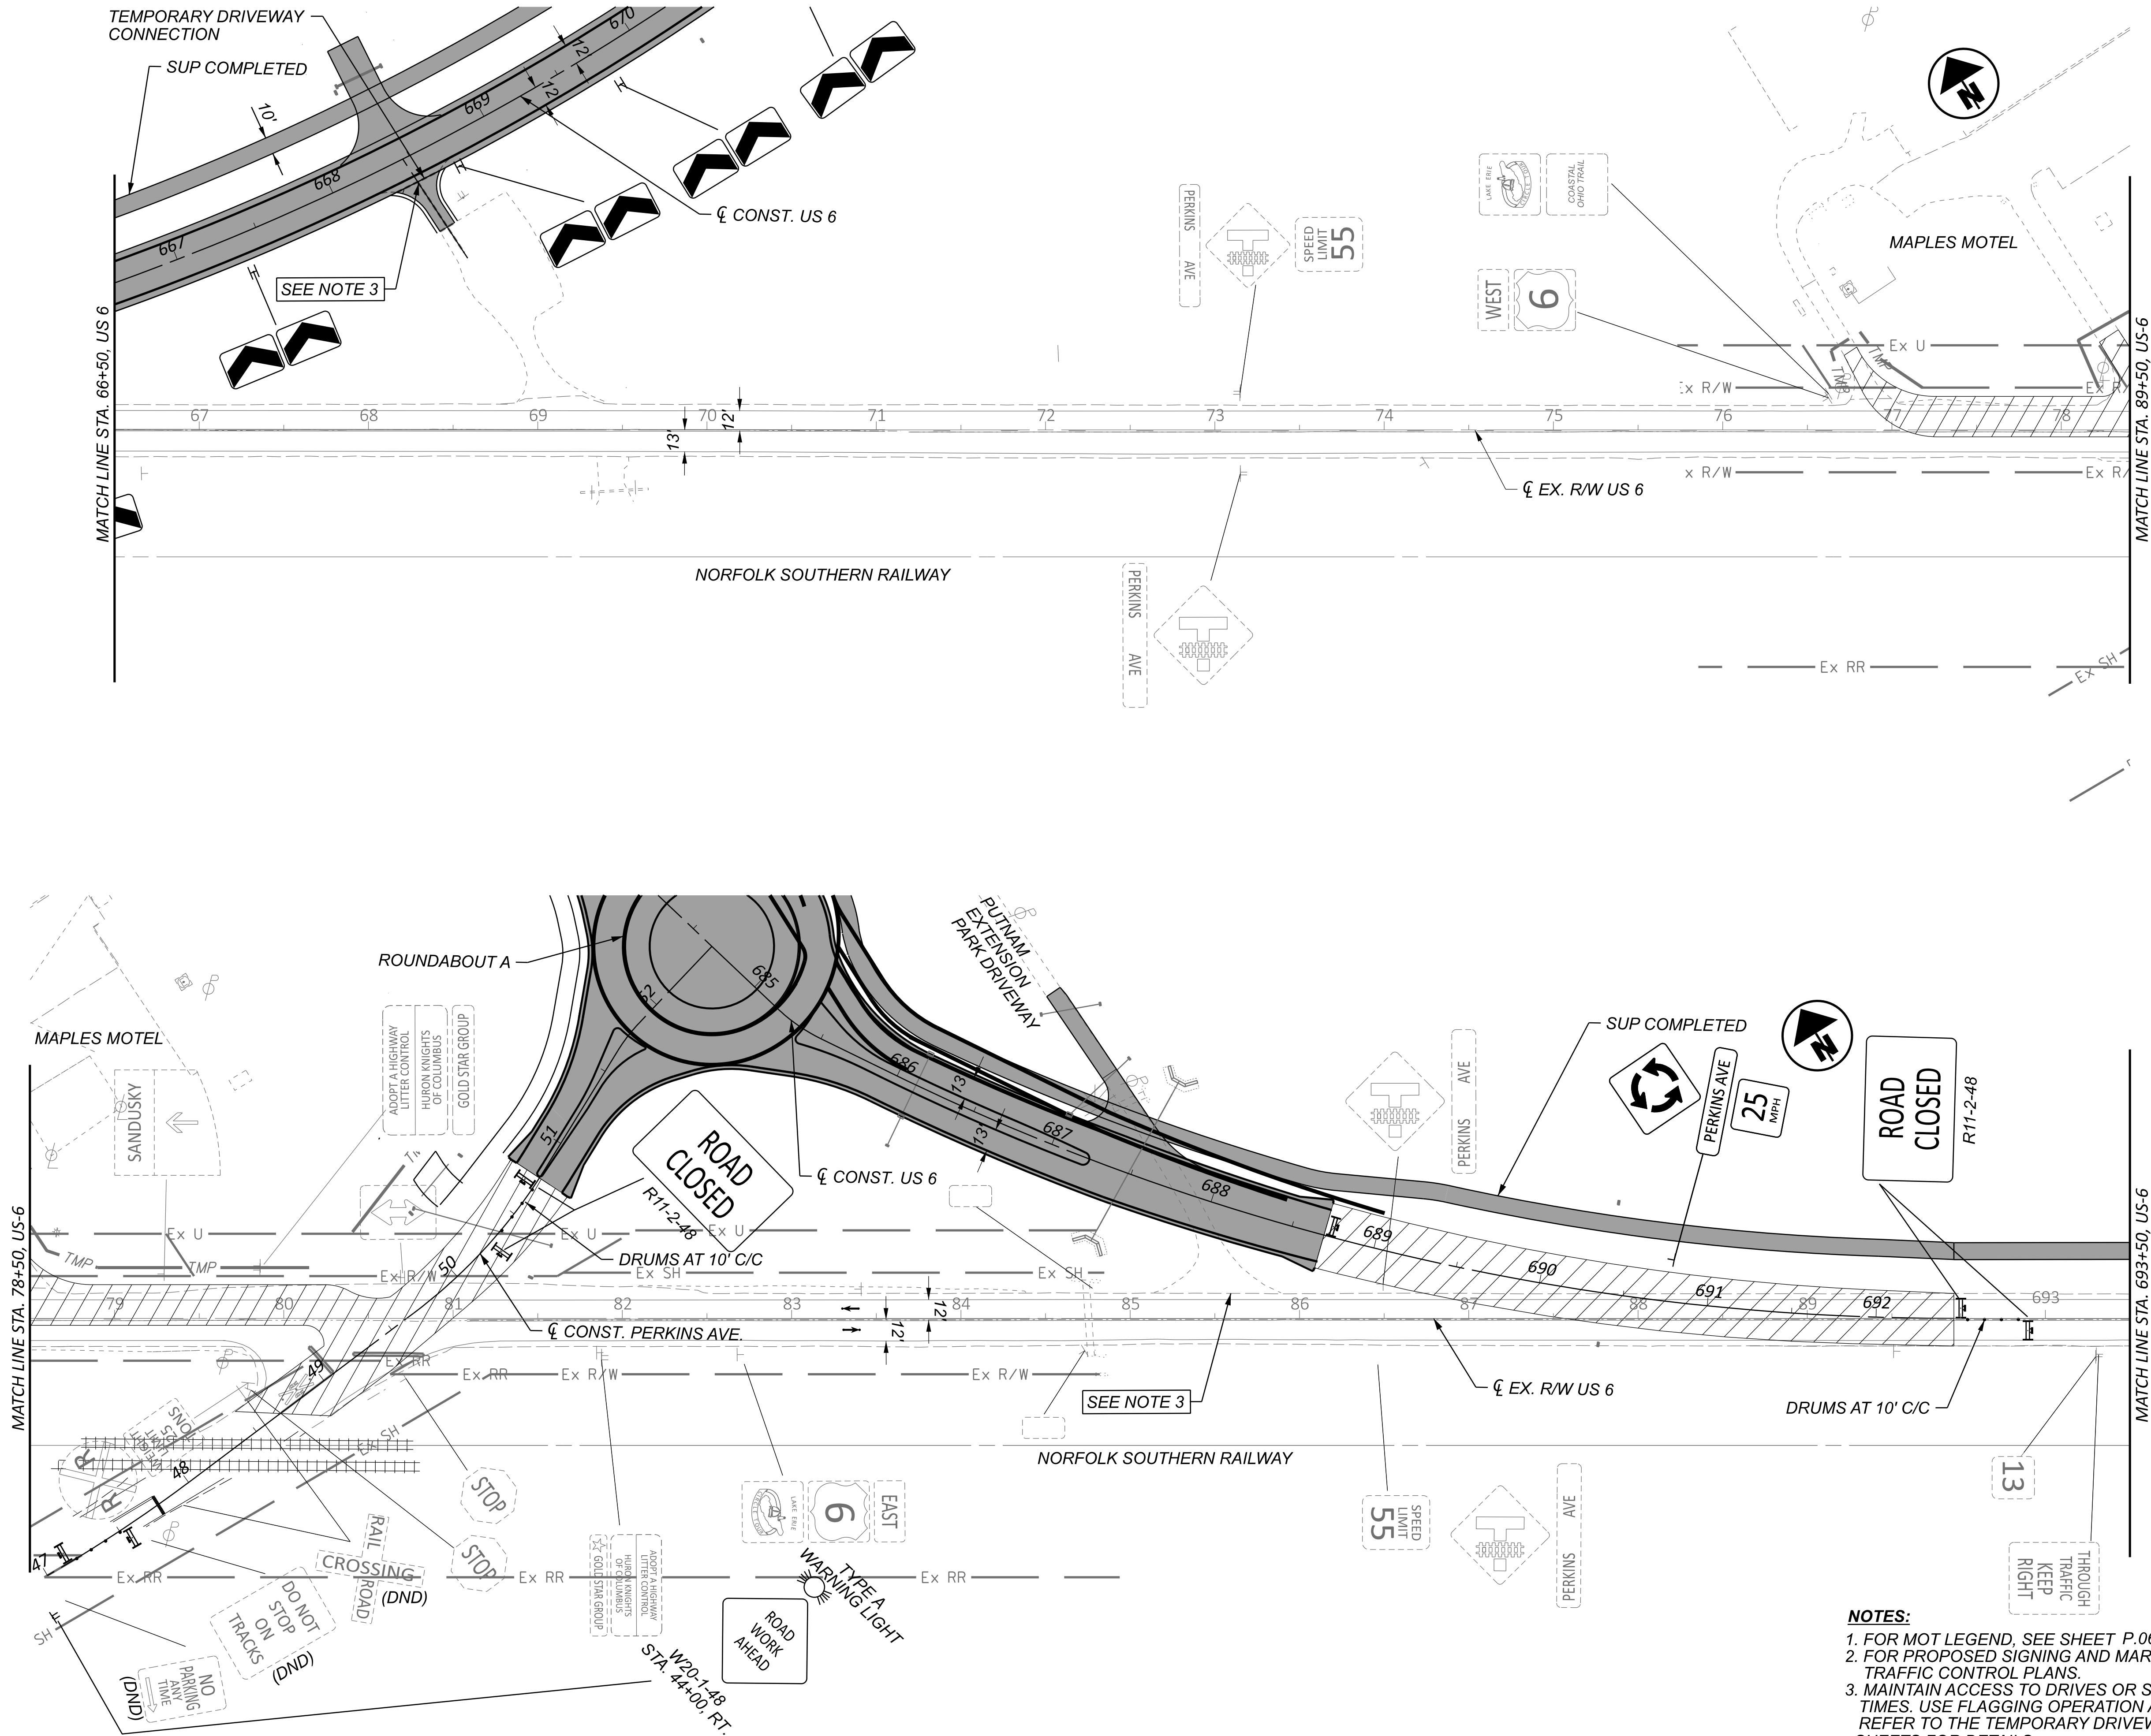

- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY. REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.


MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 67+00.00 EX. US 6 TO 693+50.00 CONST. US 6 SUP



DESIGN AGENCY	
TRANSYSTEMS	
400 W. WATSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.142	TOTAL 782

ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 1 - Plan 9-10 [Sheet] PAPER SIZE: 34x22 (in) DATE: 6/9/2025 TIME: 5:35:30 PM USER: ssadusei
 \\pw\ohiodor-pw.bentley.com:ohiodor-pw-02\Documents\01 Active Projects\District 03\Erie\116570\402-Engineering_TransSystems\TransSystems\MOT\Sheets\116570_MP001_2026.dgn

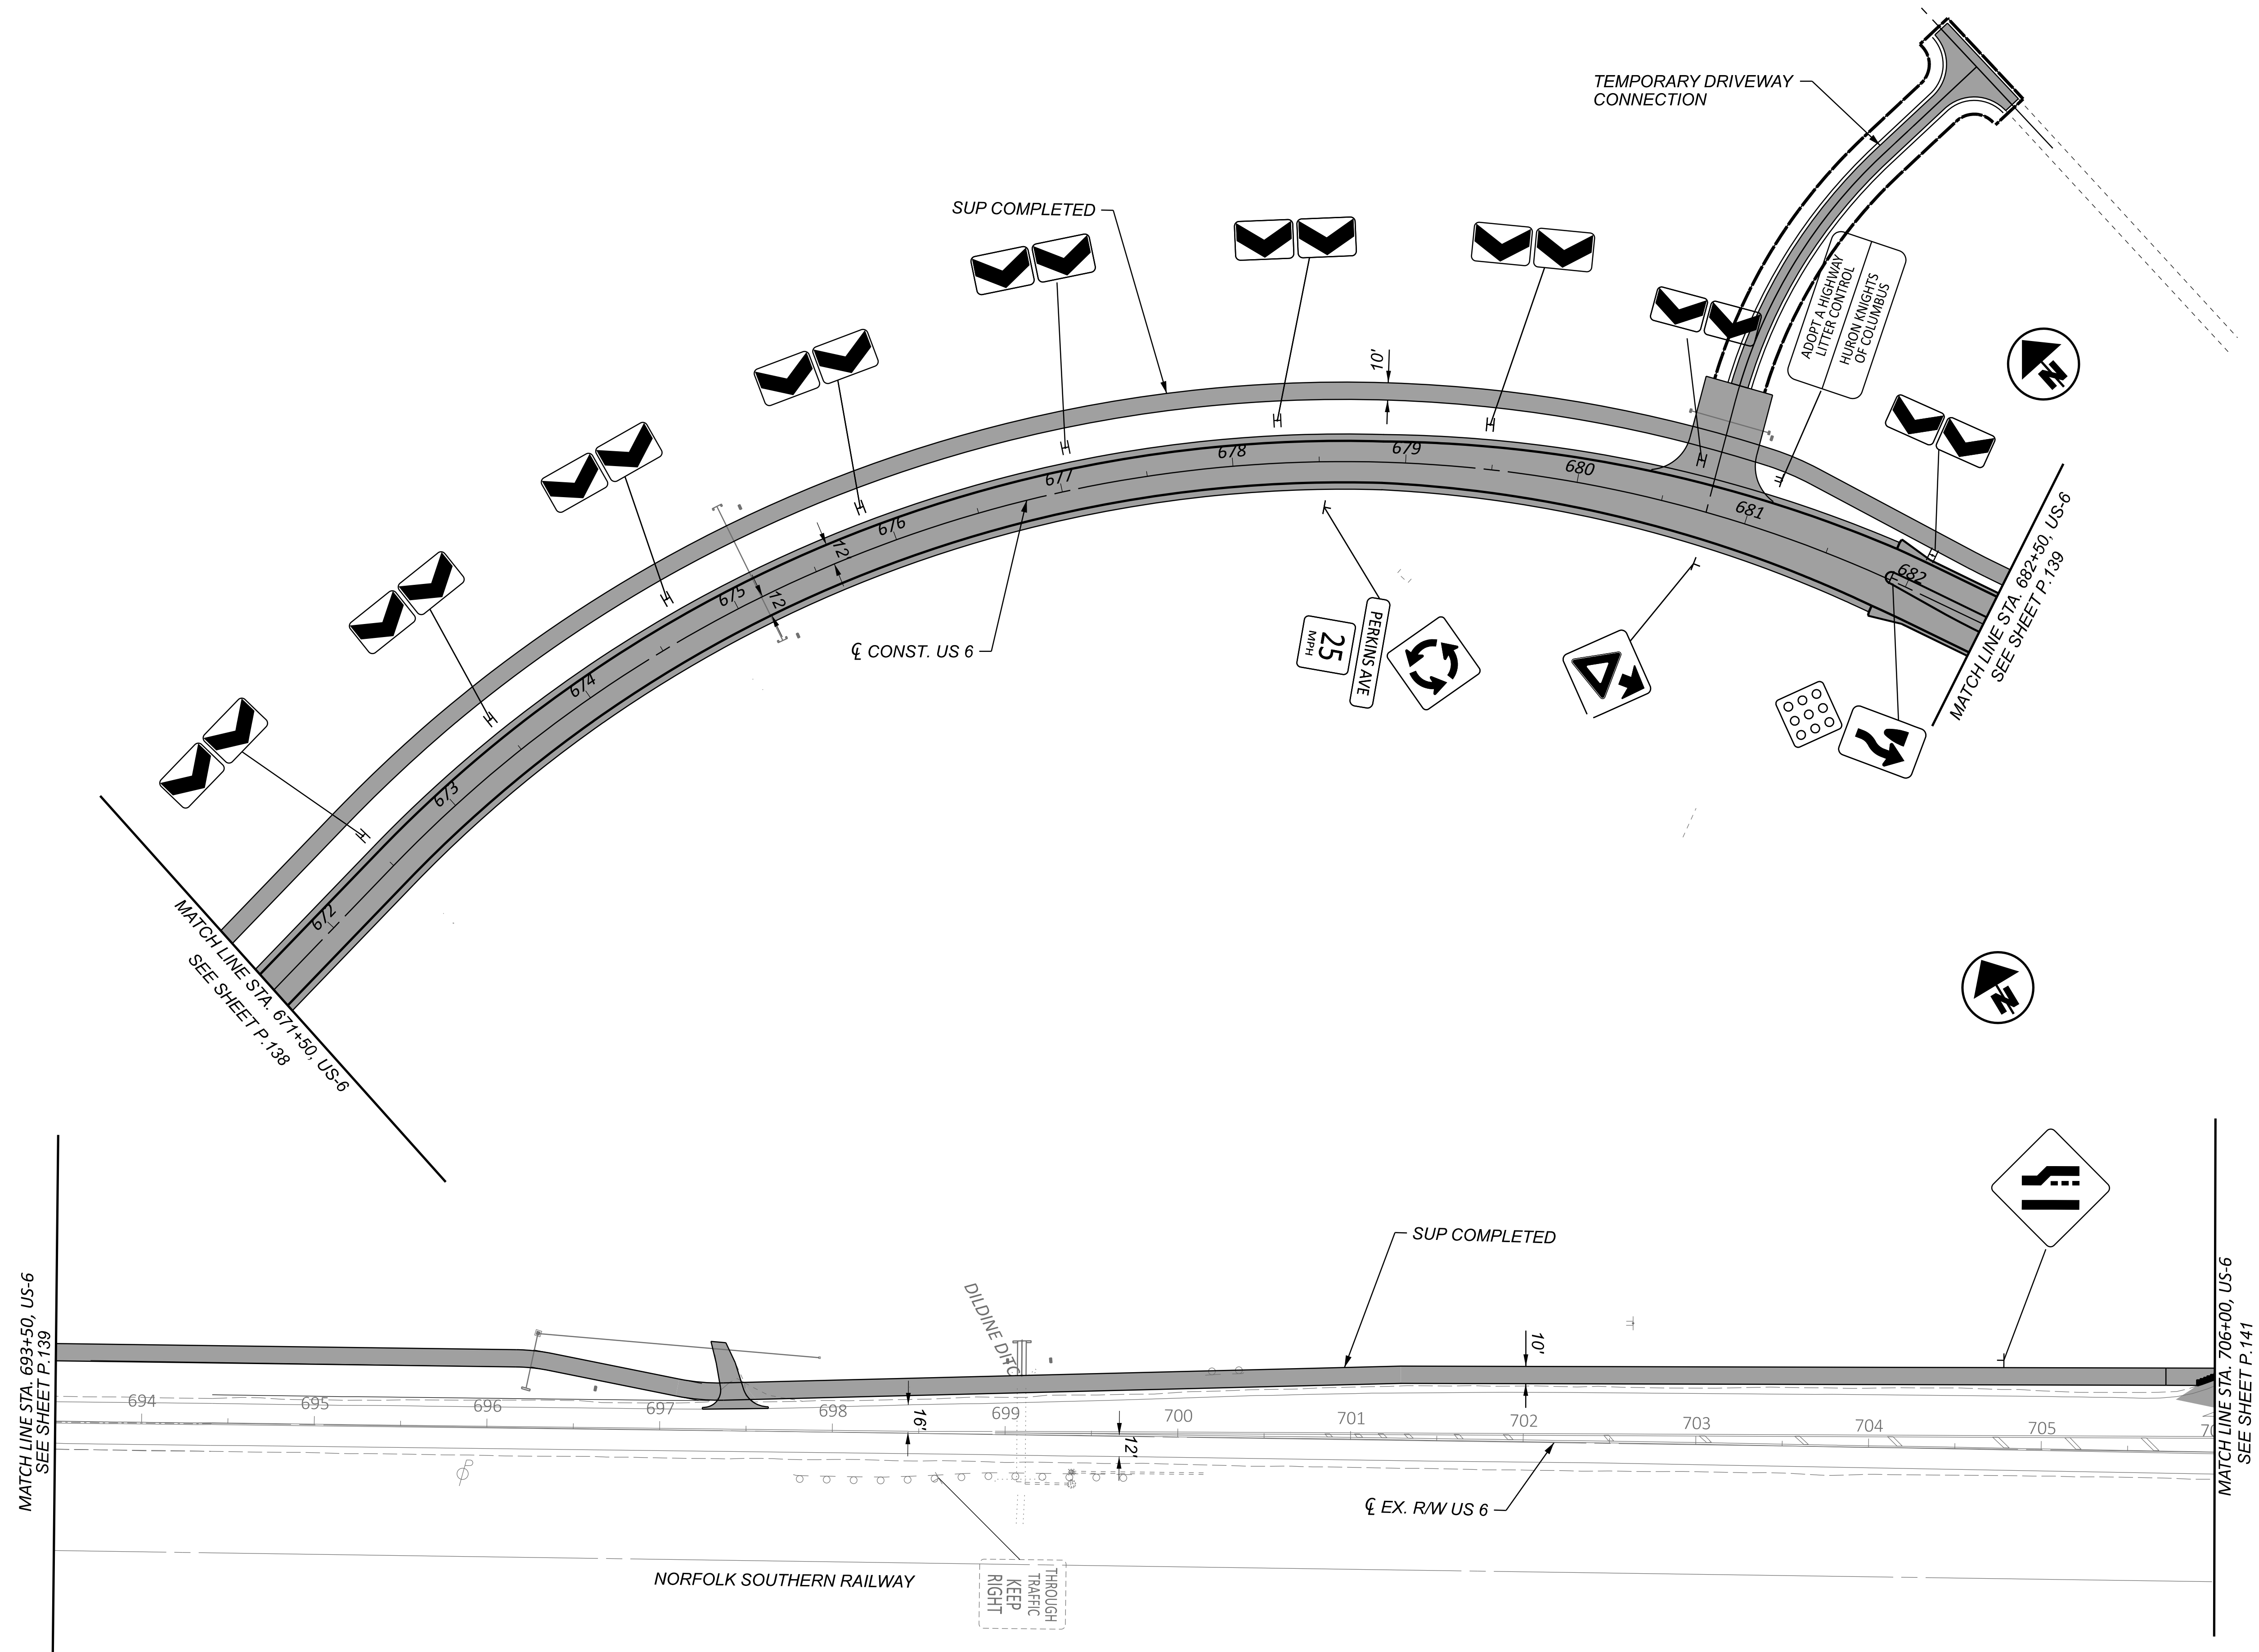



NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION) US 6 - STA. 671+50.00 TO STA. 706+00.00	HORIZONTAL SCALE IN FEET
--	-------------------------------------

DESIGN AGENCY	
TRANSYSTEMS	400 W. NATIONWIDE BLVD., STE 228 COLUMBUS, OHIO 43215
DESIGNER	
SSA	
REVIEWER	
SS	02/28/
PROJECT ID	
116570	
SHEET	TOTAL
P.143	78

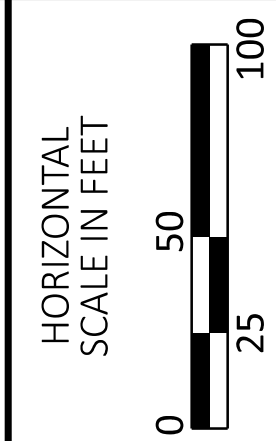



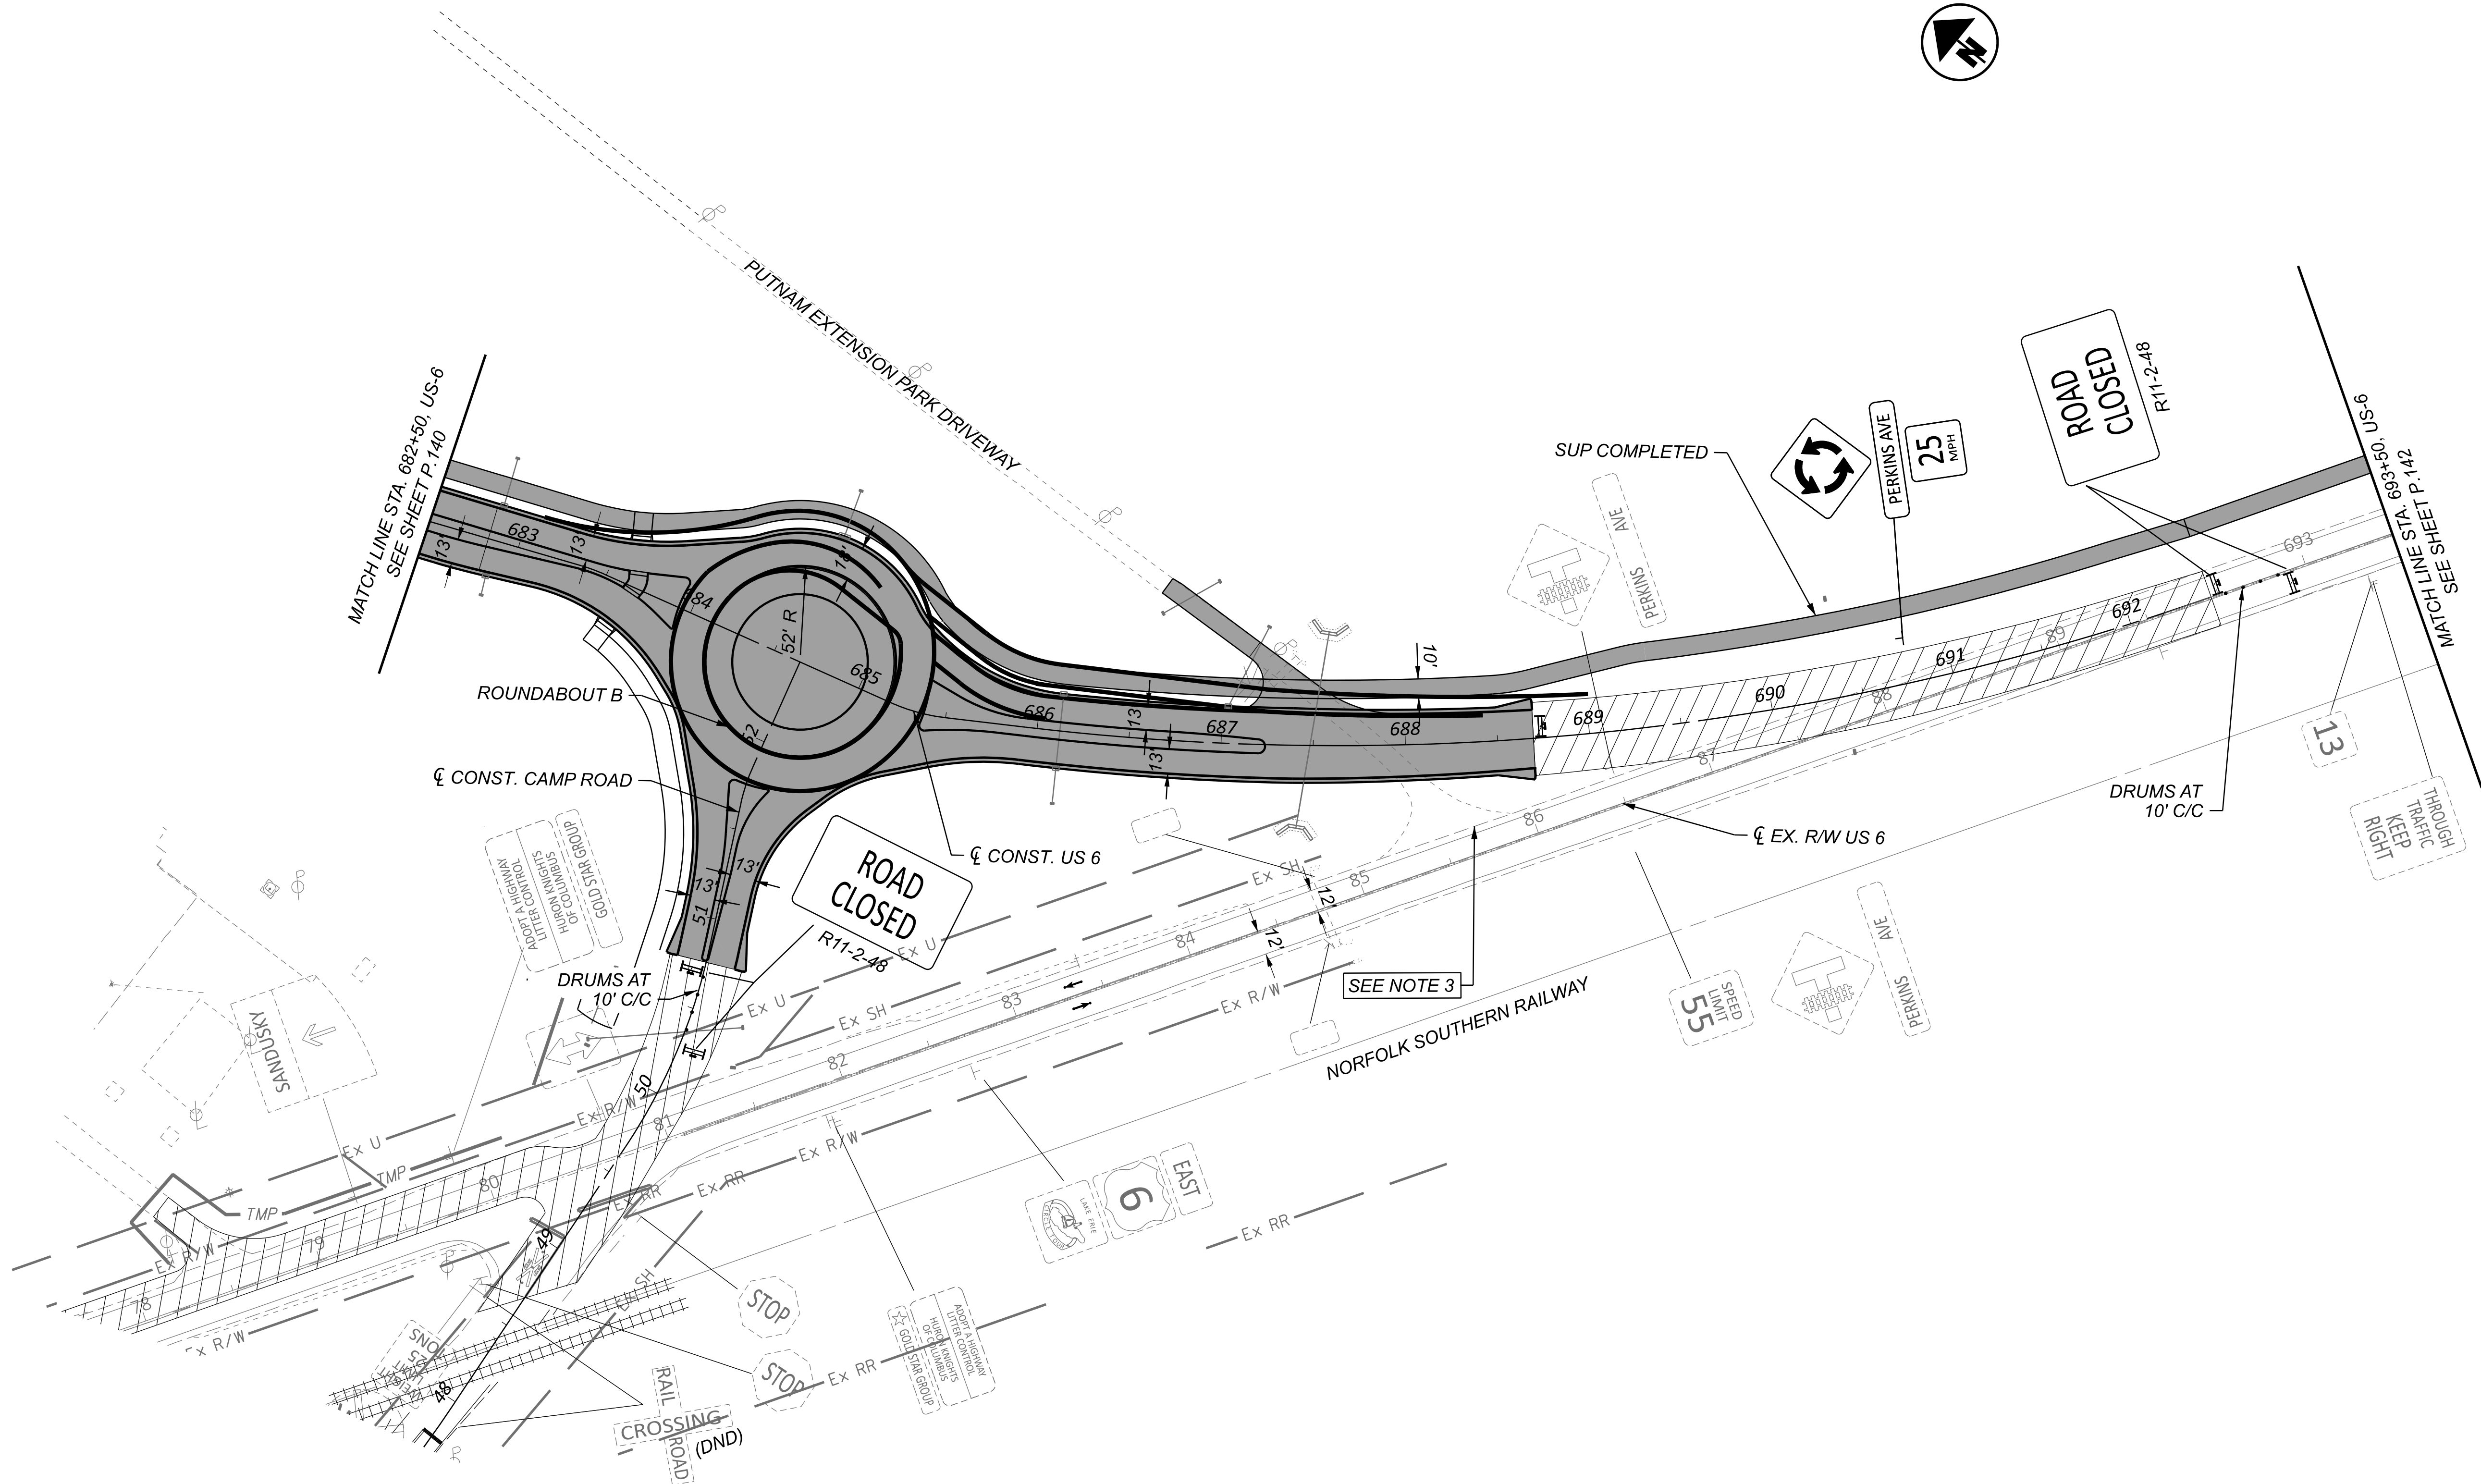


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.
REFER TO THE TEMPORARY DRIVEWAY PLAN & PROFILE SHEETS FOR DETAILS.

DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS
PROJECT ID	02/28/24
	116570
SHEET	TOTAL
P.144	782

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 683+00.00 TO STA. 693+50.00




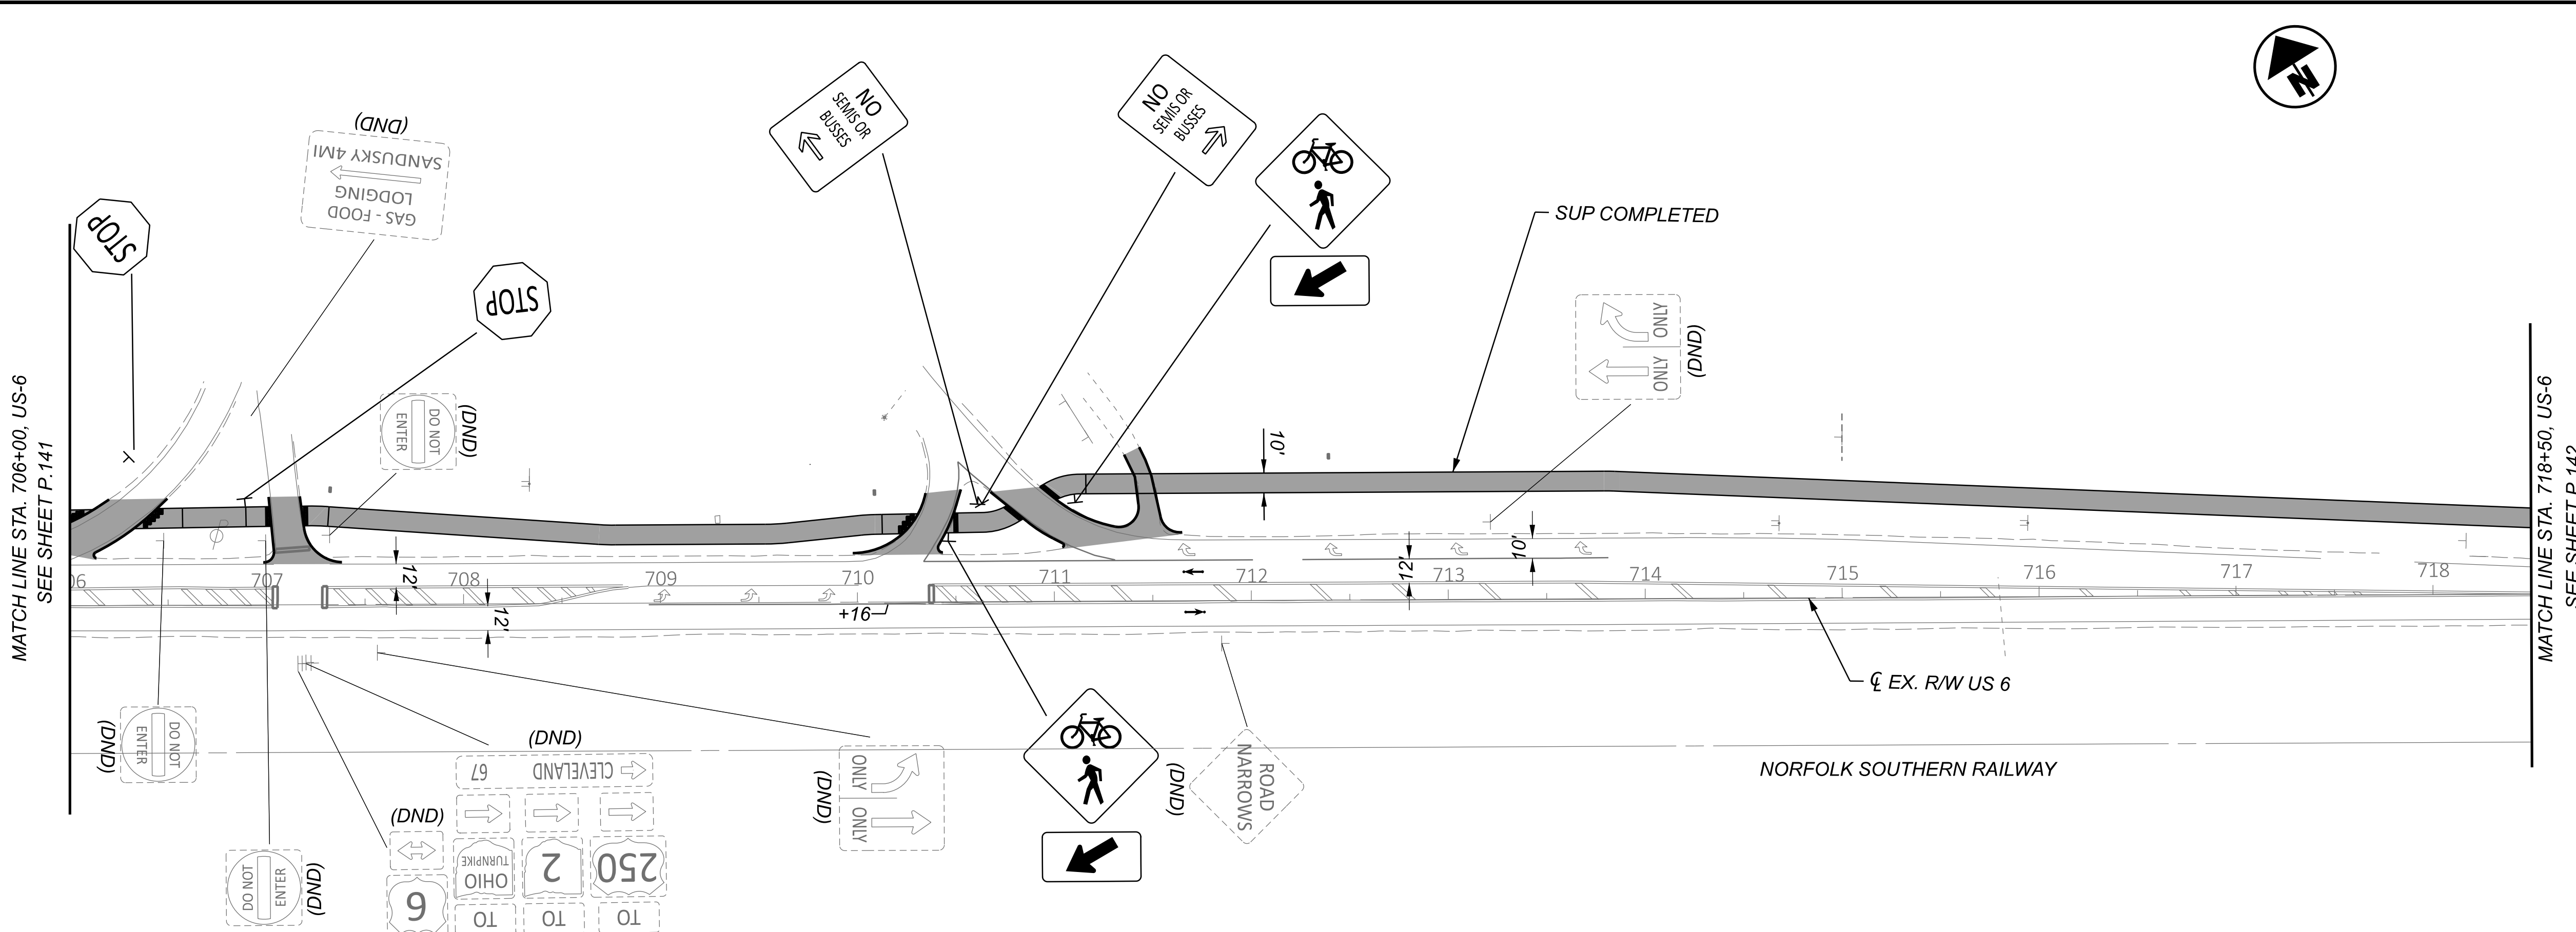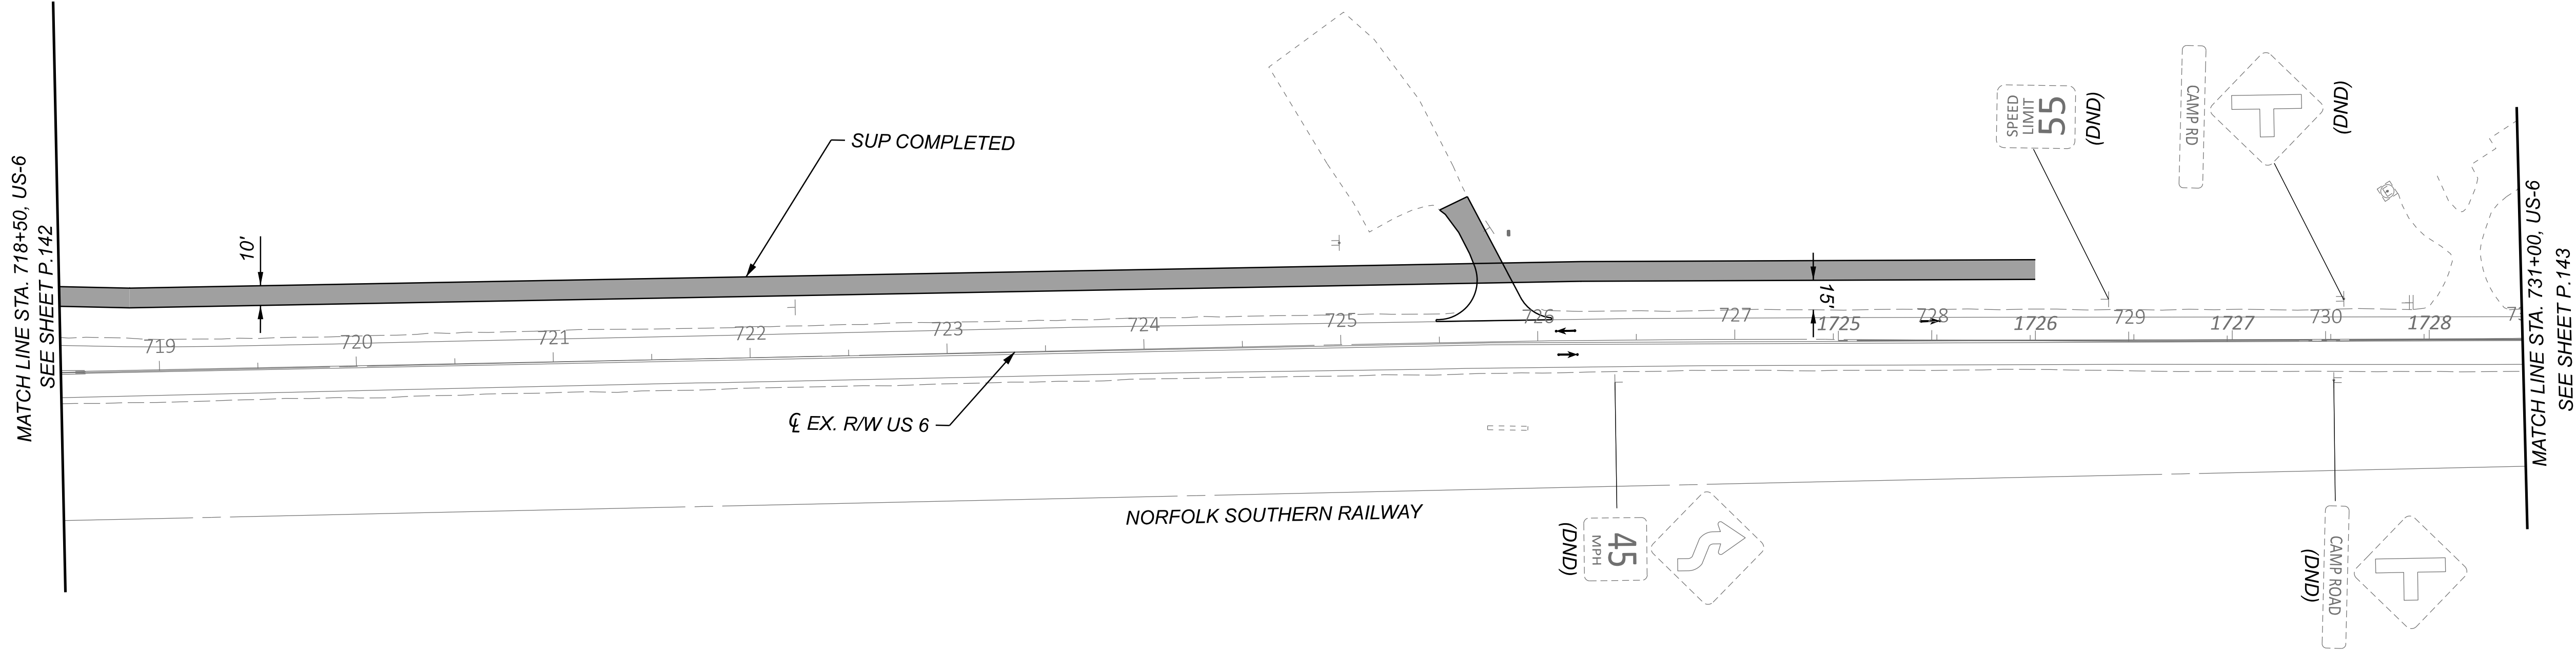


- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068 .
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 706+00.00 TO STA. 730+00.00

DESIGN AGENCY	
TRANSYSTEMS 400 W. NATIONWIDE BLVD., STE 225 COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.145	TOTAL 782



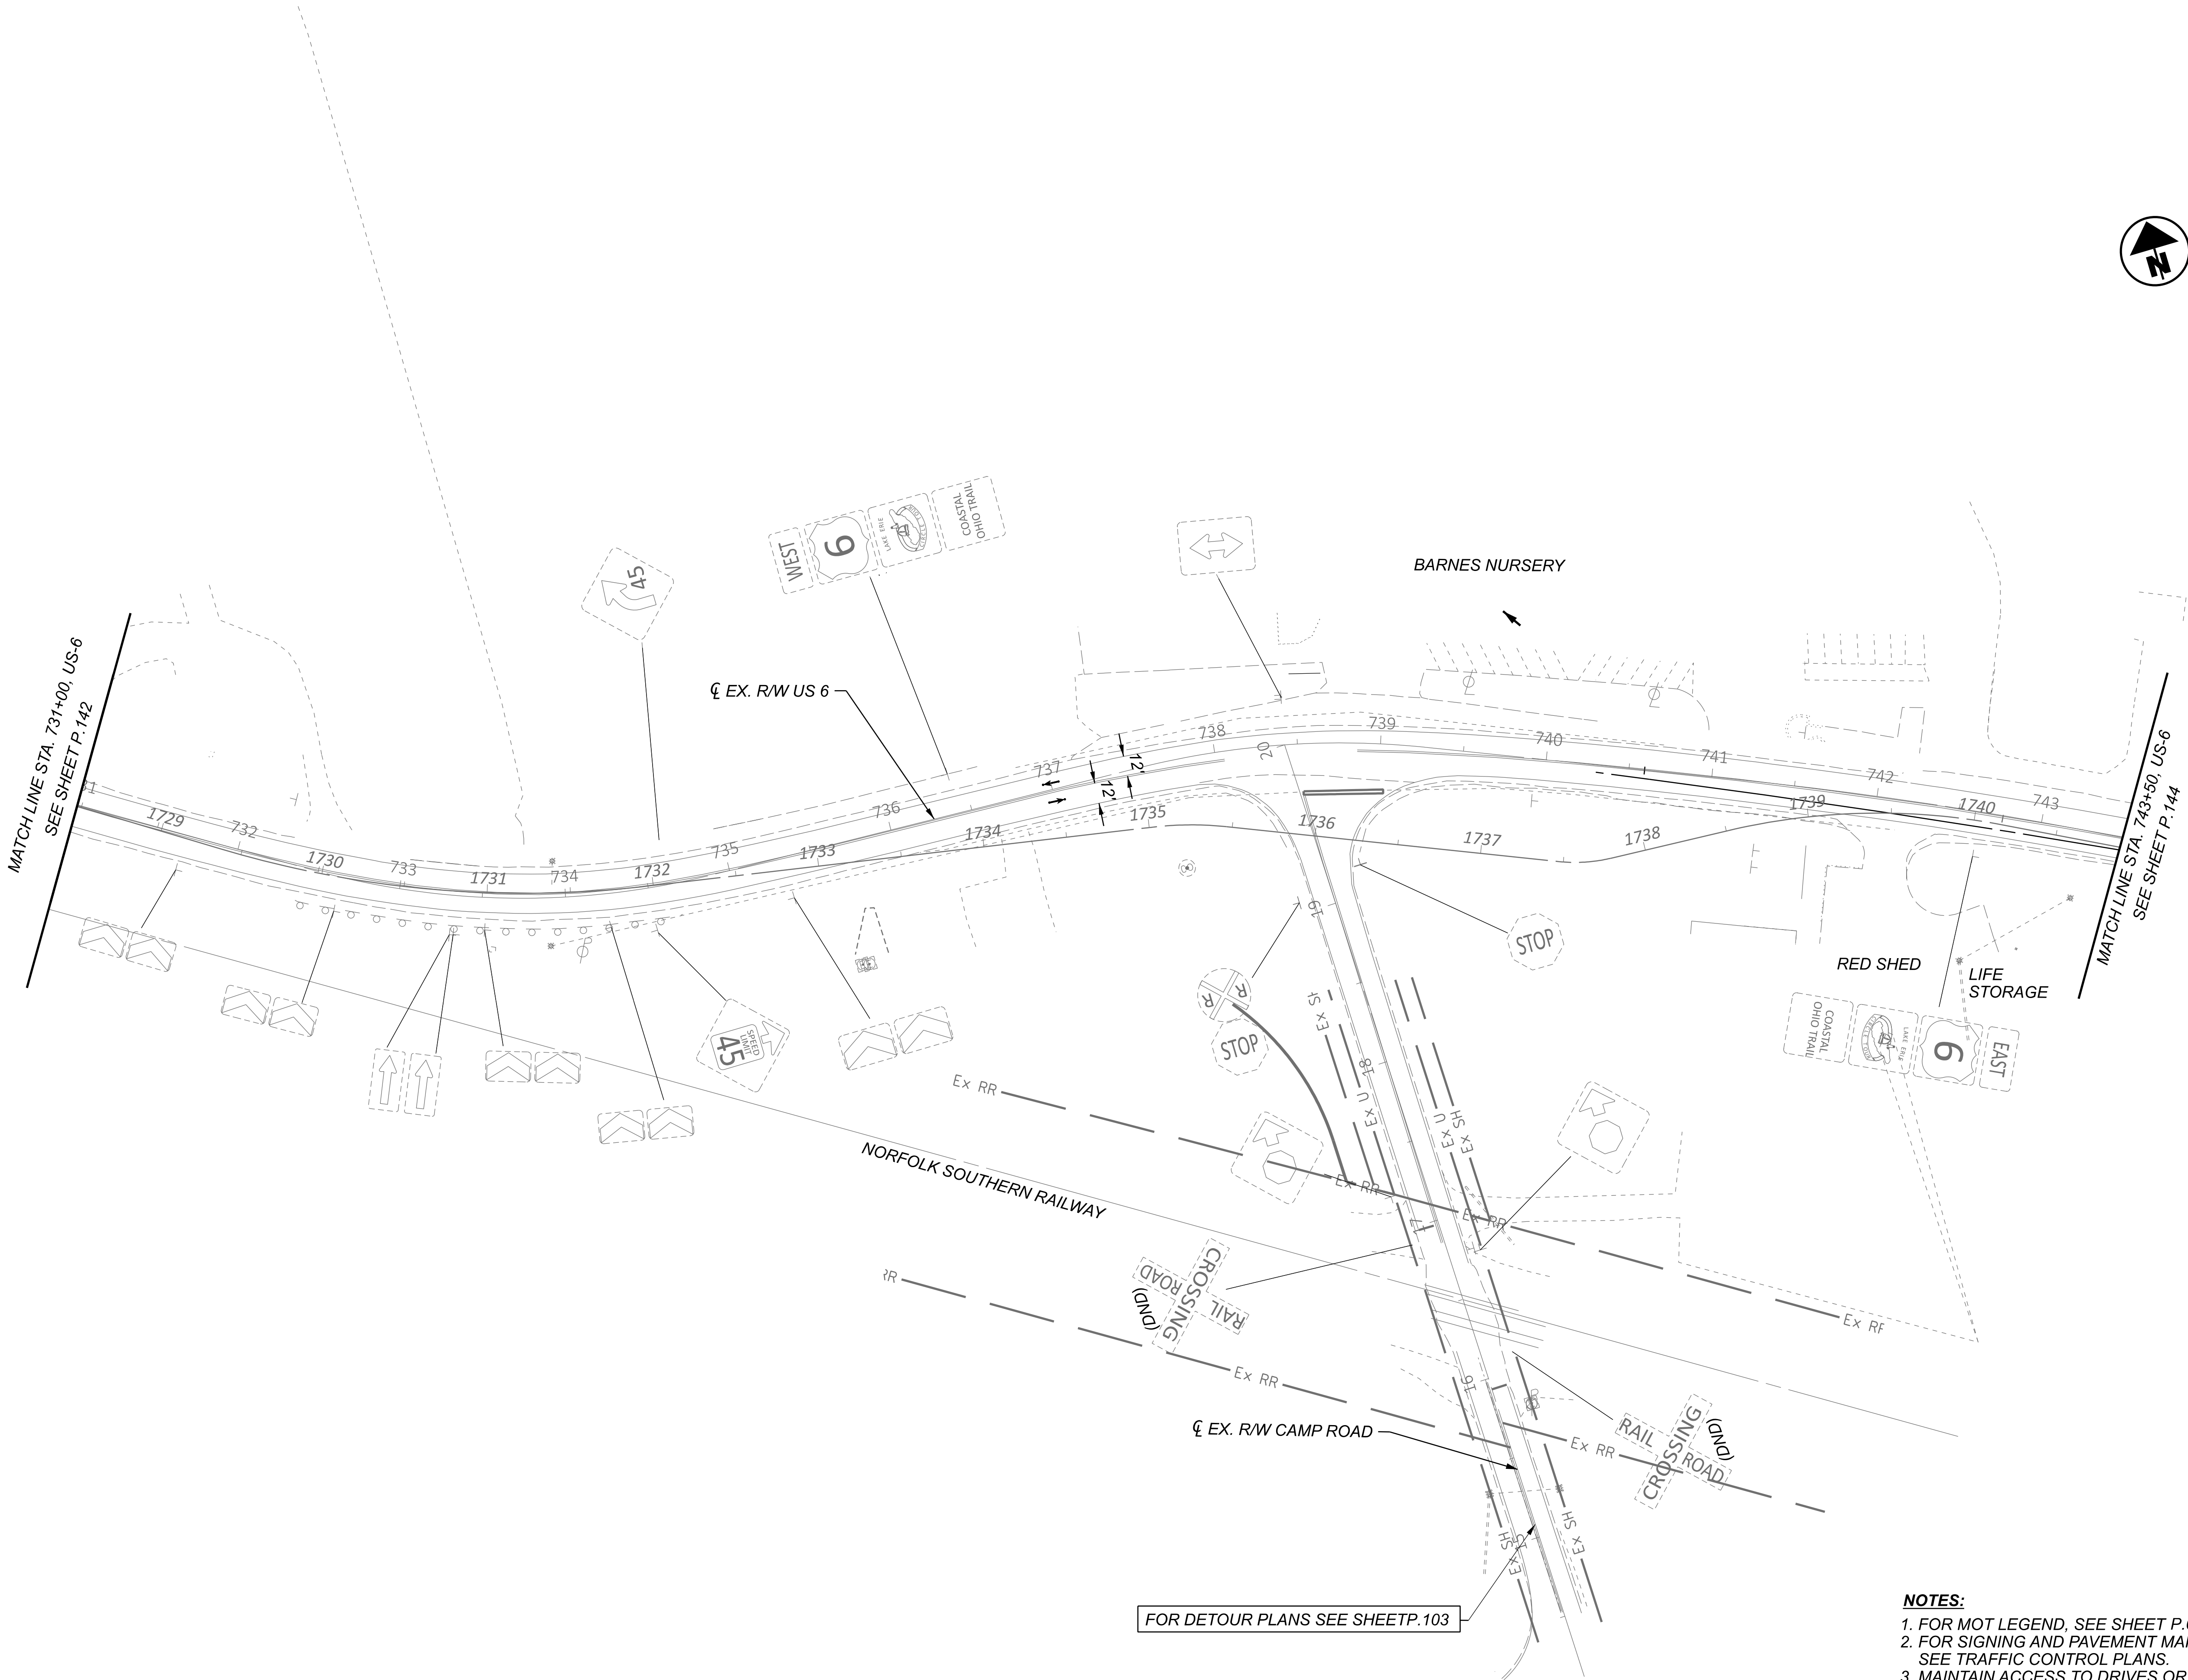

FOR DETOUR PLANS SEE SHEET P.103

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068 .
 - 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 731+00.00 TO STA. 743+50.00


DESIGN AGENCY
TRANSYSTEMS
400 W. WATKINSON BLVD., STE. 225
COLUMBUS, OHIO 43215

DESIGNER
SSA

REVIEWER
SS 02/28/24


PROJECT ID
116570

SHEET	TOTAL
P.146	782

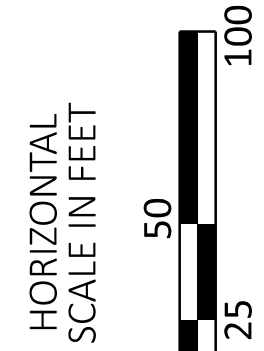

ERI-US 0006-CONNECTIVITY CORRIDOR


MODEL: CLP_SUP 1 - Plan 15-16 [Sheet] PAPER SIZE: 34x22 (in.) DATE: 6/9/2025 TIME: 5:35:39 PM USER: ssadusei
pw:\ohiodot-pw\entley.com\ohiodot-pw-02\Documents\01 Active Projects\District 03\Err\116570\402-Engineering_Transystems\MOT\Sheets\116570_MP001_2026.dgn

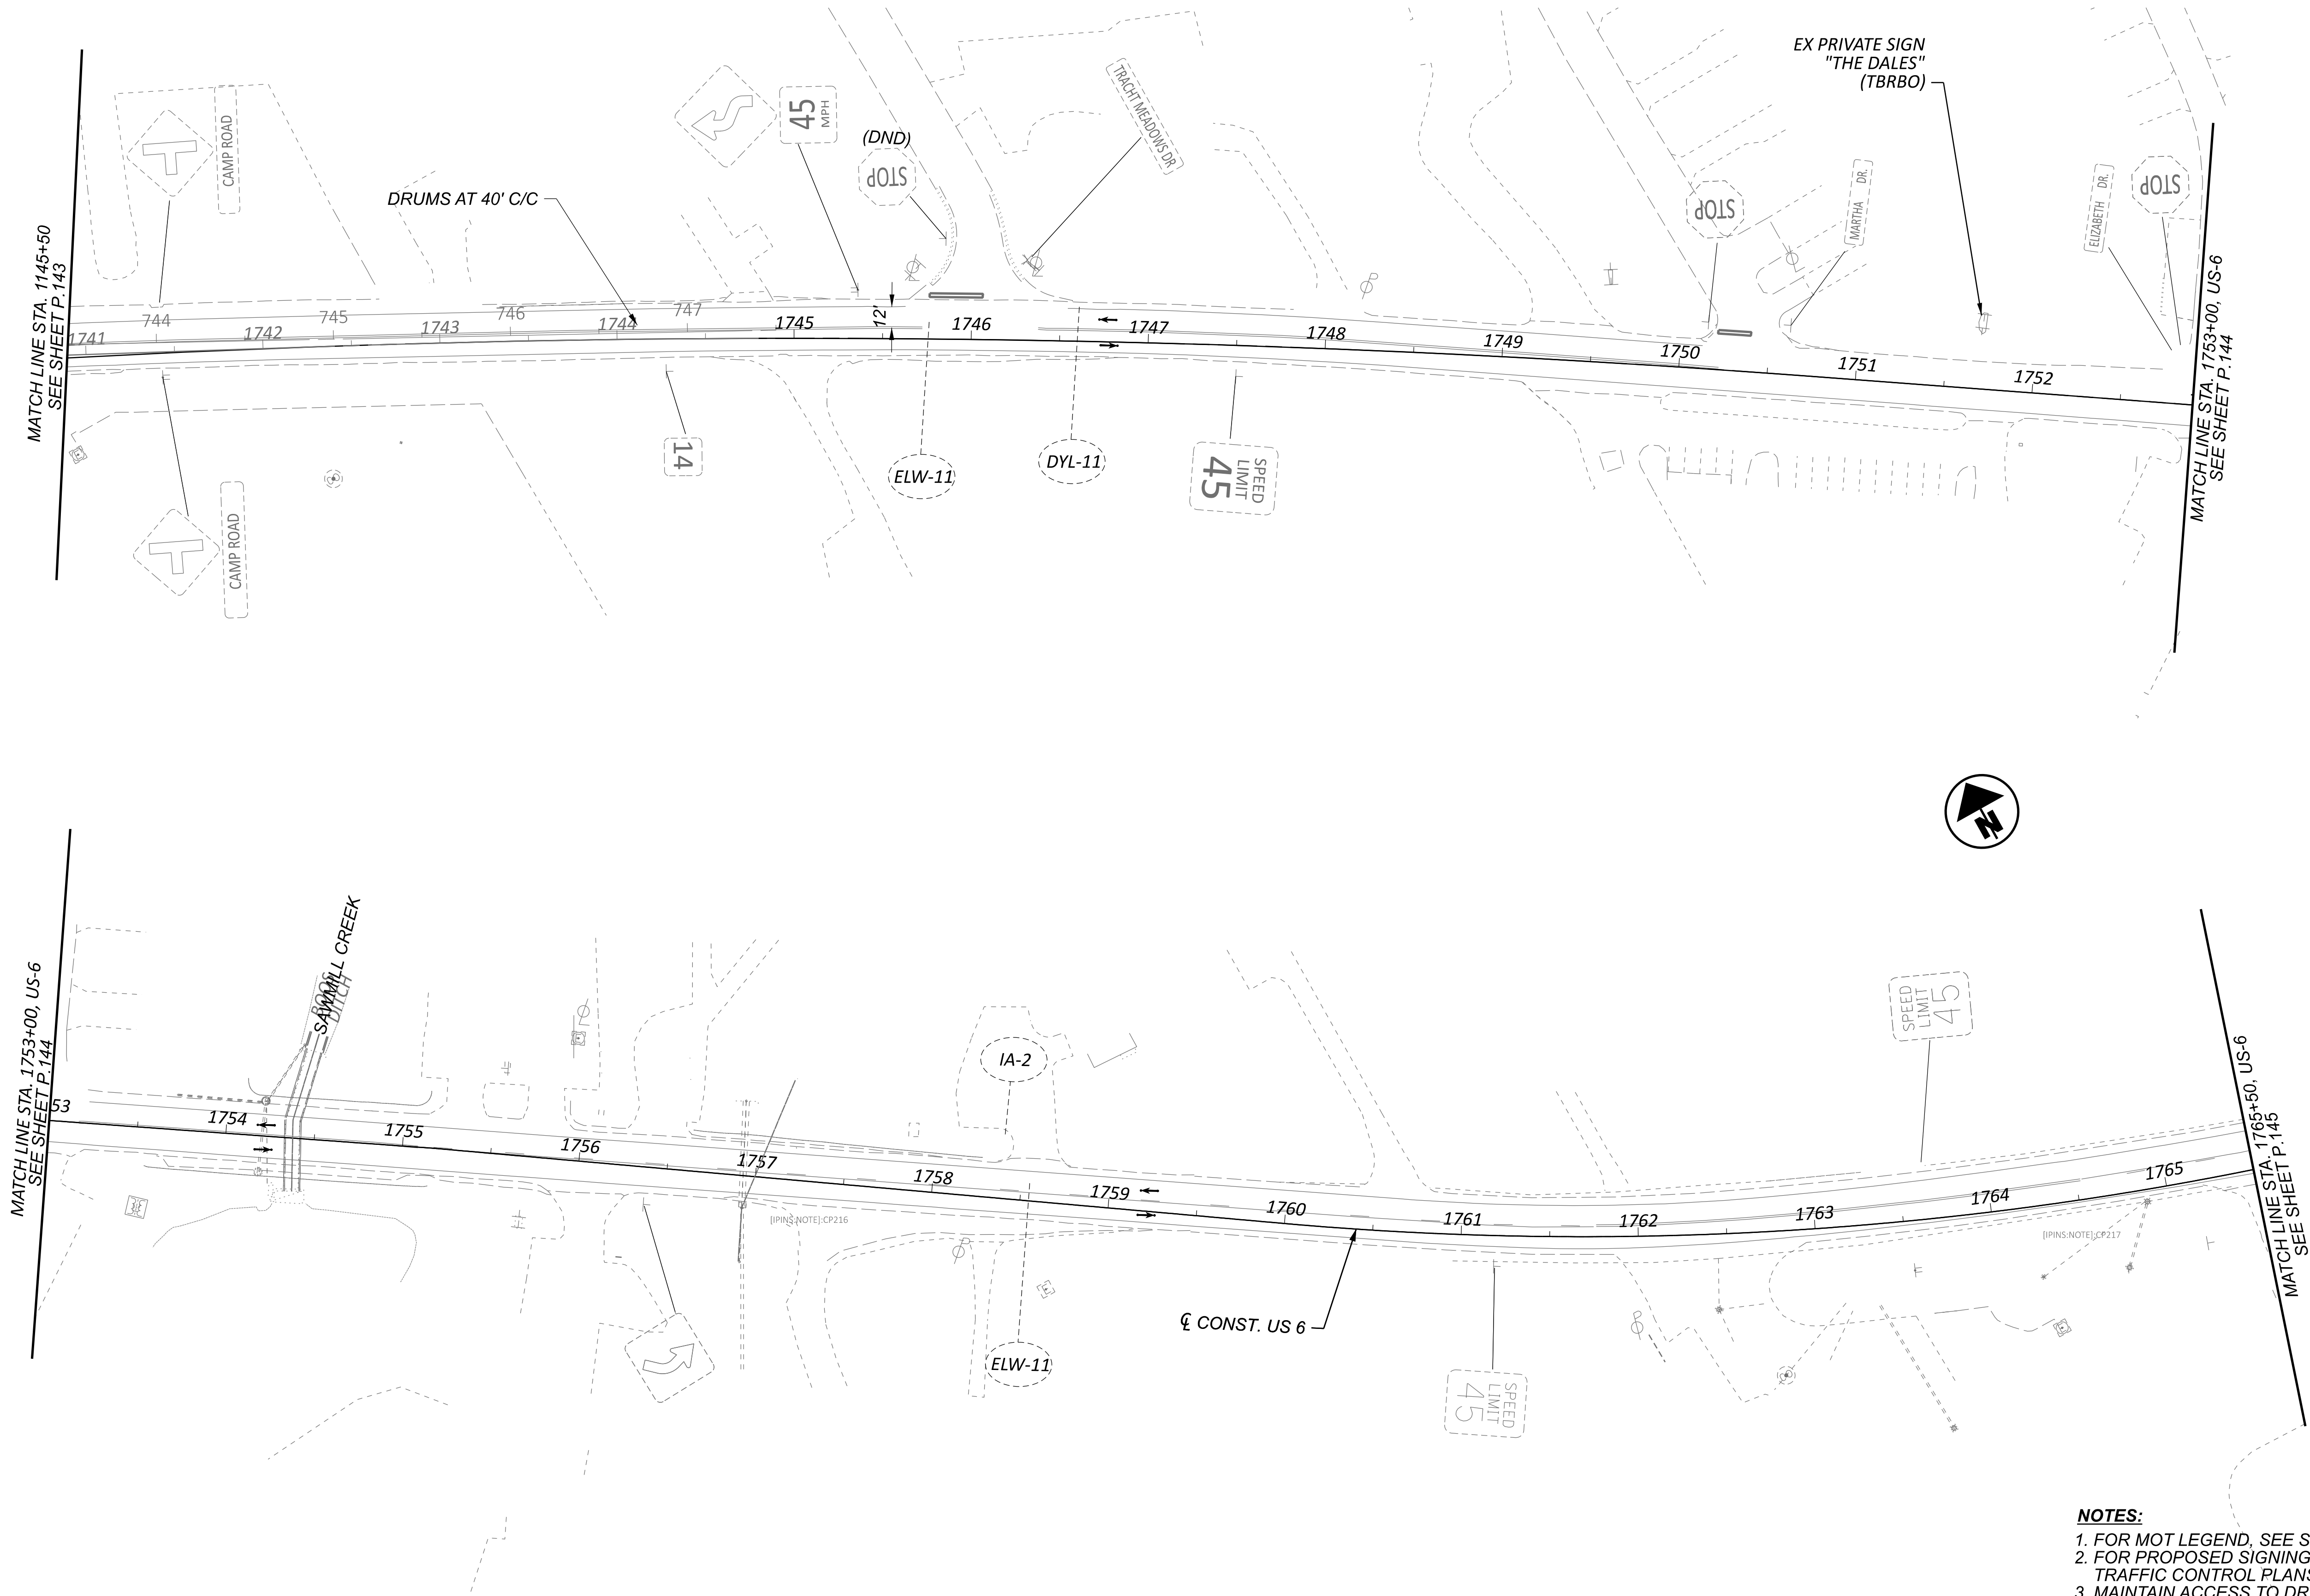

- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068.
 - 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


DESIGN AGENCY	
TRANSYSTEMS	
400 W. NATIONWIDE BLVD., STE 225	
COLUMBUS, OHIO 43215	
DESIGNER	
SSA	
REVIEWER	
SS 02/28/24	
PROJECT ID	
116570	
SHEET	
P.147	TOTAL
	782

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - EX. US 6 STA. 743+50.00 TO CONST. US 6 STA. 1765+50.00



ERI-US 0006-CONNECTIVITY CORRIDOR

MODEL: CLP_SUP 1 - Plan 17-18 [Sheet] PAPER: 34x22 (in.) DATE: 6/9/2025 TIME: 5:35:43 PM USER: ssadusei
 www.vohiodod-pw.bentley.com:ohiodod-pw-02/Documents/01 Active Projects/District 03/Erie/116570/402_Engineering_TransSystems\WOT\Sheets\116570_MP001_2026.dgn

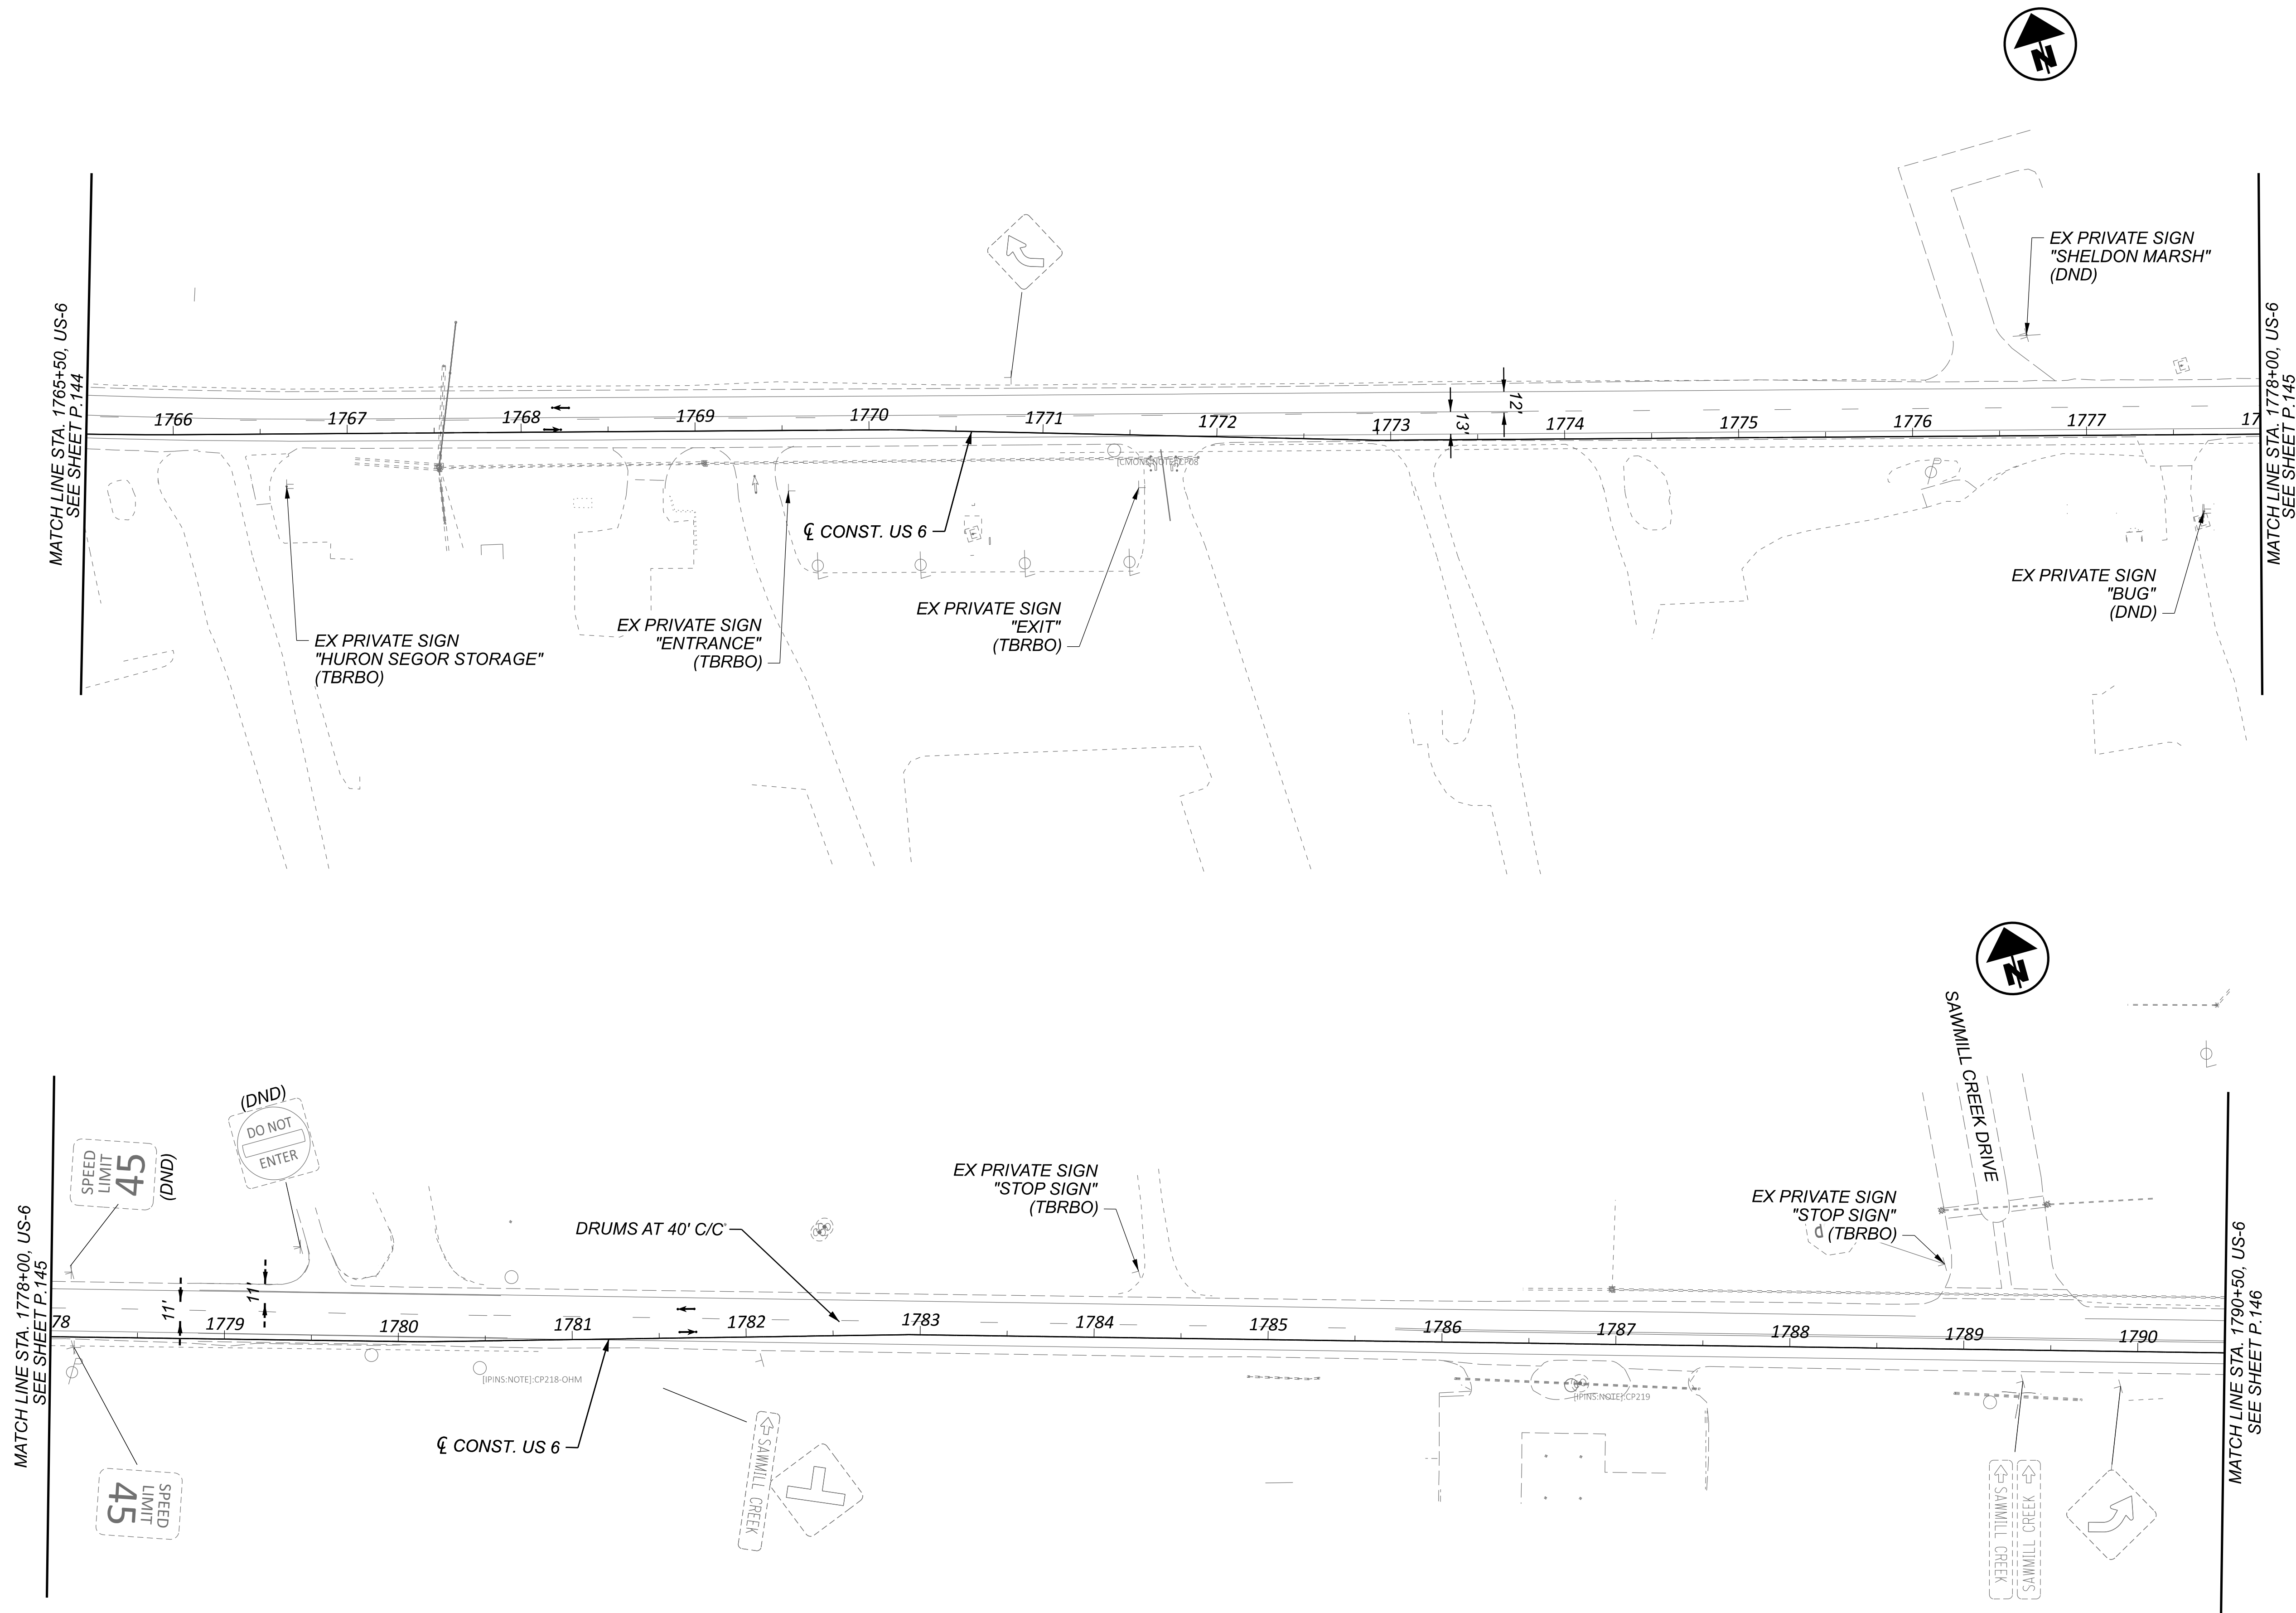

NOTES:

1. FOR MOT LEGEND, SEE SHEET P.068.
2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.


DESIGN AGENCY


TRANSYSTEMS

400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.148	782

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US 6 - STA. 1765+50.00 TO STA. 1790+50.00





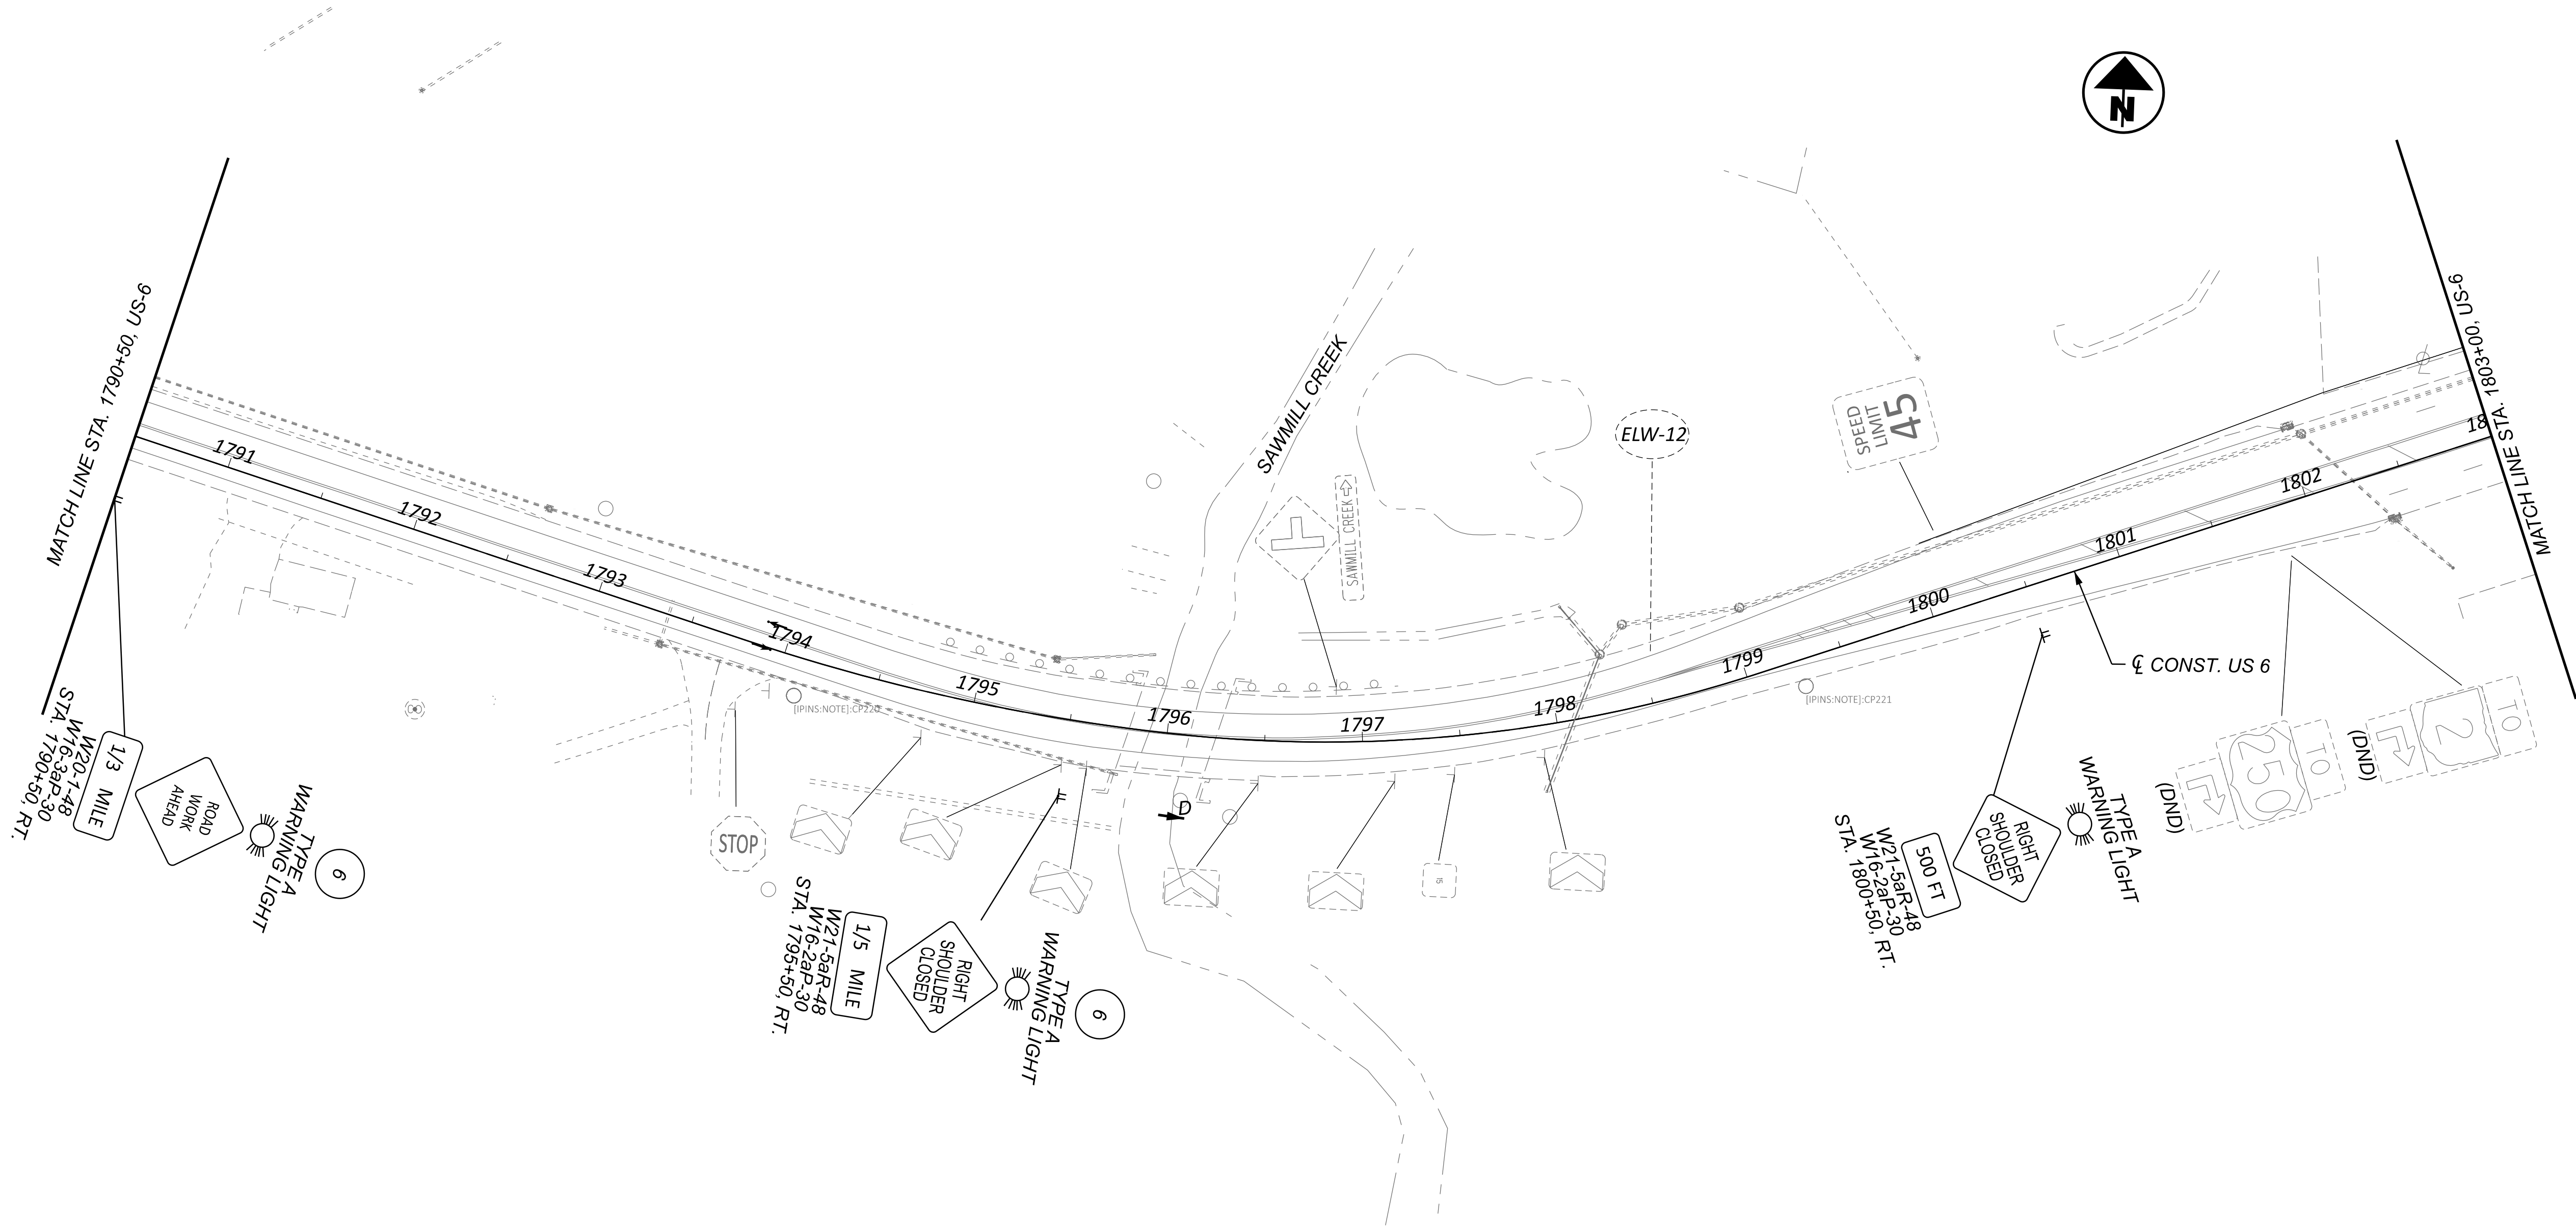



- NOTES:**
- 1. FOR MOT LEGEND, SEE SHEET P.068 .
 - 2. FOR SIGNING AND PAVEMENT MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 - 3. FOR SECTION D-D, SEE SHEET P.113 .
 - 4. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATIONS AS NECESSARY.

MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
US - 6 STA. 1790+50.00 TO STA. 1803+00.00


DESIGN AGENCY	
TRANSYSTEMS 400 W. WATSONWIDE BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.149	782






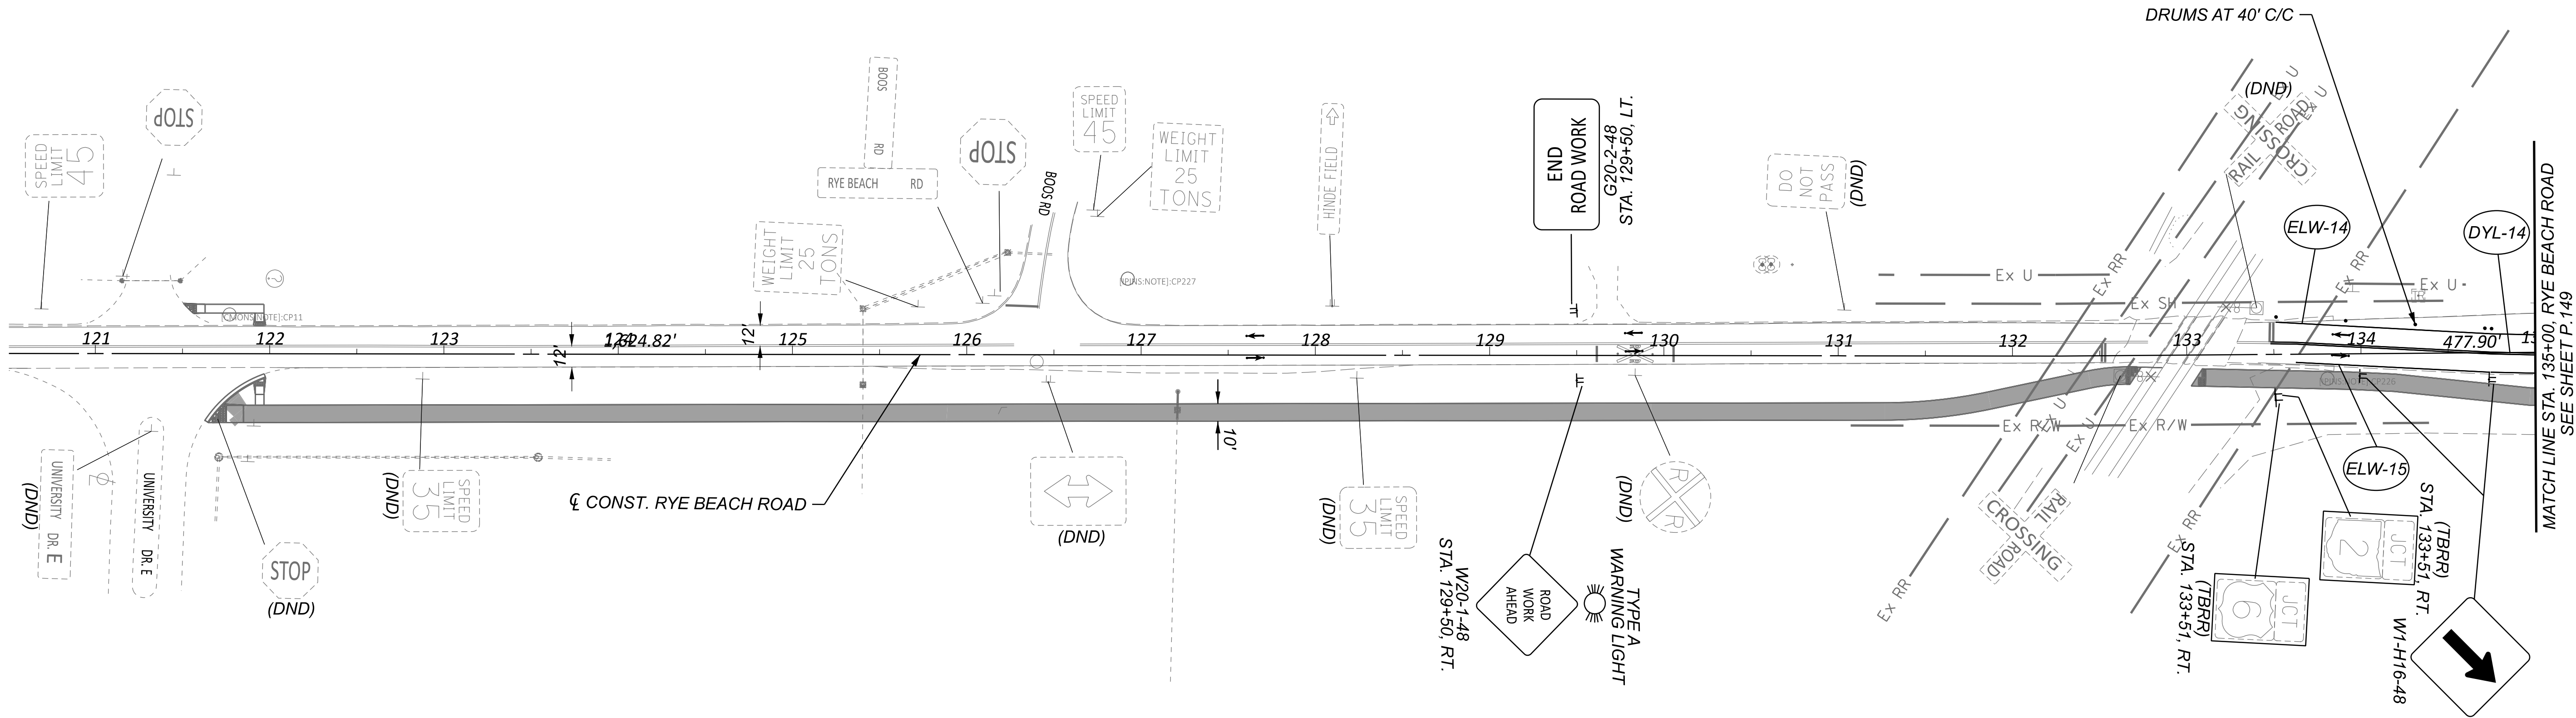



- NOTES:**
1. FOR MOT LEGEND, SEE SHEET P.068.
 2. FOR PROPOSED SIGNING AND MARKING DETAILS, SEE TRAFFIC CONTROL PLANS.
 3. MAINTAIN ACCESS TO DRIVES OR SIDE ROADS AT ALL TIMES. USE FLAGGING OPERATION AS NECESSARY.




MAINTENANCE OF TRAFFIC - PHASE 1 (2026 CONSTRUCTION)
RYE BEACH ROAD - BEGIN PROJECT TO STA. 135+00.00



TRANSYSTEMS 400 W. WATKINSON BLVD., STE. 225 COLUMBUS, OHIO 43215	
DESIGNER	SSA
REVIEWER	SS 02/28/24
PROJECT ID	116570
SHEET	TOTAL
P.151	782

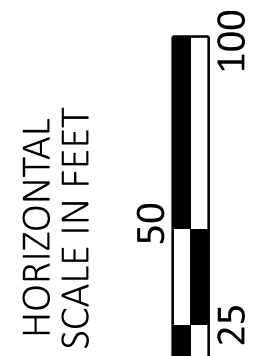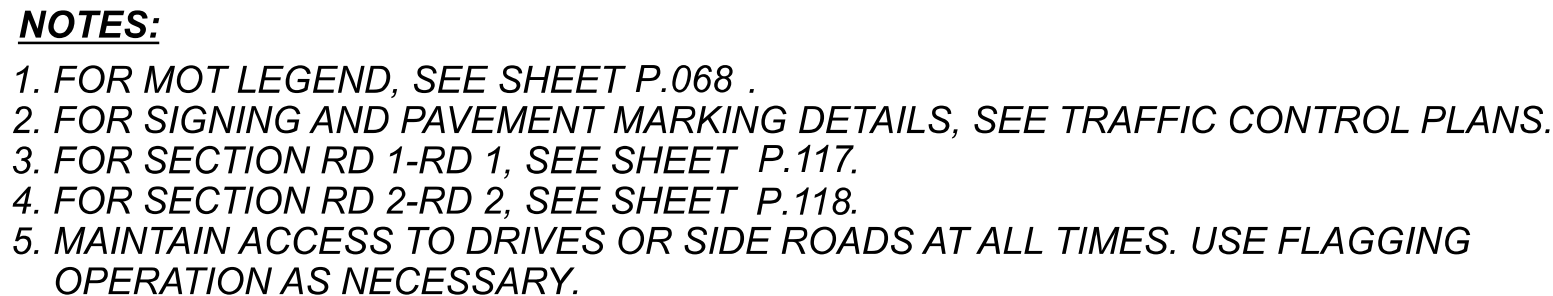

pw:\\ohiodot-pw.bentley.com:ohiodot-pw-02\\Documents\\01 Active Projects\\District 03\\Erie\\116570\\402-Engineering TransSystems\\MOT\\Sheets\\116570 MP001 2026.dgn



21



R3-1-48
STA. 153+75, LT.
(PER SCD MT-98.30)

23

TYPE A
WARNING LIGHT



RAMP
CLOSED
AHEAD

E5-H2f-48
STA. 151+40. RT. &
STA. 156+00. LT.
(PER MT-98.30)

25

TYPE A
WARNING LIGHT

ROAD
WORK
AHEAD

W20-1-48
(PER SCD MT-98.30)
STA. 157+00, LT.

HORIZONTAL
SCALE IN FEET



25 50 100

TRANSYSTEMS
400 W. NATIONWIDE BLVD., STE 225
COLUMBUS, OHIO 43215

DESIGNER	
SSA	
REVIEWER	
SS	02/28/24
PROJECT ID	
116570	
SHEET	TOTAL
P.153	782
